Santa Ynez Valley Community Plan

ID	Task Name	Baseline Start	Baseline Finish	Start	Finish
1	3rd District Consultations/memos	NA	NA	Mon 4/4/05	Mon 9/19/05
2	VPAC Meetings re: Mixed-Use, Housing, & Design	Mon 4/4/05	Fri 5/27/05	Mon 4/4/05	Fri 5/27/05
3	Initiated Community Plan Recompiled and Updated	NA	NA	Tue 8/16/05	Thu 9/15/05
4	VPAC Meeting Prep re: Montanaro\Corner Park	NA	NA	Wed 10/12/05	Wed 10/19/05
5	Prepare Heritage Sites\Downzone Memo	NA	NA	Mon 10/10/05	Fri 10/14/05
6	VPAC Meeting re: Montanaro\Corner Park	NA	NA	Wed 10/19/05	Wed 10/19/05
7	Consult w/ 3rd Dist. Re: Reevaluation of Community Plan Components	NA	NA	Thu 10/20/05	Fri 12/30/05
8	VPAC Meetings re: Downzones & others	NA	NA	Mon 1/2/06	Fri 4/28/06
9	VPAC Meetings TBD	NA	NA	Mon 1/2/06	Wed 2/28/07
10	Docket, hearing prep, Notice PC Hearing	NA	NA	Mon 5/1/06	Fri 5/12/06
11	BOS Re-initiation	NA	NA	Mon 5/15/06	Fri 5/26/06
12	Revise NOP & EIR Scoping Summary	Mon 6/13/05	Mon 6/20/05	Mon 5/29/06	Mon 6/5/06
13	**Release NOP & EIR Scoping Summary**	Mon 6/20/05	Mon 6/20/05	Mon 6/5/06	Mon 6/5/06
14	**Environmental Review**	Tue 6/21/05	Wed 4/12/06	Tue 6/6/06	Wed 3/21/07
15	NOP 30 days Public Comment Period	Tue 6/21/05	Wed 7/20/05	Tue 6/6/06	Wed 7/5/06
16	EIR Scoping Hearing	Mon 7/4/05	Mon 7/4/05	Mon 6/19/06	Mon 6/19/06
17	Prepare Admin Draft EIR	Tue 7/5/05	Fri 10/14/05	Tue 6/20/06	Mon 10/2/06
18	Internal County Review & Finalize Admin Draft EIR	Fri 10/14/05	Fri 12/16/05	Tue 10/3/06	Wed 11/29/06
19	Print Draft EIR	Tue 12/13/05	Tue 12/20/05	Tue 11/28/06	Mon 12/4/06
20	NOC Draft EIR	Fri 12/16/05	Tue 12/20/05	Thu 11/30/06	Mon 12/4/06
21	Release Draft EIR	Tue 12/20/05	Tue 12/20/05	Mon 12/4/06	Mon 12/4/06
22	60 day Public Comment period	Wed 12/21/05	Mon 2/20/06	Tue 12/5/06	Thu 2/1/07
23	Environmental hearing	Fri 1/20/06	Fri 1/20/06	Mon 1/1/07	Mon 1/1/07
24	Respond to EIR Public Comments	Thu 2/23/06	Tue 3/28/06	Thu 2/1/07	Tue 3/6/07
25	Prepare Admin Draft FEIR	Tue 2/28/06	Tue 3/28/06	Wed 2/7/07	Tue 3/6/07
26	Internal Review & Finalize Admin Draft Final EIR	Wed 3/29/06	Fri 4/7/06	Wed 3/7/07	Fri 3/16/07
27	Printing Draft Final EIR	Wed 4/5/06	Wed 4/12/06	Wed 3/14/07	Wed 3/21/07
28	**Public Hearings/Implementation**	Thu 4/13/06	Fri 9/29/06	Wed 3/21/07	Fri 9/28/07
29	Prepare PC staff report	Thu 4/13/06	Thu 4/27/06	Wed 3/21/07	Wed 4/4/07
30	Docket, hearing prep, Notice PC Hearing	Thu 4/27/06	Thu 5/4/06	Wed 4/4/07	Wed 4/11/07
31	PC Hearings (6)	Thu 5/4/06	Tue 7/4/06	Wed 4/11/07	Wed 6/20/07
32	Prepare Board Staff Report	Tue 7/4/06	Fri 7/14/06	Wed 6/20/07	Wed 7/4/07
33	Docket, hearing prep, Notice PC Hearing	Fri 7/14/06	Fri 7/21/06	Wed 7/4/07	Wed 7/11/07
34	Board Hearings (4)	Fri 7/21/06	Fri 9/8/06	Wed 7/11/07	Wed 9/5/07
35	Implementation	Fri 9/8/06	Fri 9/29/06	Wed 9/5/07	Fri 9/28/07

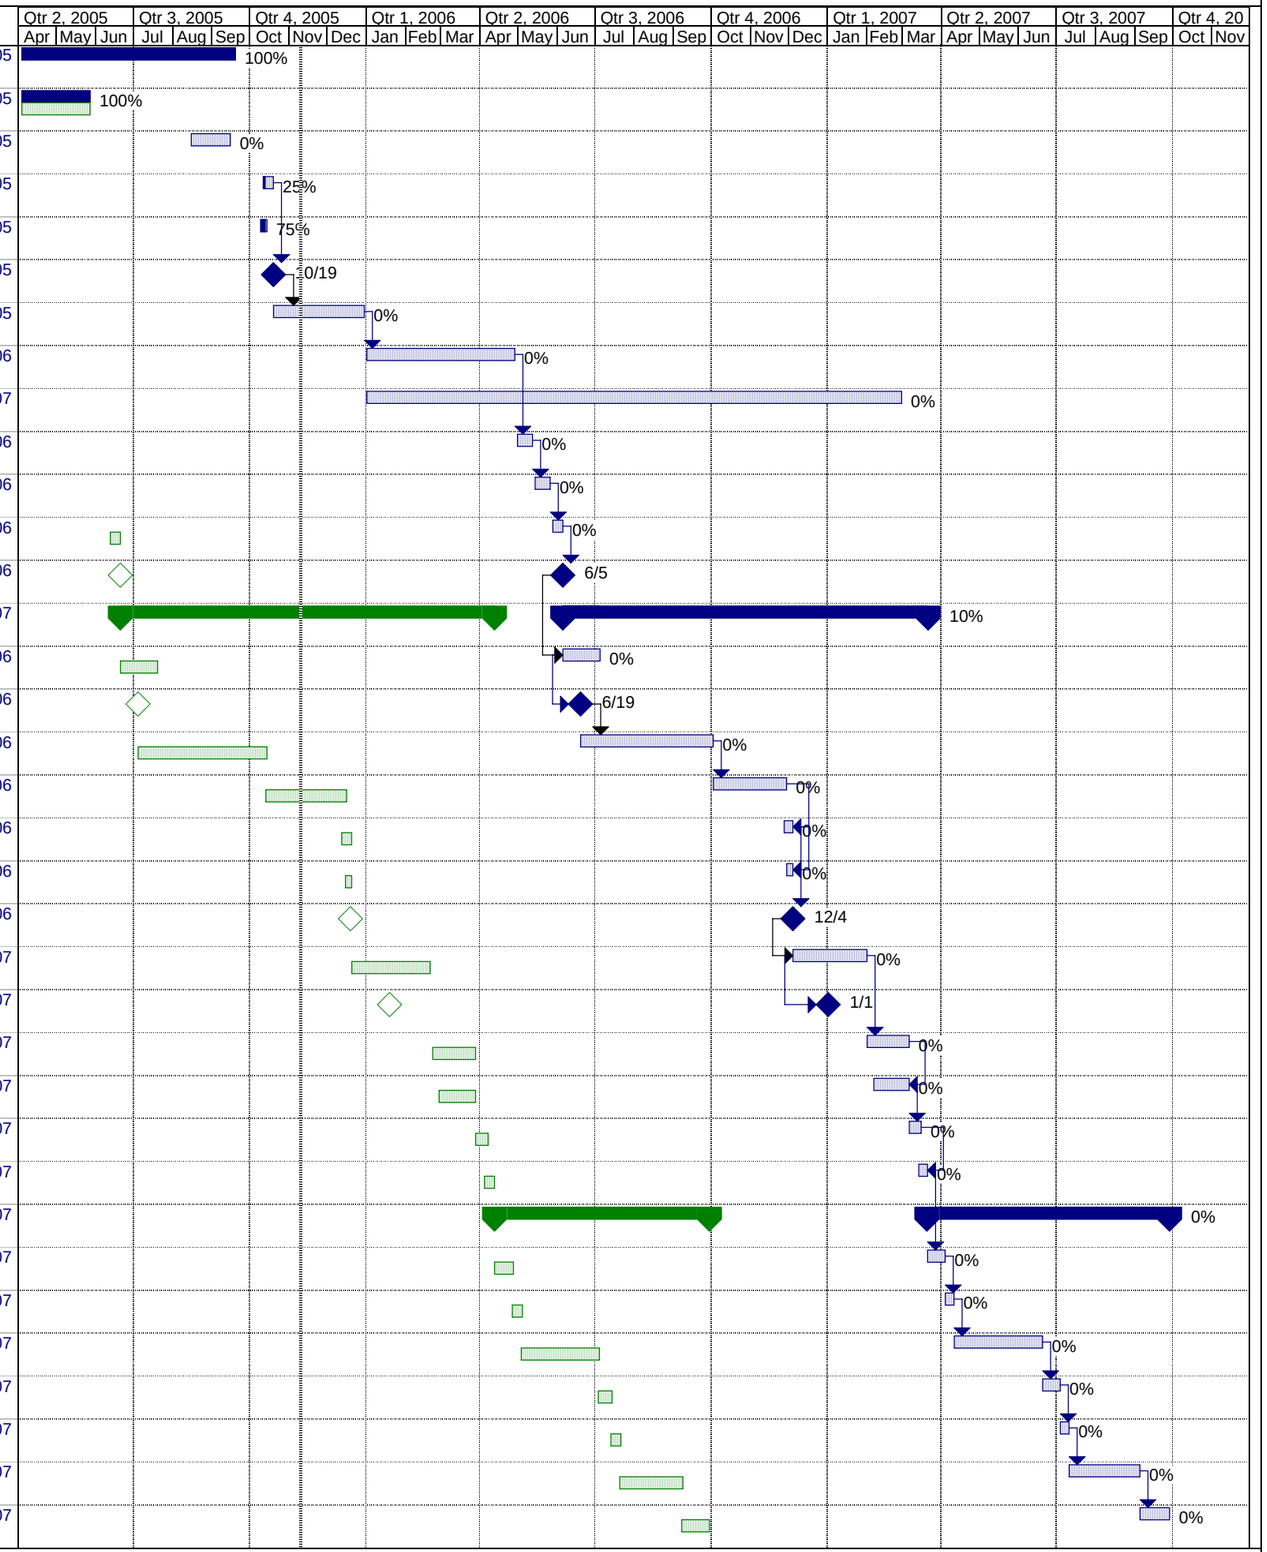

Pink - New Tasks / **Green** - Baseline Schedule, **Blue** - Revised Schedule
