Docusign Envelope ID: BDFFABE1-7061-435E-B267-F8568CF044D6

COUNTY OF SANTA BARBARA
AGREEMENT FOR:
General Services Project No. PRJ-001065 (25107)
County of Santa Barbara
REHABILITATE TIE-DOWN APRON
900 AIRPORT ROAD, SANTA YNEZ, CALIFORNIA
BC: _____-_____

THIS AGREEMENT ("Agreement") is made by and between the County of Santa Barbara, a political subdivision of the State of California ("**COUNTY**"), and AMERICAN ROAD MAINTENANCE, INC. ("**CONTRACTOR**" and together with COUNTY, collectively, the "Parties" and each individually a "Party"), for the completion of the Work (defined below), on the following terms, conditions, and provisions. All references in the General Terms to the "Agreement" shall have the meaning ascribed to the term "Agreement" in the immediately preceding sentence.

1. CONTRACT: This Agreement incorporates by reference all of the General Conditions and Special Conditions, Specifications and Drawings provided by the COUNTY for the REHABILITATE TIE-DOWN APRON, Project No. PRJ-001065 (25107), the Invitation for Bids as amended by Addenda Number 1 and 2, the Bid Bond, the Performance Bond, the Payment Bond, and the bid documents executed and submitted by the CONTRACTOR for the Project ("Bid"), to the extent the Bid is consistent with the provisions of this Agreement other than the Bid (all of the foregoing documents, together with this Agreement, collectively, the "Contract" or "Contract Documents"). A copy of each of the General and Special Conditions, Specifications and Drawings provided by the COUNTY for the REHABILITATE TIE-DOWN PROJECT, PRJ-001065 (25107), the Notice to Bidders, the Bid Bond, the Performance Bond, and the Payment Bond are attached hereto as EXHIBIT A, and a copy of the Bid is attached hereto as EXHIBIT B. All capitalized terms used but not defined herein shall have the respective meanings ascribed to such terms in the Notice to Bidders. Copies of all Contract Documents are on file in the Department of General Services Office of the COUNTY, and have been and will be made available to the CONTRACTOR during the term of this Agreement. CONTRACTOR acknowledges receipt of all Contract Documents.

2. WORK: CONTRACTOR, at CONTRACTOR's own cost and expense, shall perform all the work described in the Contract Documents ("Work"), and shall furnish all equipment and materials necessary to perform and complete the Work, in a good and workmanlike manner and to the satisfaction of the Director of the COUNTY's General Services Department ("Director"), or the Director's designee, all in strict accordance with the Contract Documents.

3. EXCAVATIONS: Before any pavement resurfacing, displacement, or excavation of the ground that may be required in connection with the Work under this Contract, the CONTRACTOR shall obtain an inquiry identification number by calling Underground Service Alert (USA) 1 (800) 422-4133 or by such other means as may be required; shall conform to all requirements of Sections 4215 through 4217 of the Government Code regarding any such pavement resurfacing, displacement or excavation, including the payment of any fees required; and shall facilitate performance by the COUNTY of any obligation required of the COUNTY under the Government Code. There shall be no performance under this Contract by either party hereto unless and until CONTRACTOR complies with all of the foregoing provisions of this Sections 3, and notifies the County Representative (defined below) in writing regarding such compliance.

4. COUNTY REPRESENTATIVE: The "County Representative" referred to in the Contract Documents is STEVEN MANUEL.

5. PAYMENT: As full compensation for furnishing all labor, supervision, overhead, materials, and equipment and for completing all of the Work contemplated by this Contract, and subject to adjustments and liquidated damages, if any, as provided in the Contract Documents, the base amount to be paid to the CONTRACTOR for satisfactory completion of all requirements of the CONTRACTOR under this Contract is and shall be THREE HUNDRED EIGHTY-EIGHT THOUSAND, THREE HUNDRED FIFTY DOLLARS AND ZERO CENTS ($388,350.00) ("Base Contract Amount"), to be paid as provided in the Contract Documents. CONTRACTOR assumes and will provide against any loss or damage arising out of the nature of the Work undertaken, or the action of the elements, or from any unforeseen difficulties or obstructions which may arise or be encountered in the performance of the Work until its acceptance by the COUNTY, and assumes any and all expenses incurred by or in consequence of suspension or discontinuance of the Work, for well and faithfully completing the Work and the whole thereof, in the manner and to

Docusign Envelope ID: BDFFABE1-7061-435E-B267-F8568CF044D6

the requirements of the Contract and directions of the County Representative to the extent not inconsistent with any provisions of the Contract Documents.

6. **RIGHT TO AUDIT**: CONTRACTOR shall maintain and make available all books, papers, records, detail costs, estimates, claims, and accounts, including payment, property, payroll, personnel, subcontractors, and financial records related to or which arise in connection with the Contract (collectively, the "Records"). The form of record keeping with respect to the Records shall be subject to approval by COUNTY. The Records shall be made available during normal business hours for examination by COUNTY or the County Representative and shall be retained at CONTRACTOR'S principal place of business in California for audit during normal business hours at such place for four (4) years after the recording of the Notice of Completion for the Project. CONTRACTOR shall provide an office in which COUNTY and the County Representative may conduct such audit(s).

The COUNTY will have the right to audit CONTRACTOR'S Project records. Records must be made available in a form satisfactory to the Santa Barbara County Auditor-Controller.

7. EXTRA WORK: Extra work and materials, may only be authorized via written Change Order(s) duly executed by the Director or his designee in accordance with Section 30, below, including Change Order(s) providing for compensation in addition to the Base Contract Amount; *provided*, *however*, that the aggregate amount of such compensation in addition to the Base Contract Amount that may be authorized by the Director or his designee pursuant to duly executed Change Orders shall not exceed $31,917.50 ("Contingency Amount"). Compensation in such other equitable amount as is appropriate for the requirements of the COUNTY may be authorized by resolution or minute order of the Santa Barbara County Board of Supervisors.

8. COMPLIANCE WITH LAW: CONTRACTOR shall keep fully informed of, and shall at all times during the Term (defined below) ensure the performance of the Work is in compliance with, all laws, statutes, ordinances, decrees, orders, and regulations which do or may affect the Project, performance of the Work, the materials used therein, or persons engaged in connection therewith, and all such orders of bodies and tribunals having any jurisdiction over same (collectively, "Applicable Laws"). If CONTRACTOR has reason to believe that any provision of the Contract Documents conflict with any Applicable Law(s), the CONTRACTOR shall immediately report same to the County Representative in writing. CONTRACTOR shall at all times observe and comply with, and shall cause all agents, employees, and subcontractors to observe and comply with, all Applicable Laws. CONTRACTOR acknowledges and shall comply with the provisions of Sections 9364 and Sections 9550 and 9566, inclusive, of the Civil Code of California.

9. PAYMENTS NOT ACCEPTANCE: No certificate given or payments made under this Contract, except the final payment hereunder, shall be evidence of the performance of this Contract, either wholly or in part, against any claim upon CONTRACTOR. Final payment for the Work performed under this Contract shall not be made until the lapse of thirty (30) days after the Notice of Completion of the Work has been filed for record and no payment shall be construed to be acceptance of any defective Work or improper materials. CONTRACTOR agrees that the payment for final quantities due under this Contract and the payment of amounts due for any Work in accordance with this Contract shall release the COUNTY from any claims or liabilities on account of Work performed under this Contract, as the same may be amended from time to time during the Term. In addition to guarantees required elsewhere, CONTRACTOR shall and does hereby guarantee all workmanship and material to be free of defects and fit for the purposes intended for a period of one year from and after both the date of acceptance of the work and the recordation of the Notice of Completion by the COUNTY and CONTRACTOR shall repair or replace all Work and materials, together with any other portions of the Work which may be displaced in so doing, that, in the opinion of the County Representative, is or becomes defective during the period of said guarantee, without expense whatsoever to the COUNTY.

10. PREVAILING WAGE RATES: Rates of wages, including overtime, holiday, and Sunday rates provided for the Work shall comply with and are subject to the California Labor Code, Sections 1770 et. seq., Executive Orders of the President of the United States No. 9240, dated September 9, 1942, and No. 9250, dated October 3, 1942, and to any modifications thereof, and to and any orders of the President or any authorized Federal Officer or agency, insofar as the same may apply to this Contract.

No contractor or subcontractor may be listed on a bid for a public works project unless registered with the Department of Industrial Relations pursuant to Labor Code section 1725.5 [with limited exceptions from this requirement for bid purposes only under Labor Code section 1771.1(a)]. No contractor or subcontractor may be awarded a contract for public work on a public works project unless registered with the Department of Industrial Relations pursuant to Labor Code section 1725.5. This Project is subject to compliance monitoring and enforcement by the Department of

Docusign Envelope ID: BDFFABE1-7061-435E-B267-F8568CF044D6

Industrial Relations.

11. CONTRACT DOCUMENTS ACKNOWLEDGED: CONTRACTOR hereby declares that CONTRACTOR has read the Contract Documents, has carefully examined the plans and detailed drawings of the Work to be performed, and fully understands the intent and meaning of the same.

12. TIME FOR COMMENCEMENT, COMPLETION: The term of this Contract shall commence effective as of the first date that this Agreement is duly executed by all of the parties hereto ("Effective Date") and shall terminate on the date that is 180 calendar days after the Effective Date unless earlier terminated in accordance with the provisions of this Agreement ("Term"). As soon as practicable after the Contract has been executed by both the CONTRACTOR and the COUNTY, a Notice to Proceed will be issued by the County Representative stating the starting date of work performance under the Contract ("Work Start Date"). CONTRACTOR shall complete all Work specified in the Contract Documents within 50 working days after the Work Start Date ("Contract Time" as that term is used in the General Conditions). The provisions of this Agreement pertaining to Liquidated Damages shall apply in the event of the CONTRACTOR's failure to complete the Work within the Contract Time. In the event that CONTRACTOR does not complete the Work during the Term, CONTRACTOR shall only be paid for the Work actually performed during the Term and accepted by COUNTY in accordance with the provisions of this Agreement.

13. WORKERS' COMPENSATION INSURANCE: CONTRACTOR certifies that CONTRACTOR has knowledge of, is in compliance with, and warrants that CONTRACTOR at all times during the Term shall remain in compliance with, the provisions of Section 3700 of the Labor Code, which requires every employer to be insured against liability for Workers' Compensation or to undertake self-insurance by the provisions of that Code. CONTRACTOR shall comply with such provisions before commencing the performance of the Work.

14. PROGRESS PAYMENT; NO WAIVER FOR DELAY: Any progress payment made after the scheduled completion date for the Work shall not constitute a waiver of any liquidated damages under this Contract.

15. GUARANTEE BONDS: Before any performance under this Contract, the CONTRACTOR shall provide the security required by statute for the payment of all workers and suppliers, and security for the faithful performance of all terms and conditions of this Contract, in an amount and form approved by the COUNTY. Both securities shall contain provisions that automatically increase amounts thereof and/or time of completion or both for all change orders, extensions, and additions to the Work provided under this Contract.

16. DISPUTES: Should any dispute(s) arise respecting the construction or meaning of any of the plans or specifications affecting the Work or respecting the true value of any extra work or work omitted, such dispute(s) shall be resolved by the Director of the COUNTY's General Services Department or his Assistant Director of General Services designee ("Director"), whose decision shall be final and binding upon the parties hereto. If, after the decision of the Director as provided herein, claims (as defined in Public Contracts Code Section 20104) under this Contract are filed by CONTRACTOR against COUNTY, and those claims are in the aggregate amount of $375,000 or less, such claims shall be resolved under Public Contracts Code Sections 20104 through 20104.8, inclusive.

17. SURVIVAL: All provisions of this Contract which by their nature are intended to survive the termination or expiration of this Agreement shall survive such termination or expiration.

18. INDEMNIFICATION AND INSURANCE: CONTRACTOR shall at all times comply with the indemnification and insurance provisions set forth in EXHIBIT C, attached hereto and incorporated herein by reference.

19. FEDERAL PROVISIONS: CONTRACTOR acknowledges that Federal financial assistance will be used to fund this Agreement. CONTRACTOR shall only use federal funds as authorized herein. CONTRACTOR will comply will all applicable federal law, regulations, executive orders, federal policies, procedures, and directives, including, but not limited to, Title 2 of the Code of Federal Regulations (CFR) Part 200, entitled, "Uniform Administrative Requirements, Cost Principles, and Audit Requirements for Federal Awards." In addition, CONTRACTOR shall comply with all Federal Terms and Conditions throughout the Technical Specifications and Appendix A, Appendix B and Appendix C of the Invitation for Bids. CONTRACTOR shall comply with grant agreement attached hereto as Exhibit D and incorporated herein by reference, assurances in applications, notices of award, and all other applicable federal, state, and local laws, regulations, ordinances, orders, rules, guidelines, directives, circulars, bulletins, notices, and policies governing the Federal funds provided in

Docusign Envelope ID: BDFFABE1-7061-435E-B267-F8568CF044D6

connection with this Agreement. CONTRACTOR shall be responsible for providing services in a manner consistent with all federal and state requirements and standards required as a condition of receiving and expending funds provided in connection with this Agreement.

20. **TAXES**: CONTRACTOR shall pay all taxes, levies, duties, and assessments of every nature due in connection with any Work under this Contract, and shall make any and all payroll deductions required by law. CONTRACTOR is responsible for all CONTRACTOR personnel and for the payment of their compensation, including, if applicable, withholding of income taxes, and the payment and withholding of social security and other payroll taxes, unemployment insurance, workers' compensation insurance payments, and disability benefits. In no event shall COUNTY pay or be responsible for any taxes imposed on, or with respect to, CONTRACTOR's income, revenues, gross receipts, personnel, real or personal property, or other assets. COUNTY shall not be responsible for paying any taxes on CONTRACTOR's behalf, and should COUNTY be required to do so by state, federal, or local taxing agencies, CONTRACTOR agrees to promptly reimburse COUNTY for the full value of such paid taxes plus interest and penalty, if any. These taxes shall include, but not be limited to, the following: FICA (Social Security), unemployment insurance contributions, income tax, disability insurance, and workers' compensation insurance.

21. **CONFLICT OF INTEREST**: CONTRACTOR covenants that CONTRACTOR presently has no employment or interest and shall not acquire any employment or interest, direct or indirect, including any interest in any business, property, or source of income, which would conflict in any manner or degree with the performance of Word required to be performed under this Contract. CONTRACTOR further covenants that in the performance of this Contract, no person having any such interest shall be employed by CONTRACTOR. CONTRACTOR must promptly disclose to COUNTY, in writing, any potential conflict of interest. COUNTY retains the right to waive a conflict of interest disclosed by CONTRACTOR if COUNTY determines it to be immaterial, and such waiver is only effective if provided by COUNTY to CONTRACTOR in writing.

22. **NONDISCRIMINATION**: COUNTY hereby notifies CONTRACTOR that COUNTY's Unlawful Discrimination Ordinance (Article XIII of Chapter 2 of the Santa Barbara County Code) applies to this Contract and is incorporated herein by this reference with the same force and effect as if the ordinance were specifically set out herein and CONTRACTOR agrees to comply with said ordinance.

23. **NON-ASSIGNMENT**: CONTRACTOR shall not assign, subcontract, delegate, or otherwise transfer, directly or indirectly, whether by operation of law or otherwise ("Transfer") this Contract, in whole or in part, or any of CONTRACTOR's rights or obligations under this Contract, without the prior written consent of COUNTY in each instance. Any attempted or purported Transfer in violation of this Section 24, or in violation of Section 2.08 of the General Conditions, attached hereto as part of Exhibit A, shall be null and void and without legal effect and shall constitute grounds for termination by COUNTY. No Transfer shall relieve CONTRACTOR of any of its obligations hereunder.

24. **SEVERABILITY**: If any one or more of the provisions contained in the Contract shall for any reason be held to be invalid, illegal or unenforceable in any respect by a court of competent jurisdiction, then such provision or provisions shall be deemed severable from the remaining provisions hereof, and such invalidity, illegality or unenforceability shall not affect any other provision hereof, and this Contract shall be construed as if such invalid, illegal or unenforceable provision had never been contained herein.

25. **TIME IS OF THE ESSENCE**: Time is of the essence in this Contract, and each covenant and term is a condition herein.

26. **ENTIRE AGREEMENT AND AMENDMENT**: The Contract Documents, as may be modified from time to time during the Term by duly authorized and executed Change Orders in accordance with the provisions of this Agreement and the General Terms, contain the entire understanding and agreement of the Parties with respect to the subject matter hereof and thereof, and there have been no promises, representations, agreements, warranties or undertakings by any of the Parties, either oral or written, of any character or nature hereafter binding except as set forth herein and therein. This Contract may be altered, amended or modified only by an instrument in writing, duly executed by each of the Parties, and by no other means, except as otherwise set forth in Section 30, below, to the extent such delegated authority is expressly authorized by the COUNTY Board of Supervisors in approving this Contract. Each Party waives its future right to claim, contest or assert that this Agreement was modified, canceled, superseded, or changed by any oral agreements, course of conduct, waiver or estoppel.

27. **EXECUTION OF COUNTERPARTS**: This Contract may be executed electronically and in any number of

Docusign Envelope ID: BDFFABE1-7061-435E-B267-F8568CF044D6

counterparts, and each of such counterparts shall for all purposes be deemed to be an original; and all such counterparts, or as many of them as the Parties shall preserve undestroyed, shall together constitute one and the same instrument.

28. **SUBCONTRACTORS**: CONTRACTOR is authorized to subcontract with only the subcontractor(s) identified in the Bid as attached hereto and as set forth in Exhibit B ("Subcontractors"). Contractor shall be fully responsible for all services and Work performed by its Subcontractors. Contractor shall secure from each of its Subcontractors legally binding written agreements to comply with the provisions of this Agreement pertaining to CONTRACTOR's obligations as if such obligations pertained to such Subcontractor, including, but not limited to, audit obligations.

29. **CHANGE ORDERS**: No Change Order shall be valid or enforceable against the COUNTY unless in the form of the Form of Change Order attached here as Exhibit E and duly executed by both CONTRACTOR and the Director in accordance with this Section 29 and Article 13 of the General Conditions ("Change Order").

30. **FLEET REQUIREMENTS**: Vehicles with a Gross vehicle weight rating ("GVWR") greater than 8,500 lbs. and light-duty package delivery vehicles operated in California may be subject to the California Air Resources Board ("CARB") Advanced Clean Fleets regulations. Such vehicles may therefore be subject to requirements to reduce emissions of air pollutants. For more information, please visit the CARB Advanced Clean Fleets webpage at https://ww2.arb.ca.gov/our-work/programs/advanced-clean-fleets. Contractor shall at all times have a valid Certificate of Reported Compliance, as described in section 2449(n) of Title 13 of the California Code of Regulations ("CARB Certificate of Compliance"), and shall confirm that each subcontractor listed in Contractor's Bid has a valid CARB Certificate of Compliance, for each fleet of vehicles subject to 13 CCR section 2449 that may be used in performance of this Contract. No such vehicle is permitted on the project site unless and until Contractor provides County with a valid Certificate of Reported Compliance applicable to such vehicle.

31. **ORDER OF PRECEDENCE**: In the event of conflict between the provisions contained in the numbered sections 1 through 35 of this Agreement ("Numbered Section") and the provisions contained in the Exhibits, the provisions contained in the Numbered Sections of this Agreement shall prevail over those in the Exhibits other than Exhibit C, which Exhibit C shall control and prevail over all other provisions of this Contract. CONTRACTOR agrees that in the event of any discrepancy, inconsistency, gap, ambiguity, or conflicting language between the Bid attached hereto as Exhibit B, on the one hand, and any other provision(s) of this Contract on the other, the provisions of this Contract (including the Numbered Sections of this Agreement, Exhibit A, and Exhibit C) other than Exhibit B shall take precedence and control and prevail over the provisions of the Bid attached hereto as Exhibit B.

32. **TERMINATION.**

A. COUNTY may, by written notice to CONTRACTOR, terminate this Contract in whole or in part at any time, whether for COUNTY's convenience, for nonappropriation of funds, or because of the failure of CONTRACTOR to fulfill its obligations hereunder.

1. **For Convenience.** COUNTY may terminate this Contract in whole or in part upon thirty (30) days' written notice. During such thirty (30) day period, CONTRACTOR shall, as directed by COUNTY, wind down and cease Work as quickly and efficiently as reasonably possible, without performing unnecessary services or activities and by minimizing negative effects on COUNTY from such winding down and cessation of Work.

2. **For Nonappropriation of Funds.** Notwithstanding any other provision of this Contract, in the event that no funds or insufficient funds are appropriated or budgeted by federal, State or COUNTY governments, or sufficient funds are not otherwise available for payments hereunder in the fiscal year(s) covered by the Term of this Agreement, then COUNTY will notify CONTRACTOR of such occurrence, and COUNTY may terminate or suspend this Contract in whole or in part, with or without a prior notice period. Subsequent to termination of this Contract under this provision, COUNTY shall have no obligation to make payments with regard to the remainder of the Term.

3. **For Cause.** Should CONTRACTOR default in the performance of this Contract or materially breach any of the provisions hereof, COUNTY may, at COUNTY's sole option, terminate or suspend this Contract in whole or in part upon written notice ("Termination Notice"). Upon receipt of such Termination Notice, CONTRACTOR shall immediately discontinue all Work (unless

Docusign Envelope ID: BDFFABE1-7061-435E-B267-F8568CF044D6

otherwise directed in such Termination Notice) and notify COUNTY in writing of the status of CONTRACTOR's performance of Work hereunder. The date of termination shall be the date the Termination Notice is received by CONTRACTOR, unless the Termination Notice directs otherwise.

B. Upon termination, CONTRACTOR shall deliver to COUNTY all data, estimates, graphs, summaries, reports, and all other property, records, documents or papers as may have been accumulated or produced by CONTRACTOR in performing this Contract, whether completed or in process, except such items as COUNTY may, by written permission, permit CONTRACTOR to retain. Notwithstanding any other payment provision of this Contract, COUNTY shall pay CONTRACTOR for satisfactory Work performed as of the date of termination to include a prorated amount of compensation due hereunder less payments, if any, previously made. In no event shall CONTRACTOR be paid an amount in excess of the Maximum Contract Amount, or for unperformed portions of Work. CONTRACTOR shall furnish to COUNTY such financial information as in the judgment of COUNTY is necessary to determine the reasonable value of the Work rendered by CONTRACTOR. The foregoing is cumulative and shall not affect any right or remedy which COUNTY may have in law or equity.

33. JURISDICTION; VENUE. This Contract shall be governed by the laws of the State of California. Any litigation arising out of this Contract shall be filed in the County of Santa Barbara, if in state court, or in the federal district court nearest to the County of Santa Barbara, if in federal court.

34. NO WAIVER. COUNTY's delay or failure to act with respect to a breach of this Contract by CONTRACTOR shall not constitute or be construed as a waiver of COUNTY's rights with respect to subsequent or similar breaches. Any delay or failure of COUNTY to exercise or enforce any right or provision of this Contract shall not constitute a waiver of such right or provision, and every power and remedy given by this Contract to COUNTY shall be exercised from time to time and as often as may be deemed expedient in the sole discretion of COUNTY. No remedy herein conferred upon or reserved to COUNTY is intended to be exclusive of any other remedy or remedies, and each and every such remedy, to the extent permitted by law, shall be cumulative and in addition to any other remedy given hereunder or now or hereafter existing at law or in equity or otherwise.

35. SIGNATORY AUTHORITY. Each of the Parties hereby represents and warrants to the other Party that:

(a) Such Party has the full right, power, and authority to enter into this Contract and to perform its obligations hereunder.

(b) The execution of this Contract by the individual whose signature is set forth at the end of this Agreement on behalf of such Party, and the delivery of this Contract by such Party, have been duly authorized by all necessary corporate or other action on the part of such Party.

(c) This Contract has been executed and delivered by such Party and (assuming due authorization, execution, and delivery by the other Party) constitutes the legal, valid, and binding obligation of such Party, enforceable against such Party in accordance with its provisions.

Docusign Envelope ID: BDFFABE1-7061-435E-B267-F8568CF044D6

IN WITNESS WHEREOF, the parties hereto have executed this Agreement to be effective as of the first date fully executed by all of the parties hereto.

COUNTY
County of Santa Barbara

By: _____
LAURA CAPPS, CHAIR
BOARD OF SUPERVISORS

Dated: 10-14-25

ATTEST:
MONA MIYASATO,

_____
COUNTY EXECUTIVE OFFICER

CLERK OF THE BOARD

By: _____
Deputy Clerk of the Board

CONTRACTOR

AMERICAN ROAD MAINTENANCE, INC., an Arizona corporation

By: DocuSigned by: Kyle Paulson
4C085AA88F81497...
AUTHORIZED REPRESENTATIVE

Name: KYLE PAULSON

Title: OFFICER

APPROVED AS TO FORM:
RACHEL VAN MULLEM,
COUNTY COUNSEL

By: Signed by: Lauren Wideman
8F464D822C8445A...
Deputy County Counsel

APPROVED AS TO ACCOUNTING FORM:
BETSY SCHAFFER, CPA, CPFO
AUDITOR-CONTROLLER

By: Signed by: James E Munro
02BA147EF6A84DE...
Deputy Auditor-Controller

APPROVED AS TO FORM:
GREG MILLIGAN, ARM
RISK MANAGER

By: Signed by: Greg Milligan
05F555F00269466...
Risk Management

RECOMMENDED FOR APPROVAL
KIRK LAGERQUIST, DIRECTOR
GENERAL SERVICES DEPARTMENT

By: DocuSigned by: Kirk Lagerquist
19AEDA90054E4CE...
Department Head

Dept 063 Fund 0030 Program 1920 Account 8200 Project 22011

EXHIBIT A

CONTRACT DOCUMENTS

NOTICE TO BIDDERS

Notice is hereby given that the General Services Department, County of Santa Barbara will receive bids for:

COUNTY OF SANTA BARBARA,

Rehabilitate Tie-Down Apron

Santa Ynez Airport

900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

JOB WALK:
Monday, May 19, 2025 at 11:00 A.M.
900 Airport Road, Santa Ynez, C.A.

BID DUE DATE:
3:00 P.M., Friday, May 30, 2025

CONSTRUCTION COST ESTIMATE: $550,000.00 Dollars

PROJECT LOCATION:
Santa Ynez Airport, 900 Airport Road, Santa Ynez, Santa Barbara County, California

JOB WALK:
There will be a job walk on Monday, May 19, 2025 at 11:00 A.M. Meet outside the Airport Administration office, 900 Airport Road, Santa Ynez, California**.**

PROJECT DESCRIPTION:
The project focuses on rehabilitating the tie-down apron including crack repair and a surface treatment with the following work elements:

- Airfield safety and security.
- Clearing, grubbing, and removals.
- Temporary removal of tie down cables, chains, and fasteners.
- Pavement cleaning.
- Crack fill and seal.
- Application of an emulsified asphalt seal coat.
- Pavement markings.
- Reinstallation of aircraft tie down cables, chains, and fasteners

BIDDERS QUESTIONS:
All questions MUST be submitted electronically through the project Public Purchase Portal (www.publicpurchase.com) on or before 3:00 pm, five (5) business days prior to the day of the bid opening. Any changes or additional information needed for bidding will be provided in an Addendum posted on the Public Purchase site. Contractors shall be responsible for addendums

BID SUBMITTAL INSTRUCTIONS: Each bid shall be in accordance with the plans and specifications approved by the General Services Department. The bid MUST be submitted electronically through the Public Purchase website (www.publicpurchase.com) on or before **3:00 P.M., Friday, May 30, 2025**

SUBSTITUTION OF SECURITIES: Pursuant to Section 22300 of the Public Contract Code and the project specifications, the CONTRACTOR may substitute securities or request that the County make payment of retentions to an escrow agent for any money held by the COUNTY to ensure contract performance.

REGISTRATION: No contractor or subcontractor may be listed on a bid proposal for a public works project (submitted on or after March 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5 [with limited exceptions from this requirement for bid purposes only under Labor Code § 1771.1(a)]; no contractor or subcontractor may be awarded a contract for public work on a public works project (awarded on or after April 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5; and this project is subject to compliance monitoring and enforcement by the Department of Industrial Relations.

QUALIFYING CONTRACTOR OR SUBCONTRACTOR: Pursuant to the provisions of Section 4104 of the California Public Contracting Code a contractor or subcontractor shall not be qualified to bid on, be listed in a bid proposal or engage in the performance of any contract for public work, as defined in Section 4104, unless currently registered with the Department of Industrial Relations and qualified to perform public work pursuant to Section 1725.5 California Labor Code.

WITHDRAWAL OF BIDS:
The COUNTY reserves the right to reject any and or all bids or waive any informality in a bid. No bidder may withdraw his bid for a period of one hundred twenty (120) days after the date set for the opening thereof.

BID SELECTION:
The COUNTY reserves the right to select any one or any combination of bids, whichever is in the best interest of the COUNTY.

CONSTRUCTION TIME:
The successful CONTRACTOR (after receiving the Notice to Proceed) shall have **50 Working days** to complete all work called for under the Contract Documents.

LIQUIDATED DAMAGES:
The liquidated damages will be **$500.00 Dollars** per calendar day for project delays that are determined to be attributable to the CONTRACTOR.

VIRTUAL BID OPENING:
Bids will be opened and read aloud in a public virtual meeting. Meeting can be attended by using the following Teams link:
https://teams.microsoft.com/l/meetup-join/19%3ameeting_YmNlMmYzZDktYmUyOC00YTg1LTllYzAtNDE0MzAzYjQ0MDk5%40thread.v2/0?context=%7b%22Tid%22%3a%22e64b3773-9890-4a2f-87cd-23725df35ace%22%2c%22Oid%22%3a%2204175e35-b632-4b01-b53f-3238cd5f291d%22%7d or call in (audio only) 805-724-0311 and use Phone Conference ID: 398 509 356#

County of Santa Barbara

Rehabilitate Tie-Down Apron

Santa Ynez Airport

900 Airport Road, Santa Ynez, California

AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

JOB WALK:
Monday, May 19, 2025 at 11:00 A.M.
900 Airport Road, Santa Ynez, C.A.

BID OPENING DATE:
3:00 P.M., Friday, May 30, 2025

BID OPENING LOCATION:
Bids to be Submitted Electronically

Table of Contents

NOTICE TO BIDDERS 1
INFORMATION FOR BIDDERS 7
PROPOSAL 12
PROJECT BID SCHEDULE 13
SIGNATURE PAGE 15
DESIGNATION OF SUBCONTRACTORS 16
CERTIFICATE OF COMPLIANCE 18
BIDDER'S STATEMENTS 19
ANTI-FRAUD CERTIFICATION 20
BIDDER'S BOND 21
NONCOLLUSION AFFIDAVIT 23
NONLOBBYING CERTIFICATION FOR FEDERAL-AID CONTRACTS 24
DISCLOSURE OF LOBBYING ACTIVITIES FORM 25
INSTRUCTIONS FOR COMPLETION OF SF-LLL, DISCLOSURE OF LOBBYING ACTIVITIES 26
LOCAL AGENCY BIDDER – DBE – INFORMATION 28
DBE INFORMATION-GOOD FAITH EFFORTS 29
BUY AMERICAN PREFERENCE 31
REQUIRED CONTRACT PROVISIONS FOR AIRPORT IMPROVEMENT PROGRAM AND FOR OBLIGATED SPONSORS 33
CONTRACT FORMS 34
PAYMENT BOND 35
PERFORMANCE BOND 37
CERTIFICATE OF INSURANCE TRANSMITTAL FORM 39
COUNTY OF SANTA BARBARA UNLAWFUL DISCRIMINATION ORDINANCE 40
SAMPLE AGREEMENT 43
INDEMNIFICATION AND INSURANCE REQUIREMENTS 51
TECHNICAL SPECIFICATIONS 54
Part 1 – General Contract Provisions 54
Section 10 Definition of Terms 54
Section 20 Proposal Requirements and Conditions 62
Section 30 Award and Execution of Contract 65
Section 40 Scope of Work 67
Section 50 Control of Work 70

Section 60 Control of Materials 75
Section 70 Legal Regulations and Responsibility to Public 78
Section 80 Execution and Progress 84
Section 90 Measurement and Payment 90
Part 2 – General Construction Items 97
Item C-10T General Requirements 97
Item C-100 Contractor Quality Control Program (CQCP) 101
Item C-104T Airport Safety and Security 108
Item C-105 Mobilization 111
Part 3 – Sitework 113
Item P-101 Preparation/Removal of Existing Pavements 113
Part 8– Surface Treatments 116
Item P-608 Emulsified Asphalt Seal Coat 116
Part 9– Miscellaneous 124
Item P-605 Joint Sealants for Pavements 124
Item P-620 Runway and Taxiway Marking 126

APPENDIX A CONSTRUCTION SAFETY AND PHASING PLAN

APPENDIX B ADVISORY CIRCULAR 150/5370-2G:
OPERATIONAL SAFETY ON AIRPORTS DURING CONSTRUCTION

APPENDIX C FAA CONTRACT PROVISIONS

APPENDIX D COUNTY OF SANTA BARBARA GENERAL CONDITIONS

NOTICE TO BIDDERS

Notice is hereby given that the General Services Department, County of Santa Barbara will receive bids for:

COUNTY OF SANTA BARBARA,

Rehabilitate Tie-Down Apron

Santa Ynez Airport

900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

JOB WALK:
Monday, May 19, 2025 at 11:00 A.M.
900 Airport Road, Santa Ynez, C.A.

BID DUE DATE:
3:00 P.M., Friday, May 30, 2025

CONSTRUCTION COST ESTIMATE: $705,000.00 Dollars

PROJECT LOCATION:
Santa Ynez Airport, 900 Airport Road, Santa Ynez, Santa Barbara County, California

MANDATORY JOB WALK:
There will be a job walk on Monday, May 19, 2025 at 11:00 A.M. Meet outside the Airport Administration office, 900 Airport Road, Santa Ynez, California**.**

PROJECT DESCRIPTION:
The project focuses on rehabilitating the tie-down apron including crack repair and a surface treatment with the following work elements:

- Airfield safety and security.
- Clearing, grubbing, and removals.
- Temporary removal of tie down cables, chains, and fasteners.
- Pavement cleaning.
- Crack fill and seal.
- Application of an emulsified asphalt seal coat.
- Pavement markings.
- Reinstallation of aircraft tie down cables, chains, and fasteners

BIDDERS QUESTIONS:
All questions MUST be submitted electronically through the project Public Purchase Portal (www.publicpurchase.com) on or before 3:00 pm, five (5) business days prior to the day of the bid opening. Any changes or additional information needed for bidding will be provided in an Addendum posted on the Public Purchase site. Contractors shall be responsible for addendums

BID SUBMITTAL INSTRUCTIONS: Each bid shall be in accordance with the plans and specifications approved by the General Services Department. The bid MUST be submitted electronically through the Public Purchase website (www.publicpurchase.com) on or before **3:00 P.M., Friday, May 30, 2025**

SUBSTITUTION OF SECURITIES: Pursuant to Section 22300 of the Public Contract Code and the project specifications, the CONTRACTOR may substitute securities or request that the County make payment of retentions to an escrow agent for any money held by the COUNTY to ensure contract performance.

REGISTRATION: No contractor or subcontractor may be listed on a bid proposal for a public works project (submitted on or after March 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5 [with limited exceptions from this requirement for bid purposes only under Labor Code § 1771.1(a)]; no contractor or subcontractor may be awarded a contract for public work on a public works project (awarded on or after April 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5; and this project is subject to compliance monitoring and enforcement by the Department of Industrial Relations.

QUALIFYING CONTRACTOR OR SUBCONTRACTOR: Pursuant to the provisions of Section 4104 of the California Public Contracting Code a contractor or subcontractor shall not be qualified to bid on, be listed in a bid proposal or engage in the performance of any contract for public work, as defined in Section 4104, unless currently registered with the Department of Industrial Relations and qualified to perform public work pursuant to Section 1725.5 California Labor Code.

WITHDRAWAL OF BIDS:
The COUNTY reserves the right to reject any and or all bids or waive any informality in a bid. No bidder may withdraw his bid for a period of one hundred twenty (120) days after the date set for the opening thereof.

BID SELECTION:
The COUNTY reserves the right to select any one or any combination of bids, whichever is in the best interest of the COUNTY.

CONSTRUCTION TIME:
The successful CONTRACTOR (after receiving the Notice to Proceed) shall have **50 Working days** to complete all work called for under the Contract Documents.

LIQUIDATED DAMAGES:
The liquidated damages will be **$500.00 Dollars** per calendar day for project delays that are determined to be attributable to the CONTRACTOR.

BID BOND:
Each bid must be accompanied by a Certified Check, a Cashier's Check or a Bid Bond, as here and after provided in the amount of Ten Percent (10%) of the total of the bid, made payable to the County of Santa Barbara, as a guarantee that the bidder, if awarded the contract, will enter into a Contract for the performance thereof, satisfactory to said County's Board of Supervisors. Surety shall be listed in the Insurance Organizations Authorized By The Insurance Commissioner To Transact Business Of Insurance In The State Of California During 1994 (including changes effective January 1, 1995) published by the Department of Insurance, State of California, or successor publication. Personal and Corporate guarantees will not be acceptable.

The Contractor shall use the Bidder's Bond Form found in the book entitled "County of Santa Barbara, Department of General Services, Notice to Contractors, Special Provisions, Proposal and Contract" for the project and it shall be properly filled out and executed. ***(Note: This form may be reproduced for transmittal to the Surety for execution and attached to the front of the original Bid Bond Form.)***

PERSONAL CHECKS WILL NOT BE ACCEPTED.

Pursuant to Section 10263 of the Public Contract Code, and the project specifications, the Contractor may substitute securities for monies withheld to ensure contract performance.

DISADVANTAGED BUSINESS ENTERPRISE PARTICIPATION:
This Contract is subject to State Contract Nondiscrimination and Compliance requirements pursuant to Government Code Section 12990.

The County of Santa Barbara hereby notifies all bidders that it will affirmatively insure that in any Contract entered into pursuant to this advertisement, minority business enterprises will be afforded full opportunity to submit bids in response to this invitation, and will not be discriminated against on the grounds of race, color, or national origin, in consideration for an award.

This project is subject to Part 26, Title 49, Code of Federal Regulations entitled, "Participation by Minority Business Enterprise in the Department of Transportation Programs."

The County of Santa Barbara has established a goal of **10.0%** Disadvantaged Business Enterprise participation for this project. It is the bidder's responsibility to make sufficient portions of the work available to subcontractors and suppliers, and to select those portions of the work or material needs consistent with the available DBE subcontractors and suppliers, so as to assure meeting the goal for DBE participation.

ASSURANCE OF MINORITY BUSINESS ENTERPRISE PARTICIPATION:
The Bidder's execution of the signature portion of this Proposal shall also constitute execution of this assurance.

The Bidder hereby gives assurance pursuant to the requirements of Title 49, CFR Part 26, that Bidder has made a reasonable effort to meet the goal for Disadvantaged Business Enterprise participation specified for the Contract for which this Proposal is submitted.

Bidder further gives assurance that Bidder will submit the documentation required by said regulations and the specifications for the Listing of Disadvantaged Business Enterprises with which the Bidder will subcontract if the contract is awarded to Bidder, and if Bidder is unable to obtain Disadvantaged Business Enterprise participation, of the steps Bidder has taken to obtain Disadvantaged Business Enterprise participation.

Preference will be given to the lowest responsible Bidders that comply with the Disadvantaged Business Enterprise requirements, pursuant to Federal Regulation (49 CFR 26). In order to qualify, prospective Disadvantaged Business Enterprises must be certified by CalTrans on the date bids are opened.

The Contractor shall be subject to the provisions of Article XIII, Chapter 2, of the Santa Barbara County Code, prohibiting unlawful discrimination in employment practices.

PERFORMANCE GUARANTEES:
The successful bidder shall be required to guarantee the performance of this Contract, by a "Faithful Performance Bond" in the amount of One Hundred Percent (100%) of the Contract Bid, a "Payment Bond" in the amount of One Hundred Percent (100%) of the Contract Bid.

FEDERAL FUNDED PROJECT:

This project is funded in part with funds from the Federal Government. The project is subject to numerous federal financial and contractual requirements including the following:

AFFIRMATIVE ACTION REQUIREMENT

NOTICE OF REQUIREMENT FOR AFFIRMATIVE ACTION to ENSURE EQUAL EMPLOYMENT OPPORTUNITY

1. The Offeror's or Bidder's attention is called to the "Equal Opportunity Clause" and the "Standard Federal Equal Employment Opportunity Construction Contract Specifications" set forth herein.

2. The goals and timetables for minority and female participation, expressed in percentage terms for the Contractor's aggregate workforce in each trade on all construction work in the covered area, are as follows:

Goals for minority participation for each trade:	19.7%
Goals for female participation in each trade:	6.9%

These goals are applicable to all of the Contractor's construction work (whether or not it is Federal or federally assisted) performed in the covered area. If the Contractor performs construction work in a geographical area located outside of the covered area, it shall apply the goals established for such geographical area where the work is actually performed. With regard to this second area, the Contractor also is subject to the goals for both its federally involved and non-federally involved construction.

The Contractor's compliance with the Executive Order and the regulations in 41 CFR Part 60-4 shall be based on its implementation of the Equal Opportunity Clause, specific affirmative action obligations required by the specifications set forth in 41 CFR 60-4.3(a) and its efforts to meet the goals. The hours of minority and female employment and training must be substantially uniform throughout the length of the contract, and in each trade, and the Contractor shall make a good faith effort to employ minorities and women evenly on each of its projects. The transfer of minority or female employees or trainees from Contractor to Contractor or from project to project for the sole purpose of meeting the Contractor's goals shall be a violation of the contract, the Executive Order and the regulations in 41 CFR Part 60-4. Compliance with the goals will be measured against the total work hours performed.

3. The Contractor shall provide written notification to the Director of the Office of Federal Contract Compliance Programs (OFCCP) within 10 working days of award of any construction subcontract in excess of $10,000 at any tier for construction work under the contract resulting from this solicitation. The notification shall list the name, address, and telephone number of the subcontractor; employer identification number of the subcontractor; estimated dollar amount of the subcontract; estimated starting and completion dates of the subcontract; and the geographical area in which the subcontract is to be performed.

4. As used in this notice and in the contract resulting from this solicitation, the "covered area" is the County of Santa Barbara, California.

BUY AMERICAN PREFERENCE
(Reference: 49 USC § 50101)

(Reference Only – Refer to Federal Register)

CIVIL RIGHTS – TITLE VI ASSURANCE

Title VI Solicitation Notice:

The **County**, in accordance with the provisions of Title VI of the Civil Rights Act of 1964 (78 Stat. 252, 42 USC §§ 2000d to 2000d-4) and the Regulations, hereby notifies all bidders or offerors that it will affirmatively ensure that any contract entered into pursuant to this advertisement, disadvantaged business enterprises will be afforded full and fair opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award.

DAVIS-BACON REQUIREMENTS
(Reference: 2 CFR § 200 Appendix II(D))

(Reference Only – Refer to Federal Register)

DEBARMENT AND SUSPENSION (NON-PROCUREMENT).
(Reference: 2 CFR part 180 (Subpart C), 2 CFR part 1200, DOT Order 4200.5 DOT Suspension & Debarment Procedures & Ineligibility)

(Reference Only – Refer to Federal Register)

DISADVANTAGED BUSINESS ENTERPRISE.
(Reference: 49 CFR part 26)

(Reference Only – Refer to Federal Register)

TRADE RESTRICTION
(Reference: 49 CFR part 30)

(Reference Only – Refer to Federal Register)

LOBBYING AND INFLUENCING FEDERAL EMPLOYEES
(Reference: 31 USC § 1352, 2 CFR part 200, Appendix II(J), 49 CFR part 20, Appendix A)

(Reference Only – Refer to Federal Register)

PROCUREMENT OF RECOVERED MATERIALS
(Reference: 2 CFR § 200.322, 40 CFR part 247)

(Reference Only – Refer to Federal Register)

Award of contract is subject to Federal Aviation Administration Funding and Approval.

By order of the County of Santa Barbara.

_____ Steven Manual, Project Manager

County of Santa Barbara, California

Dated: _____

INFORMATION FOR BIDDERS

1. AVAILABILITY OF CONTRACT DOCUMENTS

Bid and Contract Documents may be obtained by contacting the County as indicated in the Notice To Bidders. Any applicable charges for the Contract Documents are stated in the Notice To Bidders.

2. EXAMINATION OF CONTRACT DOCUMENTS

Bidders shall be solely responsible for examining the Bid and Contract Documents, including any Addenda issued during the bidding period, and for informing itself with respect to local labor availability, means of transportation, necessity for security, laws and codes, local permit requirements, wage scales, local tax structure, contractors' licensing requirements, availability of required insurance, and other factors that could affect the Work. Bidders are responsible for consulting the standards referenced in the Contract. Failure of Bidder to investigate and inform itself shall be at its sole risk, and no relief for error or omission will be given except as required under State law.

3. INTERPRETATION OF CONTRACT DOCUMENTS

Discrepancies in, and/or omissions from the Bid or the contract documents or questions as to their meaning shall be immediately brought to the attention of the County by submission of a written request for an interpretation or correction to the County. Such submission, if any, must be sent to the County not later than four (4) days prior to the day of the bid opening date.

Any interpretation of the Bid or Contract Documents will be made only by written addenda duly issued and mailed or delivered to each person or firm who has purchased the Bid Documents. The County will not be responsible for any explanations or interpretations provided in any other manner. No person is authorized to make any oral interpretation of any provision in the Bid or Contract Documents to any bidder, and no bidder should rely on any such oral interpretation.

4. INSPECTION OF SITE

Each bidder shall examine the site of work before bidding and shall be responsible for having acquired full knowledge of the job and of all problems affecting it. No variations or allowances from the contract sum will be made because of lack of such examination. By submitting a Bid, each bidder acknowledges that it has visited the Project Site, has prepared its Bid accordingly, and assumes any and all risks and liabilities arising therefrom.

5. ADDENDA

Addendums, if necessary, will be issued by the office of the Project Manager. Addendums will be issued via the public purchase portal. Once issued, Addendums are considered an equal part of the construction contract, with all material, information, and provisions to be incorporated into the plans, specifications, and contract documents.

Please Note: Bidders are responsible for ensuring that they have received any and all Addenda.

6. COMPLETION OF BID FORMS

Bids shall be prepared using copies of the Bid Forms which are included in the Bid Documents. The use of substitute bid forms other than clear and correct photocopies of those provided by the County will not be permitted. Bids shall be executed by an authorized signatory as described in these Instructions to Bidders. In addition, Bidders shall fill in all blank spaces (including inserting "N/A" where applicable) and initial all interlineations, alterations, or erasures to the Bid Forms. Bidders shall neither delete, modify, nor supplement the printed matter on the Bid Forms nor make substitutions thereon. Deviations in the bid form may result in the bid being deemed non-responsive.

7. MODIFICATIONS OF BIDS

Each Bidder shall submit its Bid in strict conformity with the requirements of the Bid and Contract Documents. Unauthorized additions, modifications, revisions, conditions, limitations, exclusions or provisions attached to a Bid may render it non-responsive and may cause its rejection. Bidders shall neither delete, modify, nor supplement the printed matter on the Bid Forms, nor make substitutions thereon. Oral, telephonic and electronic modifications will not be considered.

8. DESIGNATION OF SUBCONTRACTORS

Pursuant to State law, the Bidders must identify each subcontractor who will perform work or render services for the Bidder in an amount that exceeds one-half of one percent (½%) of the Bidder's Total Bid Price, as well as the portion of work each such subcontractor will perform on the form provided herein by the County. No additional time will be provided to bidders to submit any of the requested information in the Designation of Subcontractor form.

9. LICENSING REQUIREMENTS

The CONTRACTOR shall possess a **Class A or C-32** license at the time this Contract is awarded.

10. SIGNING OF BIDS

All Bids submitted shall be executed by the Bidder or its authorized representative. If a Bidder is a joint venture or partnership, it may be asked to submit an authenticated Power of Attorney executed by each joint venturer or partner appointing and designating one of the joint venturers or partners as a management sponsor to execute the Bid on behalf of Bidder. Only that joint venturer or partner shall execute the Bid. The Power of Attorney shall also: (1) authorize that particular joint venturer or partner to act for and bind Bidder in all matters relating to the Bid; and (2) provide that each venturer or partner shall be jointly and severally liable for any and all of the duties and obligations of Bidder assumed under the Bid and under any Contract arising therefrom. The Bid shall be executed by the designated joint venturer or partner on behalf of the joint venture or partnership in its legal name.

11. SUBMISSION OF BIDS

Bids shall be submitted electronically to www.publicpurchase.com. No paper copy bids will be accepted.

12. BASIS OF AWARD; BALANCED BIDS

The quantities given in the proposal and contract forms are approximate only, being given as a basis for the comparison of bids, and the County does not, expressly or by implication, agree that the actual amount of work will correspond therewith, but reserves the right to increase or decrease the amount of any portion of the Work, or to omit portions of the Work, as may be deemed necessary or advisable by the Engineer.

The County shall award the Contract to the lowest responsible Bidder submitting a responsive Bid. The County may reject any Bid that in its opinion when compared to other bids received or to the County's internal estimates, does not accurately reflect the cost to perform the Work. The County may reject as non-responsive any bid which unevenly weights or allocates costs, including but not limited to overhead and profit, to one or more particular bid items.

13. DISQUALIFICATION OF BIDDERS; INTEREST IN MORE THAN ONE BID

No bidder shall be allowed to make, submit or be interested in more than one bid. However, a person, firm, corporation or other entity that has submitted a subbid to a bidder, or that has quoted prices of materials to a bidder, is not thereby disqualified from submitting a subbid or quoting prices to other bidders submitting a bid to The County.

14. INSURANCE REQUIREMENTS

The successful bidder shall procure the insurance in the form and in the amount specified in the Contract Documents. For insurance requirements, bidder shall refer to the Exhibit A Indemnification and Insurance Requirements located in the Contract Forms section of this specification booklet.

15. AWARD PROCESS

Once all Bids are opened and reviewed to determine the lowest responsive and responsible Bidder, the County may award the contract. The apparent successful Bidder should begin to prepare the following documents: (1) the Performance Bond; (2) the Payment Bond; and (3) the required insurance certificates and endorsements. Once the County notifies the Bidder of the award, the Bidder will have ten (10) consecutive calendar days from the date of the notification to execute the Contract and supply the County with all of the required documents and certifications. Regardless whether the Bidder supplies the required documents and certifications in a timely manner, the Contract Time will begin to run ten (10) calendar days from the date of the notification. Once the County receives all of the properly drafted and executed documents and certifications from the Bidder, the County shall issue a Notice to Proceed to that Bidder.

Award of contract is subject to the County receipt of state and federal grants.

16. WORKERS COMPENSATION

Each bidder shall submit the Contractor's Certificate Regarding Workers' Compensation form.

17. SUBSTITUTION OF SECURITY

The Contract Documents call for monthly progress payments based upon the amount of work completed. The County will retain five percent (5%) of each progress payment unless otherwise

provided by the Contract Documents. At the Contractor's request and expense, the Contractor may substitute securities for the amount so retained in accordance with Public Contract Code Section 22300.

18. PREVAILING WAGES

Minimum wages, as ascertained from the Secretary of Labor or State of California, whichever is greater, currently prevailing in Santa Barbara County, California, on the date of bid, are required to be paid all operators, drivers, mechanics and laborers, employed directly upon the site of the work. Bidders are responsible to keep informed as to local and state labor conditions such as length of work day and work week, overtime compensation, prospective changes or adjustments of wage rates and other conditions.

The successful bidder must insure that employees and applicants for employment are not discriminated against on the basis of age, color, race, national origin, ancestry, religion, sex, sexual preference, or marital status, and shall comply with the Americans with Disabilities Act.

The County complies with SB 854. All contractors and subcontractors must be registered with the State Department of Industrial Relations (DIR) at the time of bid, for prevailing wage monitoring. The District will review the DIR registration list for confirmation of participation.

19. DEBARMENT OF CONTRACTORS AND SUBCONTRACTORS

In accordance with the provisions of the Labor Code, contractors or subcontractors may not perform work on a public works project with a subcontractor who is ineligible to perform work on a public project pursuant to Section 1777.1 or Section 1777.7 of the Labor Code. Any contract on a public works project entered into between a contractor and a debarred subcontractor is void as a matter of law. A debarred subcontractor may not receive any public money for performing work as a subcontractor on a public works contract. Any public money that is paid to a debarred subcontractor by the Contractor for the Project shall be returned to the County. The Contractor shall be responsible for the payment of wages to workers of a debarred subcontractor who has been allowed to work on the Project.

20. PERFORMANCE BOND AND PAYMENT BOND REQUIREMENTS

The successful bidder shall be required to guarantee the performance of this Contract, by a "Faithful Performance Bond" in the amount of One Hundred Percent (100%) of the Contract Bid, and a "Payment Bond – General Services," in the amount of One Hundred Percent (100%) of the Contract Bid.

21. SALES AND OTHER APPLICABLE TAXES, PERMITS, LICENSES AND FEES

Contractor and its subcontractors performing work under this Contract will be required to pay California sales tax and other applicable taxes, and to pay for permits, licenses and fees required by the agencies with authority in the jurisdiction in which the work will be located, unless otherwise expressly provided by the Contract Documents.

22. EXECUTION OF CONTRACT

As required herein the Bidder to whom an award is made shall execute the Contract in the amount determined by the Contract Documents. The County may require appropriate evidence that the persons executing the Contract are duly empowered to do so.

23. FEDERAL CONTRACT REQUIREMENTS

The contractor (including all subcontractors) shall insert the federal contract provisions and clauses, located in the appendix, in each contract and subcontract.

The contractor (or subcontractor) shall incorporate applicable requirements of the contract provisions by reference for work done under any purchase orders, rental agreements and other agreements for supplies or services.

The prime contractor will be responsible for compliance with these contract provisions by any subcontractor, lower-tier subcontractor or service provider.

No modifications to the provisions are allowed. Minor additions covering state or sponsor requirements may be included in a separate supplemental specification, provided they do not conflict with federal laws and regulations and do not change the intent of the required contract provision.

24. DBE DOCUMENTATION

DBE documentation including documentation of all good faith efforts shall be submitted with the bid or through separate submission before 5:00 pm of the third business day following the day of bid.

END OF INFORMATION FOR BIDDERS

PROPOSAL

Pursuant to and in compliance with your Notice to Bidders and the Contract Documents relating to the construction of:

County of Santa Barbara

Rehabilitate Tie-Down Apron

900 Airport Road, Santa Ynez, California
County Project No. 22011-AIP XX
Bid Date 3:00 pm, **Friday, May 30, 2025**

including Addendum No(s). ___, ___, ___, ___, ___, ___, ___, the undersigned bidder, having become thoroughly familiar with the terms and conditions of the Contract Documents and with local conditions affecting the performance and the costs of the Work at the place where the Work is to be done, hereby proposes and agrees to fully perform the Work within the time stated in and in strict accordance with the Contract Documents (including the furnishing of any and all labor, materials, tools, expendable equipment and utility and transportation services necessary to fully perform the work and complete it in a workmanlike manner) for the total sum of:

Written if Figures: $_____

Written in Words: _____

Bid Schedule follows on the next page. Bidding Contractors to complete all blanks on the Bid Schedule:

Name of Bidder: _____

California Contractors License Number (Class): _____

PROJECT BID SCHEDULE

ITEM NO.	SPEC SECTION	DESCRIPTION	UNIT	ESTIMATED QUANTITY	UNIT PRICE (Figures)	EXTENDED TOTAL (Figures)
1	C-105	Mobilization (8% Max)	LS	1.0	$	$
2	C-104T	Airport Safety and Security (5% Max)	LS	1.0	$	$
3	P-101	Uninstall & Re-Install Tie Down Cables and Chains	LS	1.0	$	$
4	P-101	Remove Pavement Markings	SF	1.0	$	$
5	P-101	Crack Seal	LF	1.0	$	$
6	P-608	Emulsified Asphalt Seal Coat	SY	1.0	$	$
7	P-620	Markings: 2-Coat with Reflective Media	SF	1.0	$	$
8	P-620	Markings: 2-Coat w/o Reflective Media	SF	1.0	$	$
TOTAL, BID SCHEDULE (Written in Figures):						$

Abbreviations to Bid Schedule(s):

LS = lump sum	TON = 2000 pounds	LF = lineal foot	EA = each unit
SF = square foot	CY = cubic yard	SY = square yard	T&M = time and materials
ACRE = 43,560 square feet		CF = cubic foot	GAL = 1 U.S. Gallon, liquid measure

Total Bid, Basis of Award:

Written in Words:_____

Written in Figures: $_____

In the event of discrepancy between words and figures, the words shall prevail.

In the event that the product of a unit price and an estimated quantity does not equal the extended amount quoted, the unit price shall govern and the correct product of the unit price and the estimated quantity shall be deemed to be the amount bid.

In order for a Bid to be responsive, Bidder must complete all blanks in the Bid Schedule. The failure to do so shall result in the Bid being rejected as non-responsive.

It is understood that Owner reserves the right to reject the proposal and that it shall remain open and not be withdrawn for a period of one hundred twenty (120) calendar days from the date prescribed for its opening.

Attached hereto and incorporated herein is the complete and entire list of subcontractors to be employed by the undersigned and in the performance of the Work.

It is understood and agreed that if written notice of the acceptance of this proposal is mailed or delivered personally to the undersigned bidder within **one hundred twenty (120) calendar days** after the opening of the proposal, or at any time thereafter before it is withdrawn, the undersigned bidder will execute and deliver the Contract Documents to Owner in accordance with the proposal as accepted, and will also furnish and deliver to Owner any Payment Bond required under the provisions of California Civil Code Section 3247 through 3252 and Performance Bond as required under the provisions of the California Government Code and/or California Public Contract Code all within fourteen (14) calendar days after personal delivery or deposit in the mails, as the case may be, of the notifications of award. The work under the contract shall be commenced by the undersigned bidder on the date stated in COUNTY'S written Notice to Proceed and shall be completed within **50 Working** days thereafter.

Notice of acceptance or request for additional information may be addressed to the undersigned bidder at the business address set forth below.

The bid, contract or other submittal of the CONTRACTOR identified below in connection with the foregoing project is not made in the interest of or on behalf or any undisclosed person, partnership, company, association, organization, or corporation; and that the bid is genuine, and not collusive or sham; that the undersigned bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid and has not directly or indirectly colluded, conspired, connived or agreed with any bidder or anyone else to put in a sham bid, or to refrain from bidding; that the undersigned bidder has not directly or indirectly sought by agreement, communication or conference with anyone to fix his bid price or the bid price of any other bidder or to fix any overhead, profit or cost element of such bid price or of that of any other bidder or to secure any advantage against the COUNTY of Santa Barbara of anyone interested in the proposed contract; or all statements contained in this proposal are true; and that the undersigned bidder has not directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay any fee to any corporation, partnership, company association, organization, Bid Depository or to any member or agent thereof to effectuate a collusive or sham bid. I declare under the penalty of perjury under the laws of the State of California that the foregoing is true and correct.

In accordance with the provisions of Sections 1860 and 1861 of the California Labor Code, every CONTRACTOR will be required to secure the payment of compensation of his or her employees. Each CONTRACTOR to whom a public works contract is awarded shall sign the following certification prior to performing the work of the contract: "I am aware of the provisions of Section 3700 of the Labor Code which requires every employer to be insured against liability for worker's compensation or to undertake self-insurance in accordance with the provisions of that code, and I will comply with such provisions before commencing the performance of the work of this contract."

SIGNATURE PAGE

CONTRACTOR

(Company)	(IRS No)
(Street Address)	(Mailing Address)
(City)	(Phone Number)
(DIR Registration No)	(License Classification(s))
By (Name)	
(Signature)	(Title)

DESIGNATION OF SUBCONTRACTORS

The bidder agrees if this proposal is accepted, that he will contract with the County of Santa Barbara to do all work and furnish all labor, materials, machinery, tools and apparatus necessary to completely perform said Contracts in the manner and time prescribed by said Contract.

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011
Bid Date 3:00 pm, **Friday, May 30, 2025**

In compliance with the provisions of Section 4100-4107 of the Public Contract Code of the State of California, and any amendments, thereof, the undersigned bidder has set forth below the name and location of the place of business of each subcontractor who will perform work or labor or render service to the undersigned in or about the construction of the work to be performed. That portion of the work which will be done by each subcontractor for each subcontract in excess of one-half of one percent of the undersigned's total aggregate bid shall be listed..

SUBCONTRACTORS LIST		
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )

SUBCONTRACTORS LIST		
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )

NOTE: This form may be reproduced and attached behind this page to list more Subcontractors.

Bidding Contractor:_____

Bidder's Signature_____

CERTIFICATE OF COMPLIANCE

This is to certify that all requirements for insurance of subcontractors as specified for this project will be met.

Signature of Principal Dated

Printed Name, Title of Principal

Company

Address

City, State & Zip

BIDDER'S STATEMENTS

REGARDING INSURANCE COVERAGE:
Bidder hereby certifies that he has reviewed the insurance coverage requirements specified in the Contract Specifications. Should he be awarded the contract for the work, Bidder further certifies that he can meet all the Contract Specification requirements for insurance including insurance coverage of his subcontractors.

REGARDING TITLE 13 OF THE CA CODE OF REGULATIONS, BIDDER'S FLEET:
Bidder must provide to the County, prior to executing the Contract, a true and correct copy of each valid Certificate of Reported Compliance, as described in section 2449(n) of Title 13 of the California Code of Regulations, for Bidder's fleet, and for each fleet of each subcontractor listed in Bidder's Bid, of vehicles subject to 13 CCR section 2449 that may be used in performance of the Contract.

REGARDING PUBLIC CONTRACT CODE SECTION 10232:
In accordance with Public Contract Code Section 10232, the Contractor hereby states, under penalty of perjury, that no more than one final unappealable finding of contempt of court by a Federal Court has been issued against the Contractor within the immediately preceding two year period because of the Contractor's failure to comply with an order of a Federal Court which orders the Contractor to comply with an order of the National Labor Relations Board.

REGARDING PUBLIC CONTRACT CODE SECTION 10162:
In accordance with Public Contract Code Section 10162, the Bidder shall complete, under penalty of perjury, the following questionnaire:

Has the bidder, any officer of the bidder, or any employee of the bidder who has proprietary interest in the bidder, ever been disqualified, removed, or otherwise prevented from bidding on, or completing, a federal, state, or local government project because of a violation of law or safety regulation?

Yes ____ No ____

(If the answer is yes, explain the circumstances on a separate sheet of paper and attach to proposal)

_____ _____
Date Signature of Principal

_____
Printed Name, Title of Principal

_____
Company

_____
Address

_____
City, State & Zip

ANTI-FRAUD CERTIFICATION

County of Santa Barbara

Rehabilitate Tie-Down Apron

900 Airport Road, Santa Ynez, California

AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

In accordance with Public Contract Code Section 10285.1 (Chapter 376, Stats. 1985), the bidder hereby declares under penalty of perjury that the bidder **has ___, has not ___**, been convicted within the preceding three years of any offenses referred to in that section, including any charge of fraud, bribery, collusion, conspiracy, or any other act in violation of any state or federal antitrust law in connection with the bidding upon award of, or performance of, any public works contract, as defined in Public Contract Code Section 1101, with any public entity, as defined in Public Contract Code Section 1100, including the Regents of the University of California or Trustees of the California State University.

The term "bidder" is understood to include any partner, member, officer, director, responsible managing officer, or responsible managing employee thereof, as referred to in Section 10285.1.

NOTE: The bidder must place a check mark after "has" or "has not" in one of the blank spaces provided.

Date	Signature of Principal
	Printed Name, Title of Principal
	Company
	Address
	City, State & Zip

BIDDER'S BOND

KNOW ALL MEN BY THESE PRESENTS:

That we, _____ as Principal, and _____ as Surety (hereinafter referred to as Surety), are held firmly bound unto the County of Santa Barbara, State of California (hereinafter called "Owner") in the penal sum of Ten Percent (10%) of the total aggregate amount of the bid of the Principal above named, submitted by said Principal to Owner for the work described below, for the payment of which sum in lawful money of the United States, well and truly to be made, we bind ourselves, our heirs, executors, administrators, and successors, jointly and severally, firmly by these presents. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications. In no case shall the liability of the Surety hereunder exceed the sum of _____ DOLLARS ($_____). The condition of this obligation is such that a bid to Owner for certain construction specifically described as follows:

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
County Project No. 22011-AIG XX

for which bids are to be opened on **3:00 pm, Friday, May 30, 2025,** has been submitted by Principal to Owner.

NOW, THEREFORE, if the aforesaid Principal shall not withdraw said bid within the period therein after the opening of the same, or, if no period be specified within one hundred twenty (120) days after said opening and shall within the period specified therefore, or, if no period be specified, within eight (8) days after the prescribed forms are presented to him for signature, enter into a written Contract with Owner, in the prescribed form, in accordance with the bid as accepted, and file the two Bonds with Owner, one to guarantee faithful performance and the other to guarantee payment for labor and materials, as required by law, then this obligation shall be null and void; otherwise, it shall remain in full force, virtue and affect.

Said Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration or addition to the terms of said Contract or to the work to be performed thereunder or the Specifications accompanying the same shall in any manner affects its obligations on this bond, and it does hereby waive notice of any change, extension, alteration, or addition.

It is hereby agreed that any progress payment made after the scheduled completion date will not constitute a waiver of any liquidated damages heretofore agreed upon.

In the event suit is brought upon said Bond by Owner and judgment is recovered, the Surety shall pay all costs incurred by Owner in such suit, including a reasonable attorney's fee to be fixed by the Court.

Death, Bankruptcy, Receivership, Going Out of Business for any reason, or incompetence of the

Principal shall not relieve the Surety of its obligations hereunder.

Name of Principal

Date

(Seal)
Signature of Principal

Name of Surety

Address

City, State & Zip

Date

(Seal)
Signature of Surety's Attorney-In-Fact

Surety's Agent for Service of Process (located within the State of California):

Name of Agent

Address

City, State & Zip

Telephone Number

NOTE: Signatures of those executing for Surety MUST be properly acknowledged. This form may be reproduced for transmittal to the Surety for execution and attached to the front of the original Bid Bond Form.

NONCOLLUSION AFFIDAVIT

In accordance with Public Contract Code § 7106. _____
(Bidder's full name)

being first duly sworn, deposes and says that he or she is _____
(Bidder's title)

of _____
(Company's name)

the party making the foregoing Bid, that the Bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the Bid is genuine and not collusive or sham; that the Bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham Bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any Bidder or anyone else to put in a sham Bid, or that anyone shall refrain from bidding; that the Bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the Bid price of the Bidder or any other Bidder, or to fix any overhead, profit, or cost element of the Bid price, or of that of any other Bidder, or to secure any advantage against the public body awarding the contract of anyone interested in the proposed Contract; that all statements contained in the Bid are true; and further, that the Bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, to any corporation, partnership, company, association, organization, bid depository, or to any member or agent thereof to effectuate a collusive or sham Bid and has not paid, and will not pay, any person or entity for such purpose.

Any person executing this declaration on behalf of a bidder that is a corporation, partnership, joint venture, limited liability company, limited liability partnership, or any other entity, hereby represents that he or she has full power to execute, and does execute, this declaration on behalf of the bidder.

I declare under penalty of perjury under the laws of the State of California that the foregoing is true and correct.

SIGNATURE BLOCK **(**Signature Block **must be completed in** ink**& changes must be** initialed**.)**
Bidder's Signature:_____Date:_____
Bidder's Name & Title (Print):_____
At CITY: _____ STATE: _____

NONLOBBYING CERTIFICATION FOR FEDERAL-AID CONTRACTS

The prospective participant certifies, by signing and submitting this bid or proposal, to the best of his or her knowledge and belief, that:

(l) No Federal appropriated funds have been paid or will be paid, by or on behalf of the undersigned, to any person for influencing or attempting to influence an officer or employee of any Federal agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with the awarding of any Federal contract, the making of any Federal grant, the making of any Federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment, or modification of any Federal contract, grant, loan, or cooperative agreement.

(2) If any funds other than Federal appropriated funds have been paid or will be paid to any person for influencing or attempting to influence an officer or employee of any Federal agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with this Federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form-LLL, "Disclosure of Lobbying Activities," in conformance with its instructions.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by Section 1352, Title 31, U.S. Code. Any person who fails to file the required certification shall be subject to a civil penalty of not less than $10,000 and not more than $100,000 for each such failure.

The prospective participant also agrees by submitting his or her bid or proposal that he or she shall require that the language of this certification be included in all lower tier subcontracts, which exceed $100,000 and that all such subrecipients shall certify and disclose accordingly.

DISCLOSURE OF LOBBYING ACTIVITIES FORM

COMPLETE THIS FORM TO DISCLOSE LOBBYING ACTIVITIES PURSUANT TO 31 U.S.C. 1352

Standard Form LLL Rev. 09-12-97

1. Type of Federal Action:

☐ a. contract
b. grant
c. cooperative agreement
d. loan
e. loan guarantee
f. loan insurance

2. Status of Federal Action:

☐ a. bid/offer/application
b. initial award
c. post-award

3. Report Type:

☐ a. initial
b. material change

For Material Change Only:
Year _____ quarter _____
date of last report _____

4. Name and Address of Reporting Entity

☐ Prime ☐ Subawardee
Tier _____ , if known

Congressional District, if known

5. If Reporting Entity in No. 4 is Subawardee, Enter Name and Address of Prime:

Congressional District, if known

6. Federal Department/Agency:

7. Federal Program Name/Description:

CFDA Number, if applicable _____

8. Federal Action Number, if known:

9. Award Amount, if known:

10. a. Name and Address of Lobby Entity
(If individual, last name, first name, MI)

b. Individuals Performing Services (including address if different from No. 10a)
(last name, first name, MI)

(attach Continuation Sheet(s) if necessary)

11. Amount of Payment (check all that apply)

$ _____ ☐ actual ☐ Planned

12. Form of Payment (check all that apply):

☐ a. cash
☐ b. in-kind; specify: nature _____
value _____

13. Type of Payment (check all that apply)

☐ a. retainer
☐ b. one-time fee
☐ c. commission
☐ d. contingent fee
☐ e deferred
☐ f. other, specify _____

14. Brief Description of Services Performed or to be performed and Date(s) of Service, including officer(s), employee(s), or member(s) contacted, for Payment Indicated in Item 11:

(attach Continuation Sheet(s) if necessary)

15. Continuation Sheet(s) attached: **Yes** ☐ **No** ☐

16. Information requested through this form is authorized by Title 31 U.S.C. Section 1352. This disclosure of lobbying reliance was placed by the tier above when his transaction was made or entered into. This disclosure is required pursuant to 31 U.S.C. 1352. This information will be reported to Congress semiannually and will be available for public inspection. Any person who fails to file the required disclosure shall be subject to a civil penalty of not less than $10,000 and not more than $100,000 for each such failure.

Signature: _____

Print Name: _____

Title: _____

Telephone No.: _____ Date: _____

Federal Use Only:

Authorized for Local Reproduction
Standard Form – LLL

INSTRUCTIONS FOR COMPLETION OF SF-LLL, DISCLOSURE OF LOBBYING ACTIVITIES

This disclosure form shall be completed by the reporting entity, whether subawardee or prime Federal recipient, at the initiation or receipt of covered Federal action or a material change to previous filing pursuant to title 31 U.S.C. section 1352. The filing of a form is required for such payment or agreement to make payment to lobbying entity for influencing or attempting to influence an officer or employee of any agency, a Member of Congress an officer or employee of Congress or an employee of a Member of Congress in connection with a covered Federal action. Attach a continuation sheet for additional information if the space on the form is inadequate. Complete all items that apply for both the initial filing and material change report. Refer to the implementing guidance published by the Office of Management and Budget for additional information.

1. Identify the type of covered Federal action for which lobbying activity is and/or has been secured to influence, the outcome of a covered Federal action.
2. Identify the status of the covered Federal action.
3. Identify the appropriate classification of this report. If this is a follow-up report caused by a material change to the information previously reported, enter the year and quarter in which the change occurred. Enter the date of the last, previously submitted report by this reporting entity for this covered Federal action.
4. Enter the full name, address, city, state and zip code of the reporting entity. Include Congressional District if known. Check the appropriate classification of the reporting entity that designates if it is or expects to be a prime or subaward recipient. Identify the tier of the subawardee, e.g., the first subawardee of the prime is the first tier. Subawards include but are not limited to subcontracts, subgrants and contract awards under grants.
5. If the organization filing the report in Item 4 checks "Subawardee" then enter the full name, address, city, state and zip code of the prime Federal recipient. Include Congressional District, if known.
6. Enter the name of the Federal agency making the award or loan commitment. Include at least one organization level below agency name, if known. For example, Department of Transportation, United States Coast Guard.
7. Enter the Federal program name or description for the covered Federal action (item 1). If known, enter the full Catalog of Federal Domestic Assistance (CFDA) number for grants, cooperative agreements, loans and loan commitments.
8. Enter the most appropriate Federal identifying number available for the Federal action identification in item 1 (e.g., Request for Proposal (RFP) number, Invitation for Bid (IFB) number, grant announcement number, the contract grant. or loan award number, the application/proposal control number assigned by the Federal agency). Include prefixes, e.g., "RFP-DE-90-001."
9. For a covered Federal action where there has been an award or loan commitment by the Federal agency, enter the Federal amount of the award/loan commitments for the prime entity identified in item 4 or 5.
10. (a) Enter the full name, address, city, state and zip code of the lobbying entity engaged by the reporting entity identified in item 4 to influenced the covered Federal action.
    (b) Enter the full names of the individual(s) performing services and include full address if different from 10 (a). Enter Last Name, First Name and Middle Initial (Ml).
11. Enter the amount of compensation paid or reasonably expected to be paid by the reporting entity (item 4) to the lobbying entity (item 10). Indicate whether the payment has been made (actual) or will be made (planned). Check all boxes that apply. If this is a material change report, enter the cumulative amount of payment made or planned to be made.
12. Check the appropriate box(es). Check all boxes that apply. If payment is made through an in-kind

contribution, specify the nature and value of the in-kind payment.

13. Check the appropriate box(es). Check all boxes that apply. If other, specify nature.
14. Provide a specific and detailed description of the services that the lobbyist has performed or will be expected to perform and the date(s) of any services rendered. Include all preparatory and related activity not just time spent in actual contact with Federal officials. Identify the Federal officer(s) or employee(s) contacted or the officer(s) employee(s) or Member(s) of Congress that were contacted.
15. Check whether or not a continuation sheet(s) is attached.
16. The certifying official shall sign and date the form, print his/her name title and telephone number.

Public reporting burden for this collection of information is estimated to average 30 minutes per response, including time for reviewing instruction, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information.

LOCAL AGENCY BIDDER – DBE – INFORMATION

This information may be submitted with your bid proposal. If it is not, and you are the apparent low bidder or the second or third low bidder, it must be submitted and received as specified in Section 2-1.02B of the Special Provisions. Failure to submit the required DBE information will be grounds for finding the proposal nonresponsive.

CO.-RTE.-K.P.:_____
CONTRACT NO.:_____
BID AMOUNT: $ _____
BID OPENING DATE:_____
BIDDER'S NAME:_____
DBE GOAL FROM CONTRACT:_____
DBE PRIME CONTRACTOR CERTIFICATION [1]:_____

CONTRACT ITEM NO.	ITEM OF WORK AND DESCRIPTION OR SERVICES TO BE SUBCONTRACTED OR MATERIALS TO BE PROVIDED [2]	DBE CERT. NO.	NAME OF DBEs (Must be certified on the date bids are opened - include DBE address and phone number)	DOLLAR AMOUNT DBE [3]

IMPORTANT: Identify all DBE firms being claimed for credit, regardless of tier. Copies of the DBE quotes are required. Names of the First Tier DBE Subcontractors and their respective item(s) of work listed above shall be consistent, where applicable, with the names and items of work in the "List of Subcontractors" submitted with your bid pursuant to the Subcontractors Listing Law and Section 2-1.01, "General," of the Special Provisions.

Total Claimed Participation	$_____ _____%

1. DBE prime contractors shall enter their DBE certification number. DBE prime contractors shall indicate all work to be performed by DBEs including work performed by its own forces.

2. If 100% of item is not to be performed or furnished by DBE, describe exact portion of item to be performed or furnished by DBE.

3. See Section 2-1.02, "Disadvantaged Business Enterprise," to determine the credit allowed for DBE firms.

_____
Signature of Bidder

_____
Date (Area Code) Tel. No.

_____
Person to Contact (Please Type or Print)

CT Bidder - DBE Information (Rev 09-28-99)

DBE INFORMATION-GOOD FAITH EFFORTS

Federal-aid Project No. _____ Bid Opening Date _____

The County of Santa Barbara established a Disadvantaged Business Enterprise (DBE) goal of **10.0%** for this project. The information provided herein shows that adequate good faith efforts were made.

A. The names and dates of each publication in which a request for DBE participation for this project was placed by the bidder (please attach copies of advertisements or proofs of publication):

Publications	Dates of Advertisement

B. The names and dates of written notices sent to certified DBEs soliciting bids for this project and the dates and methods used for following up initial solicitations to determine with certainty whether the DBEs were interested (please attach copies of solicitations, telephone records, fax confirmations, etc.):

Names of DBEs Solicited	Date of Inital Solicitation	Follow Up Methods and Dates

C. The items of work which the bidder made available to DBE firms, including, where appropriate, any breaking down of the contract work items (including those items normally performed by the bidder with its own forces) into economically feasible units to facilitate DBE participation. It is the bidder's responsibility to demonstrate that sufficient work to facilitate DBE participation was made available to DBE firms.

Items of Work	Breakdown of Items

D. The names, addresses and phone numbers of rejected DBE firms, the reasons for the bidder's rejection of the DBEs, and the firms selected for that work (please attach copies of quotes from the firms involved):

Names, addresses and phone numbers of rejected DBEs and the reasons for the bidder's rejection of the DBEs:

_____
_____
_____
_____

Names, addresses and phone numbers of firms selected for the work above:

_____
_____
_____
_____

E. Efforts made to assist interested DBEs in obtaining bonding, lines of credit or insurance, and any technical assistance or information related to the plans, specifications and requirements for the work which was provided to DBEs:

_____
_____
_____
_____

F. Efforts made to assist interested DBEs in obtaining necessary equipment, supplies, materials, or related assistance or services, excluding supplies and equipment the DBE subcontractor purchases or leases from the prime contractor or its affiliate.

_____
_____
_____
_____

G. The names of agencies, organizations or groups contacted to provide assistance in contacting, recruiting and using DBE firms (please attach copies of requests to agencies and any responses received, i.e., lists, Internet page download, etc.).

Name of Agency/Organization	Method/Date of Contact	Results

H. Any additional data to support a demonstration of good faith efforts (use additional sheets if necessary):(Refer to the Caltrans *Local Assistance Procedures Manual* for instructions)

BUY AMERICAN PREFERENCE

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with their proposal. The bidder or offeror must indicate how they intend to comply with 49 USC § 50101 by selecting one on the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (not both) by inserting a checkmark (✓) or the letter "X".

☐ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101 by:

a) Only installing steel and manufactured products produced in the United States, or;
b) Installing manufactured products for which the FAA has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing, or;
c) Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

1. To provide to the Owner evidence that documents the source and origin of the steel and manufactured product.
2. To faithfully comply with providing US domestic product
3. To furnish US domestic product for any waiver request that the FAA rejects
4. To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

☐ The bidder or offeror hereby certifies it cannot comply with the 100% Buy American Preferences of 49 USC § 50101(a) but may qualify for either a Type 3 or Type 4 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:

1. To the submit to the Owner within 15 calendar days of the bid opening, a formal waiver request and required documentation that support the type of waiver being requested.
2. That failure to submit the required documentation within the specified timeframe is cause for a non-responsive determination may result in rejection of the proposal.
3. To faithfully comply with providing US domestic products at or above the approved US domestic content percentage as approved by the FAA.
4. To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

Required Documentation

Type 3 Waiver - The cost of the item components and subcomponents produced in the United States is more that 60% of the cost of all components and subcomponents of the "item". The required documentation for a type 3 waiver is:

a) Listing of all product components and subcomponents that are not comprised of 100% US domestic content (Excludes products listed on the FAA Nationwide Buy American Waivers Issued listing and products excluded by Federal Acquisition Regulation Subpart 25.108; products of unknown origin must be considered as non-domestic products in their entirety)
b) Cost of non-domestic components and subcomponents, excluding labor costs associated

with final assembly at place of manufacture.

c) Percentage of non-domestic component and subcomponent cost as compared to total "item" component and subcomponent costs, excluding labor costs associated with final assembly at place of manufacture.

Type 4 Waiver – Total cost of project using US domestic source product exceeds the total project cost using non-domestic product by 25%. The required documentation for a type 4 of waiver is:

a) Detailed cost information for total project using US domestic product
b) Detailed cost information for total project using non-domestic product

False Statements: Per 49 USC § 47126, this certification concerns a matter within the jurisdiction of the Federal Aviation Administration and the making of a false, fictitious or fraudulent certification may render the maker subject to prosecution under Title 18, United States Code.

Date	Signature
Company Name	Title

REQUIRED CONTRACT PROVISIONS FOR AIRPORT IMPROVEMENT PROGRAM AND FOR OBLIGATED SPONSORS

1. ACCESS TO RECORDS AND REPORTS. (Reference: 2 CFR § 200.334; 2 CFR § 200.337; FAA Order 5100.38)
2. AFFIRMATIVE ACTION REQUIREMENT. (Reference: 41 CFR part 60-4; Executive Order 11246)
3. BREACH OF CONTRACT TERMS. (Reference 2 CFR § 200 Appendix II(A))
4. BUY AMERICAN PREFERENCE. (Reference: 49 USC § 50101)
5. CIVIL RIGHTS – GENERAL. (Reference: 49 USC § 47123)
6. CIVIL RIGHTS – TITLE VI ASSURANCES. (Reference: 49 USC § 47123)
7. CLEAN AIR AND WATER POLLUTION CONTROL. (Reference: 2 CFR § 200, Appendix II(G))
8. CONTRACT WORKHOURS AND SAFETY STANDARDS ACT REQUIREMENTS. (Reference: 2 CFR § 200, Appendix II(E))
9. COPELAND "ANTI-KICKBACK" ACT (Reference: 2 CFR § 200, Appendix II(D); 29 CFR parts 3 & 5)
10. DAVIS BACON REQUIREMENTS. (Reference: 2 CFR § 200, Appendix II(D); 29 CFR Part 5)
11. DEBARMENT AND SUSPENSION (NON-PROCUREMENT). (Reference: 2 CFR part 180 (Subpart C), 2 CFR part 1200, DOT Order 4200.5 DOT Suspension & Debarment Procedures & Ineligibility)
12. DISADVANTAGED BUSINESS ENTERPRISE. (Reference: 49 CFR part 26)
13. DISTRACTED DRIVING. (Reference: Executive Order 13513, DOT Order 3902.10)
14. PROHIBITION ON CERTAIN TELECOMMUNICATIONS AND VIDEO SURVEILLANCE SERVICES OR EQUIPMENT (Reference 2 CFR § 200, Appendix II(K), 2 CFR § 200.216)
15. DRUG FREE WORKPLACE (Reference: 49 CFR Part 29)
16. EQUAL EMPLOYMENT OPPORTUNITY (E.E.O.). (Reference: 2 CFR 200, Appendix II(C); 41 CFR § 60-1.4; 41 CFR § 60-4.3; Executive Order 11246)
17. FEDERAL FAIR LABOR STANDARDS ACT (FEDERAL MINIMUM WAGE). (Reference: 29 USC § 201, et seq.)
18. LOBBYING AND INFLUENCING FEDERAL EMPLOYEES. (Reference: 31 U.S.C. § 1352 – Byrd Anti-Lobbying Amendment; 2 CFR part 200, Appendix II(J); 49 CFR part 20, Appendix A)
19. PROHIBITION OF SEGREGATED FACILITIES. (Reference: 41 CFR § 60-1.8)
20. OCCUPATIONAL SAFETY AND HEALTH ACT OF 1970. (Reference 20 CFR part 1910)
21. PROCUREMENT OF RECOVERED MATERIALS. (Reference: 2 CFR § 200.322, 40 CFR part 247)
22. RIGHT TO INVENTIONS. (Reference 2 CFR § 200, Appendix II(F); 37 CFR §401)
23. SEISMIC SAFETY (Reference: National Earthquake Hazards Reduction Program)
24. TAX DELINQUENCY AND FELONY CONVICTIONS (Reference: Section 8113 of the Consolidated Appropriations Act, 2022)
25. TERMINATION OF CONTRACT. (Reference: 2 CFR § 200 Appendix II(A))
26. TRADE RESTRICTION CERTIFICATION. (Reference: 49 USC § 50104; 49 CFR part 30)
27. VETERAN'S PREFERENCE. (Reference: 49 USC § 47112(c))
28. DOMESTIC PREFERENCES FOR PROCUREMENTS (Reference 2 CFR § 200.322, 2 CFR Part 200, Appendix II(L)

The contractor (including all subcontractors) shall insert the federal contract provisions and clauses located in the appendix in each contract and subcontract. The contractor (or subcontractor) shall incorporate applicable requirements of the contract provisions by reference for work done under any purchase orders, rental agreements and other agreements for supplies or services. The prime contractor will be responsible for compliance with these contract provisions by any subcontractor, lower-tier subcontractor or service provider. No modifications to the provisions are allowed. Minor additions covering state or sponsor requirements may be included in a separate supplemental specification, provided they do not conflict with federal laws and regulations and do not change the intent of the required contract provision. By signing this signature page ensures that the contractor agrees with all terms of the required federal contract provisions.

_____
Signature of Bidder

_____
Date

CONTRACT FORMS

PAYMENT BOND

KNOW ALL MEN BY THESE PRESENTS:

That the County of Santa Barbara of the State of California (hereinafter referred to as the County) and_____ (hereinafter referred to as Principal) have by written agreement dated _____, entered into a contract identified as:

Project Title: County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, CA 93460
County Project No. 22011-AIG XX
(Hereinafter referred to as the Contract) and

That, pursuant to law and to said Contract, and before entering upon the performance of said Contract, the principal is required to file with the County a good and sufficient bond to secure the payment of labor and materials claims.

NOW, THEREFORE, said Principal a_____

_____

as corporate surety (hereinafter referred to as Surety), are held firmly bound unto the County in the amount of $_____, for the payment of which Principal and Surety bind themselves, their heirs, executors, administrators, successors and assigns both jointly and severally. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications.

THE CONDITION OF THIS OBLIGATION IS SUCH that if said principal, his or its subcontractors, heirs, executors, administrators, successors, or assigns, shall fail to pay any of the persons named or referred to in Section 9100 of the California Civil Code, or amounts due under Unemployment Insurance Code with respect to work or labor performed by any such claimant, or for any amounts required to be deducted, withheld and paid over to the Employment Development Department from the wages of employees of the Contractor and his subcontractors pursuant to Section 13020 of the Unemployment Insurance Code with respect to such work and labor as required by the California Civil Code, or this bond, then said Surety will pay for the same, in an amount not to exceed the amount hereinafter set forth.

This bond shall insure to the benefit of any and all persons, entities, companies and corporations named or referred to in Section 9100 of the California Civil Code, so as to give a right of action to them or their assign in any suit brought upon this bond.

And the said Surety, for value received, hereby agrees that no change, extension of time, alteration or addition to the terms of the Contract, or to the work to be performed thereunder, or the Specifications accompanying the same, shall in anywise affect its obligations on this bond, and it does hereby waive notice of any such change, extension of time, alteration or addition to the terms of the Contract or to the Specifications.

In the event suit is brought upon this Bond by County and judgment is recovered, Surety shall pay all costs incurred by the County in such suit, including a reasonable attorney's fee to be fixed by the court.

Death, illness, disability or disqualification of the Principal shall not relieve Surety of its obligations hereunder.

(Principal)	(Surety)
(By)	(Signature of Attorney-In-Fact)
(Dated)	(Address)
	(City, State & Zip)

Surety's Agent for Service of Process (located within the State of California):

Name of Agent
Address
City, State & Zip
Telephone Number

NOTE: Signature of those executing for Surety must be properly acknowledged.

PERFORMANCE BOND

KNOW ALL MEN BY THESE PRESENTS:

That the County of Santa Barbara of the State of California (hereinafter referred to as the County) and _____. (hereinafter referred to as Principal) have by written agreement dated _____, entered into a contract identified as:

Project Title: County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, CA 93460
County Project No. 22011-AIG XX
(Hereinafter referred to as the Contract) and

That, pursuant to law and to said Contract, and before entering upon the performance of said Contract, the Principal is required under the terms and conditions of said Contract to furnish a bond for the faithful performance of Contract.

NOW, THEREFORE, said Principal and _____

_____

_____

_____

as corporate surety (hereinafter referred to as Surety), are held firmly bound unto the County in the amount of $_____, for the payment of which Principal and Surety bind themselves, their heirs, executors, administrators, successors and assigns both jointly and severally. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications.

THE CONDITION OF THIS OBLIGATION IS SUCH that if the Principal, his heirs, executors, administrators, successors, or assigns, shall perform all of the covenants, conditions and agreements in said Contract and any alteration thereof made as herein provided, in his or their part, to be kept and performed at the time, and in the manner therein specified, and shall indemnify and save harmless County, its officers, agents, and employees, as therein stipulated, then this obligation shall become null and void; otherwise it shall be and remain in full force, virtue and effect.

And the said Surety, for value received, hereby agrees that no change, extension of time, alteration or

addition to the terms of the Contract, or to the work to be performed thereunder, or the specifications accompanying the same shall in anywise affect its obligations on this bond, and it does hereby waive notice of any such change, extension of time, alteration or additions to the terms of the Contract or to the work or to the specifications.

In the event suit is brought upon this Bond by County and judgment is recovered, Surety shall pay all costs incurred by the County in such suit, including a reasonable attorney's fee to be fixed by the court.

Death, illness, disability or disqualification of the Principal shall not relieve Surety of its obligations hereunder.

(Principal)	(Surety)
(By)	(Signature of Attorney-In-Fact)
(Dated)	(Address)
	(City, State & Zip)

Surety's Agent for Service of Process (located within the State of California):

Name of Agent

Address

City, State & Zip

Telephone Number

NOTE: Signature of those executing for Surety must be properly acknowledged.

CERTIFICATE OF INSURANCE TRANSMITTAL FORM

FOR THE FOLLOWING DESCRIBED PROJECT:

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, CA 93460
County Project No. 22011-AIG XX

CONTRACTOR:

_____
Name

_____
Address

_____
City, State & Zip Code

The successful bidder shall furnish satisfactory proof of the maintenance of adequate Worker's Compensation Insurance, and the maintenance of Comprehensive General and Automobile Liability Insurance in the amount of not less than $1,000,000 per occurrence and $2,000,000 in the aggregate. The County of Santa Barbara (COUNTY), its officers, employees, and agents shall be named as additional insured on all certificates. A copy of the endorsement evidencing that the County has been added to the policy must be attached to the certificate of insurance. Said policy or policies shall provide that the COUNTY shall be given thirty (30) days written notice prior to cancellation or expiration of the policy or reduction in coverage. Refer to section 5.18 of the General Conditions.

In addition to the above, the following information must appear on the certificates:

County of Santa Barbara, Rehabilitate Tie-Down Apron, County Project No. 22011-AIG XX
900 Airport Rd., Santa Ynez, CA 93460

This form must be attached to all insurance forms sent to the County of Santa Barbara, General Services Department:

_____
Authorized Insurance Company Representative's Signature

This form may be reproduced as required.

COUNTY OF SANTA BARBARA UNLAWFUL DISCRIMINATION ORDINANCE

Section 2-95. Prohibition of unlawful discrimination in employment practices. The COUNTY reserves the right to terminate forthwith each and every written contract and agreement (except purchase orders) respecting real property for goods and/or services entered into by the COUNTY or by its joint powers, agencies, or agents with the consent of the other parties (hereinafter called "CONTRACTOR") including but not limited to concessions, franchises, construction agreements, leases, whether now in effect or hereinafter made if the COUNTY finds that the CONTRACTOR is discriminating or has discriminated against any employee or applicant for employment in violation of any applicable state or federal laws, rules, or regulations which may now or hereafter specifically prohibit such discrimination on such grounds as race, religion, sex, color, national origin, physical or mental handicap when otherwise qualified, Vietnam war veteran/disabled, age, medical condition, marital status, ancestry, sexual orientation, or other legally protected status.

Such finding may only be made after CONTRACTOR has had a full and fair hearing on notice of thirty (30) days before an impartial hearing officer at which hearing CONTRACTOR may introduce evidence, produce witness, and have the opportunity to cross-examine witnesses produced by the COUNTY. Further, any finding of discrimination must be fully supported by the facts developed at such hearing and set forth in a written opinion; and in addition, CONTRACTOR may move in the appropriate court of law for damages and/or to compel specific performance of a CONTRACTOR or agreement if any of the above procedures are not afforded to the CONTRACTOR. If CONTRACTOR is not found to have engaged in unlawful discriminatory practices, COUNTY shall pay all costs and expense of such hearing, including reasonable attorney's fees to CONTRACTOR in accordance with current Santa Barbara County Superior Court schedule of attorney's fees for civil trials. If CONTRACTOR is found to have engaged in such unlawful discriminatory employment practices, CONTRACTOR shall pay all such costs, expenses, and attorney's fees.

Whether or not a contract or agreement is still in existence at the time of final determination of such unlawful discrimination, the CONTRACTOR shall forthwith reimburse COUNTY for all damages directly stemming from such discrimination; however, those damages shall not exceed and are not reimbursable in an amount which exceeds amounts paid CONTRACTOR under the terms of the contract or agreement.

Nothing in this Section 2-95 shall directly or by interpretation give a private cause of action to any third party (not a signatory to the contract or agreement) including employees past or present, or applicants for employment to CONTRACTOR, it being the sole purpose of this clause to administratively assure compliance with the nondiscrimination clauses contained herein.

Employment practices shall include, but are not limited to employment, promotion, demotion, transfer, recruitment and advertising for recruitment, layoff or other termination, rate of pay, employee benefits, and all other forms of compensation selection for training and apprenticeship and probationary periods.

CONTRACTOR shall permit access at all reasonable time and places to all of its records of employment, advertising, application forms, tests, and all other pertinent employment data and records, to the COUNTY, its officers, employees, and agents for the purpose of investigation to ascertain if any unlawful discrimination as described herein has occurred or is being practiced, provided that such records are relevant to a complaint of an unlawful discriminatory practice which has been forwarded to CONTRACTOR reasonably prior to the time CONTRACTOR is asked to make such records available. In addition, all such records shall be deemed "Confidential" by the officers, employees, and agents of the COUNTY. No records or copies of such records may be removed from the premises of CONTRACTOR and no disclosure, oral, or written of such record, may be made to third parties except as provided within the agreement.

Provided, however, that in the event of a hearing to determine whether or not CONTRACTOR is engaging in unlawful discrimination in employment practices as defined herein, the Board of Supervisor of Santa Barbara County may issue subpoenas to require that certified copies of such records be made available to the hearing.

Failure to fully comply with any of the foregoing provisions relating to unlawful discrimination in employment practices shall be deemed to be a material breach of any contract or agreement with the COUNTY. All persons contracting with or who have contracts for goods or services with the COUNTY shall be notified that this chapter applied to their contract or agreement with the COUNTY (Ordinance No. 2946, SS1; Ordinance No. 2993, SS1; and Ordinance No. 3018, SS1).

Section 2-95.5. Exceptions. Notwithstanding any other provisions in this article, any party contracting with the COUNTY having an affirmative action program which has been approved within twelve (12) months from the date of the contract by an agency of the federal government shall be deemed to be in compliance with the provisions of this article upon furnishing documentary evidence of such approval satisfactory to the COUNTY affirmative action officer. Loss of such approval shall be immediately reported by such party to the COUNTY affirmative action officer.

Section 2-96. Purchase orders. Purchase orders shall contain the following clause as grounds for termination of such purchase orders:

"If complaint is made that seller is engaging in discriminatory employment practices made unlawful by applicable state and federal laws, rules, or regulations, and the State Fair Employment Practice Commission or the Federal Equal Employment Opportunities Commission determines that such unlawful discrimination exists, then the COUNTY may forthwith terminate this order." (Ordinance No. 2946, SS 1)

Section 2-97. Affirmative action officer. At the discretion of the COUNTY affirmative action officer, he or she shall promptly and thoroughly investigate, or cause to be investigated reports and complaints from whatever source, that any party contracting with the COUNTY is engaging, or during the term of a contract or agreement with the COUNTY has engaged, in any unlawful discriminatory employment practices as described in Section 2-95 of this Code. If the investigation discloses reason to believe such unlawful discrimination does exist or has existed and the conditions giving rise thereto have not been changed so as to prevent further such unlawful discrimination, and the said party shall forthwith terminate such unlawful discrimination, take all appropriate steps to prevent a recurrence of such or other unlawful practices, and compensate the person or persons unlawfully discriminated against for any and all loss incurred by reason of such unlawful discrimination, all to the satisfaction of the affirmative action officer, then the affirmative action officer shall cause the matter to be presented for action to the State Fair Employment Practices Commission or the Federal Equal Employment Opportunities Commission, or both, and to any other concerned state or federal agencies or officers.

If and when it has been finally determined by the affirmative action officer, COUNTY counsel, or state or federal regulatory agencies that such unlawful discriminatory employment practice has in fact so occurred or are being carried on, then the affirmative action officer shall forthwith present the entire matter to the Board of Supervisors of the COUNTY, together with all damages, costs, and expense related thereto and incurred by COUNTY, for appropriate action by the Board of Supervisors in accord with the intent and purposes of this article and of the affirmative action program of the COUNTY (Ordinance No. 2946, SS 1).

SAMPLE AGREEMENT

COUNTY OF SANTA BARBARA
AGREEMENT FOR:
County Project No. 22011-AIG XX
Rehabilitate Tie-Down Apron
900 Airport Rd., Santa Ynez, CA 93460

THIS AGREEMENT is made by and between the County of Santa Barbara, a political subdivision of the State of California, hereinafter called **COUNTY**, and_____, referred to as **CONTRACTOR**, for the completion of the Work (defined below), on the following terms, conditions, and provisions. All references in the General Terms to the "Agreement" shall have the meaning ascribed to the term "Agreement" in the immediately preceding sentence.

1. **CONTRACT**: This Agreement incorporates by reference all of the General Conditions and Special Conditions, Specifications and Drawings provided by the COUNTY for the **Rehabilitate Tie-Down Apron**, Project No. 22011, the Notice to Bidders as amended by Addenda Number {xx-xx}, the Bid Bond, the Performance Bond, the Payment Bond, and the bid documents executed and submitted by the CONTRACTOR for the Project ("Bid"), to the extent the Bid is consistent with the provisions of this Agreement other than the Bid (all of the foregoing documents, together with this Agreement, collectively, the "Contract" or "Contract Documents"). A copy of each of the General and Special Conditions, Specifications and Drawings provided by the COUNTY for the **Rehabilitate Tie-Down Apron**, Project No. 22011, the Notice to Contractors, the Bid Bond, the Performance Bond, and the Payment Bond are attached hereto as EXHIBIT A, and a copy of the Bid is attached hereto as EXHIBIT B. All capitalized terms used but not defined herein shall have the respective meanings ascribed to such terms in the Notice to Bidders. Copies of all Contract Documents are on file in the Department of General Services Office of the COUNTY, and have been and will be made available to the CONTRACTOR during the term of this Agreement. CONTRACTOR acknowledges receipt of all Contract Documents.

2. **WORK**: CONTRACTOR, at CONTRACTOR's own cost and expense, shall perform all the work described in the Contract Documents ("Work"), and shall furnish all equipment and materials necessary to perform and complete the Work, in a good and workmanlike manner and to the satisfaction of the Director of the COUNTY's General Services Department ("Director"), or the Director's designee, all in strict accordance with the Contract Documents.

3. **EXCAVATIONS**: Before any pavement resurfacing, displacement, or excavation of the ground that may be required in connection with the Work under this Contract, the CONTRACTOR shall obtain an inquiry identification number by calling Underground Service Alert (USA) 1 (800) 422-4133 or by such other means as may be required; shall conform to all requirements of Sections 4215 through 4217 of the Government Code regarding any such pavement resurfacing, displacement or excavation, including the payment of any fees required; and shall facilitate performance by the COUNTY of any obligation required of the COUNTY under the Government Code. There shall be no performance under this Contract by either party hereto unless and until CONTRACTOR complies with all of the foregoing provisions of this Sections 3, and notifies the County Representative (defined below) in writing regarding such compliance.

4. COUNTY REPRESENTATIVE: The "County Representative" referred to in the Contract Documents is STEVEN MANUEL

5. PAYMENT: As full compensation for furnishing all labor, supervision, overhead, materials, and equipment and for completing all of the Work contemplated by this Contract, and subject to adjustments and liquidated damages, if any, as provided in the Contract Documents, the base amount to be paid to the CONTRACTOR for satisfactory completion of all requirements of the CONTRACTOR under this Contract is and shall be WRITTEN AMOUNT IN DOLLARS AND CENTS ($NUMERICAL) ("Base Contract Amount"), to be paid as provided in the Contract Documents. The CONTRACTOR assumes and will provide against any loss or damage arising out of the nature of the Work undertaken, or the action of the elements, or from any unforeseen difficulties or obstructions which may arise or be encountered in the performance of the Work until its acceptance by the COUNTY, and assumes any and all expenses incurred by or in consequence of suspension or discontinuance of the Work, for well and faithfully completing the Work and the whole thereof, in the manner and to the requirements of the Contract and directions of the County Representative to the extent not inconsistent with any provisions of the Contract Documents.

6. **RIGHT TO AUDIT**: CONTRACTOR shall maintain and make available all books, papers, records, detail costs, estimates, claims, and accounts, including payment, property, payroll, personnel, subcontractors, and financial records related to or which arise in connection with the Contract (collectively, the "Records"). The form of record keeping with respect to the Records shall be subject to approval by COUNTY. The Records shall be made available during normal business hours for examination by COUNTY or the County Representative and shall be retained at CONTRACTOR'S principal place of business in California for audit during normal business hours at such place for four (4) years after the recording of the Notice of Completion for the Project. CONTRACTOR shall provide an office in which COUNTY and the County Representative may conduct such audit(s).

The COUNTY will have the right to audit CONTRACTOR'S Project records. Records must be made available in a form satisfactory to the Santa Barbara County Auditor-Controller.

7. EXTRA WORK: Extra work and materials, may be authorized via written Change Order(s) duly executed by the Director, including agreement(s) providing for compensation in addition to the Base Contract Amount at the same rates per unit provided for in the Contract Documents; *provided*, *however*, that the aggregate amount of such compensation in addition to the Base Contract Amount that may be authorized by the Director shall not exceed [__] (i.e., ten percent (10%) of the original Base Contract Amount, if the original Base Contract Amount is less than $250,000, or (ii) $25,000 + 5% of the amount of the original Base Contract Amount in excess of $250,000). Compensation in such other equitable amount as is appropriate for the requirements of the COUNTY may be authorized by resolution or minute order of the Santa Barbara County Board of Supervisors.

8. COMPLIANCE WITH LAW: CONTRACTOR shall keep fully informed of, and shall at all times during the Term (defined below) ensure the performance of the Work is in compliance with, all laws, statutes, ordinances, decrees, orders, and regulations which do or may affect the Project, performance of the Work, the materials used therein, or persons engaged in connection therewith, and all such orders of bodies and tribunals having any jurisdiction over same (collectively, "Applicable Laws"). If CONTRACTOR has reason to believe that any provision of the Contract Documents conflict with any Applicable Law(s), the CONTRACTOR shall immediately report same to the County Representative in writing. CONTRACTOR shall at all times observe and comply with, and shall cause all agents, employees, and subcontractors to observe and comply with, all Applicable Laws. CONTRACTOR acknowledges and shall comply with the provisions of Sections 9364 and Sections 9550 and 9566, inclusive, of the Civil Code of California.

9. PAYMENTS NOT ACCEPTANCE: No certificate given or payments made under this Contract, except the final payment hereunder, shall be evidence of the performance of this Contract, either wholly or in part, against any claim upon CONTRACTOR. Final payment for the Work performed under this Contract shall not be made until the lapse of thirty (30) days after the Notice of Completion of the Work has been filed for record and no payment shall be construed to be acceptance of any defective Work or improper materials. CONTRACTOR agrees that the payment for final quantities due under this Contract and the payment of amounts due for any Work in accordance with this Contract shall release the COUNTY from any claims or liabilities on account of Work performed under this Contract, as the same may be amended from time to time during the Term. In addition to guarantees required elsewhere, CONTRACTOR shall and does hereby guarantee all workmanship and material to be free of defects and fit for the purposes intended for a period of one year from and after both the date of acceptance of the work and the recordation of the Notice of Completion by the COUNTY and CONTRACTOR shall repair or replace all Work and materials, together with any other portions of the Work which may be displaced in so doing, that, in the opinion of the County Representative, is or becomes defective during the period of said guarantee, without expense whatsoever to the COUNTY.

10. PREVAILING WAGE RATES: Rates of wages, including overtime, holiday, and Sunday rates provided for the Work shall comply with and are subject to the California Labor Code, Sections 1770 et. seq., Executive Orders of the President of the United States No. 9240, dated September 9, 1942, and No. 9250, dated October 3, 1942, and to any modifications thereof, and to and any orders of the President or any authorized Federal Officer or agency, insofar as the same may apply to this Contract.

No contractor or subcontractor may be listed on a bid for a public works project unless registered with the Department of Industrial Relations pursuant to Labor Code section 1725.5 [with limited exceptions from this requirement for bid purposes only under Labor Code section 1771.1(a)]. No contractor or subcontractor may be awarded a contract for public work on a public works project unless registered with the Department of Industrial Relations pursuant to Labor Code section 1725.5. This Project is subject to compliance monitoring and enforcement by the Department of Industrial Relations.

11. CONTRACT DOCUMENTS ACKNOWLEDGED: CONTRACTOR hereby declares that CONTRACTOR has read the Contract Documents, has carefully examined the plans and detailed drawings of the Work to be performed, and fully understands the intent and meaning of the same.

12. TIME FOR COMMENCEMENT, COMPLETION: The term of this Contract shall commence effective as of the first date that this Agreement is duly executed by all of the parties hereto ("Effective Date") and shall terminate on the date that is 100 working days after the Effective Date unless earlier terminated in accordance with the provisions of this Agreement ("Term"). As soon as practicable after the Contract has been executed by both the CONTRACTOR and the COUNTY, a Notice to Proceed will be issued by the County Representative stating the starting date of work performance under the Contract. The CONTRACTOR shall begin work within fifteen (15) calendar days after receiving the Notice to Proceed unless otherwise provided therein. The provisions of this Agreement pertaining to Liquidated Damages shall apply in the event of the CONTRACTOR's failure to complete the Work within the Term. In the event that CONTRACTOR does not complete the Work during the Term, CONTRACTOR shall only be paid for the Work actually performed during the Term and accepted by COUNTY in accordance with the provisions of this Agreement.

13. WORKERS' COMPENSATION INSURANCE: CONTRACTOR certifies that CONTRACTOR has knowledge of, is in compliance with, and warrants that CONTRACTOR at all times during the Term shall remain in compliance with, the provisions of Section 3700 of the Labor Code, which requires every employer to be insured against liability for Workers' Compensation or to undertake self-insurance by the provisions of that Code. CONTRACTOR shall comply with such provisions before

commencing the performance of the Work.

14. PROGRESS PAYMENT; NO WAIVER FOR DELAY: Any progress payment made after the scheduled completion date for the Work shall not constitute a waiver of any liquidated damages under this Contract.

15. GUARANTEE BONDS: Before any performance under this Contract, the CONTRACTOR shall provide the security required by statute for the payment of all workers and suppliers, and security for the faithful performance of all terms and conditions of this Contract, in an amount and form approved by the COUNTY. Both securities shall contain provisions that automatically increase amounts thereof and/or time of completion or both for all change orders, extensions, and additions to the Work provided under this Contract.

16. DISPUTES: Should any dispute(s) arise respecting the construction or meaning of any of the plans or specifications affecting the Work or respecting the true value of any extra work or work omitted, such dispute(s) shall be resolved by the Director of the COUNTY's General Services Department or his Assistant Director of General Services designee ("Director"), whose decision shall be final and binding upon the parties hereto. If, after the decision of the Director as provided herein, claims (as defined in Public Contracts Code Section 20104) under this Contract are filed by CONTRACTOR against COUNTY, and those claims are in the aggregate amount of $375,000 or less, such claims shall be resolved under Public Contracts Code Sections 20104 through 20104.8, inclusive.

17. SUBSTITUTION OF MATERIALS, SUBSTITUTION OF CONTRACTORS: The County Representative is authorized to act on behalf of the COUNTY in any matters requiring consent to substitutions of materials or equipment; provided, however, that the County Representative is not authorized to [_____].

18. SURVIVAL: All provisions of this Contract which by their nature are intended to survive the termination or expiration of this Agreement shall survive such termination or expiration.

19. INDEMNIFICATION AND INSURANCE: CONTRACTOR shall at all times comply with the indemnification and insurance provisions set forth in EXHIBIT C, attached hereto and incorporated herein by reference.

20. FEDERAL PROVISIONS: CONTRACTOR acknowledges that Federal financial assistance will be used to fund this Agreement. CONTRACTOR shall only use federal funds as authorized herein. CONTRACTOR will comply will all applicable federal law, regulations, executive orders, federal policies, procedures, and directives, including, but not limited to, Title 2 of the Code of Federal Regulations (CFR) Part 200, entitled, "Uniform Administrative Requirements, Cost Principles, and Audit Requirements for Federal Awards." In addition, CONTRACTOR shall comply with the Federal Terms and Conditions attached hereto as EXHIBIT D and incorporated herein by reference. CONTRACTOR shall comply with grant agreements, assurances in applications, notices of award, and all other applicable federal, state, and local laws, regulations, ordinances, orders, rules, guidelines, directives, circulars, bulletins, notices, and policies governing the Federal funds provided in connection with this Agreement. CONTRACTOR shall be responsible for providing services in a manner consistent with all federal and state requirements and standards required as a condition of receiving and expending funds provided in connection with this Agreement.

21. **TAXES**: CONTRACTOR shall pay all taxes, levies, duties, and assessments of every nature due in connection with any Work under this Contract, and shall make any and all payroll deductions required by

law. CONTRACTOR is responsible for all CONTRACTOR personnel and for the payment of their compensation, including, if applicable, withholding of income taxes, and the payment and withholding of social security and other payroll taxes, unemployment insurance, workers' compensation insurance payments, and disability benefits. In no event shall COUNTY pay or be responsible for any taxes imposed on, or with respect to, CONTRACTOR's income, revenues, gross receipts, personnel, real or personal property, or other assets. COUNTY shall not be responsible for paying any taxes on CONTRACTOR's behalf, and should COUNTY be required to do so by state, federal, or local taxing agencies, CONTRACTOR agrees to promptly reimburse COUNTY for the full value of such paid taxes plus interest and penalty, if any. These taxes shall include, but not be limited to, the following: FICA (Social Security), unemployment insurance contributions, income tax, disability insurance, and workers' compensation insurance.

22. CONFLICT OF INTEREST: CONTRACTOR covenants that CONTRACTOR presently has no employment or interest and shall not acquire any employment or interest, direct or indirect, including any interest in any business, property, or source of income, which would conflict in any manner or degree with the performance of Word required to be performed under this Contract. CONTRACTOR further covenants that in the performance of this Contract, no person having any such interest shall be employed by CONTRACTOR. CONTRACTOR must promptly disclose to COUNTY, in writing, any potential conflict of interest. COUNTY retains the right to waive a conflict of interest disclosed by CONTRACTOR if COUNTY determines it to be immaterial, and such waiver is only effective if provided by COUNTY to CONTRACTOR in writing.

23. NONDISCRIMINATION: COUNTY hereby notifies CONTRACTOR that COUNTY's Unlawful Discrimination Ordinance (Article XIII of Chapter 2 of the Santa Barbara County Code) applies to this Contract and is incorporated herein by this reference with the same force and effect as if the ordinance were specifically set out herein and CONTRACTOR agrees to comply with said ordinance.

24. NON-ASSIGNMENT: CONTRACTOR shall not assign, subcontract, delegate, or otherwise transfer, directly or indirectly, whether by operation of law or otherwise ("Transfer") this Contract, in whole or in part,, or any of CONTRACTOR's rights or obligations under this Contract, without the prior written consent of COUNTY in each instance. Any attempted or purported Transfer in violation of this Section 24, or in violation of Section 2.08 of the General Conditions, attached hereto as part of Exhibit A, shall be null and void and without legal effect and shall constitute grounds for termination by COUNTY. No Transfer shall relieve CONTRACTOR of any of its obligations hereunder.

25. SEVERABILITY: If any one or more of the provisions contained in the Contract shall for any reason be held to be invalid, illegal or unenforceable in any respect by a court of competent jurisdiction, then such provision or provisions shall be deemed severable from the remaining provisions hereof, and such invalidity, illegality or unenforceability shall not affect any other provision hereof, and this Contract shall be construed as if such invalid, illegal or unenforceable provision had never been contained herein.

26. TIME IS OF THE ESSENCE: Time is of the essence in this Contract, and each covenant and term is a condition herein.

27. ENTIRE AGREEMENT AND AMENDMENT: The Contract Documents, as may be modified from time to time during the Term by duly authorized and executed Change Orders in accordance with the provisions of this Agreement and the General Terms, contain the entire understanding and agreement of the Parties with respect to the subject matter hereof and thereof, and there have been no promises, representations, agreements, warranties or undertakings by any of the Parties, either oral or written, of any character or nature hereafter binding except as set forth herein and therein. This Contract may be altered, amended or modified only by an instrument in writing, duly executed by each of the Parties, and by no

other means, except as otherwise set forth in Section 30, below, to the extent such delegated authority is expressly authorized by the COUNTY Board of Supervisors in approving this Contract. Each Party waives its future right to claim, contest or assert that this Agreement was modified, canceled, superseded, or changed by any oral agreements, course of conduct, waiver or estoppel.

28. EXECUTION OF COUNTERPARTS: This Contract may be executed electronically and in any number of counterparts, and each of such counterparts shall for all purposes be deemed to be an original; and all such counterparts, or as many of them as the Parties shall preserve undestroyed, shall together constitute one and the same instrument.

29. SUBCONTRACTORS: CONTRACTOR is authorized to subcontract with only the subcontractor(s) identified in the Bid as attached hereto and as set forth in Exhibit B ("Subcontractors"). Contractor shall be fully responsible for all services and Work performed by its Subcontractors. Contractor shall secure from each of its Subcontractors legally binding written agreements to comply with the provisions of this Agreement pertaining to CONTRACTOR's obligations as if such obligations pertained to such Subcontractor, including, but not limited to, audit obligations.

30. CHANGE ORDERS: No Change Order shall be valid or enforceable against the COUNTY unless in the form of the Form of Change Order attached here as Exhibit [_] and duly executed by both CONTRACTOR and the Director. in accordance with this Section 30 and Article 6 of the General Conditions ("Change Order"). No Change Order may (i) extend the Term, (ii) authorize Work to be performed hereunder after the Term or after the expiration or termination of this Agreement, (iii) increase the Maximum Contract Amount, or (iv) change the plans or specifications.

31. FLEET REQUIREMENTS: Vehicles with a Gross vehicle weight rating ("GVWR") greater than 8,500 lbs. and light-duty package delivery vehicles operated in California may be subject to the California Air Resources Board ("CARB") Advanced Clean Fleets regulations. Such vehicles may therefore be subject to requirements to reduce emissions of air pollutants. For more information, please visit the CARB Advanced Clean Fleets webpage at https://ww2.arb.ca.gov/our-work/programs/advanced-clean-fleets. Contractor shall at all times have a valid Certificate of Reported Compliance, as described in section 2449(n) of Title 13 of the California Code of Regulations ("CARB Certificate of Compliance"), and shall confirm that each subcontractor listed in Contractor's Bid has a valid CARB Certificate of Compliance, for each fleet of vehicles subject to 13 CCR section 2449 that may be used in performance of this Contract. No such vehicle is permitted on the project site unless and until Contractor provides County with a valid Certificate of Reported Compliance applicable to such vehicle.

32. ORDER OF PRECEDENCE: In the event of conflict between the provisions contained in the numbered sections 1 through 35 of this Agreement ("Numbered Section") and the provisions contained in the Exhibits, the provisions contained in the Numbered Sections of this Agreement shall prevail over those in the Exhibits other than Exhibit C, which Exhibit C shall control and prevail over all other provisions of this Contract. CONTRACTOR agrees that in the event of any discrepancy, inconsistency, gap, ambiguity, or conflicting language between the Bid attached hereto as Exhibit B, on the one hand, and any other provision(s) of this Contract on the other, the provisions of this Contract (including the Numbered Sections of this Agreement, Exhibit A, and Exhibit C) other than Exhibit B shall take precedence and control and prevail over the provisions of the Bid attached hereto as Exhibit B.

33. TERMINATION.

A. COUNTY may, by written notice to CONTRACTOR, terminate this Contract in whole or in part at any time, whether for COUNTY's convenience, for nonappropriation of funds, or because of the failure of CONTRACTOR to fulfill its obligations hereunder.

1. For Convenience. COUNTY may terminate this Contract in whole or in part upon thirty (30) days'

written notice. During such thirty (30) day period, CONTRACTOR shall, as directed by COUNTY, wind down and cease Work as quickly and efficiently as reasonably possible, without performing unnecessary services or activities and by minimizing negative effects on COUNTY from such winding down and cessation of Work.

2. For Nonappropriation of Funds. Notwithstanding any other provision of this Contract, in the event that no funds or insufficient funds are appropriated or budgeted by federal, State or COUNTY governments, or sufficient funds are not otherwise available for payments hereunder in the fiscal year(s) covered by the Term of this Agreement, then COUNTY will notify CONTRACTOR of such occurrence, and COUNTY may terminate or suspend this Contract in whole or in part, with or without a prior notice period. Subsequent to termination of this Contract under this provision, COUNTY shall have no obligation to make payments with regard to the remainder of the Term.

3. For Cause. Should CONTRACTOR default in the performance of this Contract or materially breach any of the provisions hereof, COUNTY may, at COUNTY's sole option, terminate or suspend this Contract in whole or in part upon written notice ("Termination Notice"). Upon receipt of such Termination Notice, CONTRACTOR shall immediately discontinue all Work (unless otherwise directed in such Termination Notice) and notify COUNTY in writing of the status of CONTRACTOR's performance of Work hereunder. The date of termination shall be the date the Termination Notice is received by CONTRACTOR, unless the Termination Notice directs otherwise.

B. Upon termination, CONTRACTOR shall deliver to COUNTY all data, estimates, graphs, summaries, reports, and all other property, records, documents or papers as may have been accumulated or produced by CONTRACTOR in performing this Contract, whether completed or in process, except such items as COUNTY may, by written permission, permit CONTRACTOR to retain. Notwithstanding any other payment provision of this Contract, COUNTY shall pay CONTRACTOR for satisfactory Work performed as of the date of termination to include a prorated amount of compensation due hereunder less payments, if any, previously made. In no event shall CONTRACTOR be paid an amount in excess of the Maximum Contract Amount, or for unperformed portions of Work. CONTRACTOR shall furnish to COUNTY such financial information as in the judgment of COUNTY is necessary to determine the reasonable value of the Work rendered by CONTRACTOR. The foregoing is cumulative and shall not affect any right or remedy which COUNTY may have in law or equity.

34. JURISDICTION; VENUE. This Contract shall be governed by the laws of the State of California. Any litigation arising out of this Contract shall be filed in the County of Santa Barbara, if in state court, or in the federal district court nearest to the County of Santa Barbara, if in federal court.

35. NO WAIVER. COUNTY's delay or failure to act with respect to a breach of this Contract by CONTRACTOR shall not constitute or be construed as a waiver of COUNTY's rights with respect to subsequent or similar breaches. Any delay or failure of COUNTY to exercise or enforce any right or provision of this Contract shall not constitute a waiver of such right or provision, and every power and remedy given by this Contract to COUNTY shall be exercised from time to time and as often as may be deemed expedient in the sole discretion of COUNTY. No remedy herein conferred upon or reserved to COUNTY is intended to be exclusive of any other remedy or remedies, and each and every such remedy, to the extent permitted by law, shall be cumulative and in addition to any other remedy given hereunder or now or hereafter existing at law or in equity or otherwise.

IN WITNESS WHEREOF, the parties hereto have executed this Agreement to be effective as of the date executed by the County.

COUNTY
County of Santa Barbara

By: _____
LAURA CAPPS, CHAIR
BOARD OF SUPERVISORS

Dated: _____

ATTEST:
MONA MIYASATO,

CONTRACTOR

Name of Contractor, a California corporation

_____
COUNTY EXECUTIVE OFFICER

CLERK OF THE BOARD

By: _____
Deputy Clerk of the Board

By: _____
AUTHORIZED REPRESENTATIVE
Name:

Title:

APPROVED AS TO FORM: APPROVED AS TO ACCOUNTING FORM:

RACHEL VAN MULLEM,
COUNTY COUNSEL

By: _____
Deputy County Counsel

BETSY SCHAFFER, CPA, CPFO
AUDITOR-CONTROLLER

By: _____
Deputy Auditor-Controller

APPROVED AS TO FORM: RECOMMENDED FOR APPROVAL

GREG MILLIGAN, ARM
RISK MANAGER

By: _____
Risk Management

KIRK LAGERQUIST, DIRECTOR
GENERAL SERVICES DEPARTMENT

By: _____
Department Head

Dept 063 Fund 0052 Program 1920 Account 8200

EXHIBIT C

INDEMNIFICATION AND INSURANCE REQUIREMENTS
(For Construction Contracts)

INDEMNIFICATION

CONTRACTOR agrees to indemnify, defend (with counsel reasonably approved by COUNTY) and hold harmless COUNTY and its officers, officials, employees, agents and volunteers from and against any and all claims, actions, losses, damages, judgments and/or liabilities arising out of this Agreement from any cause whatsoever, including the acts, errors or omissions of any person or entity and for any costs or expenses (including but not limited to attorneys' fees) incurred by COUNTY on account of any claim except where such indemnification is caused by the active negligence, sole negligence, or willful misconduct of the COUNTY.

NOTIFICATION OF ACCIDENTS AND SURVIVAL OF INDEMNIFICATION PROVISIONS

CONTRACTOR shall notify COUNTY immediately in the event of any accident or injury arising out of or in connection with this Agreement. The indemnification provisions in this Agreement shall survive any expiration or termination of this Agreement.

INSURANCE

CONTRACTOR shall procure and maintain for the duration of this Agreement insurance against claims for injuries to persons or damages to property which may arise from or in connection with the performance of the work hereunder and the results of that work by the CONTRACTOR, its agents, representatives, employees or subcontractors.

A. Minimum Scope and Limit of Insurance
Coverage shall be at least as broad as:

1. **Commercial General Liability (CGL):** Insurance Services Office (ISO) Form CG 00 01 covering CGL on an "occurrence" basis, including products-completed operations, personal & advertising injury, with limits no less than $2,000,000 per occurrence and $4,000,000 in the aggregate.
2. **Automobile Liability**: Insurance Services Office Form CA 0001 covering Code 1 (any auto), with limits no less than $2,000,000 per accident for bodily injury and property damage.
3. **Workers' Compensation**: Insurance as required by the State of California, with Statutory Limits, and Employer's Liability Insurance with limit of no less than $1,000,000 per accident for bodily injury or disease.
4. **Contractor's Pollution Legal Liability and/or Asbestos Legal Liability:** (if project involves environmental hazards) with limits no less than $1,000,000 per occurrence or claim, and $2,000,000 policy aggregate.

If the CONTRACTOR maintains higher limits than the minimums shown above, the COUNTY requires and shall be entitled to coverage for the higher limits maintained by the CONTRACTOR. Any available insurance proceeds in excess of the specified minimum limits of insurance and coverage shall be available to the COUNTY.

B. Other Insurance Provisions

The insurance policies are to contain, or be endorsed to contain, the following provisions:

1. **Additional Insured** – COUNTY, its officers, officials, employees, agents and volunteers are to be covered as additional insureds on the CGL policy with respect to liability arising out of work or operations performed by or on behalf of the CONTRACTOR including materials, parts, or equipment furnished in connection with such work or operations. General liability coverage can be provided in the form of an endorsement to the CONTRACTOR'S insurance at least as broad as ISO Form CG 20 10 11 85 or **both** CG 20 10, CG 20 26, CG 20 33, or CG 20 38; **and** CG 20 37 forms if later revisions used).
2. **Primary Coverage** – For any claims related to this Agreement, the CONTRACTOR'S insurance coverage shall be primary insurance coverage at least as broad as ISO CG 20 01 04 13 as respects the COUNTY, its officers, officials, employees, agents and volunteers. Any insurance or self-insurance maintained by the COUNTY, its officers, officials, employees, agents or volunteers shall be excess of the CONTRACTOR'S insurance and shall not contribute with it.
3. **Notice of Cancellation** – Each insurance policy required above shall provide that coverage shall not be canceled, except with notice to the COUNTY.
4. **Waiver of Subrogation Rights** – **CONTRACTOR hereby agrees to waive rights of subrogation which any insurer of CONTRACTOR may acquire** from CONTRACTOR by virtue of the payment of any loss. CONTRACTOR agrees to obtain any endorsement that may be necessary to effect this waiver of subrogation. **The Workers' Compensation policy shall be endorsed with a waiver of subrogation** in favor of the COUNTY for all work performed by the CONTRACTOR, its employees, agents and subcontractors. This provision applies regardless of whether or not the COUNTY has received a waiver of subrogation endorsement from the insurer.
5. **Deductibles and Self-Insured Retention** – Any deductibles or self-insured retentions must be declared to and approved by the COUNTY. At the option of the COUNTY, either: the CONTRACTOR shall cause the insurer shall reduce or eliminate such deductibles or self-insured retentions as respects the COUNTY, its officers, officials, employees, agents and volunteers; or the CONTRACTOR shall provide a financial guarantee satisfactory to the COUNTY guaranteeing payment of losses and related investigations, claim administration, and defense expenses.
6. **Acceptability of Insurers** – Unless otherwise approved by Risk Management, insurance shall be written by insurers authorized to do business in the State of California and with a minimum A.M. Best's Insurance Guide rating of "A- VII".
7. **Verification of Coverage** – CONTRACTOR shall furnish the COUNTY with proof of insurance, original certificates and amendatory endorsements as required by this Agreement. The proof of insurance, certificates and endorsements are to be received and approved by the COUNTY before work commences. However, failure to obtain the required documents prior to the work beginning shall not waive the CONTRACTOR'S obligation to provide them. The CONTRACTOR shall furnish evidence of renewal of coverage throughout the term of the Agreement. The COUNTY reserves the right to require complete, certified copies of all required insurance policies, including endorsements required by these specifications, at any time.
8. **Failure to Procure Coverage** – In the event that any policy of insurance required under this Agreement does not comply with the requirements, is not procured, or is canceled and not replaced, COUNTY has the right but not the obligation or duty to terminate the Agreement. Maintenance of required insurance coverage is a material element of the Agreement and failure to maintain or renew such coverage or to provide evidence of renewal may be treated by COUNTY as a material breach of contract.

9. **Subcontractors** – CONTRACTOR shall require and verify that all subcontractors maintain insurance meeting all the requirements stated herein, and CONTRACTOR shall ensure that COUNTY is an additional insured on insurance required from subcontractors. For CGL coverage subcontractors shall provide coverage with a format least as broad as CG 20 38 04 13.
10. **Claims Made Policies** – If any of the required policies provide coverage on a claims-made basis:
    i. The Retroactive Date must be shown and must be before the date of the contract or the beginning of contract work.
    ii. Insurance must be maintained and evidence of insurance must be provided for at least five (5) years after completion of contract work.
    iii. If coverage is canceled or non-renewed, and not replaced with another claims-made policy form with a Retroactive Date prior to the contract effective date, the CONTRACTOR must purchase "extended reporting" coverage for a minimum of five (5) years after completion of contract work.
11. **Special Risks or Circumstances** – COUNTY reserves the right to modify these requirements, including limits, based on the nature of the risk, prior experience, insurer, coverage, or other circumstances.

Any change requiring additional types of insurance coverage or higher coverage limits must be made by amendment to this Agreement. CONTRACTOR agrees to execute any such amendment within thirty (30) days of receipt.

Any failure, actual or alleged, on the part of COUNTY to monitor or enforce compliance with any of the insurance and indemnification requirements will not be deemed as a waiver of any rights on the part of COUNTY.

TECHNICAL SPECIFICATIONS

Part 1 – General Contract Provisions

Section 10 Definition of Terms

When the following terms are used in these specifications, in the contract, or in any documents or other instruments pertaining to construction where these specifications govern, the intent and meaning shall be defined as follows:

Paragraph Number	Term	Definition
10-01	**AASHTO**	The American Association of State Highway and Transportation Officials.
10-02	**Access Road**	The right-of-way, the roadway and all improvements constructed thereon connecting the airport to a public roadway.
10-03	**Advertisement**	A public announcement, as required by local law, inviting bids for work to be performed and materials to be furnished.
10-04	**Airport**	Airport means an area of land or water which is used or intended to be used for the landing and takeoff of aircraft; an appurtenant area used or intended to be used for airport buildings or other airport facilities or rights of way; airport buildings and facilities located in any of these areas, and a heliport.
10-05	**Airport Improvement Program (AIP)**	A grant-in-aid program, administered by the Federal Aviation Administration (FAA).
10-06	**Air Operations Area (AOA)**	The term air operations area (AOA) shall mean any area of the airport used or intended to be used for the landing, takeoff, or surface maneuvering of aircraft. An air operation area shall include such paved or unpaved areas that are used or intended to be used for the unobstructed movement of aircraft in addition to its associated runway, taxiway, or apron.
10-07	**Apron**	Area where aircraft are parked, unloaded or loaded, fueled and/or serviced.
10-08	**ASTM International (ASTM)**	Formerly known as the American Society for Testing and Materials (ASTM).

Paragraph Number	Term	Definition
10-09	**Award**	The Owner's notice to the successful bidder of the acceptance of the submitted bid.
10-10	**Bidder**	Any individual, partnership, firm, or corporation, acting directly or through a duly authorized representative, who submits a proposal for the work contemplated.
10-11	**Building Area**	An area on the airport to be used, considered, or intended to be used for airport buildings or other airport facilities or rights-of-way together with all airport buildings and facilities located thereon.
10-12	**Calendar Day**	Every day shown on the calendar.
10-13	**Certificate of Analysis (COA)**	The COA is the manufacturer's Certificate of Compliance (COC) including all applicable test results required by the specifications.
10-14	**Certificate of Compliance (COC)**	The manufacturer's certification stating that materials or assemblies furnished fully comply with the requirements of the contract. The certificate shall be signed by the manufacturer's authorized representative.
10-15	**Change Order**	A written order to the Contractor covering changes in the plans, specifications, or proposal quantities and establishing the basis of payment and contract time adjustment, if any, for work within the scope of the contract and necessary to complete the project.
10-16	**Contract**	A written agreement between the Owner and the Contractor that establishes the obligations of the parties including but not limited to performance of work, furnishing of labor, equipment and materials and the basis of payment. The awarded contract includes but may not be limited to: Advertisement, Contract form, Proposal, Performance bond, payment bond, General provisions, certifications and representations, Technical Specifications, Plans, Supplemental Provisions, standards incorporated by reference and issued addenda.
10-17	**Contract Item (Pay Item)**	A specific unit of work for which a price is provided in the contract.
10-18	**Contract Time**	The number of calendar days or working days, stated in the proposal, allowed for completion of the contract, including authorized time extensions. If a calendar date of completion is stated in the proposal, in lieu of a number of

Paragraph Number	Term	Definition
		calendar or working days, the contract shall be completed by that date.
10-19	**Contractor**	The individual, partnership, firm, or corporation primarily liable for the acceptable performance of the work contracted and for the payment of all legal debts pertaining to the work who acts directly or through lawful agents or employees to complete the contract work.
10-20	**Contractors Quality Control (QC) Facilities**	The Contractor's QC facilities in accordance with the Contractor Quality Control Program (CQCP).
10-21	**Contractor Quality Control Program (CQCP)**	Details the methods and procedures that will be taken to assure that all materials and completed construction required by the contract conform to contract plans, technical specifications and other requirements, whether manufactured by the Contractor, or procured from subcontractors or vendors.
10-22	**Control Strip**	A demonstration by the Contractor that the materials, equipment, and construction processes results in a product meeting the requirements of the specification.
10-23	**Construction Safety and Phasing Plan (CSPP)**	The overall plan for safety and phasing of a construction project developed by the airport operator, or developed by the airport operator's consultant and approved by the airport operator. It is included in the invitation for bids and becomes part of the project specifications.
10-24	**Drainage System**	The system of pipes, ditches, and structures by which surface or subsurface waters are collected and conducted from the airport area.
10-25	**Engineer**	The individual, partnership, firm, or corporation duly authorized by the Owner to be responsible for engineering, inspection, and/or observation of the contract work and acting directly or through an authorized representative.
10-26	**Equipment**	All machinery, together with the necessary supplies for upkeep and maintenance; and all tools and apparatus necessary for the proper construction and acceptable completion of the work.
10-27	**Extra Work**	An item of work not provided for in the awarded contract as previously modified by change order or supplemental agreement, but which is found by the Owner's Engineer or Resident Project Representative (RPR) to be necessary to

Paragraph Number	Term	Definition
		complete the work within the intended scope of the contract as previously modified.
10-28	**FAA**	The Federal Aviation Administration. When used to designate a person, FAA shall mean the Administrator or their duly authorized representative.
10-29	**Federal Specifications**	The federal specifications and standards, commercial item descriptions, and supplements, amendments, and indices prepared and issued by the General Services Administration.
10-30	**Force Account**	**a.** Contract Force Account - A method of payment that addresses extra work performed by the Contractor on a time and material basis. **b.** Owner Force Account - Work performed for the project by the Owner's employees.
10-31	**Intention of Terms**	Whenever, in these specifications or on the plans, the words “directed,” “required,” “permitted,” “ordered,” “designated,” “prescribed,” or words of like import are used, it shall be understood that the direction, requirement, permission, order, designation, or prescription of the Engineer and/or Resident Project Representative (RPR) is intended; and similarly, the words “approved,” “acceptable,” “satisfactory,” or words of like import, shall mean approved by, or acceptable to, or satisfactory to the Engineer and/or RPR, subject in each case to the final determination of the Owner. Any reference to a specific requirement of a numbered paragraph of the contract specifications or a cited standard shall be interpreted to include all general requirements of the entire section, specification item, or cited standard that may be pertinent to such specific reference.
10-32	**Lighting**	A system of fixtures providing or controlling the light sources used on or near the airport or within the airport buildings. The field lighting includes all luminous signals, markers, floodlights, and illuminating devices used on or near the airport or to aid in the operation of aircraft landing at, taking off from, or taxiing on the airport surface.
10-33	**Major and Minor Contract Items**	A major contract item shall be any item that is listed in the proposal, the total cost of which is equal to or greater than 20% of the total amount of the award contract. All other items shall be considered minor contract items.

Paragraph Number	Term	Definition
10-34	**Materials**	Any substance specified for use in the construction of the contract work.
10-35	**Modification of Standards (MOS)**	Any deviation from standard specifications applicable to material and construction methods in accordance with FAA Order 5300.1.
10-36	**Notice to Proceed (NTP)**	A written notice to the Contractor to begin the actual contract work on a previously agreed to date. If applicable, the Notice to Proceed shall state the date on which the contract time begins.
10-37	**Owner**	The term "Owner" shall mean the party of the first part or the contracting agency signatory to the contract. Where the term "Owner" is capitalized in this document, it shall mean airport Sponsor only. The Owner for this project is the **County of Santa Barbara.**
10-38	Passenger Facility Charge (PFC)	Per 14 Code of Federal Regulations (CFR) Part 158 and 49 United States Code (USC) § 40117, a PFC is a charge imposed by a public agency on passengers enplaned at a commercial service airport it controls.
10-39	**Pavement Structure**	The combined surface course, base course(s), and subbase course(s), if any, considered as a single unit.
10-40	**Payment bond**	The approved form of security furnished by the Contractor and their own surety as a guaranty that the Contractor will pay in full all bills and accounts for materials and labor used in the construction of the work.
10-41	**Performance bond**	The approved form of security furnished by the Contractor and their own surety as a guaranty that the Contractor will complete the work in accordance with the terms of the contract.
10-42	**Plans**	The official drawings or exact reproductions which show the location, character, dimensions and details of the airport and the work to be done and which are to be considered as a part of the contract, supplementary to the specifications. Plans may also be referred to as 'contract drawings.'
10-43	**Project**	The agreed scope of work for accomplishing specific airport development with respect to a particular airport.

Paragraph Number	Term	Definition
10-44	**Proposal**	The written offer of the bidder (when submitted on the approved proposal form) to perform the contemplated work and furnish the necessary materials in accordance with the provisions of the plans and specifications.
10-45	**Proposal guaranty**	The security furnished with a proposal to guarantee that the bidder will enter into a contract if their own proposal is accepted by the Owner.
10-46	**Quality Assurance (QA)**	Owner's responsibility to assure that construction work completed complies with specifications for payment.
10-47	**Quality Control (QC)**	Contractor's responsibility to control material(s) and construction processes to complete construction in accordance with project specifications.
10-48	**Quality Assurance (QA) Inspector**	An authorized representative of the Engineer and/or Resident Project Representative (RPR) assigned to make all necessary inspections, observations, tests, and/or observation of tests of the work performed or being performed, or of the materials furnished or being furnished by the Contractor.
10-49	**Quality Assurance (QA) Laboratory**	The official quality assurance testing laboratories of the Owner or such other laboratories as may be designated by the Engineer or RPR. May also be referred to as Engineer's, Owner's, or QA Laboratory.
10-50	**Resident Project Representative (RPR)**	The individual, partnership, firm, or corporation duly authorized by the Owner to be responsible for all necessary inspections, observations, tests, and/or observations of tests of the contract work performed or being performed, or of the materials furnished or being furnished by the Contractor, and acting directly or through an authorized representative.
10-51	**Runway**	The area on the airport prepared for the landing and takeoff of aircraft.
10-52	**Runway Safety Area (RSA)**	A defined surface surrounding the runway prepared or suitable for reducing the risk of damage to aircraft. See the construction safety and phasing plan (CSPP) for limits of the RSA.
10-53	**Safety Plan Compliance Document (SPCD)**	Details how the Contractor will comply with the CSPP.

Paragraph Number	Term	Definition
10-54	**Specifications**	A part of the contract containing the written directions and requirements for completing the contract work. Standards for specifying materials or testing which are cited in the contract specifications by reference shall have the same force and effect as if included in the contract physically.
10-55	**Sponsor**	A Sponsor is defined in 49 USC § 47102(24) as a public agency that submits to the FAA for an AIP grant; or a private Owner of a public-use airport that submits to the FAA an application for an AIP grant for the airport.
10-56	**Structures**	Airport facilities such as bridges; culverts; catch basins, inlets, retaining walls, cribbing; storm and sanitary sewer lines; water lines; underdrains; electrical ducts, manholes, handholes, lighting fixtures and bases; transformers; navigational aids; buildings; vaults; and, other manmade features of the airport that may be encountered in the work and not otherwise classified herein.
10-57	**Subgrade**	The soil that forms the pavement foundation.
10-58	**Superintendent**	The Contractor's executive representative who is present on the work during progress, authorized to receive and fulfill instructions from the RPR, and who shall supervise and direct the construction.
10-59	**Supplemental Agreement**	A written agreement between the Contractor and the Owner that establishes the basis of payment and contract time adjustment, if any, for the work affected by the supplemental agreement. A supplemental agreement is required if: (1) in scope work would increase or decrease the total amount of the awarded contract by more than 25%: (2) in scope work would increase or decrease the total of any major contract item by more than 25%; (3) work that is not within the scope of the originally awarded contract; or (4) adding or deleting of a major contract item.
10-60	**Surety**	The corporation, partnership, or individual, other than the Contractor, executing payment or performance bonds that are furnished to the Owner by the Contractor.
10-61	**Taxilane**	A taxiway designed for low speed movement of aircraft between aircraft parking areas and terminal areas.
10-62	**Taxiway**	The portion of the air operations area of an airport that has been designated by competent airport authority for

Paragraph Number	Term	Definition
		movement of aircraft to and from the airport's runways, aircraft parking areas, and terminal areas.
10-63	**Taxiway/Taxilane Safety Area (TSA)**	A defined surface alongside the taxiway prepared or suitable for reducing the risk of damage to an aircraft. See the construction safety and phasing plan (CSPP) for limits of the TSA.
10-64	**Work**	The furnishing of all labor, materials, tools, equipment, and incidentals necessary or convenient to the Contractor's performance of all duties and obligations imposed by the contract, plans, and specifications.
10-65	**Working day**	A working day shall be any day other than a legal holiday, Saturday, or Sunday on which the normal working forces of the Contractor may proceed with regular work for at least six (6) hours toward completion of the contract. When work is suspended for causes beyond the Contractor's control, it will not be counted as a working day. Saturdays, Sundays and holidays on which the Contractor's forces engage in regular work will be considered as working days.
10-66	**Owner Defined terms**	None

END OF SECTION 10

Section 20 Proposal Requirements and Conditions

20-01 Advertisement (Notice to Bidders). Refer to the Notice to Bidders located elsewhere in this contract book.

20-02 Qualification of bidders. Each bidder shall submit evidence of competency and evidence of financial responsibility to perform the work to the Owner at the time of bid opening.

Evidence of competency, unless otherwise specified, shall consist of statements covering the bidder's past experience on similar work, and a list of equipment and a list of key personnel that would be available for the work.

Each bidder shall furnish the Owner satisfactory evidence of their financial responsibility. Evidence of financial responsibility, unless otherwise specified, shall consist of a confidential statement or report of the bidder's financial resources and liabilities as of the last calendar year or the bidder's last fiscal year. Such statements or reports shall be certified by a public accountant. At the time of submitting such financial statements or reports, the bidder shall further certify whether their financial responsibility is approximately the same as stated or reported by the public accountant. If the bidder's financial responsibility has changed, the bidder shall qualify the public accountant's statement or report to reflect the bidder's true financial condition at the time such qualified statement or report is submitted to the Owner.

Unless otherwise specified, a bidder may submit evidence that they are prequalified with the State Highway Division and are on the current "bidder's list" of the state in which the proposed work is located. Evidence of State Highway Division prequalification may be submitted as evidence of financial responsibility in lieu of the certified statements or reports specified above.

20-03 Contents of proposal forms. The Owner's proposal forms state the location and description of the proposed construction; the place, date, and time of opening of the proposals; and the estimated quantities of the various items of work to be performed and materials to be furnished for which unit bid prices are asked. The proposal form states the time in which the work must be completed, and the amount of the proposal guaranty that must accompany the proposal. The Owner will accept only those Proposals properly executed on physical forms or electronic forms provided by the Owner. Bidder actions that may cause the Owner to deem a proposal irregular are given in paragraph 20-09 *Irregular proposals*. Mobilization is limited to 10 percent of the total project cost.

20-04 Issuance of proposal forms. The Owner reserves the right to refuse to issue a proposal form to a prospective bidder if the bidder is in default for any of the following reasons:

a. Failure to comply with any prequalification regulations of the Owner, if such regulations are cited, or otherwise included, in the proposal as a requirement for bidding.

b. Failure to pay, or satisfactorily settle, all bills due for labor and materials on former contracts in force with the Owner at the time the Owner issues the proposal to a prospective bidder.

c. Documented record of Contractor default under previous contracts with the Owner.

d. Documented record of unsatisfactory work on previous contracts with the Owner.

20-05 Interpretation of estimated proposal quantities. An estimate of quantities of work to be done and materials to be furnished under these specifications is given in the proposal. It is the result of careful calculations and is believed to be correct. It is given only as a basis for comparison of proposals and the award of the contract. The Owner does not expressly, or by implication, agree that the actual quantities involved will correspond exactly therewith; nor shall the bidder plead misunderstanding or deception because of such estimates of quantities, or of the character, location, or other conditions pertaining to the work. Payment to the Contractor will be made only for the actual quantities of work performed or

materials furnished in accordance with the plans and specifications. It is understood that the quantities may be increased or decreased as provided in the Section 40, paragraph 40-02, Alteration of Work and Quantities, without in any way invalidating the unit bid prices.

20-06 Examination of plans, specifications, and site. The bidder is expected to carefully examine the site of the proposed work, the proposal, plans, specifications, and contract forms. Bidders shall satisfy themselves to the character, quality, and quantities of work to be performed, materials to be furnished, and to the requirements of the proposed contract. The submission of a proposal shall be prima facie evidence that the bidder has made such examination and is satisfied to the conditions to be encountered in performing the work and the requirements of the proposed contract, plans, and specifications.

Boring logs and other records of subsurface investigations and tests are available for inspection of bidders. It is understood and agreed that such subsurface information, whether included in the plans, specifications, or otherwise made available to the bidder, was obtained and is intended for the Owner's design and estimating purposes only. Such information has been made available for the convenience of all bidders. It is further understood and agreed that each bidder is solely responsible for all assumptions, deductions, or conclusions which the bidder may make or obtain from their own examination of the boring logs and other records of subsurface investigations and tests that are furnished by the Owner.

20-07 Preparation of proposal. The bidder shall submit their proposal on the forms furnished by the Owner. All blank spaces in the proposal forms, unless explicitly stated otherwise, must be correctly filled in where indicated for each and every item for which a quantity is given. The bidder shall state the price (written in ink or typed) both in words and numerals which they propose for each pay item furnished in the proposal. In case of conflict between words and numerals, the words, unless obviously incorrect, shall govern.

The bidder shall correctly sign the proposal in ink. If the proposal is made by an individual, their name and post office address must be shown. If made by a partnership, the name and post office address of each member of the partnership must be shown. If made by a corporation, the person signing the proposal shall give the name of the state where the corporation was chartered and the name, titles, and business address of the president, secretary, and the treasurer. Anyone signing a proposal as an agent shall file evidence of their authority to do so and that the signature is binding upon the firm or corporation.

20-08 Responsive and responsible bidder. A responsive bid conforms to all significant terms and conditions contained in the Owner's invitation for bid. It is the Owner's responsibility to decide if the exceptions taken by a bidder to the solicitation are material or not and the extent of deviation it is willing to accept.

A responsible bidder has the ability to perform successfully under the terms and conditions of a proposed procurement, as defined in 2 CFR § 200.318(h). This includes such matters as Contractor integrity, compliance with public policy, record of past performance, and financial and technical resources.

20-09 Irregular proposals. Proposals shall be considered irregular for the following reasons:

a. If the proposal is on a form other than that furnished by the Owner, or if the Owner's form is altered, or if any part of the proposal form is detached.

b. If there are unauthorized additions, conditional or alternate pay items, or irregularities of any kind that make the proposal incomplete, indefinite, or otherwise ambiguous.

c. If the proposal does not contain a unit price for each pay item listed in the proposal, except in the case of authorized alternate pay items, for which the bidder is not required to furnish a unit price.

d. If the proposal contains unit prices that are obviously unbalanced.

e. If the proposal is not accompanied by the proposal guaranty specified by the Owner.

f. If the applicable Disadvantaged Business Enterprise information is incomplete.

The Owner reserves the right to reject any irregular proposal and the right to waive technicalities if such waiver is in the best interest of the Owner and conforms to local laws and ordinances pertaining to the letting of construction contracts.

20-10 Bid guarantee. Each separate proposal shall be accompanied by a bid bond, certified check, or other specified acceptable collateral, in the amount specified in the proposal form. Such bond, check, or collateral, shall be made payable to the Owner.

20-11 Delivery of proposal. Each proposal submitted shall be placed in a sealed envelope plainly marked with the project number, location of airport, and name and business address of the bidder on the outside. When sent by mail, preferably registered, the sealed proposal, marked as indicated above, should be enclosed in an additional envelope. No proposal will be considered unless received at the place specified in the advertisement or as modified by Addendum before the time specified for opening all bids. Proposals received after the bid opening time shall be returned to the bidder unopened.

20-12 Withdrawal or revision of proposals. A bidder may withdraw or revise (by withdrawal of one proposal and submission of another) a proposal provided that the bidder's request for withdrawal is received by the Owner in writing or by email before the time specified for opening bids. Revised proposals must be received at the place specified in the advertisement before the time specified for opening all bids.

20-13 Public opening of proposals. Due to the Coronavirus, there will be no public bid opening.

20-14 Disqualification of bidders. A bidder shall be considered disqualified for any of the following reasons:

a. Submitting more than one proposal from the same partnership, firm, or corporation under the same or different name.

b. Evidence of collusion among bidders. Bidders participating in such collusion shall be disqualified as bidders for any future work of the Owner until any such participating bidder has been reinstated by the Owner as a qualified bidder.

c. If the bidder is considered to be in "default" for any reason specified in paragraph 20-04, *Issuance of Proposal Forms,* of this section.

20-15 Discrepancies and Omissions. A Bidder who discovers discrepancies or omissions with the project bid documents shall immediately notify the Owner's Engineer of the matter. A bidder that has doubt as to the true meaning of a project requirement may submit to the Owner's Engineer a written request for interpretation no later than four (4) days prior to the day of the bid opening.

Any interpretation of the project bid documents by the Owner's Engineer will be by written addendum issued by the Owner. The Owner will not consider any instructions, clarifications or interpretations of the bidding documents in any manner other than written addendum.

END OF SECTION 20

Section 30 Award and Execution of Contract

30-01 Consideration of proposals. Proposals will be compared on the basis of the summation of the products obtained by multiplying the estimated quantities shown in the proposal by the unit bid prices. If a bidder's proposal contains a discrepancy between unit bid prices written in words and unit bid prices written in numbers, the unit bid price written in words shall govern.

Until the award of a contract is made, the Owner reserves the right to reject a bidder's proposal for any of the following reasons:

a. If the proposal is irregular as specified in Section 20, paragraph 20-09, *Irregular Proposals*.

b. If the bidder is disqualified for any of the reasons specified Section 20, paragraph 20-14, *Disqualification of Bidders*.

In addition, until the award of a contract is made, the Owner reserves the right to reject any or all proposals, waive technicalities, if such waiver is in the best interest of the Owner and is in conformance with applicable state and local laws or regulations pertaining to the letting of construction contracts; advertise for new proposals; or proceed with the work otherwise. All such actions shall promote the Owner's best interests.

30-02 Award of contract. The award of a contract, if it is to be awarded, shall be made within **120 calendar days** of the bid date, unless otherwise specified herein.

If the Owner elects to proceed with an award of contract, the Owner will make award to the responsible bidder whose bid, conforming with all the material terms and conditions of the bid documents, is the lowest in price.

30-03 Cancellation of award. The Owner reserves the right to cancel the award without liability to the bidder, except return of proposal guaranty, at any time before a contract has been fully executed by all parties and is approved by the Owner in accordance with paragraph 30-07 *Approval of Contract*.

30-04 Return of proposal guaranty. All proposal guaranties, except those of the two lowest bidders, will be returned immediately after the Owner has made a comparison of bids as specified in the paragraph 30-01, *Consideration of Proposals.* Proposal guaranties of the two lowest bidders will be retained by the Owner until such time as an award is made, at which time, the unsuccessful bidder's proposal guaranty will be returned. The successful bidder's proposal guaranty will be returned as soon as the Owner receives the contract bonds as specified in paragraph 30-05, *Requirements of Contract Bonds.*

30-05 Requirements of contract bonds. At the time of the execution of the contract, the successful bidder shall furnish the Owner a surety bond or bonds that have been fully executed by the bidder and the surety guaranteeing the performance of the work and the payment of all legal debts that may be incurred by reason of the Contractor's performance of the work. The surety and the form of the bond or bonds shall be acceptable to the Owner. Unless otherwise specified in this subsection, the surety bond or bonds shall be in a sum equal to the full amount of the contract.

30-06 Execution of contract. The successful bidder shall sign (execute) the necessary agreements for entering into the contract and return the signed contract to the Owner, along with the fully executed surety bond or bonds specified in paragraph 30-05, *Requirements of Contract Bonds,* of this section, within 15 calendar days from the date mailed or otherwise delivered to the successful bidder.

30-07 Approval of contract. Upon receipt of the contract and contract bond or bonds that have been executed by the successful bidder, the Owner shall complete the execution of the contract in accordance with local laws or ordinances, and return the fully executed contract to the Contractor. Delivery of the fully executed contract to the Contractor shall constitute the Owner's approval to be bound by the successful bidder's proposal and the terms of the contract.

30-08 Failure to execute contract. Failure of the successful bidder to execute the contract and furnish an acceptable surety bond or bonds within the period specified in paragraph 30-06, *Execution of Contract,* of this section shall be just cause for cancellation of the award and forfeiture of the proposal guaranty, not as a penalty, but as liquidated damages to the Owner.

END OF SECTION 30

Section 40 Scope of Work

40-01 Intent of contract. The intent of the contract is to provide for construction and completion, in every detail, of the work described. It is further intended that the Contractor shall furnish all labor, materials, equipment, tools, transportation, and supplies required to complete the work in accordance with the plans, specifications, and terms of the contract.

40-02 Alteration of work and quantities. The Owner reserves the right to make such changes in quantities and work as may be necessary or desirable to complete, in a satisfactory manner, the original intended work. Unless otherwise specified in the Contract, the Owner's Engineer or RPR shall be and is hereby authorized to make, in writing, such in-scope alterations in the work and variation of quantities as may be necessary to complete the work, provided such action does not represent a significant change in the character of the work.

For purpose of this section, a significant change in character of work means: any change that is outside the current contract scope of work; any change (increase or decrease) in the total contract cost by more than 25%; or any change in the total cost of a major contract item by more than 25%.

Work alterations and quantity variances that do not meet the definition of significant change in character of work shall not invalidate the contract nor release the surety. Contractor agrees to accept payment for such work alterations and quantity variances in accordance with Section 90, paragraph 90-03, *Compensation for Altered Quantities*.

Should the value of altered work or quantity variance meet the criteria for significant change in character of work, such altered work and quantity variance shall be covered by a supplemental agreement. Supplemental agreements shall also require consent of the Contractor's surety and separate performance and payment bonds. If the Owner and the Contractor are unable to agree on a unit adjustment for any contract item that requires a supplemental agreement, the Owner reserves the right to terminate the contract with respect to the item and make other arrangements for its completion.

40-03 Omitted items. The Owner, the Owner's Engineer or the RPR may provide written notice to the Contractor to omit from the work any contract item that does not meet the definition of major contract item. Major contract items may be omitted by a supplemental agreement. Such omission of contract items shall not invalidate any other contract provision or requirement.

Should a contract item be omitted or otherwise ordered to be non-performed, the Contractor shall be paid for all work performed toward completion of such item prior to the date of the order to omit such item. Payment for work performed shall be in accordance with Section 90, paragraph 90-04, *Payment for Omitted Items*.

40-04 Extra work. Should acceptable completion of the contract require the Contractor to perform an item of work not provided for in the awarded contract as previously modified by change order or supplemental agreement, Owner may issue a Change Order to cover the necessary extra work. Change orders for extra work shall contain agreed unit prices for performing the change order work in accordance with the requirements specified in the order, and shall contain any adjustment to the contract time that, in the RPR's opinion, is necessary for completion of the extra work.

When determined by the RPR to be in the Owner's best interest, the RPR may order the Contractor to proceed with extra work as provided in Section 90, paragraph 90-05, *Payment for Extra Work*. Extra work that is necessary for acceptable completion of the project, but is not within the general scope of the work covered by the original contract shall be covered by a supplemental agreement as defined in Section 10, paragraph 10-59, *Supplemental Agreement*.

If extra work is essential to maintaining the project critical path, RPR may order the Contractor to commence the extra work under a Time and Material contract method. Once sufficient detail is available

to establish the level of effort necessary for the extra work, the Owner shall initiate a change order or supplemental agreement to cover the extra work.

Any claim for payment of extra work that is not covered by written agreement (change order or supplemental agreement) shall be rejected by the Owner.

40-05 Maintenance of traffic. It is the explicit intention of the contract that the safety of aircraft, as well as the Contractor's equipment and personnel, is the most important consideration. The Contractor shall maintain traffic in the manner detailed in the Construction Safety and Phasing Plan (CSPP).

a. It is understood and agreed that the Contractor shall provide for the free and unobstructed movement of aircraft in the air operations areas (AOAs) of the airport with respect to their own operations and the operations of all subcontractors as specified in Section 80, paragraph 80-04, *Limitation of Operations*. It is further understood and agreed that the Contractor shall provide for the uninterrupted operation of visual and electronic signals (including power supplies thereto) used in the guidance of aircraft while operating to, from, and upon the airport as specified in Section 70, paragraph 70-15, *Contractor's Responsibility for Utility Service and Facilities of Others*.

b. With respect to their own operations and the operations of all subcontractors, the Contractor shall provide marking, lighting, and other acceptable means of identifying personnel, equipment, vehicles, storage areas, and any work area or condition that may be hazardous to the operation of aircraft, fire-rescue equipment, or maintenance vehicles at the airport in accordance with the construction safety and phasing plan (CSPP) and the safety plan compliance document (SPCD).

c. When the contract requires the maintenance of an existing road, street, or highway during the Contractor's performance of work that is otherwise provided for in the contract, plans, and specifications, the Contractor shall keep the road, street, or highway open to all traffic and shall provide maintenance as may be required to accommodate traffic. The Contractor, at their expense, shall be responsible for the repair to equal or better than preconstruction conditions of any damage caused by the Contractor's equipment and personnel. The Contractor shall furnish, erect, and maintain barricades, warning signs, flag person, and other traffic control devices in reasonable conformity with the Manual on Uniform Traffic Control Devices (MUTCD) (http://mutcd.fhwa.dot.gov/), unless otherwise specified. The Contractor shall also construct and maintain in a safe condition any temporary connections necessary for ingress to and egress from abutting property or intersecting roads, streets or highways.

40-06 Removal of existing structures. All existing structures encountered within the established lines, grades, or grading sections shall be removed by the Contractor, unless such existing structures are otherwise specified to be relocated, adjusted up or down, salvaged, abandoned in place, reused in the work or to remain in place. The cost of removing such existing structures shall not be measured or paid for directly, but shall be included in the various contract items.

Should the Contractor encounter an existing structure (above or below ground) in the work for which the disposition is not indicated on the plans, the Resident Project Representative (RPR) shall be notified prior to disturbing such structure. The disposition of existing structures so encountered shall be immediately determined by the RPR in accordance with the provisions of the contract.

Except as provided in Section 40, paragraph 40-07, *Rights in and Use of Materials Found in the Work*, it is intended that all existing materials or structures that may be encountered (within the lines, grades, or grading sections established for completion of the work) shall be used in the work as otherwise provided for in the contract and shall remain the property of the Owner when so used in the work.

40-07 Rights in and use of materials found in the work. Should the Contractor encounter any material such as (but not restricted to) sand, stone, gravel, slag, or concrete slabs within the established lines, grades, or grading sections, the use of which is intended by the terms of the contract to be embankment, the Contractor may at their own option either:

a. Use such material in another contract item, providing such use is approved by the RPR and is in conformance with the contract specifications applicable to such use; or,

b. Remove such material from the site, upon written approval of the RPR; or

c. Use such material for the Contractor's own temporary construction on site; or,

d. Use such material as intended by the terms of the contract.

Should the Contractor wish to exercise option a., b., or c., the Contractor shall request the RPR's approval in advance of such use.

Should the RPR approve the Contractor's request to exercise option a., b., or c., the Contractor shall be paid for the excavation or removal of such material at the applicable contract price. The Contractor shall replace, at their expense, such removed or excavated material with an agreed equal volume of material that is acceptable for use in constructing embankment, backfills, or otherwise to the extent that such replacement material is needed to complete the contract work. The Contractor shall not be charged for use of such material used in the work or removed from the site.

Should the RPR approve the Contractor's exercise of option a., the Contractor shall be paid, at the applicable contract price, for furnishing and installing such material in accordance with requirements of the contract item in which the material is used.

It is understood and agreed that the Contractor shall make no claim for delays by reason of their own exercise of option a., b., or c.

The Contractor shall not excavate, remove, or otherwise disturb any material, structure, or part of a structure which is located outside the lines, grades, or grading sections established for the work, except where such excavation or removal is provided for in the contract, plans, or specifications.

40-08 Final cleanup. Upon completion of the work and before acceptance and final payment will be made, the Contractor shall remove from the site all machinery, equipment, surplus and discarded materials, rubbish, temporary structures, and stumps or portions of trees. The Contractor shall cut all brush and woods within the limits indicated and shall leave the site in a neat and presentable condition. Material cleared from the site and deposited on adjacent property will not be considered as having been disposed of satisfactorily, unless the Contractor has obtained the written permission of the property Owner.

END OF SECTION 40

Section 50 Control of Work

50-01 Authority of the Resident Project Representative (RPR). The RPR has final authority regarding the interpretation of project specification requirements. The RPR shall determine acceptability of the quality of materials furnished, method of performance of work performed, and the manner and rate of performance of the work. The RPR does not have the authority to accept work that does not conform to specification requirements.

50-02 Conformity with plans and specifications. All work and all materials furnished shall be in reasonably close conformity with the lines, grades, grading sections, cross-sections, dimensions, material requirements, and testing requirements that are specified (including specified tolerances) in the contract, plans, or specifications.

If the RPR finds the materials furnished, work performed, or the finished product not within reasonably close conformity with the plans and specifications, but that the portion of the work affected will, in their opinion, result in a finished product having a level of safety, economy, durability, and workmanship acceptable to the Owner, the RPR will advise the Owner of their determination that the affected work be accepted and remain in place. The RPR will document the determination and recommend to the Owner a basis of acceptance that will provide for an adjustment in the contract price for the affected portion of the work. Changes in the contract price must be covered by contract change order or supplemental agreement as applicable.

If the RPR finds the materials furnished, work performed, or the finished product are not in reasonably close conformity with the plans and specifications and have resulted in an unacceptable finished product, the affected work or materials shall be removed and replaced or otherwise corrected by and at the expense of the Contractor in accordance with the RPR's written orders.

The term "reasonably close conformity" shall not be construed as waiving the Contractor's responsibility to complete the work in accordance with the contract, plans, and specifications. The term shall not be construed as waiving the RPR's responsibility to insist on strict compliance with the requirements of the contract, plans, and specifications during the Contractor's execution of the work, when, in the RPR's opinion, such compliance is essential to provide an acceptable finished portion of the work.

The term "reasonably close conformity" is also intended to provide the RPR with the authority, after consultation with the Sponsor and FAA, to use sound engineering judgment in their determinations to accept work that is not in strict conformity, but will provide a finished product equal to or better than that required by the requirements of the contract, plans and specifications.

The RPR will not be responsible for the Contractor's means, methods, techniques, sequences, or procedures of construction or the safety precautions incident thereto.

50-03 Coordination of contract, plans, and specifications. The contract, plans, specifications, and all referenced standards cited are essential parts of the contract requirements. If electronic files are provided and used on the project and there is a conflict between the electronic files and hard copy plans, the hard copy plans shall govern. A requirement occurring in one is as binding as though occurring in all. They are intended to be complementary and to describe and provide for a complete work. In case of discrepancy, calculated dimensions will govern over scaled dimensions; contract technical specifications shall govern over contract general provisions, plans, cited standards for materials or testing, and cited advisory circulars (ACs); contract general provisions shall govern over plans, cited standards for materials or testing, and cited ACs; plans shall govern over cited standards for materials or testing and cited ACs. If any paragraphs contained in the Special Provisions conflict with General Provisions or Technical Specifications, the Special Provisions shall govern.

From time to time, discrepancies within cited testing standards occur due to the timing of the change, edits, and/or replacement of the standards. If the Contractor discovers any apparent discrepancy within

standard test methods, the Contractor shall immediately ask the RPR for an interpretation and decision, and such decision shall be final.

The Contractor shall not take advantage of any apparent error or omission on the plans or specifications. In the event the Contractor discovers any apparent error or discrepancy, Contractor shall immediately notify the Owner or the designated representative in writing requesting their written interpretation and decision.

50-04 List of Special Provisions. (not used)

50-05 Cooperation of Contractor. The Contractor shall be supplied with five hard copies or an electronic PDF of the plans and specifications. The Contractor shall have available on the construction site at all times one hardcopy each of the plans and specifications. Additional hard copies of plans and specifications may be obtained by the Contractor for the cost of reproduction.

The Contractor shall give constant attention to the work to facilitate the progress thereof, and shall cooperate with the RPR and their inspectors and with other Contractors in every way possible. The Contractor shall have a competent superintendent on the work at all times who is fully authorized as their agent on the work. The superintendent shall be capable of reading and thoroughly understanding the plans and specifications and shall receive and fulfill instructions from the RPR or their authorized representative.

50-06 Cooperation between Contractors. The Owner reserves the right to contract for and perform other or additional work on or near the work covered by this contract.

When separate contracts are let within the limits of any one project, each Contractor shall conduct the work not to interfere with or hinder the progress of completion of the work being performed by other Contractors. Contractors working on the same project shall cooperate with each other as directed.

Each Contractor involved shall assume all liability, financial or otherwise, in connection with their own contract and shall protect and hold harmless the Owner from any and all damages or claims that may arise because of inconvenience, delays, or loss experienced because of the presence and operations of other Contractors working within the limits of the same project.

The Contractor shall arrange their work and shall place and dispose of the materials being used to not interfere with the operations of the other Contractors within the limits of the same project. The Contractor shall join their work with that of the others in an acceptable manner and shall perform it in proper sequence to that of the others.

50-07 Construction layout and stakes. The Engineer/RPR shall establish necessary horizontal and vertical control. The establishment of Survey Control and/or reestablishment of survey control shall be by a State Licensed Land Surveyor. Contractor is responsible for preserving integrity of horizontal and vertical controls established by Engineer/RPR. In case of negligence on the part of the Contractor or their employees, resulting in the destruction of any horizontal and vertical control, the resulting costs will be deducted as a liquidated damage against the Contractor.

Prior to the start of construction, the Contractor will check all control points for horizontal and vertical accuracy and certify in writing to the RPR that the Contractor concurs with survey control established for the project. All lines, grades and measurements from control points necessary for the proper execution and control of the work on this project will be provided to the RPR. The Contractor is responsible to establish all layout required for the construction of the project.

Copies of survey notes will be provided to the RPR for each area of construction and for each placement of material as specified to allow the RPR to make periodic checks for conformance with plan grades, alignments and grade tolerances required by the applicable material specifications. Surveys will be

provided to the RPR prior to commencing work items that cover or disturb the survey staking. Survey(s) and notes shall be provided in the following format(s): .dwg, .pdf, .xlx

Laser, GPS, String line, or other automatic control shall be checked with temporary control as necessary. In the case of error, on the part of the Contractor, their surveyor, employees or subcontractors, resulting in established grades, alignment or grade tolerances that do not concur with those specified or shown on the plans, the Contractor is solely responsible for correction, removal, replacement and all associated costs at no additional cost to the Owner.

No direct payment will be made, unless otherwise specified in contract documents, for this labor, materials, or other expenses. The cost shall be included in the price of the bid for the various items of the Contract.

50-08 Authority and duties of Quality Assurance (QA) inspectors. QA inspectors shall be authorized to inspect all work done and all material furnished. Such QA inspection may extend to all or any part of the work and to the preparation, fabrication, or manufacture of the materials to be used. QA inspectors are not authorized to revoke, alter, or waive any provision of the contract. QA inspectors are not authorized to issue instructions contrary to the plans and specifications or to act as foreman for the Contractor.

QA Inspectors are authorized to notify the Contractor or their representatives of any failure of the work or materials to conform to the requirements of the contract, plans, or specifications and to reject such nonconforming materials in question until such issues can be referred to the RPR for a decision.

50-09 Inspection of the work. All materials and each part or detail of the work shall be subject to inspection. The RPR shall be allowed access to all parts of the work and shall be furnished with such information and assistance by the Contractor as is required to make a complete and detailed inspection.

If the RPR requests it, the Contractor, at any time before acceptance of the work, shall remove or uncover such portions of the finished work as may be directed. After examination, the Contractor shall restore said portions of the work to the standard required by the specifications. Should the work thus exposed or examined prove acceptable, the uncovering, or removing, and the replacing of the covering or making good of the parts removed will be paid for as extra work; but should the work so exposed or examined prove unacceptable, the uncovering, or removing, and the replacing of the covering or making good of the parts removed will be at the Contractor's expense.

Provide advance written notice to the RPR of work the Contractor plans to perform each week and each day. Any work done or materials used without written notice and allowing opportunity for inspection by the RPR may be ordered removed and replaced at the Contractor's expense.

Should the contract work include relocation, adjustment, or any other modification to existing facilities, not the property of the (contract) Owner, authorized representatives of the Owners of such facilities shall have the right to inspect such work. Such inspection shall in no sense make any facility owner a party to the contract, and shall in no way interfere with the rights of the parties to this contract.

50-10 Removal of unacceptable and unauthorized work. All work that does not conform to the requirements of the contract, plans, and specifications will be considered unacceptable, unless otherwise determined acceptable by the RPR as provided in paragraph 50-02, *Conformity with Plans and Specifications*.

Unacceptable work, whether the result of poor workmanship, use of defective materials, damage through carelessness, or any other cause found to exist prior to the final acceptance of the work, shall be removed immediately and replaced in an acceptable manner in accordance with the provisions of Section 70, paragraph 70-14, *Contractor's Responsibility for Work*.

No removal work made under provision of this paragraph shall be done without lines and grades having been established by the RPR. Work done contrary to the instructions of the RPR, work done beyond the

lines shown on the plans or as established by the RPR, except as herein specified, or any extra work done without authority, will be considered as unauthorized and will not be paid for under the provisions of the contract. Work so done may be ordered removed or replaced at the Contractor's expense.

Upon failure on the part of the Contractor to comply with any order of the RPR made under the provisions of this subsection, the RPR will have authority to cause unacceptable work to be remedied or removed and replaced; and unauthorized work to be removed and recover the resulting costs as a liquidated damage against the Contractor.

50-11 Load restrictions. The Contractor shall comply with all legal load restrictions in the hauling of materials on public roads beyond the limits of the work. A special permit will not relieve the Contractor of liability for damage that may result from the moving of material or equipment.

The operation of equipment of such weight or so loaded as to cause damage to structures or to any other type of construction will not be permitted. Hauling of materials over the base course or surface course under construction shall be limited as directed. No loads will be permitted on a concrete pavement, base, or structure before the expiration of the curing period. The Contractor, at their own expense, shall be responsible for the repair to equal or better than preconstruction conditions of any damage caused by the Contractor's equipment and personnel.

50-12 Maintenance during construction. The Contractor shall maintain the work during construction and until the work is accepted. Maintenance shall constitute continuous and effective work prosecuted day by day, with adequate equipment and forces so that the work is maintained in satisfactory condition at all times.

In the case of a contract for the placing of a course upon a course or subgrade previously constructed, the Contractor shall maintain the previous course or subgrade during all construction operations.

All costs of maintenance work during construction and before the project is accepted shall be included in the unit prices bid on the various contract items, and the Contractor will not be paid an additional amount for such work.

50-13 Failure to maintain the work. Should the Contractor at any time fail to maintain the work as provided in paragraph 50-12, *Maintenance during Construction*, the RPR shall immediately notify the Contractor of such noncompliance. Such notification shall specify a reasonable time within which the Contractor shall be required to remedy such unsatisfactory maintenance condition. The time specified will give due consideration to the exigency that exists.

Should the Contractor fail to respond to the RPR's notification, the Owner may suspend any work necessary for the Owner to correct such unsatisfactory maintenance condition, depending on the exigency that exists. Any maintenance cost incurred by the Owner, shall be recovered as a liquidated damage against the Contractor.

50-14 Partial acceptance. If at any time during the execution of the project the Contractor substantially completes a usable unit or portion of the work, the occupancy of which will benefit the Owner, the Contractor may request the RPR to make final inspection of that unit. If the RPR finds upon inspection that the unit has been satisfactorily completed in compliance with the contract, the RPR may accept it as being complete, and the Contractor may be relieved of further responsibility for that unit. Such partial acceptance and beneficial occupancy by the Owner shall not void or alter any provision of the contract.

50-15 Final acceptance. Upon due notice from the Contractor of presumptive completion of the entire project, the RPR and Owner will make an inspection. If all construction provided for and contemplated by the contract is found to be complete in accordance with the contract, plans, and specifications, such inspection shall constitute the final inspection. The RPR shall notify the Contractor in writing of final acceptance as of the date of the final inspection.

If, however, the inspection discloses any work, in whole or in part, as being unsatisfactory, the RPR will notify the Contractor and the Contractor shall correct the unsatisfactory work. Upon correction of the work, another inspection will be made which shall constitute the final inspection, provided the work has been satisfactorily completed. In such event, the RPR will make the final acceptance and notify the Contractor in writing of this acceptance as of the date of final inspection.

50-16 Claims for adjustment and disputes. If for any reason the Contractor deems that additional compensation is due for work or materials not clearly provided for in the contract, plans, or specifications or previously authorized as extra work, the Contractor shall notify the RPR in writing of their intention to claim such additional compensation before the Contractor begins the work on which the Contractor bases the claim. If such notification is not given or the RPR is not afforded proper opportunity by the Contractor for keeping strict account of actual cost as required, then the Contractor hereby agrees to waive any claim for such additional compensation. Such notice by the Contractor and the fact that the RPR has kept account of the cost of the work shall not in any way be construed as proving or substantiating the validity of the claim. When the work on which the claim for additional compensation is based has been completed, the Contractor shall, within 10 calendar days, submit a written claim to the RPR who will present it to the Owner for consideration in accordance with local laws or ordinances.

Nothing in this subsection shall be construed as a waiver of the Contractor's right to dispute final payment based on differences in measurements or computations.

END OF SECTION 50

Section 60 Control of Materials

60-01 Source of supply and quality requirements. The materials used in the work shall conform to the requirements of the contract, plans, and specifications. Unless otherwise specified, such materials that are manufactured or processed shall be new (as compared to used or reprocessed).

In order to expedite the inspection and testing of materials, the Contractor shall furnish documentation to the RPR as to the origin, composition, and manufacture of all materials to be used in the work. Documentation shall be furnished promptly after execution of the contract but, in all cases, prior to delivery of such materials.

At the RPR's option, materials may be approved at the source of supply before delivery. If it is found after trial that sources of supply for previously approved materials do not produce specified products, the Contractor shall furnish materials from other sources.

The Contractor shall furnish airport lighting equipment that meets the requirements of the specifications; and is listed in AC 150/5345-53, *Airport Lighting Equipment Certification Program* and *Addendum*, that is in effect on the date of advertisement.

60-02 Samples, tests, and cited specifications. All materials used in the work shall be inspected, tested, and approved by the RPR before incorporation in the work unless otherwise designated. Any work in which untested materials are used without approval or written permission of the RPR shall be performed at the Contractor's risk. Materials found to be unacceptable and unauthorized will not be paid for and, if directed by the RPR, shall be removed at the Contractor's expense.

Unless otherwise designated, quality assurance tests will be made by and at the expense of the Owner in accordance with the cited standard methods of ASTM, American Association of State Highway and Transportation Officials (AASHTO), federal specifications, Commercial Item Descriptions, and all other cited methods, which are current on the date of advertisement for bids.

The testing organizations performing on-site quality assurance field tests shall have copies of all referenced standards on the construction site for use by all technicians and other personnel. Unless otherwise designated, samples for quality assurance will be taken by a qualified representative of the RPR. All materials being used are subject to inspection, test, or rejection at any time prior to or during incorporation into the work. Copies of all tests will be furnished to the Contractor's representative at their request after review and approval of the RPR.

A copy of all Contractor QC test data shall be provided to the RPR daily, along with printed reports, in an approved format, on a weekly basis. After completion of the project, and prior to final payment, the Contractor shall submit a final report to the RPR showing all test data reports, plus an analysis of all results showing ranges, averages, and corrective action taken on all failing tests.

The Contractor shall employ a Quality Control (QC) testing organization to perform all Contractor required QC tests in accordance with Item C-100 Contractor Quality Control Program (CQCP).

60-03 Certification of compliance/analysis (COC/COA). The RPR may permit the use, prior to sampling and testing, of certain materials or assemblies when accompanied by manufacturer's COC stating that such materials or assemblies fully comply with the requirements of the contract. The certificate shall be signed by the manufacturer. Each lot of such materials or assemblies delivered to the work must be accompanied by a certificate of compliance in which the lot is clearly identified. The COA is the manufacturer's COC and includes all applicable test results.

Materials or assemblies used on the basis of certificates of compliance may be sampled and tested at any time and if found not to be in conformity with contract requirements will be subject to rejection whether in place or not.

The form and distribution of certificates of compliance shall be as approved by the RPR.

When a material or assembly is specified by "brand name or equal" and the Contractor elects to furnish the specified "or equal," the Contractor shall be required to furnish the manufacturer's certificate of compliance for each lot of such material or assembly delivered to the work. Such certificate of compliance shall clearly identify each lot delivered and shall certify as to:

a. Conformance to the specified performance, testing, quality or dimensional requirements; and,

b. Suitability of the material or assembly for the use intended in the contract work.

The RPR shall be the sole judge as to whether the proposed "or equal" is suitable for use in the work.

The RPR reserves the right to refuse permission for use of materials or assemblies on the basis of certificates of compliance.

60-04 Plant inspection. The RPR or their authorized representative may inspect, at its source, any specified material or assembly to be used in the work. Manufacturing plants may be inspected from time to time for the purpose of determining compliance with specified manufacturing methods or materials to be used in the work and to obtain samples required for acceptance of the material or assembly.

Should the RPR conduct plant inspections, the following conditions shall exist:

a. The RPR shall have the cooperation and assistance of the Contractor and the producer with whom the Contractor has contracted for materials.

b. The RPR shall have full entry at all reasonable times to such parts of the plant that concern the manufacture or production of the materials being furnished.

c. If required by the RPR, the Contractor shall arrange for adequate office or working space that may be reasonably needed for conducting plant inspections. Place office or working space in a convenient location with respect to the plant.

It is understood and agreed that the Owner shall have the right to retest any material that has been tested and approved at the source of supply after it has been delivered to the site. The RPR shall have the right to reject only material which, when retested, does not meet the requirements of the contract, plans, or specifications.

60-05 Engineer/ Resident Project Representative (RPR) field office. The Contractor shall provide dedicated space for the use of the engineer, RPR, and inspectors, as a field office for the duration of the project. This space shall be located conveniently near the construction and shall be separate from any space used by the Contractor. The Contractor shall furnish water, sanitary facilities, heat, air conditioning, Wireless internet, and utility electricity (no portable generator). The Field Office shall comply with the requirements of Section 8 – Facilities for Agency Personnel, Greenbook Specification, Class "A", The designated space, furniture, and facilities shall be for use by the Owner's on-site representative.

A. It is the Contractors responsibility for establishing, maintaining, and paying for associated utility service (electricity and wireless internet) for the duration of the project.

B. Contractor-provided Field Office shall include conference table and chairs for up to 10 attendees at the periodic progress meetings.

C. Chemical toilet adjacent to field office is acceptable.

Contractor to provide weekly cleaning including solid waste disposal.

60-06 Storage of materials. Materials shall be stored to assure the preservation of their quality and fitness for the work. Stored materials, even though approved before storage, may again be inspected prior to their use in the work. Stored materials shall be located to facilitate their prompt inspection. The Contractor shall coordinate the storage of all materials with the RPR. Materials to be stored on airport property shall not create an obstruction to air navigation nor shall they interfere with the free and

unobstructed movement of aircraft. Unless otherwise shown on the plans and/or CSPP, the storage of materials and the location of the Contractor's plant and parked equipment or vehicles shall be as directed by the RPR. Private property shall not be used for storage purposes without written permission of the Owner or lessee of such property. The Contractor shall make all arrangements and bear all expenses for the storage of materials on private property. Upon request, the Contractor shall furnish the RPR a copy of the property Owner's permission.

All storage sites on private or airport property shall be restored to their original condition by the Contractor at their expense, except as otherwise agreed to (in writing) by the Owner or lessee of the property.

60-07 Unacceptable materials. Any material or assembly that does not conform to the requirements of the contract, plans, or specifications shall be considered unacceptable and shall be rejected. The Contractor shall remove any rejected material or assembly from the site of the work, unless otherwise instructed by the RPR.

Rejected material or assembly, the defects of which have been corrected by the Contractor, shall not be returned to the site of the work until such time as the RPR has approved its use in the work.

60-08 Owner furnished materials. The Contractor shall furnish all materials required to complete the work, except those specified, if any, to be furnished by the Owner. Owner-furnished materials shall be made available to the Contractor at the location specified.

All costs of handling, transportation from the specified location to the site of work, storage, and installing Owner-furnished materials shall be included in the unit price bid for the contract item in which such Owner-furnished material is used.

After any Owner-furnished material has been delivered to the location specified, the Contractor shall be responsible for any demurrage, damage, loss, or other deficiencies that may occur during the Contractor's handling, storage, or use of such Owner-furnished material. The Owner will deduct from any monies due or to become due the Contractor any cost incurred by the Owner in making good such loss due to the Contractor's handling, storage, or use of Owner-furnished materials.

END OF SECTION 60

Section 70 Legal Regulations and Responsibility to Public

70-01 Laws to be observed. The Contractor shall keep fully informed of all federal and state laws, all local laws, ordinances, and regulations and all orders and decrees of bodies or tribunals having any jurisdiction or authority, which in any manner affect those engaged or employed on the work, or which in any way affect the conduct of the work. The Contractor shall at all times observe and comply with all such laws, ordinances, regulations, orders, and decrees; and shall protect and indemnify the Owner and all their officers, agents, or servants against any claim or liability arising from or based on the violation of any such law, ordinance, regulation, order, or decree, whether by the Contractor or the Contractor's employees.

70-02 Permits, licenses, and taxes. The Contractor shall procure all permits and licenses, pay all charges, fees, and taxes, and give all notices necessary and incidental to the due and lawful execution of the work.

70-03 Patented devices, materials, and processes. If the Contractor is required or desires to use any design, device, material, or process covered by letters of patent or copyright, the Contractor shall provide for such use by suitable legal agreement with the Patentee or Owner. The Contractor and the surety shall indemnify and hold harmless the Owner, any third party, or political subdivision from any and all claims for infringement by reason of the use of any such patented design, device, material or process, or any trademark or copyright, and shall indemnify the Owner for any costs, expenses, and damages which it may be obliged to pay by reason of an infringement, at any time during the execution or after the completion of the work.

70-04 Restoration of surfaces disturbed by others. The Owner reserves the right to authorize the construction, reconstruction, or maintenance of any public or private utility service, FAA or National Oceanic and Atmospheric Administration (NOAA) facility, or a utility service of another government agency at any time during the progress of the work. To the extent that such construction, reconstruction, or maintenance has been coordinated with the Owner, such authorized work (by others) must be shown on the plans.

Except as listed above, the Contractor shall not permit any individual, firm, or corporation to excavate or otherwise disturb such utility services or facilities located within the limits of the work without the written permission of the RPR.

Should the Owner of public or private utility service, FAA, or NOAA facility, or a utility service of another government agency be authorized to construct, reconstruct, or maintain such utility service or facility during the progress of the work, the Contractor shall cooperate with such Owners by arranging and performing the work in this contract to facilitate such construction, reconstruction or maintenance by others whether or not such work by others is listed above. When ordered as extra work by the RPR, the Contractor shall make all necessary repairs to the work which are due to such authorized work by others, unless otherwise provided for in the contract, plans, or specifications. It is understood and agreed that the Contractor shall not be entitled to make any claim for damages due to such authorized work by others or for any delay to the work resulting from such authorized work.

70-05 Federal Participation. The United States Government has agreed to reimburse the Owner for some portion of the contract costs. The contract work is subject to the inspection and approval of duly authorized representatives of the FAA Administrator. No requirement of this contract shall be construed as making the United States a party to the contract nor will any such requirement interfere, in any way, with the rights of either party to the contract.

70-06 Sanitary, health, and safety provisions. The Contractor's worksite and facilities shall comply with applicable federal, state, and local requirements for health, safety and sanitary provisions.

70-07 Public convenience and safety. The Contractor shall control their operations and those of their subcontractors and all suppliers, to assure the least inconvenience to the traveling public. Under all circumstances, safety shall be the most important consideration.

The Contractor shall maintain the free and unobstructed movement of aircraft and vehicular traffic with respect to their own operations and those of their own subcontractors and all suppliers in accordance with Section 40, paragraph 40-05, *Maintenance of Traffic,* and shall limit such operations for the convenience and safety of the traveling public as specified in Section 80, paragraph 80-04, *Limitation of Operations*.

The Contractor shall remove or control debris and rubbish resulting from its work operations at frequent intervals, and upon the order of the RPR. If the RPR determines the existence of Contractor debris in the work site represents a hazard to airport operations and the Contractor is unable to respond in a prompt and reasonable manner, the RPR reserves the right to assign the task of debris removal to a third party and recover the resulting costs as a liquidated damage against the Contractor.

70-08 Construction Safety and Phasing Plan (CSPP). The Contractor shall complete the work in accordance with the approved Construction Safety and Phasing Plan (CSPP) developed in accordance with AC 150/5370-2, Operational Safety on Airports During Construction.

The CSPP is included in an appendix in this specification package.

70-09 Use of explosives. The use of explosives is not permitted on this project.

70-10 Protection and restoration of property and landscape. The Contractor shall be responsible for the preservation of all public and private property, and shall protect carefully from disturbance or damage all land monuments and property markers until the Engineer/RPR has witnessed or otherwise referenced their location and shall not move them until directed.

The Contractor shall be responsible for all damage or injury to property of any character, during the execution of the work, resulting from any act, omission, neglect, or misconduct in manner or method of executing the work, or at any time due to defective work or materials, and said responsibility shall not be released until the project has been completed and accepted.

When or where any direct or indirect damage or injury is done to public or private property by or on account of any act, omission, neglect, or misconduct in the execution of the work, or in consequence of the non-execution thereof by the Contractor, the Contractor shall restore, at their expense, such property to a condition similar or equal to that existing before such damage or injury was done, by repairing, or otherwise restoring as may be directed, or the Contractor shall make good such damage or injury in an acceptable manner.

70-11 Responsibility for damage claims. The Contractor shall indemnify and hold harmless the Engineer/RPR and the Owner and their officers, agents, and employees from all suits, actions, or claims, of any character, brought because of any injuries or damage received or sustained by any person, persons, or property on account of the operations of the Contractor; or on account of or in consequence of any neglect in safeguarding the work; or through use of unacceptable materials in constructing the work; or because of any act or omission, neglect, or misconduct of said Contractor; or because of any claims or amounts recovered from any infringements of patent, trademark, or copyright; or from any claims or amounts arising or recovered under the "Workmen's Compensation Act," or any other law, ordinance, order, or decree. Money due the Contractor under and by virtue of their own contract considered necessary by the Owner for such purpose may be retained for the use of the Owner or, in case no money is due, their own surety may be held until such suits, actions, or claims for injuries or damages shall have been settled and suitable evidence to that effect furnished to the Owner, except that money due the Contractor will not be withheld when the Contractor produces satisfactory evidence that he or she is adequately protected by public liability and property damage insurance.

70-12 Third party beneficiary clause. It is specifically agreed between the parties executing the contract that it is not intended by any of the provisions of any part of the contract to create for the public or any member thereof, a third-party beneficiary or to authorize anyone not a party to the contract to maintain a suit for personal injuries or property damage pursuant to the terms or provisions of the contract.

70-13 Opening sections of the work to traffic. If it is necessary for the Contractor to complete portions of the contract work for the beneficial occupancy of the Owner prior to completion of the entire contract, such "phasing" of the work must be specified below and indicated on the approved Construction Safety and Phasing Plan (CSPP) and the project plans. When so specified, the Contractor shall complete such portions of the work on or before the date specified or as otherwise specified.

Contractor to refer to and comply with the phasing plans (if work is phased) included in the project drawings and the CSPP.

Upon completion of any portion of work listed above, such portion shall be accepted by the Owner in accordance with Section 50, paragraph 50-14, *Partial Acceptance*.

No portion of the work may be opened by the Contractor until directed by the Owner in writing. Should it become necessary to open a portion of the work to traffic on a temporary or intermittent basis, such openings shall be made when, in the opinion of the RPR, such portion of the work is in an acceptable condition to support the intended traffic. Temporary or intermittent openings are considered to be inherent in the work and shall not constitute either acceptance of the portion of the work so opened or a waiver of any provision of the contract. Any damage to the portion of the work so opened that is not attributable to traffic which is permitted by the Owner shall be repaired by the Contractor at their expense.

The Contractor shall make their own estimate of the inherent difficulties involved in completing the work under the conditions herein described and shall not claim any added compensation by reason of delay or increased cost due to opening a portion of the contract work.

The Contractor must conform to safety standards contained AC 150/5370-2 and the approved CSPP.

Contractor shall refer to the plans, specifications, and the approved CSPP to identify barricade requirements, temporary and/or permanent markings, airfield lighting, guidance signs and other safety requirements prior to opening up sections of work to traffic.

70-14 Contractor's responsibility for work. Until the RPR's final written acceptance of the entire completed work, excepting only those portions of the work accepted in accordance with Section 50, paragraph 50-14, *Partial Acceptance*, the Contractor shall have the charge and care thereof and shall take every precaution against injury or damage to any part due to the action of the elements or from any other cause, whether arising from the execution or from the non-execution of the work. The Contractor shall rebuild, repair, restore, and make good all injuries or damages to any portion of the work occasioned by any of the above causes before final acceptance and shall bear the expense thereof except damage to the work due to unforeseeable causes beyond the control of and without the fault or negligence of the Contractor, including but not restricted to acts of God such as earthquake, tidal wave, tornado, hurricane or other cataclysmic phenomenon of nature, or acts of the public enemy or of government authorities.

If the work is suspended for any cause whatever, the Contractor shall be responsible for the work and shall take such precautions necessary to prevent damage to the work. The Contractor shall provide for normal drainage and shall erect necessary temporary structures, signs, or other facilities at their own expense. During such period of suspension of work, the Contractor shall properly and continuously maintain in an acceptable growing condition all living material in newly established planting, seeding, and sodding furnished under the contract, and shall take adequate precautions to protect new tree growth and other important vegetative growth against injury.

70-15 Contractor's responsibility for utility service and facilities of others. As provided in paragraph 70-04, *Restoration of Surfaces Disturbed by Others*, the Contractor shall cooperate with the owner of any

public or private utility service, FAA or NOAA, or a utility service of another government agency that may be authorized by the Owner to construct, reconstruct or maintain such utility services or facilities during the progress of the work. In addition, the Contractor shall control their operations to prevent the unscheduled interruption of such utility services and facilities.

To the extent that such public or private utility services, FAA, or NOAA facilities, or utility services of another governmental agency are known to exist within the limits of the contract work, the approximate locations have been indicated on the plans and/or in the contract documents and the owner(s) are indicated as follows:

Airport and FAA Utilities and Systems

Contact:

Project Manager

Steven Manual, County of Santa Barbara

stmanuel@countyofsb.org

It is understood and agreed that the Owner does not guarantee the accuracy or the completeness of the location information relating to existing utility services, facilities, or structures that may be shown on the plans or encountered in the work. Any inaccuracy or omission in such information shall not relieve the Contractor of the responsibility to protect such existing features from damage or unscheduled interruption of service.

It is further understood and agreed that the Contractor shall, upon execution of the contract, notify the Owners of all utility services or other facilities of their plan of operations. Such notification shall be in writing addressed to "The Person to Contact" as provided in this paragraph and paragraph 70-04, *Restoration of Surfaces Disturbed By Others*. A copy of each notification shall be given to the RPR.

In addition to the general written notification provided, it shall be the responsibility of the Contractor to keep such individual Owners advised of changes in their plan of operations that would affect such Owners.

Prior to beginning the work in the general vicinity of an existing utility service or facility, the Contractor shall again notify each such Owner of their plan of operation. If, in the Contractor's opinion, the Owner's assistance is needed to locate the utility service or facility or the presence of a representative of the Owner is desirable to observe the work, such advice should be included in the notification. Such notification shall be given by the most expeditious means to reach the utility owner's "Person to Contact" no later than two normal business days prior to the Contractor's commencement of operations in such general vicinity. The Contractor shall furnish a written summary of the notification to the RPR.

The Contractor's failure to give the two days' notice shall be cause for the Owner to suspend the Contractor's operations in the general vicinity of a utility service or facility.

Where the outside limits of an underground utility service have been located and staked on the ground, the Contractor shall be required to use hand excavation methods within 3 feet (1 m) of such outside limits at such points as may be required to ensure protection from damage due to the Contractor's operations.

Should the Contractor damage or interrupt the operation of a utility service or facility by accident or otherwise, the Contractor shall immediately notify the proper authority and the RPR and shall take all reasonable measures to prevent further damage or interruption of service. The Contractor, in such events, shall cooperate with the utility service or facility owner and the RPR continuously until such damage has been repaired and service restored to the satisfaction of the utility or facility owner.

The Contractor shall bear all costs of damage and restoration of service to any utility service or facility due to their operations whether due to negligence or accident. The Owner reserves the right to deduct such costs from any monies due or which may become due the Contractor, or their own surety.

70-15.1 FAA facilities and cable runs. The Contractor is hereby advised that the construction limits of the project include existing facilities and buried cable runs that are owned, operated and maintained by the FAA. The Contractor, during the execution of the project work, shall comply with the following:

a. The Contractor shall permit FAA maintenance personnel the right of access to the project work site for purposes of inspecting and maintaining all existing FAA owned facilities.

b. The Contractor shall provide notice to the FAA a minimum of seven (7) calendar days prior to commencement of construction activities in order to permit sufficient time to locate and mark existing buried cables and to schedule any required facility outages.

c. If execution of the project work requires a facility outage, the Contractor shall contact the FAA Point-of-Contact a minimum of 72 hours prior to the time of the required outage.

d. Any damage to FAA cables, access roads, or FAA facilities during construction caused by the Contractor's equipment or personnel whether by negligence or accident will require the Contractor to repair or replace the damaged cables, access road, or FAA facilities to FAA requirements. The Contractor shall not bear the cost to repair damage to underground facilities or utilities improperly located by the FAA.

e. If the project work requires the cutting or splicing of FAA owned cables, the FAA Point-of-Contact shall be contacted a minimum of 72 hours prior to the time the cable work commences. The FAA reserves the right to have a FAA representative on site to observe the splicing of the cables as a condition of acceptance. All cable splices are to be accomplished in accordance with FAA specifications and require approval by the FAA Point-of-Contact as a condition of acceptance by the Owner. The Contractor is hereby advised that FAA restricts the location of where splices may be installed. If a cable splice is required in a location that is not permitted by FAA, the Contractor shall furnish and install a sufficient length of new cable that eliminates the need for any splice.

70-16 Furnishing rights-of-way. The Owner will be responsible for furnishing all rights-of-way upon which the work is to be constructed in advance of the Contractor's operations.

70-17 Personal liability of public officials. In carrying out any of the contract provisions or in exercising any power or authority granted by this contract, there shall be no liability upon the Engineer, RPR, their authorized representatives, or any officials of the Owner either personally or as an official of the Owner. It is understood that in such matters they act solely as agents and representatives of the Owner.

70-18 No waiver of legal rights. Upon completion of the work, the Owner will expeditiously make final inspection and notify the Contractor of final acceptance. Such final acceptance, however, shall not preclude or stop the Owner from correcting any measurement, estimate, or certificate made before or after completion of the work, nor shall the Owner be precluded or stopped from recovering from the Contractor or their surety, or both, such overpayment as may be sustained, or by failure on the part of the Contractor to fulfill their obligations under the contract. A waiver on the part of the Owner of any breach of any part of the contract shall not be held to be a waiver of any other or subsequent breach.

The Contractor, without prejudice to the terms of the contract, shall be liable to the Owner for latent defects, fraud, or such gross mistakes as may amount to fraud, or as regards the Owner's rights under any warranty or guaranty.

70-19 Environmental protection. The Contractor shall comply with all federal, state, and local laws and regulations controlling pollution of the environment. The Contractor shall take necessary precautions to

prevent pollution of streams, lakes, ponds, and reservoirs with fuels, oils, asphalts, chemicals, or other harmful materials and to prevent pollution of the atmosphere from particulate and gaseous matter.

70-20 Archaeological and historical findings. Unless otherwise specified in this subsection, the Contractor is advised that the site of the work is not within any property, district, or site, and does not contain any building, structure, or object listed in the current National Register of Historic Places published by the United States Department of Interior.

Should the Contractor encounter, during their operations, any building, part of a building, structure, or object that is incongruous with its surroundings, the Contractor shall immediately cease operations in that location and notify the RPR. The RPR will immediately investigate the Contractor's finding and the Owner will direct the Contractor to either resume operations or to suspend operations as directed.

Should the Owner order suspension of the Contractor's operations in order to protect an archaeological or historical finding, or order the Contractor to perform extra work, such shall be covered by an appropriate contract change order or supplemental agreement as provided in Section 40, paragraph 40-04, *Extra Work,* and Section 90, paragraph 90-05, *Payment for Extra Work*. If appropriate, the contract change order or supplemental agreement shall include an extension of contract time in accordance with Section 80, paragraph 80-07, *Determination and Extension of Contract Time*.

70-21 Insurance Requirements. Refer to the Contract Forms Section located elsewhere in the contract document package.

END OF SECTION 70

Section 80 Execution and Progress

80-01 Subletting of contract. The Owner will not recognize any subcontractor on the work. The Contractor shall at all times when work is in progress be represented either in person, by a qualified superintendent, or by other designated, qualified representative who is duly authorized to receive and execute orders of the Resident Project Representative (RPR).

The Contractor shall perform, with his organization, an amount of work equal to at least **twenty five percent (25%) of the total contract cost**.

Should the Contractor elect to assign their contract, said assignment shall be concurred in by the surety, shall be presented for the consideration and approval of the Owner, and shall be consummated only on the written approval of the Owner.

The Contractor shall provide copies of all subcontracts to the RPR 14 calendar days prior to being utilized on the project. As a minimum, the information shall include the following:

- Subcontractor's legal company name.
- Subcontractor's legal company address, including County name.
- Principal contact person's name, telephone and fax number.
- Complete narrative description, and dollar value of the work to be performed by the subcontractor.
- Copies of required insurance certificates in accordance with the specifications.
- Minority/ non-minority status.

80-02 Notice to proceed (NTP). The Owners notice to proceed will state the date on which contract time commences. The Contractor is expected to commence project operations within 10 days of the NTP date. The Contractor shall notify the RPR at least 24 hours in advance of the time contract operations begins. The Contractor shall not commence any actual operations prior to the date on which the notice to proceed is issued by the Owner.

80-03 Execution and progress. Unless otherwise specified, the Contractor shall submit their coordinated construction schedule showing all work activities for the RPR's review and acceptance at least 10 days prior to the start of work. The Contractor's progress schedule, once accepted by the RPR, will represent the Contractor's baseline plan to accomplish the project in accordance with the terms and conditions of the Contract. The RPR will compare actual Contractor progress against the baseline schedule to determine that status of the Contractor's performance. The Contractor shall provide sufficient materials, equipment, and labor to guarantee the completion of the project in accordance with the plans and specifications within the time set forth in the proposal.

If the Contractor falls significantly behind the submitted schedule, the Contractor shall, upon the RPR's request, submit a revised schedule for completion of the work within the contract time and modify their operations to provide such additional materials, equipment, and labor necessary to meet the revised schedule. Should the execution of the work be discontinued for any reason, the Contractor shall notify the RPR at least 48 hours in advance of resuming operations.

The Contractor shall not commence any actual construction prior to the date on which the NTP is issued by the Owner.

The project schedule shall be prepared as a network diagram in Critical Path Method (CPM). It shall include information on the sequence of work activities, milestone dates, and activity duration. The

schedule shall show all work items identified in the project proposal for each work area and shall include the project start date and end date.

The Contractor shall maintain the work schedule and provide an update and analysis of the progress schedule on a **weekly** basis, or as otherwise specified in the contract. Submission of the work schedule shall not relieve the Contractor of overall responsibility for scheduling, sequencing, and coordinating all work to comply with the requirements of the contract.

80-04 Limitation of operations. The Contractor shall control their operations and the operations of their subcontractors and all suppliers to provide for the free and unobstructed movement of aircraft in the air operations areas (AOA) of the airport.

When the work requires the Contractor to conduct their operations within an AOA of the airport, the work shall be coordinated with airport operations (through the RPR) at least 48 hours prior to commencement of such work. The Contractor shall not close an AOA until so authorized by the RPR and until the necessary temporary marking, signage and associated lighting is in place as provided in Section 70, paragraph 70-08, *Construction Safety and Phasing Plan (CSPP)*.

When the contract work requires the Contractor to work within an AOA of the airport on an intermittent basis (intermittent opening and closing of the AOA), the Contractor shall maintain constant communications as specified; immediately obey all instructions to vacate the AOA; and immediately obey all instructions to resume work in such AOA. Failure to maintain the specified communications or to obey instructions shall be cause for suspension of the Contractor's operations in the AOA until satisfactory conditions are provided. The areas of the AOA identified in the Construction Safety Phasing Plan (CSPP) and as listed below, cannot be closed to operating aircraft to permit the Contractor's operations on a continuous basis and will therefore be closed to aircraft operations intermittently as follows:

Contractor shall refer to the phasing plans on the project drawings and the CSPP.

The Contractor shall be required to conform to safety standards contained in AC 150/5370-2, Operational Safety on Airports During Construction and the approved CSPP.

80-04.1 Operational safety on airport during construction. All Contractors' operations shall be conducted in accordance with the approved project Construction Safety and Phasing Plan (CSPP) and the Safety Plan Compliance Document (SPCD) and the provisions set forth within the current version of AC 150/5370-2, Operational Safety on Airports During Construction. The CSPP included within the contract documents conveys minimum requirements for operational safety on the airport during construction activities. The Contractor shall prepare and submit a SPCD that details how it proposes to comply with the requirements presented within the CSPP.

The Contractor shall implement all necessary safety plan measures prior to commencement of any work activity. The Contractor shall conduct routine checks to assure compliance with the safety plan measures.

The Contractor is responsible to the Owner for the conduct of all subcontractors it employs on the project. The Contractor shall assure that all subcontractors are made aware of the requirements of the CSPP and SPCD and that they implement and maintain all necessary measures.

No deviation or modifications may be made to the approved CSPP and SPCD unless approved in writing by the Owner. The necessary coordination actions to review Contractor proposed modifications to an approved CSPP or approved SPCD can require a significant amount of time.

80-05 Character of workers, methods, and equipment. The Contractor shall, at all times, employ sufficient labor and equipment for prosecuting the work to full completion in the manner and time required by the contract, plans, and specifications.

All workers shall have sufficient skill and experience to perform properly the work assigned to them. Workers engaged in special work or skilled work shall have sufficient experience in such work and in the operation of the equipment required to perform the work satisfactorily.

Any person employed by the Contractor or by any subcontractor who violates any operational regulations or operational safety requirements and, in the opinion of the RPR, does not perform his work in a proper and skillful manner or is intemperate or disorderly shall, at the written request of the RPR, be removed immediately by the Contractor or subcontractor employing such person, and shall not be employed again in any portion of the work without approval of the RPR.

Should the Contractor fail to remove such person or persons, or fail to furnish suitable and sufficient personnel for the proper execution of the work, the RPR may suspend the work by written notice until compliance with such orders.

All equipment that is proposed to be used on the work shall be of sufficient size and in such mechanical condition as to meet requirements of the work and to produce a satisfactory quality of work. Equipment used on any portion of the work shall not cause injury to previously completed work, adjacent property, or existing airport facilities due to its use.

When the methods and equipment to be used by the Contractor in accomplishing the work are not prescribed in the contract, the Contractor is free to use any methods or equipment that will accomplish the work in conformity with the requirements of the contract, plans, and specifications.

When the contract specifies the use of certain methods and equipment, such methods and equipment shall be used unless otherwise authorized by the RPR. If the Contractor desires to use a method or type of equipment other than specified in the contract, the Contractor may request authority from the RPR to do so. The request shall be in writing and shall include a full description of the methods and equipment proposed and of the reasons for desiring to make the change. If approval is given, it will be on the condition that the Contractor will be fully responsible for producing work in conformity with contract requirements. If, after trial use of the substituted methods or equipment, the RPR determines that the work produced does not meet contract requirements, the Contractor shall discontinue the use of the substitute method or equipment and shall complete the remaining work with the specified methods and equipment. The Contractor shall remove any deficient work and replace it with work of specified quality, or take such other corrective action as the RPR may direct. No change will be made in basis of payment for the contract items involved nor in contract time as a result of authorizing a change in methods or equipment under this paragraph.

80-06 Temporary suspension of the work. The Owner shall have the authority to suspend the work wholly, or in part, for such period or periods the Owner may deem necessary, due to unsuitable weather, or other conditions considered unfavorable for the execution of the work, or for such time necessary due to the failure on the part of the Contractor to carry out orders given or perform any or all provisions of the contract.

In the event that the Contractor is ordered by the Owner, in writing, to suspend work for some unforeseen cause not otherwise provided for in the contract and over which the Contractor has no control, the Contractor may be reimbursed for actual money expended on the work during the period of shutdown. No allowance will be made for anticipated profits. The period of shutdown shall be computed from the effective date of the written order to suspend work to the effective date of the written order to resume the work. Claims for such compensation shall be filed with the RPR within the time period stated in the RPR's order to resume work. The Contractor shall submit with their own claim information substantiating the amount shown on the claim. The RPR will forward the Contractor's claim to the Owner for consideration in accordance with local laws or ordinances. No provision of this article shall be construed as entitling the Contractor to compensation for delays due to inclement weather or for any other delay provided for in the contract, plans, or specifications.

If it becomes necessary to suspend work for an indefinite period, the Contractor shall store all materials in such manner that they will not become an obstruction nor become damaged in any way. The Contractor shall take every precaution to prevent damage or deterioration of the work performed and provide for normal drainage of the work. The Contractor shall erect temporary structures where necessary to provide for traffic on, to, or from the airport.

80-07 Determination and extension of contract time. The number of calendar days or the number of working days shall be stated in the proposal and contract and shall be known as the Contract Time.

If the contract time requires extension for reasons beyond the Contractor's control, it shall be adjusted as follows:

80-07.1 Contract time based on working days. Contract time based on working days shall be calculated weekly by the Resident Project Representative (RPR). The RPR will furnish the Contractor a copy of their weekly statement of the number of working days charged against the contract time during the week and the number of working days currently specified for completion of the contract (the original contract time plus the number of working days, if any, that have been included in approved Change Orders or Supplemental Agreements covering Extra Work).

The weekly statement of contract time charged is based on the following considerations:

(1) Time will be charged for days on which the Contractor could proceed with scheduled work under construction at the time for at least six (6) hours with the normal work force employed on such items. When normal work force is a double-shift, use 12 hours; and when the normal work force is on a triple-shift, use 18 hours. Conditions beyond the Contractor's control such as strikes, lockouts, unusual delays in transportation, temporary suspension of the scheduled work items under construction or temporary suspension of the entire work which have been ordered by the Owner for reasons not the fault of the Contractor, shall not be charged against the contract time.

(2) The RPR will not make charges against the contract time prior to the effective date of the notice to proceed.

(3) The RPR will begin charges against the contract time on the first working day after the effective date of the notice to proceed.

(4) The RPR will not make charges against the contract time after the date of final acceptance as defined in Section 50, paragraph 50-14, *Final Acceptance*.

(5) The Contractor will be allowed one (1) week in which to file a written protest setting forth their own objections to the RPR's weekly statement. If no objection is filed within such specified time, the weekly statement shall be considered as acceptable to the Contractor.

The contract time (stated in the proposal) is based on the originally estimated quantities as described in the Section 20, paragraph 20-05, *Interpretation of Estimated Proposal Quantities*. Should the satisfactory completion of the contract require performance of work in greater quantities than those estimated in the proposal, the contract time shall be increased in the same proportion as the cost of the actually completed quantities bears to the cost of the originally estimated quantities in the proposal. Such increase in contract time shall not consider either the cost of work or the extension of contract time that has been covered by change order or supplemental agreement and shall be made at the time of final payment.

80-08 Failure to complete on time. For each calendar day or working day, as specified in the contract, that any work remains uncompleted after the contract time (including all extensions and adjustments as provided in paragraph 80-07, *Determination and Extension of Contract Time*) the sum specified in the contract and proposal as liquidated damages (LD) will be deducted from any money due or to become due the Contractor or their own surety. Such deducted sums shall not be deducted as a penalty but shall be considered as liquidation of a reasonable portion of damages including but not limited to additional

engineering services that will be incurred by the Owner should the Contractor fail to complete the work in the time provided in their contract.

Contractor shall refer to the CSPP for liquidated damages and penalties.

The maximum construction time allowed is 50 Working days.

Permitting the Contractor to continue and finish the work or any part of it after the time fixed for its completion, or after the date to which the time for completion may have been extended, will in no way operate as a wavier on the part of the Owner of any of its rights under the contract.

80-09 Default and termination of contract. The Contractor shall be considered in default of their contract and such default will be considered as cause for the Owner to terminate the contract for any of the following reasons, if the Contractor:

a. Fails to begin the work under the contract within the time specified in the Notice to Proceed, or

b. Fails to perform the work or fails to provide sufficient workers, equipment and/or materials to assure completion of work in accordance with the terms of the contract, or

c. Performs the work unsuitably or neglects or refuses to remove materials or to perform anew such work as may be rejected as unacceptable and unsuitable, or

d. Discontinues the execution of the work, or

e. Fails to resume work which has been discontinued within a reasonable time after notice to do so, or

f. Becomes insolvent or is declared bankrupt, or commits any act of bankruptcy or insolvency, or

g. Allows any final judgment to stand against the Contractor unsatisfied for a period of 10 days, or

h. Makes an assignment for the benefit of creditors, or

i. For any other cause whatsoever, fails to carry on the work in an acceptable manner.

Should the Owner consider the Contractor in default of the contract for any reason above, the Owner shall immediately give written notice to the Contractor and the Contractor's surety as to the reasons for considering the Contractor in default and the Owner's intentions to terminate the contract.

If the Contractor or surety, within a period of 10 days after such notice, does not proceed in accordance therewith, then the Owner will, upon written notification from the RPR of the facts of such delay, neglect, or default and the Contractor's failure to comply with such notice, have full power and authority without violating the contract, to take the execution of the work out of the hands of the Contractor. The Owner may appropriate or use any or all materials and equipment that have been mobilized for use in the work and are acceptable and may enter into an agreement for the completion of said contract according to the terms and provisions thereof, or use such other methods as in the opinion of the RPR will be required for the completion of said contract in an acceptable manner.

All costs and charges incurred by the Owner, together with the cost of completing the work under contract, will be deducted from any monies due or which may become due the Contractor. If such expense exceeds the sum which would have been payable under the contract, then the Contractor and the surety shall be liable and shall pay to the Owner the amount of such excess.

80-10 Termination for national emergencies. The Owner shall terminate the contract or portion thereof by written notice when the Contractor is prevented from proceeding with the construction contract as a direct result of an Executive Order of the President with respect to the execution of war or in the interest of national defense.

When the contract, or any portion thereof, is terminated before completion of all items of work in the contract, payment will be made for the actual number of units or items of work completed at the contract

price or as mutually agreed for items of work partially completed or not started. No claims or loss of anticipated profits shall be considered.

Reimbursement for organization of the work, and other overhead expenses, (when not otherwise included in the contract) and moving equipment and materials to and from the job will be considered, the intent being that an equitable settlement will be made with the Contractor.

Acceptable materials, obtained or ordered by the Contractor for the work and that are not incorporated in the work shall, at the option of the Contractor, be purchased from the Contractor at actual cost as shown by receipted bills and actual cost records at such points of delivery as may be designated by the RPR.

Termination of the contract or a portion thereof shall neither relieve the Contractor of their responsibilities for the completed work nor shall it relieve their surety of its obligation for and concerning any just claim arising out of the work performed.

80-11 Work area, storage area and sequence of operations. The Contractor shall obtain approval from the RPR prior to beginning any work in all areas of the airport. No operating runway, taxiway, or air operations area (AOA) shall be crossed, entered, or obstructed while it is operational. The Contractor shall plan and coordinate work in accordance with the approved CSPP and SPCD.

END OF SECTION 80

Section 90 Measurement and Payment

90-01 Measurement of quantities. All work completed under the contract will be measured by the RPR, or their authorized representatives, using United States Customary Units of Measurement.

The method of measurement and computations to be used in determination of quantities of material furnished and of work performed under the contract will be those methods generally recognized as conforming to good engineering practice.

Unless otherwise specified, longitudinal measurements for area computations will be made horizontally, and no deductions will be made for individual fixtures (or leave-outs) having an area of 9 square feet (0.8 square meters) or less. Unless otherwise specified, transverse measurements for area computations will be the neat dimensions shown on the plans or ordered in writing by the RPR.

Unless otherwise specified, all contract items which are measured by the linear foot such as electrical ducts, conduits, pipe culverts, underdrains, and similar items shall be measured parallel to the base or foundation upon which such items are placed.

The term "lump sum" when used as an item of payment will mean complete payment for the work described in the contract. When a complete structure or structural unit (in effect, "lump sum" work) is specified as the unit of measurement, the unit will be construed to include all necessary fittings and accessories.

When requested by the Contractor and approved by the RPR in writing, material specified to be measured by the cubic yard (cubic meter) may be weighed, and such weights will be converted to cubic yards (cubic meters) for payment purposes. Factors for conversion from weight measurement to volume measurement will be determined by the RPR and shall be agreed to by the Contractor before such method of measurement of pay quantities is used.

Measurement and Payment Terms

Term	Description
Excavation and Embankment Volume	In computing volumes of excavation, the average end area method will be used unless otherwise specified.
Measurement and Proportion by Weight	The term "ton" will mean the short ton consisting of 2,000 pounds (907 km) avoirdupois. All materials that are measured or proportioned by weights shall be weighed on accurate, independently certified scales by competent, qualified personnel at locations designated by the RPR. If material is shipped by rail, the car weight may be accepted provided that only the actual weight of material is paid for. However, car weights will not be acceptable for material to be passed through mixing plants. Trucks used to haul material being paid for by weight shall be weighed empty daily at such times as the RPR directs, and each truck shall bear a plainly legible identification mark.
Measurement by Volume	Materials to be measured by volume in the hauling vehicle shall be hauled in approved vehicles and measured therein at the point of delivery. Vehicles for this purpose may be of any size or type acceptable for the materials hauled, provided that the body is of such shape that the actual contents may be readily and accurately determined. All vehicles shall be loaded to at least their water level

Term	Description
	capacity, and all loads shall be leveled when the vehicles arrive at the point of delivery.
Asphalt Material	Asphalt materials will be measured by the gallon (liter) or ton (kg). When measured by volume, such volumes will be measured at 60°F (16°C) or will be corrected to the volume at 60°F (16°C) using ASTM D1250 for asphalts. Net certified scale weights or weights based on certified volumes in the case of rail shipments will be used as a basis of measurement, subject to correction when asphalt material has been lost from the car or the distributor, wasted, or otherwise not incorporated in the work. When asphalt materials are shipped by truck or transport, net certified weights by volume, subject to correction for loss or foaming, will be used for computing quantities.
Cement	Cement will be measured by the ton (kg) or hundredweight (km).
Structure	Structures will be measured according to neat lines shown on the plans or as altered to fit field conditions.
Timber	Timber will be measured by the thousand feet board measure (MFBM) actually incorporated in the structure. Measurement will be based on nominal widths and thicknesses and the extreme length of each piece.
Plates and Sheets	The thickness of plates and galvanized sheet used in the manufacture of corrugated metal pipe, metal plate pipe culverts and arches, and metal cribbing will be specified and measured in decimal fraction of inch.
Miscellaneous Items	When standard manufactured items are specified such as fence, wire, plates, rolled shapes, pipe conduit, etc., and these items are identified by gauge, unit weight, section dimensions, etc., such identification will be considered to be nominal weights or dimensions. Unless more stringently controlled by tolerances in cited specifications, manufacturing tolerances established by the industries involved will be accepted.
Scales	Scales must be tested for accuracy and serviced before use. Scales for weighing materials which are required to be proportioned or measured and paid for by weight shall be furnished, erected, and maintained by the Contractor, or be certified permanently installed commercial scales. Platform scales shall be installed and maintained with the platform level and rigid bulkheads at each end. Scales shall be accurate within 0.5% of the correct weight throughout the range of use. The Contractor shall have the scales checked under the observation of the RPR before beginning work and at such other times as requested. The intervals shall be uniform in spacing throughout the graduated or marked length of the beam or dial and shall not exceed 0.1% of the nominal rated capacity of the scale, but not less than one pound (454 grams). The use of spring balances will not be permitted. In the event inspection reveals the scales have been “overweighing” (indicating more than correct weight) they will be immediately adjusted. All materials

Term	Description
	received subsequent to the last previous correct weighting-accuracy test will be reduced by the percentage of error in excess of 0.5%. In the event inspection reveals the scales have been under-weighing (indicating less than correct weight), they shall be immediately adjusted. No additional payment to the Contractor will be allowed for materials previously weighed and recorded. Beams, dials, platforms, and other scale equipment shall be so arranged that the operator and the RPR can safely and conveniently view them. Scale installations shall have available ten standard 50-pound (2.3 km) weights for testing the weighing equipment or suitable weights and devices for other approved equipment. All costs in connection with furnishing, installing, certifying, testing, and maintaining scales; for furnishing check weights and scale house; and for all other items specified in this subsection, for the weighing of materials for proportioning or payment, shall be included in the unit contract prices for the various items of the project.
Rental Equipment	Rental of equipment will be measured by time in hours of actual working time and necessary traveling time of the equipment within the limits of the work. Special equipment ordered in connection with extra work will be measured as agreed in the change order or supplemental agreement authorizing such work as provided in paragraph 90-05 *Payment for Extra Work*.
Pay Quantities	When the estimated quantities for a specific portion of the work are designated as the pay quantities in the contract, they shall be the final quantities for which payment for such specific portion of the work will be made, unless the dimensions of said portions of the work shown on the plans are revised by the RPR. If revised dimensions result in an increase or decrease in the quantities of such work, the final quantities for payment will be revised in the amount represented by the authorized changes in the dimensions.

90-02 Scope of payment. The Contractor shall receive and accept compensation provided for in the contract as full payment for furnishing all materials, for performing all work under the contract in a complete and acceptable manner, and for all risk, loss, damage, or expense of whatever character arising out of the nature of the work or the execution thereof, subject to the provisions of Section 70, paragraph 70-18, *No Waiver of Legal Rights*.

When the "basis of payment" subsection of a technical specification requires that the contract price (price bid) include compensation for certain work or material essential to the item, this same work or material will not also be measured for payment under any other contract item which may appear elsewhere in the contract, plans, or specifications.

90-03 Compensation for altered quantities. When the accepted quantities of work vary from the quantities in the proposal, the Contractor shall accept as payment in full, so far as contract items are concerned, payment at the original contract price for the accepted quantities of work actually completed and accepted. No allowance, except as provided for in Section 40, paragraph 40-02, *Alteration of Work and Quantities,* will be made for any increased expense, loss of expected reimbursement, or loss of anticipated profits suffered or claimed by the Contractor which results directly from such alterations or

indirectly from their own unbalanced allocation of overhead and profit among the contract items, or from any other cause.

90-04 Payment for omitted items. As specified in Section 40, paragraph 40-03, *Omitted Items,* the RPR shall have the right to omit from the work (order nonperformance) any contract item, except major contract items, in the best interest of the Owner.

Should the RPR omit or order nonperformance of a contract item or portion of such item from the work, the Contractor shall accept payment in full at the contract prices for any work actually completed and acceptable prior to the RPR's order to omit or non-perform such contract item.

Acceptable materials ordered by the Contractor or delivered on the work prior to the date of the RPR's order will be paid for at the actual cost to the Contractor and shall thereupon become the property of the Owner.

In addition to the reimbursement hereinbefore provided, the Contractor shall be reimbursed for all actual costs incurred for the purpose of performing the omitted contract item prior to the date of the RPR's order. Such additional costs incurred by the Contractor must be directly related to the deleted contract item and shall be supported by certified statements by the Contractor as to the nature the amount of such costs.

90-05 Payment for extra work. Extra work, performed in accordance with Section 40, paragraph 40-04, *Extra Work*, will be paid for at the contract prices or agreed prices specified in the change order or supplemental agreement authorizing the extra work.

90-06 Partial payments. Partial payments will be made to the Contractor at least once each month as the work progresses. Said payments will be based upon estimates, prepared by the RPR, of the value of the work performed and materials complete and in place, in accordance with the contract, plans, and specifications. Such partial payments may also include the delivered actual cost of those materials stockpiled and stored in accordance with paragraph 90-07, *Payment for Materials on Hand*. No partial payment will be made when the amount due to the Contractor since the last estimate amounts to less than five hundred dollars.

The Contractor is required to pay all subcontractors for satisfactory performance of their contracts no later than 30 days after the Contractor has received a partial payment. The Owner must ensure prompt and full payment of retainage from the prime Contractor to the subcontractor within 30 days after the subcontractor's work is satisfactorily completed. A subcontractor's work is satisfactorily completed when all the tasks called for in the subcontract have been accomplished and documented as required by the Owner. When the Owner has made an incremental acceptance of a portion of a prime contract, the work of a subcontractor covered by that acceptance is deemed to be satisfactorily completed.

From the total of the amount determined to be payable on a partial payment, five (5) percent of such total amount will be deducted and retained by the Owner until the final payment is made, except as may be provided (at the Contractor's option) in the subsection 90-08 titled PAYMENT OF WITHHELD FUNDS of this section. The balance of the amount payable, less all previous payments, shall be certified for payment. Should the Contractor exercise his or her option, as provided in the subsection 90-08 titled PAYMENT OF WITHHELD FUNDS of this section, no such percent retainage shall be deducted.

When at least 95% of the work has been completed, the Engineer shall, at the Owner's discretion and with the consent of the surety, prepare estimates of both the contract value and the cost of the remaining work to be done.

The Owner may retain an amount not less than twice the contract value or estimated cost, whichever is greater, of the work remaining to be done. The remainder, less all previous payments and deductions, will then be certified for payment to the Contractor.

It is understood and agreed that the Contractor shall not be entitled to demand or receive partial payment based on quantities of work in excess of those provided in the proposal or covered by approved change orders or supplemental agreements, except when such excess quantities have been determined by the RPR to be a part of the final quantity for the item of work in question.

No partial payment shall bind the Owner to the acceptance of any materials or work in place as to quality or quantity. All partial payments are subject to correction at the time of final payment as provided in paragraph 90-09, *Acceptance and Final Payment*.

The Contractor shall deliver to the Owner a complete release of all claims for labor and material arising out of this contract before the final payment is made. If any subcontractor or supplier fails to furnish such a release in full, the Contractor may furnish a bond or other collateral satisfactory to the Owner to indemnify the Owner against any potential lien or other such claim. The bond or collateral shall include all costs, expenses, and attorney fees the Owner may be compelled to pay in discharging any such lien or claim.

90-07 Payment for materials on hand. Partial payments may be made to the extent of the delivered cost of materials to be incorporated in the work, provided that such materials meet the requirements of the contract, plans, and specifications and are delivered to acceptable sites on the airport property or at other sites in the vicinity that are acceptable to the Owner. Such delivered costs of stored or stockpiled materials may be included in the next partial payment after the following conditions are met:

a. The material has been stored or stockpiled in a manner acceptable to the RPR at or on an approved site.

b. The Contractor has furnished the RPR with acceptable evidence of the quantity and quality of such stored or stockpiled materials.

c. The Contractor has furnished the RPR with satisfactory evidence that the material and transportation costs have been paid.

d. The Contractor has furnished the Owner legal title (free of liens or encumbrances of any kind) to the material stored or stockpiled.

e. The Contractor has furnished the Owner evidence that the material stored or stockpiled is insured against loss by damage to or disappearance of such materials at any time prior to use in the work.

It is understood and agreed that the transfer of title and the Owner's payment for such stored or stockpiled materials shall in no way relieve the Contractor of their responsibility for furnishing and placing such materials in accordance with the requirements of the contract, plans, and specifications.

In no case will the amount of partial payments for materials on hand exceed the contract price for such materials or the contract price for the contract item in which the material is intended to be used.

No partial payment will be made for stored or stockpiled living or perishable plant materials.

The Contractor shall bear all costs associated with the partial payment of stored or stockpiled materials in accordance with the provisions of this paragraph.

90-08 Payment of withheld funds. At the Contractor's option, if an Owner withholds retainage in accordance with the methods described in paragraph 90-06 *Partial Payments*, the Contractor may request that the Owner deposit the retainage into an escrow account. The Owner's deposit of retainage into an escrow account is subject to the following conditions:

a. The Contractor shall bear all expenses of establishing and maintaining an escrow account and escrow agreement acceptable to the Owner.

b. The Contractor shall deposit to and maintain in such escrow only those securities or bank certificates of deposit as are acceptable to the Owner and having a value not less than the retainage that would otherwise be withheld from partial payment.

c. The Contractor shall enter into an escrow agreement satisfactory to the Owner.

d. The Contractor shall obtain the written consent of the surety to such agreement.

90-09 Acceptance and final payment. When the contract work has been accepted in accordance with the requirements of Section 50, paragraph 50-15, *Final Acceptance*, the RPR will prepare the final estimate of the items of work actually performed. The Contractor shall approve the RPR's final estimate or advise the RPR of the Contractor's objections to the final estimate which are based on disputes in measurements or computations of the final quantities to be paid under the contract as amended by change order or supplemental agreement. The Contractor and the RPR shall resolve all disputes (if any) in the measurement and computation of final quantities to be paid within 30 calendar days of the Contractor's receipt of the RPR's final estimate. If, after such 30-day period, a dispute still exists, the Contractor may approve the RPR's estimate under protest of the quantities in dispute, and such disputed quantities shall be considered by the Owner as a claim in accordance with Section 50, paragraph 50-16, *Claims for Adjustment and Disputes*.

After the Contractor has approved, or approved under protest, the RPR's final estimate, and after the RPR's receipt of the project closeout documentation required in paragraph 90-11, *Contractor Final Project Documentation*, final payment will be processed based on the entire sum, or the undisputed sum in case of approval under protest, determined to be due the Contractor less all previous payments and all amounts to be deducted under the provisions of the contract. All prior partial estimates and payments shall be subject to correction in the final estimate and payment.

If the Contractor has filed a claim for additional compensation under the provisions of Section 50, paragraph 50-16, *Claims for Adjustments and Disputes,* or under the provisions of this paragraph, such claims will be considered by the Owner in accordance with local laws or ordinances. Upon final adjudication of such claims, any additional payment determined to be due the Contractor will be paid pursuant to a supplemental final estimate.

90-10 Construction warranty.

a. In addition to any other warranties in this contract, the Contractor warrants that work performed under this contract conforms to the contract requirements and is free of any defect in equipment, material, workmanship, or design furnished, or performed by the Contractor or any subcontractor or supplier at any tier.

b. This warranty shall continue for a period of one year from the date of final acceptance of the work, except as noted. If the Owner takes possession of any part of the work before final acceptance, this warranty shall continue for a period of one year from the date the Owner takes possession. However, this will not relieve the Contractor from corrective items required by the final acceptance of the project work. Light Emitting Diode emitting diode (LED) light fixtures with the exception of obstruction lighting, must be warranted by the manufacturer for a minimum of four (4) years after date of installation inclusive of all electronics.

c. The Contractor shall remedy at the Contractor's expense any failure to conform, or any defect. In addition, the Contractor shall remedy at the Contractor's expense any damage to Owner real or personal property, when that damage is the result of the Contractor's failure to conform to contract requirements; or any defect of equipment, material, workmanship, or design furnished by the Contractor.

d. The Contractor shall restore any work damaged in fulfilling the terms and conditions of this clause. The Contractor's warranty with respect to work repaired or replaced will run for one year from the date of repair or replacement.

e. The Owner will notify the Contractor, in writing, within seven (7) days after the discovery of any failure, defect, or damage.

f. If the Contractor fails to remedy any failure, defect, or damage within 14 days after receipt of notice, the Owner shall have the right to replace, repair, or otherwise remedy the failure, defect, or damage at the Contractor's expense.

g. With respect to all warranties, express or implied, from subcontractors, manufacturers, or suppliers for work performed and materials furnished under this contract, the Contractor shall: (1) Obtain all warranties that would be given in normal commercial practice; (2) Require all warranties to be executed, in writing, for the benefit of the Owner, as directed by the Owner, and (3) Enforce all warranties for the benefit of the Owner.

h. This warranty shall not limit the Owner's rights with respect to latent defects, gross mistakes, or fraud.

90-11 Contractor Final Project Documentation. Approval of final payment to the Contractor is contingent upon completion and submittal of the items listed below. The final payment will not be approved until the RPR approves the Contractor's final submittal. The Contractor shall:

a. Provide two (2) copies of all manufacturers warranties specified for materials, equipment, and installations.

b. Provide weekly payroll records (not previously received) from the general Contractor and all subcontractors.

c. Complete final cleanup in accordance with Section 40, paragraph 40-08, *Final Cleanup*.

d. Complete all punch list items identified during the Final Inspection.

e. Provide complete release of all claims for labor and material arising out of the Contract.

f. Provide a certified statement signed by the subcontractors, indicating actual amounts paid to the Disadvantaged Business Enterprise (DBE) subcontractors and/or suppliers associated with the project.

g. When applicable per state requirements, return copies of sales tax completion forms.

h. Manufacturer's certifications for all items incorporated in the work.

i. All required record drawings, as-built drawings or as-constructed drawings.

j. Project Operation and Maintenance (O&M) Manual(s).

k. Security for Construction Warranty.

l. Equipment commissioning documentation submitted, if required.

END OF SECTION 90

Part 2 – General Construction Items

Item C-10T General Requirements

10T-1 General. The County shall be supplied at all times with the names and telephone numbers of at least two (2) persons in charge of, or responsible for, the work, who can be reached for emergency work twenty-four (24) hours a day, seven (7) days a week. The Contractor shall notify the Airport and the Engineer at least forty-eight (48) hours prior to the commencement of any phase of the work on the project.

10T-2 Project Schedule, Work Schedule and Time Limitations. Award of contract is based in part on successful acquisition of a federal grant based on the amount of the low bid.

Once grant financing is secured, it is understood that time is of the essence in starting and completing construction. Therefore, the County intends to award the construction contract in a timely manner and the Contractor shall be prepared to meet the following project schedule:

Event	Date
Bid Opening:	In accordance with the Notice to Contractors
Contract Award:	Within 120 days of bid opening
Notice to Proceed:	Within 2 weeks of acceptance of contract documents including bonds and insurance
First Day of Construction:	Within 10 days of the Notice to Proceed

This schedule is tentative, and subject to change. **The dates for Contract Award and Notice to Proceed could be revised based on approval of the contract by the FAA and based on the time required to secure funding from the FAA.**

The Contractor shall submit to the Engineer at the preconstruction meeting (or sooner if possible) a work plan and schedule for accomplishment of all work called for by the contract. The Contractor's schedule shall conform to the above schedule.

10T-3 Time for Performance / Liquidated Damages. Contract – Overall: The work on the project shall begin in accordance with the project schedule in Section 10T-2 after receipt of the "Notice to Proceed" from the Owner and all work shall be completed within **50 Working days** after the starting date set forth therein.

Should the above time schedule not be met, it is agreed that the Contractor shall be liable for and shall pay to the Owner, as fixed, agreed, and liquidated damages and not as a penalty, the sum of **Five Hundred Dollars ($500.00) per day for each and every calendar day** subsequent to the time specified and until the work is completed and accepted.

10T-4 Dust Control. The Contractor's attention is directed to Section 17 of the State Specifications. Full compensation for dust control shall be included in other items of work. Additionally, the Contractor shall pay equal attention to keeping all active airfield pavements free and clear of all dirt, dust, gravel, construction residue, etc. If necessary, the Engineer will instruct the Contractor to clean all active pavements at the close of work each day. Said cleaning operation could include mechanical sweeping, vacuum effort and/or adequate blowers, as necessary. The Contractor's responsibility for Dust Control extends over evenings, weekends, holidays, and any extended non-work periods.

10T-5 Watering. Watering shall conform to the provisions of Section 17 of the State Specifications and these Special Provisions. The Contractor shall furnish all equipment necessary to apply water required in the various items of work. Water shall be applied at the locations, in the amounts and during the hours as directed by the Engineer.

The Contractor shall provide for and pay for his own source of water supply for work on this project. The Contractor shall, at his own expense, provide facilities for conveying the water from the metered source to the point of use. Full compensation for developing and applying water shall be included in other items of work and no additional allowance will be made therefore.

10T-6 Precedence of Contract Documents. The order of precedence of documents shall be:
(1) Rules & Regulations of Federal/State Agencies relating to the source of funds for this project,
(2) Permits from other agencies as may be required by law,
(3) Special Provisions,
(4) Technical Specifications,
(5) Plans, and
(6) General Contract Provisions.

Change orders, addendums, supplemental agreements, and approved revisions to plans and specifications will take precedence over documents listed above. Detailed plans shall have precedence over general plans.

Whenever any conflict appears in any portion of the contract, it shall be resolved by application of the order of precedence, unless determined otherwise by the Engineer. Additionally, with any conflict or inconsistency with contract document, unless instructed otherwise by the Engineer, the Contractor shall assume that the option or alternative that is more expensive, more labor intensive, and/or takes more time to complete, is the option or alternative required. Work required of the plans, either expressed or implied through the understanding of general, industry-standard construction practice, shall be considered as included in this contract.

10T-7 Preconstruction Meeting. Prior to the start of construction, the Engineer will schedule a meeting with the County and Airport representatives, airport tenants and users, and utility companies to coordinate the construction with the Contractor so that no delays will be encountered due to conflicts of operation. The Contractor will be called upon to indicate, at this meeting, the proposed operations to accomplish the work. Prior to, or at the preconstruction meeting, the Contractor shall submit a written schedule of work to the Engineer for approval.

A "Notice to Proceed" will not be issued until the written schedule has been reviewed and approved by the Engineer.

10T-8 Periodic Construction Meetings. Construction progress meetings shall be held **weekly** for the duration of the project. Contractor shall provide a representative at each meeting capable of presenting a detailed discussion regarding construction progress, schedule, cost and time impacts, etc. Subcontractors of significance, with active work either in the previous or the next week, shall likewise have a representative at the construction meeting. Contractor shall provide updated schedule, submittal log, and RFI log before each periodic construction meeting.

10T-9 Submittals. Submittals are required for all material intended for use on this project. Each submittal shall be clearly marked indicating all parameters that identify quality, integrity and capability, including but not limited to size, style, class, color, rating, conforming standard, etc. **Manufactures cut sheets must be clearly marked.** Material mix designs must specifically reference this project, and shall not be more than 6-months old from the date of the start of work on this project.

At Contractor option, submittals can be via electronic format, .pdf. Each submittal shall be complete, color, and marked up as previously described. Electronic file names shall be logical and uniform to allow for easy electronic filing and retrieval, one file per submittal (includes transmittal, cover sheet, and submittal material). Re-submittal file shall be a logical progression of the first submittal, for example: Resubmittal for Submittal 4 could be labeled “Submittal 4.1” or “Submittal 4, rev 1”.

10T-10 Shop Drawings and Calculations. Shop drawings and calculations shall be prepared for all fabricated components delivered to the site. Calculations shall be prepared under the direction of an engineer, registered in the State of California. Shop drawings and calculations will be considered submittals – 6 original, identical copies required.

10T-11 Project Superintendence. A representative of the general contractor shall always be on the project site while work is being performed by any contractor and /or subcontractor force. The general contractor representative shall be of a status and position to direct and control the subcontractor, and to take input and direction from the inspector and forward to the subcontractor.

10T-12 Portable Restroom Facilities. On-site restroom facilities are not available for use by Contractor forces. The Contractor shall provide restroom facilities at quantities and at locations throughout the project as necessary to adequately serve all general contractor and sub-contractor forces working on this project. Portable restroom facilities shall be serviced regularly throughout the duration of the project. Contractor shall assume portable restroom facilities shall be available for twice the contract length.

10T-13 Project Plans. Project plans, entitled:

"REHABILITATE TIE-DOWN APRON", dated February, 2025

10T-14 As-Built Plans. At the start of construction, the Contractor shall be issued a full-size paper set of the project plans marked "As-Built". It is the responsibility of the Contractor to mark up and keep current, this set of As-Built Plans, reflecting actual construction that may be different than what was shown on the plans, and identify any existing facilities (above or below ground) that may have not been accurately shown on the plans. As-Built plans shall be kept current and will be reviewed during each pay request.

10T-15 Posting of Wage Rates. The contractor shall establish and maintain throughout the duration of the project, a project posting bulletin board. The board shall be free standing and shall be established at the primary employee gathering area. The Contractor shall post copies of FAA-provided EEO posters and wage rate sheets from the Contract specifications, and any other pertinent information. The posting board shall provide weather-proof protection of documents for the life of the project.

10T-16 Progress Payments. A schedule for progress payments will be established at the Pre-Construction Conference. It is typical to receive a progress payment every 30 days. On occasion, small projects may have just one progress payment.

In advance of any progress payment, the following will be reviewed:

A. Submittal status.
B. Access control badging (if applicable).
C. As-Built Plans. Contractor is to keep these current.
D. Certified Payroll statements, including benefit statements for the general contractor and all sub-contractors.
E. Dust control and storm water pollution prevention compliance.

The status of these items may impact the progress for periodic progress payments to the Contractor.

10T-17 Construction Survey and Layout, and Documentation. Contractor to perform construction survey and layout as necessary to satisfactorily construct the improvements of this project.

A. Refer to Section 50-07 Construction Layout and Stakes of the FAA General Provisions.

B. The Engineer shall establish necessary horizontal and vertical control.

C. The Contractor is responsible for performing all staking and layout required to construct the improvements.

D. The Contractor shall perform and provide field verification survey of with data presented to the RPR for review. This includes horizontal and vertical for each construction activity, material finished surface, limits of removals, electrical and drainage layout and alignments.

E. Layout and surface verification documentation to be presented to the RPR as a submittal, for review and approval prior to progressing to the next construction activity. Documentation to include .dwg, .xlx, .pdf file formats.

10T-18 Area Lighting. No nighttime operations are anticipated for this contract. If contractor elects to perform night operations during concrete pour days, a lighting plan will be required as a submittal and gain engineer approval.

10T-19 Facilities Duration. In the event the contract requires contractor-provided facilities to support the field operation, the Contactor shall assume the duration of need for said facilities shall be the contract time period plus 50%. This applies to the following, at a minimum:

A. Portable restroom

B. Project field office

C. Delineation

D. Traffic control

E. Access control / perimeter security

F. Area lighting

10T-20 Measurement and Payment. Any costs connected with any of the general requirements outlined in this section including, shall be included in other items of work and no additional measurement or payment (compensation) will be made there for.

END OF ITEM C-10T

Item C-100 Contractor Quality Control Program (CQCP)

100-1 General. Quality is more than test results. Quality is the combination of proper materials, testing, workmanship, equipment, inspection, and documentation of the project. Establishing and maintaining a culture of quality is key to achieving a quality project. The Contractor shall establish, provide, and maintain an effective Contractor Quality Control Program (CQCP) that details the methods and procedures that will be taken to assure that all materials and completed construction required by this contract conform to contract plans, technical specifications and other requirements, whether manufactured by the Contractor, or procured from subcontractors or vendors. Although guidelines are established and certain minimum requirements are specified here and elsewhere in the contract technical specifications, the Contractor shall assume full responsibility for accomplishing the stated purpose.

The Contractor shall establish a CQCP that will:

a. Provide qualified personnel to develop and implement the CQCP.

b. Provide for the production of acceptable quality materials.

c. Provide sufficient information to assure that the specification requirements can be met.

d. Document the CQCP process.

The Contractor shall not begin any construction or production of materials to be incorporated into the completed work until the CQCP has been reviewed and approved by the Resident Project Representative (RPR). No partial payment will be made for materials subject to specific quality control (QC) requirements until the CQCP has been reviewed and approved.

The QC requirements contained in this section and elsewhere in the contract technical specifications are in addition to and separate from the quality assurance (QA) testing requirements. QA testing requirements are the responsibility of the RPR or Contractor as specified in the specifications.

A Quality Control (QC)/Quality Assurance (QA) workshop with the Engineer, Resident Project Representative (RPR), Contractor, subcontractors, testing laboratories, and Owner's representative must be held prior to start of construction. The QC/QA workshop will be facilitated by the Contractor. The Contractor shall coordinate with the Airport and the RPR on time and location of the QC/QA workshop. Items to be addressed, at a minimum, will include:

a. Review of the CQCP including submittals, QC Testing, Action & Suspension Limits for Production, Corrective Action Plans, Distribution of QC reports, and Control Charts.

b. Discussion of the QA program.

c. Discussion of the QC and QA Organization and authority including coordination and information exchange between QC and QA.

d. Establish regular meetings to discuss control of materials, methods and testing.

e. Establishment of the overall QC culture.

100-2 Description of program.

a. General description. The Contractor shall establish a CQCP to perform QC inspection and testing of all items of work required by the technical specifications, including those performed by subcontractors. The CQCP shall ensure conformance to applicable specifications and plans with respect to materials, off-site fabrication, workmanship, construction, finish, and functional performance. The CQCP shall be effective for control of all construction work performed under this Contract and shall specifically include surveillance and tests required by the technical specifications, in addition to other requirements of this section and any other activities deemed necessary by the Contractor to establish an effective level of QC.

b. Contractor Quality Control Program (CQCP). The Contractor shall describe the CQCP in a written document that shall be reviewed and approved by the RPR prior to the start of any production, construction, or off-site fabrication. The written CQCP shall be submitted to the RPR for review and approval at least **10 calendar days** before the CQCP Workshop. The Contractor's CQCP and QC testing laboratory must be approved in writing by the RPR prior to the start of work.

The CQCP shall be organized to address, as a minimum, the following:

1. QC organization and resumes of key staff
2. Project progress schedule
3. Submittals schedule
4. Inspection requirements
5. QC testing plan
6. Documentation of QC activities and distribution of QC reports
7. Requirements for corrective action when QC and/or QA acceptance criteria are not met
8. Material quality and construction means and methods. Address all elements applicable to the project that affect the quality of the pavement structure including subgrade, subbase, base, and surface course. Some elements that must be addressed include, but is not limited to mix design, aggregate grading, stockpile management, mixing and transporting, placing and finishing, quality control testing and inspection, smoothness, laydown plan, equipment, and temperature management plan.

The Contractor must add any additional elements to the CQCP that is necessary to adequately control all production and/or construction processes required by this contract.

100-3 CQCP organization. The CQCP shall be implemented by the establishment of a QC organization. An organizational chart shall be developed to show all QC personnel, their authority, and how these personnel integrate with other management/production and construction functions and personnel.

The organizational chart shall identify all QC staff by name and function, and shall indicate the total staff required to implement all elements of the CQCP, including inspection and testing for each item of work. If necessary, different technicians can be used for specific inspection and testing functions for different items of work. If an outside organization or independent testing laboratory is used for implementation of all or part of the CQCP, the personnel assigned shall be subject to the qualification requirements of paragraphs 100-03a and 100-03b. The organizational chart shall indicate which personnel are Contractor employees and which are provided by an outside organization.

The QC organization shall, as a minimum, consist of the following personnel:

a. Program Administrator. The Contractor Quality Control Program Administrator (CQCPA) must be a full-time employee of the Contractor, or a consultant engaged by the Contractor. The CQCPA must have a minimum of five (5) years of experience in QC pavement construction with prior QC experience on a project of comparable size and scope as the contract.

Included in the five (5) years of paving/QC experience, the CQCPA must meet at least one of the following requirements:

(1) Professional Engineer with one (1) year of airport paving experience.

(2) Engineer-in-training with two (2) years of airport paving experience.

(3) National Institute for Certification in Engineering Technologies (NICET) Civil Engineering Technology Level IV with three (3) years of airport paving experience.

(4) An individual with four (4) years of airport paving experience, with a Bachelor of Science Degree in Civil Engineering, Civil Engineering Technology or Construction.

The CQCPA must have full authority to institute any and all actions necessary for the successful implementation of the CQCP to ensure compliance with the contract plans and technical specifications. The CQCPA authority must include the ability to immediately stop production until materials and/or processes are in compliance with contract specifications. The CQCPA must report directly to a principal officer of the construction firm. The CQCPA may supervise the Quality Control Program on more than one project provided that person can be at the job site within two (2) hours after being notified of a problem.

b. QC technicians. A sufficient number of QC technicians necessary to adequately implement the CQCP must be provided. These personnel must be either Engineers, engineering technicians, or experienced craftsman with qualifications in the appropriate field equivalent to NICET Level II in Civil Engineering Technology or higher, and shall have a minimum of two (2) years of experience in their area of expertise.

The QC technicians must report directly to the CQCPA and shall perform the following functions:

(1) Inspection of all materials, construction, plant, and equipment for conformance to the technical specifications, and as required by paragraph 100-6.

(2) Performance of all QC tests as required by the technical specifications and paragraph100-8.

(3) Performance of tests for the RPR when required by the technical specifications.

Certification at an equivalent level of qualification and experience by a state or nationally recognized organization will be acceptable in lieu of NICET certification.

c. Staffing levels. The Contractor shall provide sufficient qualified QC personnel to monitor each work activity at all times. Where material is being produced in a plant for incorporation into the work, separate plant and field technicians shall be provided at each plant and field placement location. The scheduling and coordinating of all inspection and testing must match the type and pace of work activity. The CQCP shall state where different technicians will be required for different work elements.

100-4 Project progress schedule. Critical QC activities must be shown on the project schedule as required by Section 80, paragraph 80-03, *Execution and Progress*.

100-5 Submittals schedule. The Contractor shall submit a detailed listing of all submittals (for example, mix designs, material certifications) and shop drawings required by the technical specifications. The listing can be developed in a spreadsheet format and shall include as a minimum:

a. Specification item number

b. Item description

c. Description of submittal

d. Specification paragraph requiring submittal

e. Scheduled date of submittal

100-6 Inspection requirements. QC inspection functions shall be organized to provide inspections for all definable features of work, as detailed below. All inspections shall be documented by the Contractor as specified by paragraph 100-9.

Inspections shall be performed as needed to ensure continuing compliance with contract requirements until completion of the particular feature of work. Inspections shall include the following minimum requirements:

a. During plant operation for material production, QC test results and periodic inspections shall be used to ensure the quality of aggregates and other mix components, and to adjust and control mix proportioning to meet the approved mix design and other requirements of the technical specifications. All equipment used in proportioning and mixing shall be inspected to ensure its proper operating condition. The CQCP shall detail how these and other QC functions will be accomplished and used.

b. During field operations, QC test results and periodic inspections shall be used to ensure the quality of all materials and workmanship. All equipment used in placing, finishing, and compacting shall be inspected to ensure its proper operating condition and to ensure that all such operations are in conformance to the technical specifications and are within the plan dimensions, lines, grades, and tolerances specified. The CQCP shall document how these and other QC functions will be accomplished and used.

100-7 Contractor QC testing facility.

a. For projects that include Item P-401, Item P-403, and Item P-404, the Contractor shall ensure facilities, including all necessary equipment, materials, and current reference standards, are provided that meet requirements in the following paragraphs of ASTM D3666, *Standard Specification for Minimum Requirements for Agencies Testing and Inspecting Road and Paving Materials*:

8.1.3 Equipment Calibration and Checks;

8.1.9 Equipment Calibration, Standardization, and Check Records;

8.1.12 Test Methods and Procedures

b. For projects that include P-501, the Contractor shall ensure facilities, including all necessary equipment, materials, and current reference standards, are provided that meet requirements in the following paragraphs of ASTM C1077, Standard Practice for Agencies Testing Concrete and Concrete Aggregates for Use in Construction and Criteria for Testing Agency Evaluation:

7 Test Methods and Procedures

8 Facilities, Equipment, and Supplemental Procedures

100-8 QC testing plan. As a part of the overall CQCP, the Contractor shall implement a QC testing plan, as required by the technical specifications. The testing plan shall include the minimum tests and test frequencies required by each technical specification Item, as well as any additional QC tests that the Contractor deems necessary to adequately control production and/or construction processes.

The QC testing plan can be developed in a spreadsheet fashion and shall, as a minimum, include the following:

a. Specification item number (e.g., P-401)

b. Item description (e.g., Hot Mix Asphalt Pavements)

c. Test type (e.g., gradation, grade, asphalt content)

d. Test standard (e.g., ASTM or American Association of State Highway and Transportation Officials (AASHTO) test number, as applicable)

e. Test frequency (e.g., as required by technical specifications or minimum frequency when requirements are not stated)

f. Responsibility (e.g., plant technician)

g. Control requirements (e.g., target, permissible deviations)

The QC testing plan shall contain a statistically-based procedure of random sampling for acquiring test samples in accordance with ASTM D3665. The RPR shall be provided the opportunity to witness QC sampling and testing.

All QC test results shall be documented by the Contractor as required by paragraph 100-9.

100-9 Documentation. The Contractor shall maintain current QC records of all inspections and tests performed. These records shall include factual evidence that the required QC inspections or tests have been performed, including type and number of inspections or tests involved; results of inspections or tests; nature of defects, deviations, causes for rejection, etc.; proposed remedial action; and corrective actions taken.

These records must cover both conforming and defective or deficient features, and must include a statement that all supplies and materials incorporated in the work are in full compliance with the terms of the contract. Legible copies of these records shall be furnished to the RPR daily. The records shall cover all work placed subsequent to the previously furnished records and shall be verified and signed by the CQCPA.

Contractor QC records required for the contract shall include, but are not necessarily limited to, the following records:

a. Daily inspection reports. Each Contractor QC technician shall maintain a daily log of all inspections performed for both Contractor and subcontractor operations. These technician's daily reports shall provide factual evidence that continuous QC inspections have been performed and shall, as a minimum, include the following:

(1) Technical specification item number and description
(2) Compliance with approved submittals
(3) Proper storage of materials and equipment
(4) Proper operation of all equipment
(5) Adherence to plans and technical specifications
(6) Summary of any necessary corrective actions
(7) Safety inspection.
(8) Photographs and/or video

The daily inspection reports shall identify all QC inspections and QC tests conducted, results of inspections, location and nature of defects found, causes for rejection, and remedial or corrective actions taken or proposed.

The daily inspection reports shall be signed by the responsible QC technician and the CQCPA. The RPR shall be provided at least one copy of each daily inspection report on the work day following the day of record. When QC inspection and test results are recorded and transmitted electronically, the results must be archived.

b. Daily test reports. The Contractor shall be responsible for establishing a system that will record all QC test results. Daily test reports shall document the following information:

(1) Technical specification item number and description
(2) Test designation
(3) Location
(4) Date of test
(5) Control requirements
(6) Test results

(7) Causes for rejection
(8) Recommended remedial actions
(9) Retests

Test results from each day's work period shall be submitted to the RPR prior to the start of the next day's work period. When required by the technical specifications, the Contractor shall maintain statistical QC charts. When QC daily test results are recorded and transmitted electronically, the results must be archived.

100-10 Corrective action requirements. The CQCP shall indicate the appropriate action to be taken when a process is deemed, or believed, to be out of control (out of tolerance) and detail what action will be taken to bring the process into control. The requirements for corrective action shall include both general requirements for operation of the CQCP as a whole, and for individual items of work contained in the technical specifications.

The CQCP shall detail how the results of QC inspections and tests will be used for determining the need for corrective action and shall contain clear rules to gauge when a process is out of control and the type of correction to be taken to regain process control.

When applicable or required by the technical specifications, the Contractor shall establish and use statistical QC charts for individual QC tests. The requirements for corrective action shall be linked to the control charts.

100-11 Inspection and/or observations by the RPR. All items of material and equipment are subject to inspection and/or observation by the RPR at the point of production, manufacture or shipment to determine if the Contractor, producer, manufacturer or shipper maintains an adequate QC system in conformance with the requirements detailed here and the applicable technical specifications and plans. In addition, all items of materials, equipment and work in place shall be subject to inspection and/or observation by the RPR at the site for the same purpose.

Inspection and/or observations by the RPR does not relieve the Contractor of performing QC inspections of either on-site or off-site Contractor's or subcontractor's work.

100-12 Noncompliance.

a. The Resident Project Representative (RPR) will provide written notice to the Contractor of any noncompliance with their CQCP. After receipt of such notice, the Contractor must take corrective action.

b. When QC activities do not comply with either the CQCP or the contract provisions or when the Contractor fails to properly operate and maintain an effective CQCP, and no effective corrective actions have been taken after notification of non-compliance, the RPR will recommend the Owner take the following actions:

(1) Order the Contractor to replace ineffective or unqualified QC personnel or subcontractors and/or

(2) Order the Contractor to stop operations until appropriate corrective actions are taken.

METHOD OF MEASUREMENT

100-13 Basis of measurement and payment. The work of this section is incidental to the various items of work that require quality control. No specific / direct / individual measurement for this effort will be made.

BASIS OF PAYMENT

100-14 Payment. The work of this section is incidental to the various items of work that require quality control. No specific / direct / individual payment for this effort will be made.

REFERENCES

The publications listed below form a part of this specification to the extent referenced. The publications are referred to within the text by the basic designation only.

National Institute for Certification in Engineering Technologies (NICET)

ASTM International (ASTM)

ASTM C1077	Standard Practice for Agencies Testing Concrete and Concrete Aggregates for Use in Construction and Criteria for Testing Agency Evaluation
ASTM D3665	Standard Practice for Random Sampling of Construction Materials
ASTM D3666	Standard Specification for Minimum Requirements for Agencies Testing and Inspecting Road and Paving Materials

END OF ITEM C-100

Item C-104T Airport Safety and Security

104T-1 Description.

The purpose of this section is to bring to the attention of the Contractor special safety regulations which are required when work is being performed on, or adjacent to operational areas of an airport.

A. Operational Safety on Airports During Construction

The Contractor's attention is directed to FAA AC-150/5370-2G, Operational Safety on Airports during Construction, included in the appendix of this contract book. All provisions, limitations, restrictions, etc., identified and included in this advisory circular are made a part of this specification book and the contractors' overall obligations for airport safety and security through reference here.

B. Construction Safety Phasing Plan (CSPP)

The Contractor's attention is directed to the Construction Safety Phasing Plan (CSPP), prepared specifically for this project, included in the appendix of this contract book. All provisions, limitations, restrictions, etc., identified and included in this plan are made a part of this specification book and the contractors' overall obligations for airport safety and security through reference here.

104T-2 Storage of Equipment and Materials.

All equipment and materials shall be stored in the designated area identified on the project layout plan and the Construction Safety Phasing Plans.

104T-3 Operation of Equipment.

Each piece of self-powered equipment or vehicle shall carry, displayed in full view above the vehicle or piece of equipment, a 3-foot square flag consisting of a checkered pattern of international orange and white squares of not less than one foot on each side. Any vehicle operating within the movement area during the hours of darkness should be equipped with a flashing amber dome-type light.

The Contractor shall seek and gain specific approval for operations of any equipment, cranes, booms, lifts, in excess of 20 feet in height. Work must be scheduled a minimum of 7 days in advance to allow for review of the proposed activity and issuance of any public notifications, NOTAM's, etc.

104T-4 Project Access.

A. Refer to the project layout plan and CSPP for the contractor point of access to the airport. All vehicles must use haul routes designated by the Engineer to gain access to the various locations of work. Any deviation from designated haul routes must be approved, in advance, by the Engineer. The speed limit of 15 mph, maximum, shall be observed by all construction vehicles on the airport.

B. Aircraft taxiing, taking off or landing, emergency vehicles, or airport vehicles shall have right-of-way over all construction vehicles. Active aircraft maneuvering areas shall be kept clean of dirt, sand, oil, and other foreign material and debris at all times.

C. The contractor is encouraged to implement traffic control measures that will serve the effort through all levels of construction activity. The path of travel requires flaggers at critical locations, with additional flaggers on material haul / import days.

104T-5 Limitations on Construction.

A. Any open flame, welding, or torch-cutting operations are prohibited unless adequate fire and safety precautions are approved by the Engineer prior to commencement of said operations.

B. Any open trenches, excavations and stockpiled material at the construction site should be prominently marked with red flags and/or cones and lighted by light units acceptable to the Engineer during hours of restricted visibility and/or darkness.

104T-6 Delineation of Work Areas.

A. The Contractor shall be responsible for clearly delineating the limits, or phases, of his operation. Delineation shall be installed in accordance with the typical delineation details shown on the plans. Delineation shall be installed at critical locations that facilitate pilot judgment regarding active movement areas. Delineation left overnight shall be clearly and adequately lighted. Batteries shall be replaced monthly.

B. In addition to the work area, contractor shall be responsible for delineating the modified operations area on the apron during construction. Refer to the Project Layout Plan for delineation detail and overall length of delineation required.

104T-7 Air-Band Radio.

The Contractor's foreman shall have an air-band radio in his possession at all times while Contractor forces are on the airfield. The radio must be tuned to a frequency of 122.8 mhz. The radio shall have adequate battery capacity to assure full operation throughout the work period. The foreman shall be in a position to hear the radio and to direct workers in his charge, as necessary.

104T-8 Security.

A. Throughout the duration of the project, the security of the airport provided by the perimeter fence and access gates shall remain equal to the pre-project condition. The integrity of the perimeter fence shall remain in-tact during construction.

B. Contractor to practice automatic gate protocol:

a. Contractor clear gate induction loops so gate can close, wait, and ensure gate contractor clear gate induction loops so gate can close, wait, and ensure gate closes with no other unauthorized user enters the airport.

b. Contractor is fully responsible for vehicles, equipment, or user that enter a gate contractor is fully responsible for vehicles, equipment, or user that enter a gate behind him.

c. Contractor must be prepared to deny access to anyone unauthorized for airport contractor must be prepared to deny access to anyone unauthorized for airport access.

d. Others with access authority not affiliated with the project will wait until your others with access authority not affiliated with the project will wait until your movement is complete. Do not attempt to accommodate.

C. All vehicles and equipment entering the airport shall be labeled with the name of all vehicles and equipment entering the airport shall be labeled with the name of the firm on at least two sides of the vehicle.

D. All vehicles and equipment shall be equipped with an orange and white checkered safety all vehicles and equipment shall be equipped with an orange and white checkered safety flag (daytime) or rotating amber beacon (daytime or night time), at the highest point of the vehicle.

104T-9 Contractor Yard.

The Contractor is responsible for the establishment, maintenance, and general up-keep of the contractor yard(s) and material storage area(s). The yard shall be kept neat and tidy, with all material stored in a clean, safe manner. The airport, the engineer, and any other project or airport representatives cannot be held responsible for loss, damage, or any other acts of destruction or vandalism. It is up to the contractor to fence his own yard. The contractor shall establish his own solid waste recycle / disposal program.

104T-10 Safety Plan Compliance Document.

The Contractor shall comply with the Construction Safety Phasing Plan (CSPP), prepared specifically for this project, included in the appendix of this contract book. In addition, the contractor must prepare a Safety Plan Compliance Document (SPCD) that outlines how the contractor intends to comply with the CSPP requirements. As part of the Safety Plan Compliance Document, the contractor is shall Prepare, distribute, collect and maintain Third-Party Provider letters acknowledging the safety aspects and requirements of the project and assurance of compliance.

METHOD OF MEASUREMENT

104T-11 Basis of measurement and payment.

Measurement of Airport Safety and Security shall be on a lump sum basis for performing and complying with the work and requirements of this section. Measurement will occur in straight-line percentages, based on the overall progress of construction.

BASIS OF PAYMENT

104T-12 Payment.

Payment for Airport Safety and Security shall be at the contract lump sum price for performing and complying with the work and requirements of this section. This price shall be full compensation for furnishing all materials and for all preparation, assembly, and installation of these materials, and for all labor, equipment, tools, and incidentals necessary. The Contractor's bid price for this item shall not exceed five percent (5%) of the total amount of the bid. In the event the project includes multiple bid schedules with multiple bid items for the work in this section, the maximum amount of each bid item shall not exceed five percent (5%) of the bid schedule total.

Payment will be made under:

BID ITEM NO.	DESCRIPTION	UNIT
2	Airport Safety and Security (5% Max)	Lump Sum

Such payments as described shall be full compensation for furnishing all materials. labor, equipment, tools, and incidentals necessary to complete these items of the work.

END OF ITEM C-104T

Item C-105 Mobilization

105-1 Description. This item of work shall consist of, but is not limited to, work and operations necessary for the movement of personnel, equipment, material and supplies to and from the project site for work on the project except as provided in the contract as separate pay items.

105-2 Mobilization limit. Mobilization shall be limited to **eight percent (8%)** of the total project cost.

105-3 Posted notices. Prior to commencement of construction activities, the Contractor must post the following documents in a prominent and accessible place where they may be easily viewed by all employees of the prime Contractor and by all employees of subcontractors engaged by the prime Contractor: Equal Employment Opportunity (EEO) Poster "Equal Employment Opportunity is the Law" in accordance with the Office of Federal Contract Compliance Programs Executive Order 11246, as amended; Davis Bacon Wage Poster (WH 1321) - DOL "Notice to All Employees" Poster; and Applicable Davis-Bacon Wage Rate Determination. These notices must remain posted until final acceptance of the work by the Owner.

Links to the posters available at: https://www.faa.gov/airports/engineering/

105-4 Engineer/RPR field office. The Contractor shall provide dedicated space for the use of the engineer, RPR, and inspectors, as a field office for the duration of the project. This space shall be located conveniently near the construction and shall be separate from any space used by the Contractor. The Contractor shall furnish water, sanitary facilities, heat, air conditioning, Wireless internet, and utility electricity (no portable generator). The Field Office shall comply with the requirements of Section 8 – Facilities for Agency Personnel, Greenbook Specification, Class "A", The designated space, furniture, and facilities shall be for use by the Owner's on-site representative.

A. It is the Contractors responsibility for establishing, maintaining, and paying for associated utility service (electricity and wireless internet) for the duration of the project.

B. Contractor-provided Field Office shall include conference table and chairs for up to 10 attendees at the periodic progress meetings.

C. Chemical toilet adjacent to field office is acceptable.

Contractor to provide weekly cleaning including solid waste disposal.

105-5 Pothole Existing Facilities. Not anticipated for this project.

METHOD OF MEASUREMENT

105-6 Basis of measurement and payment. Based upon the contract lump sum price for "Mobilization" partial payments will be allowed as follows:

a. With first pay request, 25%.

b. When 25% or more of the original contract is earned, an additional 25%.

c. When 50% or more of the original contract is earned, an additional 40%.

d. After Final Inspection, Staging area clean-up and delivery of all Project Closeout materials as required by Section 90, paragraph 90-11, Contractor Final Project Documentation, the final 10%.

BASIS OF PAYMENT

105-6 Payment will be made under:

Payment will be made under:

BID ITEM NO.	DESCRIPTION	UNIT
1	Mobilization (8% Max)	Lump Sum

This price shall be full compensation for furnishing all materials and for all preparation, assembly, and installation of these materials, and for all labor, equipment, tools, and incidentals necessary. The Contractor's bid price for Mobilization shall not exceed eight percent (8%) of the total amount of the bid. In the event the project includes multiple bid schedules with multiple Mobilization bid items, the maximum amount of each Mobilization bid item shall not exceed eight percent (8%) of the bid schedule total. Payments made for mobilization will be excluded from consideration in determining compensation under changed conditions.

REFERENCES

The publications listed below form a part of this specification to the extent referenced. The publications are referred to within the text by the basic designation only.

Office of Federal Contract Compliance Programs (OFCCP)

Executive Order 11246, as amended

EEOC-P/E-1 – Equal Employment Opportunity is the Law Poster

United States Department of Labor, Wage and Hour Division (WHD)

WH 1321 – Employee Rights under the Davis-Bacon Act Poster

END OF ITEM C-105

Part 3 – Sitework
Item P-101 Preparation/Removal of Existing Pavements

DESCRIPTION

101-1 This item shall consist of preparation of existing pavement surfaces. The work shall be accomplished in accordance with these specifications and the applicable plans. Specifically, this item includes:

A. Cleaning, routing, filling, and sealing cracks on existing asphalt pavement.
B. Pavement Marking Removal.
C. Removal and off-site disposal of waste material generated through removal efforts.
D. Removal and Re-installation of aircraft tie-down anchors and chains to facilitate the seal coat effort.

EQUIPMENT AND MATERIALS

101-2.1 All equipment and materials shall be specified here and in the following paragraphs or approved by the Resident Project Representative (RPR). The equipment shall not cause damage to the pavement to remain in place.

101-2.2 Tie-Down Hardware. When re-installing the existing tie-down cables and chains, the contractor shall purchase and provide the following hardware:

A. Thimble and cable clamp. Thimbles and cable clamps shall be galvanized steel, and shall be compatible with the cable diameter.
B. Tie-Down Chain Shackle. Shackles shall be galvanized ½" threaded bolt-type chain shackle.

CONSTRUCTION

101-3.1 Removal of existing pavement. (Not Used)

101-3.2 Remove and Re-install Aircraft Tie-Down Cables and Chains. Where designated on the plans, contractor shall remove the existing tie-down cables and chains before application of P-608 Asphalt Emulsion Seal Coat. After the seal coat has cured, the tie-down cable and chains should be re-installed using new hardware (thimbles, cable clamps, as shown on the details on the plans, including:

A. Thimbles. Each end of each cable shall include a galvanized steel thimble installed around the anchor rod / hoop.
B. Cable Clamps. Each end of the tie-down cables shall include two cable clamps compatible with the cable diameter.
C. Tie-Down Chain Shackle. Each tie-down chain shall be re-installed with new galvanized ½" threaded bolt-type chain shackle to secure the chain to the tie-down cable.

Contractor shall dispose the old hardware that is intended to be replaced with the new hardware.

101-3.3 Removal of Foreign Substances/contaminates prior to seal-coat or remarking. Removal of foreign substances/contaminates from existing pavement that will affect the bond of the new treatment shall consist of removal of rubber, fuel spills, oil, crack sealer, and other foreign substances from the surface of the pavement. Areas that require removal are designated on the plans and as directed by the RPR in the field during construction.

high-pressure water, cold milling, or sandblasting may be used. Removal methods used shall not cause major damage to the pavement, or to any structure or utility within or adjacent to the work area. Major damage is defined as changing the properties of the pavement, removal of asphalt causing the aggregate to ravel, or removing pavement over 1/8 inch (3 mm) deep. If it is deemed by the RPR that damage to the existing pavement is caused by operational error, such as permitting the application method to dwell in one location for too long, the Contractor shall repair the damaged area without compensation and as directed by the RPR.

Removal of foreign substances shall not proceed until approved by the RPR. Water used for high-pressure water equipment shall be provided by the Contractor at the Contractor's expense. No material shall be deposited on the pavement shoulders. All wastes shall be disposed of off airport property, in a legal manner, at the contractor's expense.

101-3.3.2T Removal of Existing Pavement Markings. Where designated on the plans, contractor shall remove existing pavement markings to 70%, removing loose chips, creating an acceptable surface before P-608 application. Marking removal shall be by means a high-pressure water unit with vacuum waste collection capabilities.

A small test area shall be performed with adjustments in water pressure as necessary to assure removal of pavement markings to the designated level while limiting damage to the pavement surface, in the presence of the RPR. All material collected shall be loaded into street-legal weighted tank trucks, hauled off the airport, and legally disposed. The Contractor shall provide copies of disposal receipts for all loads hauled off-site. No material shall be dumped on-site. The cost for removal, hauling, and all disposal fees shall be paid by the contractor.

101-3.4 Concrete spall or failed asphaltic concrete pavement repair. (Not Used)

101-3.5 Cold milling. (Not Used)

101-3.6. Preparation of asphalt pavement surfaces prior to surface treatment. Existing asphalt pavements to be treated with a surface treatment shall be prepared as follows:

a. Remove oil or grease that has not penetrated the asphalt pavement by scrubbing with a detergent and washing thoroughly with clean water. After cleaning, treat these areas with an oil spot primer.

b. Clean pavement surface immediately prior to placing the surface treatment so that it is free of dust, dirt, grease, vegetation, oil or any type of objectionable surface film.

101-3.7 Maintenance. The Contractor shall perform all maintenance work necessary to keep the pavement in a satisfactory condition until the full section is complete and accepted by the RPR. The surface shall be kept clean and free from foreign material. The pavement shall be properly drained at all times. If cleaning is necessary or if the pavement becomes disturbed, any work repairs necessary shall be performed at the Contractor's expense.

101-3.8 Preparation of Joints in Rigid Pavement prior to resealing. (Not Used)

101-3.9 Preparation of Cracks in Flexible Pavement prior to sealing. Prior to application of sealant material, clean and dry the joints of all scale, dirt, dust, old sealant, curing compound, moisture and other foreign matter. The Contractor shall demonstrate, in the presence of the RPR, that the method used cleans the cracks and does not damage the pavement.

101-3.9.1 Preparation of Crack. For cracks between ¼" and ¾" wide, the cracks shall be widened with a router or random crack saw by removing a minimum of 1/16 inch (2 mm) from each side of crack. Immediately before sealing, cracks will be blown out with a hot air lance combined with oil and water-free compressed air.

101-3.9.2 Removal of Existing Crack Sealant. Existing sealants will be removed by routing. Following routing any remaining debris will be removed by use of a hot lance combined with oil and water-free compressed air.

101-3.9.3 Crack Sealant. Crack sealant material and installation will be in accordance with Item P-605.

METHOD OF MEASUREMENT

101-4.1 Crack Seal. The unit of measurement for crack seal on existing asphalt surface shall be the number of lineal feet of cracks that have been cleaned, prepared, routed, filled, and sealed, as measured in the field.

101-4.2 Remove Pavement Markings. The unit of measurement for pavement marking removal shall be the square foot, successfully obliterated to the percentage identified in this section, with full passage of the removal machine / equipment, for an overall dimensioned area, length by width, as measured in the field.

101-4.3 Uninstall & Re-Install Tie Down Cables and Chains. The unit of measurement for uninstalling & re-installing tie down cables and chains with new hardware shall on a lump sum basis for performing and complying

with the work and requirements described in this section. This item includes purchasing new hardware components, and disposing the old hardware, described in this section.

BASIS OF PAYMENT

101-5.1 Payment. Payment shall be made at contract unit price for the unit of measurement as specified above. This price shall be full compensation for furnishing all materials and for all preparation, hauling, and placing of the material and for all labor, equipment, tools, and incidentals necessary to complete the items in this section.

Payment will be made under:

BID ITEM NO.	DESCRIPTION	UNIT
3	Uninstall & Re-Install Tie Down Cables and Chains	Lump Sum
4	Remove Pavement Markings	Square Foot
5	Crack Seal	Linear Foot

REFERENCES

The publications listed below form a part of this specification to the extent referenced. The publications are referred to within the text by the basic designation only.

Advisory Circulars (AC)

AC 150/5380-6 Guidelines and Procedures for Maintenance of Airport Pavements.

ASTM International (ASTM)

ASTM D6690 Standard Specification for Joint and Crack Sealants, Hot Applied, for Concrete and Asphalt Pavements

END OF ITEM P-101

Part 8– Surface Treatments
Item P-608 Emulsified Asphalt Seal Coat

DESCRIPTION

608-1.1 This item shall consist of the application of a emulsified asphalt surface treatment composed of an emulsion of natural and refined asphalt materials, water and a polymer additive, for taxiways and runways with the application of a suitable aggregate to maintain adequate surface friction; and airfield secondary and tertiary pavements including low-speed taxiways, shoulders, overruns, roads, parking areas, and other general applications with or without aggregate applied as designated on the plans. The terms seal coat, asphalt sealer, and asphalt material are interchangeable throughout this specification. The term emulsified asphalt means an emulsion of natural and refined asphalt materials.

MATERIALS

608-2.1 Aggregate. The aggregate material shall be a dry, clean, dust and dirt free, sound, durable, angular shaped manufactured specialty sand, such as that used as an abrasive, with a Mohs hardness of 6 to 8. The Contractor shall submit the specialty sand manufacturer's technical data and a manufacturer's Certificate of Analysis (COA) indicating that the specialty sand meets the requirements of the specification to the RPR prior to start of construction. The sand must be approved for use by the RPR and shall meet the following gradation limits when tested in accordance with ASTM C136 and ASTM C117:

Aggregate Material Gradation Requirements[1]

Sieve Designation (square openings)	Individual Percentage Retained by Weight
No. 10 (2.00 mm)	0
No. 14 (1.41 mm)	0-4
No. 16 (1.18 mm)	0-8
No. 20 (850 µm)	0-35
No. 30 (600 µm)	20-50
No. 40 (425 µm)	10-45
No. 50 (300 µm)	0-20
No. 70 (212 µm)	0-5
No. 100 (150 µm)	0-2
No. 200 (75 µm)	0-2

[1] Locally available sand or abrasive material that is slightly outside of the gradation requirements may be approved by the RPR with concurrence by the seal coat manufacturer for the use of locally available sand or abrasive material. The RPR and manufacturer's field representative should verify acceptance during application of Control strips indicated under paragraph 608-3.2.

The Contractor shall provide a certification showing particle size analysis and properties of the material delivered for use on the project. The Contractor's certification may be subject to verification by testing the material delivered for use on the project.

608-2.2 Asphalt Emulsion. The asphalt emulsion shall meet the properties in the following table:

Concentrated Asphalt Emulsion Properties

Properties	Specification	Limits
Viscosity, Saybolt Furol at 77°F (25°C)	ASTM D7496	20 – 100 seconds
Residue by Distillation or Evaporation	ASTM D6997 or ASTM D6934	57% minimum
Sieve Test	ASTM D6933	0.1% maximum
24-hour Stability	ASTM D6930	1% maximum
5-day Settlement Test	ASTM D6930	5.0% maximum
Particle Charge [1]	ASTM D7402	Positive 6.5 maximum pH

[1] pH may be used in lieu of the particle charge test which is sometimes inconclusive in slow setting, asphalt emulsions.

The asphalt material base residue shall contain not less than 20% gilsonite, or uintaite and shall not contain any tall oil pitch or coal tar material and shall contain no less than one percent (3%) polymer.

Tests on Residue from Distillation or Evaporation

Properties	Specification	Limits
Viscosity at 275°F (135°C)	ASTM D4402	1750 cts maximum
Solubility in 1, 1, 1 trichloroethylene	ASTM D2042	97.5% minimum
Penetration	ASTM D5	50 dmm maximum
Asphaltenes	ASTM D2007	15% minimum
Saturates	ASTM D2007	15% maximum
Polar Compounds	ASTM D2007	25% minimum
Aromatics	ASTM D2007	15% minimum

The asphalt emulsion, when diluted in the volumetric proportion of two parts concentrated asphalt material to one part hot water shall have the following properties:

Two-to-One Dilution Emulsion Properties

Properties	Specification	Limits
In Ready-to-Apply Form, two parts concentrate to one part water, by volume		
Viscosity, Saybolt Furol at 77°F (25°C)	ASTM D7496	5 – 50 seconds
Residue by Distillation or Evaporation	ASTM D6997 or ASTM D6934	38% minimum
Pumping Stability		Pass

The Contractor shall provide a copy of the manufacturer's Certificate of Analysis (COA) for the emulsified asphalt delivered to the project. If the asphalt emulsion is diluted at other than the manufacturer's facility, the Contractor shall provide a supplemental COA from an independent laboratory verifying the asphalt emulsion properties.

The COA shall be provided to and approved by the RPR before the emulsified asphalt is applied. The furnishing of the vendor's certified test report for the asphalt material shall not be interpreted as a basis for final acceptance. The manufacturer's COA may be subject to verification by testing the material delivered for use on the project.

The asphalt material storage and handling temperature shall be between 50°F - 160°F (10°C - 70°C) and the material shall be protected from freezing, or whenever outside temperature drops below 40°F (4°C) for prolonged time periods.

Contractor shall provide a list of airport pavement projects, exposed to similar climate conditions, where this product has been successfully applied within at least 5 years of the project.

608-2.3 Water. Water used in mixing or curing shall be from potable water sources. Other sources shall be tested in accordance with ASTM C1602 prior to use. Water used in making and diluting the emulsion shall be potable, with a maximum hardness of 90ppm calcium and 15ppm magnesium; deleterious iron, sulfates, and phosphates maximum 7ppm, and less than 1ppm of organic byproducts. Water shall be a minimum of 140°F (60°C) prior to adding to emulsion.

608-2.4 Polymer. The polymer shall meet the properties in the following table:

Polymer Properties

Properties	Limits
Solids Content	47% to 65%, Percent by Weight
Weight	8.0 to 9.0 pounds/gallon (1.07 to 1.17 kg/L)
pH	3.0 to 8.0
Particle Charge	Nonionic/Cationic
Mechanical Stability	Excellent
Film Forming Temperature, °C	+5°C, minimum
Tg, °C	22°C, maximum

The manufacturer shall provide a copy of the Certificate of Analysis (COA) for the polymer used in the seal coat; and the Contractor shall include the COA with the emulsified asphalt COA when submitting to the RPR.

608-2.5 Seal Coat with Aggregate. The Contractor shall submit friction test data from no less than one of the airport projects identified under 608-2.2. The test data must be from the same project and include technical details on application rates, aggregate rates, and point of contact at the airport to confirm use and success of sealer with aggregate.

Friction test data in accordance with AC 150/5320-12, at 40 or 60 mph (65 or 95 km/h) wet, must include as a minimum; the friction value prior to sealant application; two values, between 24 and 96 hours after application, with a minimum of 24 hours between tests; and one value between 180 days and 360 days after the application. The results of the tests between 24 and 96 hours shall indicate friction is increasing at a rate to obtain similar friction value of the pavement surface prior to application, and the long-term

test shall indicate no apparent adverse effect with time relative to friction values and existing pavement surface.

Seal coat material submittal without required friction performance will not be approved. Friction tests performed on this project cannot be used as a substitute of this requirement.

COMPOSITION AND APPLICATION RATE

608-3.1 Application Rate. The approximate amounts of materials per square yard (square meter) for the asphalt surface treatment shall be as provided in the table for the treatment area(s) at the specified dilution rate(s) as noted on the plans. The actual application rates will vary within the range specified to suit field conditions and will be recommended by the manufacturer's representative and approved by the RPR from the test area/sections evaluation.

Application Rate

Dilution Rate	Quantity of Emulsion gal/yd^2	Quantity of Aggregate lb/yd^2
2:1	0.20-0.22	0.30-0.40

608-3.2 Control areas and control strips. Prior to full application, the control strip must be accepted by the RPR. A qualified manufacturer's representative shall be present in the field to assist the Contractor in applying control areas and/or control strips to determine the appropriate application rate of both emulsion and aggregate to be approved by the RPR.

a. For taxiway, taxilane and apron surfaces. Prior to full application, the Contractor shall place test areas at varying application rates as recommended by the Contractor's manufacturer's representative to determine appropriate application rate(s). The test areas will be located on representative section(s) of the pavement to receive the asphalt surface treatment designated by the RPR.

b. For runway and high-speed exit taxiway surfaces. N/A.

CONSTRUCTION METHODS

608-4.1 Worker safety. The Contractor shall obtain a Safety Data Sheet (SDS) for both the asphalt emulsion product and sand and require workmen to follow the manufacturer's recommended safety precautions.

608-4.2 Weather limitations. The asphalt emulsion shall be applied only when the existing pavement surface is dry and when the weather is not foggy, rainy, or when the wind velocity will prevent the uniform application of the material. No material shall be applied in strong winds that interfere with the uniform application of the material(s), or when dust or sand is blowing or when rain is anticipated within eight (8) hours of application completion. The atmospheric temperature and the pavement surface temperature shall both be at, or above 60°F (16°C) and rising. Seal coat shall not be applied when pavement temperatures are expected to exceed 130ºF within the subsequent 72 hours if traffic will be opened on pavement within those 72 hours. During application, account for wind drift. Cover existing buildings, structures, runway edge lights, taxiway edge lights, informational signs, retro-reflective marking and in-pavement duct markers as necessary to protect against overspray before applying the emulsion. Should emulsion get on any light or marker fixture, promptly clean the fixture. If cleaning is

not satisfactory to the RPR, the Contractor shall replace any light, sign or marker with equivalent equipment at no cost to the Owner.

608-4.3 Equipment and tools. The Contractor shall furnish all equipment, tools, and machinery necessary for the performance of the work.

a. Pressure distributor. The emulsion shall be applied with a manufacturer-approved computer rate-controlled asphalt distributor. The equipment shall be in good working order and contain no contaminants or diluents in the tank. Spray bar tips must be clean, free of burrs, and of a size to maintain an even distribution of the emulsion. Any type of tip or pressure source is suitable that will maintain predetermined flow rates and constant pressure during the application process with application speeds under eight (8) miles per hour (13 km per hour) or seven hundred (700) feet per minute (213 m per minute). The equipment will be tested under pressure for leaks and to ensure proper set-up before use. The Contractor will provide verification of truck set-up (via a test-shot area), including but not limited to, nozzle tip size appropriate for application per nozzle manufacturer, spray-bar height and pressure and pump speed appropriate for the viscosity and temperature of sealer material, evidence of triple-overlap spray pattern, lack of leaks, and any other factors relevant to ensure the truck is in good working order before use.

The distributor truck shall be equipped with a 12-foot (3.7-m), minimum, spray bar with individual nozzle control. The distributor truck shall be capable of specific application rates in the range of 0.05 to 0.25 gallons per square yard (0.15 to 0.80 liters per square meter). These rates shall be computer-controlled rather than mechanical. The distributor truck shall have an easily accessible thermometer that constantly monitors the temperature of the emulsion, and have an operable mechanical tank gauge that can be used to cross-check the computer accuracy.

The distributor truck shall effectively heat and mix the material to the required temperature prior to application in accordance with the manufacturer's recommendations.

The distributor shall be equipped with a hand sprayer to spray the emulsion in areas not accessible to the distributor truck.

b. Aggregate spreader. The asphalt distributor truck will be equipped with an aggregate spreader mounted to the distributor truck that can apply sand to the emulsion in a single pass operation without driving through wet emulsion. The aggregate spreader shall be equipped with a variable control system capable of uniformly distributing the sand at the specified rate at varying application widths and speeds. The aggregate spreader must be adjusted to produce an even and accurate application of specified aggregate. Prior to any seal coat application, the aggregate spreader will be calibrated onsite to ensure acceptable uniformity of spread. The RPR will observe the calibration and verify the results. The aggregate spreader will be re-calibrated each time the aggregate rate is changed either during the application of test strips or production. The Contractor may consult the seal coat manufacturer representative for procedure and guidance. The sander shall have a minimum hopper capacity of 3,000 pounds (1361 kg) of sand. Push-type hand sanders will be allowed for use around lights, signs and other obstructions, if necessary.

c. Power broom/blower. A power broom and/or blower shall be provided for removing loose material from the surface to be treated.

d. Equipment calibration. Asphalt distributors must be calibrated within the same construction season in accordance with ASTM D2995. The Contractor must furnish a current calibration certification for the asphalt distributor truck from any State or other agency as approved by the RPR.

608-4.4 Preparation of asphalt pavement surfaces. Clean pavement surface immediately prior to placing the seal coat so that it is free of dust, dirt, grease, vegetation, oil or any type of objectionable

surface film. Remove oil or grease from the asphalt pavement by scrubbing with a detergent, washing thoroughly with clean water, and then treat these areas with a spot primer.

608-4.5 Emulsion mixing. The application emulsion shall be obtained by blending asphalt material concentrate, water and polymer, if specified. Always add heated water to the asphalt material concentrate, never add asphalt material concentrate to heated water. Mix one part heated water to two parts asphalt material concentrate, by volume.

Add 3% polymer, by volume, to the emulsion mix. If the polymer is added to the emulsion mix at the plant, submit weight scale tickets to the RPR. As an option, the polymer may be added to the emulsion mix at the job site provided the polymer is added slowly while the asphalt distributor truck circulating pump is running. The mix must be agitated for a minimum of 15 minutes or until the polymer is mixed to the satisfaction of the RPR.

608-4.6 Application of asphalt emulsion. The asphalt emulsion shall be applied using a pressure distributor upon the properly prepared, clean and dry surface at the application rate recommended by the manufacturer's representative and approved by the RPR from the test area/sections evaluation for each designated treatment area. The asphalt emulsion should be applied at a temperature between 130°F (54°C) and 160°F (70°C) or in accordance with the manufacturer's recommendation.

If low spots and depressions greater than 1/2 inch (12 mm) in depth in the pavement surface cause ponding or puddling of the applied materials, the pavement surface shall be lightly broomed with a broom or brush type squeegee until the pavement surface is free of any pools of excess material.

During all applications, the surfaces of adjacent structures shall be protected to prevent their being spattered or marred.

608-4.7 Application of aggregate material. Immediately following the application of the asphalt emulsion, friction sand at the rate recommended by the manufacturer's representative and approved by the RPR from the test area/sections evaluation for each designated application area, shall be spread uniformly over the asphalt emulsion in a single-pass operation simultaneous with the sealer application. The aggregate shall be spread to the same width of application as the asphalt material and shall not be applied in such thickness as to cause blanketing.

Sprinkling of additional aggregate material, and spraying additional asphalt material over areas that show up having insufficient cover or bitumen, shall be done by hand whenever necessary. In areas where hand work is necessitated, the sand shall be applied before the sealant begins to break.

Minimize aggregate from being broadcast and accumulating on the untreated pavement adjacent to an application pass. Prior to the next application pass, the Contractor shall clean areas of excess or loose aggregate and remove from project site.

QUALITY CONTROL (QC)

608-5.1 Manufacturer's representation. The manufacturer's representative knowledgeable of the material, procedures, and equipment described in the specification is responsible to assist the Contractor and RPR in determining the appropriate application rates of the emulsion and aggregate, as well as recommendations for proper preparation and start-up of seal coat application. Documentation of the manufacturer representative's experience and knowledge for applying the seal coat product shall be furnished to the RPR a minimum of 10 work days prior to placement of the control strips. The cost of the manufacturer's representative shall be included in the Contractor's bid price.

608-5.2 Contractor qualifications. The Contractor shall provide documentation to the RPR that the seal coat Contractor is qualified to apply the seal coat, including personnel, and equipment, and has made at least three (3) applications similar to this project in the past two (2) years.

MATERIAL ACCEPTANCE

608-6.1 Application rate. The rate of application of the asphalt emulsion shall be verified at least twice per day.

608-6.2 Friction tests. Not Required.

METHOD OF MEASUREMENT

608-7.1 Asphalt surface treatment. The quantity of asphalt surface treatment shall be measured by the square yards of material applied in accordance with the plans and specifications and accepted by the RPR.

The Contractor must furnish the RPR with the certified weigh bills when materials are received for the asphalt material used under this contract. The Contractor must not remove material from the tank car or storage tank until initial amounts and temperature measurements have been verified.

BASIS OF PAYMENT

608-8.1 Payment shall be made at the contract unit price per square yard for the asphalt surface treatment applied and accepted by the RPR. This price shall be full compensation for all surface preparation, furnishing all materials, delivery and application of these materials, for all labor, equipment, tools, and incidentals necessary to complete the item, and any costs associated with furnishing a qualified manufacturer's representative to assist with control strips.

Payment will be made under:

BID ITEM NO.	DESCRIPTION	UNIT
6	Emulsified Asphalt Seal Coat	Square Yard

REFERENCES

The publications listed below form a part of this specification to the extent referenced. The publications are referred to within the text by the basic designation only.

ASTM International (ASTM)

ASTM C117	Standard Test Method for Materials Finer than 75-µm (No. 200) Sieve in Mineral Aggregates by Washing
ASTM C136	Standard Test Method for Sieve Analysis of Fine and Coarse Aggregates
ASTM C1602	Standard Specification for Mixing Water Used in the Production of Hydraulic Cement Concrete
ASTM D5	Standard Test Method for Penetration of Asphalt Materials
ASTM D244	Standard Test Methods and Practices for Emulsified Asphalts
ASTM D2007	Standard Test Method for Characteristic Groups in Rubber Extender and Processing Oils and Other Petroleum-Derived Oils by the Clay-Gel Absorption Chromatographic Method

ASTM D2042	Standard Test Method for Solubility of Asphalt Materials in Trichloroethylene
ASTM D2995	Standard Practice for Estimating Application Rate of Bituminous Distributors
ASTM D4402	Standard Test Method for Viscosity Determination of Asphalt at Elevated Temperatures Using a Rotational Viscometer
ASTM D5340	Standard Test Method for Airport Pavement Condition Index Surveys

Advisory Circulars (AC)

AC 150/5320-12	Measurement, Construction, and Maintenance of Skid-Resistant Airport Pavement Surfaces
AC 150/5320-17	Airfield Pavement Surface Evaluation and Rating (PASER) Manuals
AC 150/5380-6	Guidelines and Procedures for Maintenance of Airport Pavements

END OF ITEM P-608

Part 9– Miscellaneous
Item P-605 Joint Sealants for Pavements

DESCRIPTION

605-1.1 This item shall consist of providing and installing a resilient and adhesive joint sealing material capable of effectively sealing joints in pavement; joints between different types of pavements; and cracks in existing pavement.

MATERIALS

605-2.1 Joint sealants. Joint sealant materials shall meet the requirements of ASTM D6690 Standard Specification for Joint and Crack Sealants, Hot Applied, for Concrete and Asphalt Pavements.

Each lot or batch of sealant shall be delivered to the jobsite in the manufacturer's original sealed container. Each container shall be marked with the manufacturer's name, batch or lot number, the safe heating temperature, and shall be accompanied by the manufacturer's certification stating that the sealant meets the requirements of this specification.

CONSTRUCTION METHODS

605-3.1 Time of application. Joints shall be sealed as soon after completion of the curing period as feasible and before the pavement is opened to traffic, including construction equipment. The pavement temperature shall be 50°F (10°C) and rising at the time of application of the poured joint sealing material. Do not apply sealant if moisture is observed in the joint.

605-3.2 Equipment. Machines, tools, and equipment used in the performance of the work required by this section shall be approved before the work is started and maintained in satisfactory condition at all times. Submit a list of proposed equipment to be used in performance of construction work including descriptive data, **ten (10) days prior to use on the project**.

a. **Tractor-mounted routing tool**. Provide a routing tool, used for removing old sealant from the joints, of such shape and dimensions and so mounted on the tractor that it will not damage the sides of the joints. The tool shall be designed so that it can be adjusted to remove the old material to varying depths as required. The use of V-shaped tools or rotary impact routing devices will not be permitted. Hand-operated spindle routing devices may be used to clean and enlarge random cracks.

b. **Hand tools**. Hand tools may be used, when approved, for removing defective sealant from a crack and repairing or cleaning the crack faces. Hand tools should be carefully evaluated for potential spalling effects prior to approval for use.

c. **Hot-poured sealing equipment**. The unit applicators used for heating and installing ASTM D6690 joint sealant materials shall be mobile and shall be equipped with a double-boiler, agitator-type kettle with an oil medium in the outer space for heat transfer; a direct-connected pressure-type extruding device with a nozzle shaped for inserting in the joint to be filled; positive temperature devices for controlling the temperature of the transfer oil and sealant; and a recording type thermometer for indicating the temperature of the sealant. The applicator unit shall be designed so that the sealant will circulate through the delivery hose and return to the inner kettle when not in use.

605-3.3 Installation of sealants. cracks shall be inspected by the RPR to ensure all existing joint sealant, debris, and vegetation has been removed.

Sealants shall be installed in accordance with the following requirements:

Immediately preceding, but not more than 50 feet (15 m) ahead of the joint sealing operations, perform a final cleaning with compressed air. Fill the joints from the bottom up to ±1/16 inch below bottom of groove as shown on the details on the plans. Remove and discard excess or spilled sealant from the pavement by approved methods.

Install the sealant in such a manner as to prevent the formation of voids and entrapped air. In no case shall gravity methods or pouring pots be used to install the sealant material. Traffic shall not be permitted over newly sealed pavement until authorized by the RPR. When a primer is recommended by the manufacturer, apply it evenly to the joint faces in accordance with the manufacturer's instructions. Check the joints frequently to ensure that the newly installed sealant is cured to a tack-free condition within the time specified.

605-3.5 Inspection. The Contractor shall inspect the joint sealant for proper rate of cure and set, bonding to the joint walls, cohesive separation within the sealant, reversion to liquid, entrapped air and voids. Sealants exhibiting any of these deficiencies at any time prior to the final acceptance of the project shall be removed from the joint, wasted, and replaced as specified at no additional cost to the airport.

605-3.6 Clean-up. Upon completion of the project, remove all unused materials from the site and leave the pavement in a clean condition.

METHOD OF MEASUREMENT

Refer to Item P-101 Preparation/Removal of Existing Pavements for measurement of joint repair.

BASIS OF PAYMENT

No separate payment will be made for this section. Refer to Item P-101 Preparation/Removal of Existing Pavements for Joint Repair payment.

REFERENCES

The publications listed below form a part of this specification to the extent referenced. The publications are referred to within the text by the basic designation only.

ASTM International (ASTM)

ASTM D789	Standard Test Method for Determination of Relative Viscosity of Polyamide (PA)
ASTM D5249	Standard Specification for Backer Material for Use with Cold- and Hot-Applied Joint Sealants in Portland-Cement Concrete and Asphalt Joints
ASTM D6690	Standard Specification for Joint and Crack Sealants, Hot Applied, for Concrete and Asphalt]

Advisory Circulars (AC)

AC 150/5340-30	Design and Installation Details for Airport Visual Aids

END ITEM P-605

Item P-620 Runway and Taxiway Marking

DESCRIPTION

620-1.1 This item shall consist of the preparation and painting of numbers, markings, and stripes on the surface of aprons, service roads, runways, and taxiways, in accordance with these specifications and at the locations shown on the plans, or as directed by the Resident Project Representative (RPR). The terms "paint" and "marking material" as well as "painting" and "application of markings" are interchangeable throughout this specification.

MATERIALS

620-2.1 Materials acceptance. The Contractor shall furnish manufacturer's certified test reports, for materials shipped to the project. The certified test reports shall include a statement that the materials meet the specification requirements. This certification along with a copy of the paint manufacturer's surface preparation; marking materials, including adhesion, flow promoting and/or floatation additive; and application requirements must be submitted and approved by the Resident Project Representative (RPR) prior to the initial application of markings. The reports can be used for material acceptance or the RPR may perform verification testing. The reports shall not be interpreted as a basis for payment. The Contractor shall notify the RPR upon arrival of a shipment of materials to the site. All material shall arrive in sealed containers that are easily quantifiable for inspection by the RPR.

620-2.2 Marking materials.

Table 1. Marking Materials

Paint[1]				Glass Beads[2]	
Type	**Color**	**Fed Std. 595 Number**	**Application Rate (max)**	**Type**	**Application Rate Minimum**
II	White	37925	115 ft2/gal	III	10 lb/gal
II	Yellow	33538 or 33655	115 ft2/gal	III	10 lb/gal
II	Black	37038	115 ft2/gal	III	No Beads
II	Red	31136	115 ft2/gal	I	2 lb/gal

For two coat markings, glass beads to be used on second coat. No glass beads required for first coat.

a. Paint. Paint shall be waterborne in accordance with the requirements of this paragraph. Paint colors shall comply with Federal Standard No. 595. Paint shall meet the requirements of Federal Specification TT-P-1952F, Type II. The non-volatile portion of the vehicle for all paint types shall be composed of a 100% acrylic polymer as determined by infrared spectral analysis. The acrylic resin used for Type III shall be 100% cross linking acrylic as evidenced by infrared peaks at wavelengths 1568, 1624, and 1672 cm-l with intensities equal to those produced by an acrylic resin known to be 100% cross linking.

b. Reflective media. Glass beads for white and yellow paint shall meet the requirements for Federal Specification TT-B-1325D Type III.

Glass beads for red and pink paint shall meet the requirements for Type I Gradation A.

Glass beads shall be treated with all compatible coupling agents recommended by the manufacturers of the paint and reflective media to ensure adhesion and embedment.

Glass beads shall not be used in black and green paint.

Type III glass beads shall not be used in red and pink paint.

CONSTRUCTION METHODS

620-3.1 Weather limitations. Painting shall only be performed when the surface is dry, and the ambient temperature and the pavement surface temperature meet the manufacturer's recommendations in accordance with paragraph 620-2.1. Painting operations shall be discontinued when the ambient or surface temperatures does not meet the manufacturer's recommendations. Markings shall not be applied when the wind speed exceeds 10 mph unless windscreens are used to shroud the material guns. Markings shall not be applied when weather conditions are forecasts to not be within the manufacturers' recommendations for application and dry time.

620-3.2 Equipment. Equipment shall include the apparatus necessary to properly clean the existing surface, a mechanical marking machine, a bead dispensing machine, and such auxiliary hand-painting equipment as may be necessary to satisfactorily complete the job.

The mechanical marker shall be an atomizing spray-type or airless type marking machine with automatic glass bead dispensers suitable for application of traffic paint. It shall produce an even and uniform film thickness and appearance of both paint and glass beads at the required coverage and shall apply markings of uniform cross-sections and clear-cut edges without running or spattering and without over spray. The marking equipment for both paint and beads shall be calibrated daily.

620-3.3 Preparation of surfaces. Immediately before application of the paint, the surface shall be dry and free from dirt, grease, oil, laitance, or other contaminates that would reduce the bond between the paint and the pavement. Use of any chemicals or impact abrasives during surface preparation shall be approved in advance by the RPR. After the cleaning operations, sweeping, blowing, or rinsing with pressurized water shall be performed to ensure the surface is clean and free of grit or other debris left from the cleaning process.

a. Preparation of new pavement surfaces. The area to be painted shall be cleaned by broom, blower, water blasting, or by other methods approved by the RPR to remove all contaminants, including PCC curing compounds, minimizing damage to the pavement surface.

b. Preparation of pavement to remove existing markings. Existing pavement markings shall be removed by rotary grinding, water blasting, or by other methods approved by the RPR minimizing damage to the pavement surface. The removal area may need to be larger than the area of the markings to eliminate ghost markings. After removal of markings on asphalt pavements, apply a fog seal or seal coat to 'block out' the removal area to eliminate 'ghost' markings.

c. Preparation of pavement markings prior to remarking. Prior to remarking existing markings, loose existing markings must be removed minimizing damage to the pavement surface, with a method approved by the RPR. After removal, the surface shall be cleaned of all residue or debris.

Prior to the application of markings, the Contractor shall certify in writing that the surface is dry and free from dirt, grease, oil, laitance, or other foreign material that would prevent the bond of the paint to the pavement or existing markings. This certification along with a copy of the paint manufactures application and surface preparation requirements must be submitted to the RPR prior to the initial application of markings.

620-3.4 Layout of markings. The proposed markings shall be laid out in advance of the paint application. The locations of markings to receive glass beads shall be shown on the plans.

620-3.5 Application. A period of 30 days shall elapse between placement of surface course or seal coat and application of the permanent paint markings. Paint shall be applied at the locations and to the dimensions and spacing shown on the plans. Paint shall not be applied until the layout and condition of the surface has been approved by the RPR.

The edges of the markings shall not vary from a straight line more than 1/2 inch (12 mm) in 50 feet (15 m), and marking dimensions and spacing shall be within the following tolerances:

Marking Dimensions and Spacing Tolerance

Dimension and Spacing	Tolerance
36 inch (910 mm) or less	±1/2 inch (12 mm)
greater than 36 inch to 6 feet (910 mm to 1.85 m)	±1 inch (25 mm)
greater than 6 feet to 60 feet (1.85 m to 18.3 m)	±2 inch (50 mm)
greater than 60 feet (18.3 m)	±3 inch (76 mm)

The paint shall be mixed in accordance with the manufacturer's instructions and applied to the pavement with a marking machine at the rate shown in Table 1. The addition of thinner will not be permitted.

Glass beads shall be distributed upon the marked areas at the locations shown on the plans to receive glass beads immediately after application of the paint. A dispenser shall be furnished that is properly designed for attachment to the marking machine and suitable for dispensing glass beads. Glass beads shall be applied at the rate shown in Table 1. Glass beads shall not be applied to black paint or green paint. Glass beads shall adhere to the cured paint or all marking operations shall cease until corrections are made. Different bead types shall not be mixed. Regular monitoring of glass bead embedment and distribution should be performed.

620-3.6 Application--preformed thermoplastic airport pavement markings.

Preformed thermoplastic pavement markings not used.

620-3.7 Control strip. Prior to the full application of airfield markings, the Contractor shall prepare a control strip in the presence of the RPR. The Contractor shall demonstrate the surface preparation method and all striping equipment to be used on the project. The marking equipment must achieve the prescribed application rate of paint and population of glass beads (per Table 1) that are properly embedded and evenly distributed across the full width of the marking. Prior to acceptance of the control strip, markings must be evaluated during darkness to ensure a uniform appearance.

620-3.8 Retro-reflectance. Reflectance shall be measured with a portable retro-reflectometer meeting ASTM E1710 (or equivalent). A total of 6 reading shall be taken over a 6 square foot area with 3 readings taken from each direction. The average shall be equal to or above the minimum levels of all readings which are within 30% of each other.

Minimum Retro-Reflectance Values

Material	Retro-reflectance mcd/m^2/lux		
	White	Yellow	Red
Initial Type I	300	175	35
Initial Type III	600	300	35
Initial Thermoplastic	225	100	35
All materials, remark when less than[1]	100	75	10

[1] 'Prior to remarking determine if removal of contaminants on markings will restore retro-reflectance

620-3.9 Protection and cleanup. After application of the markings, all markings shall be protected from damage until dry. All surfaces shall be protected from excess moisture and/or rain and from disfiguration by spatter, splashes, spillage, or drippings. The Contractor shall remove from the work area all debris, waste, loose reflective media, and by-products generated by the surface preparation and application operations to the satisfaction of the RPR. The Contractor shall dispose of these wastes in strict compliance with all applicable state, local, and federal environmental statutes and regulations.

METHOD OF MEASUREMENT

620-4.1a The quantity of markings shall be paid for shall be measured by the number of square feet. For new, two coat, applications, the quantity is measured from the **exposed** pavement marking.

BASIS OF PAYMENT

620-5.1 Bid prices shall be full compensation for furnishing all materials and for all labor, equipment, tools, and incidentals necessary to complete the item complete in place and accepted by the RPR in accordance with these specifications.

Payment will be made under:

BID ITEM NO.	DESCRIPTION	UNIT
8	Markings: 2-Coat with Reflective Media	Square Foot
9	Markings: 2-Coat w/o Reflective Media	Square Foot

Refer to Section P-101 for Payment of pavement marking removal effort.

REFERENCES

The publications listed below form a part of this specification to the extent referenced. The publications are referred to within the text by the basic designation only.

ASTM International (ASTM)

ASTM D476	Standard Classification for Dry Pigmentary Titanium Dioxide Products
ASTM D968	Standard Test Methods for Abrasion Resistance of Organic Coatings by Falling Abrasive
ASTM D1652	Standard Test Method for Epoxy Content of Epoxy Resins
ASTM D2074	Standard Test Method for Total, Primary, Secondary, and Tertiary Amine Values of Fatty Amines by Alternative Indicator Method
ASTM D2240	Standard Test Method for Rubber Property - Durometer Hardness
ASTM D7585	Standard Practice for Evaluating Retroreflective Pavement Markings Using Portable Hand-Operated Instruments
ASTM E303	Standard Test Method for Measuring Surface Frictional Properties Using the British Pendulum Tester
ASTM E1710	Standard Test Method for Measurement of Retroreflective Pavement Marking Materials with CEN-Prescribed Geometry Using a Portable Retroreflectometer
ASTM E2302	Standard Test Method for Measurement of the Luminance Coefficient Under Diffuse Illumination of Pavement Marking Materials Using a Portable Reflectometer
ASTM G154	Standard Practice for Operating Fluorescent Ultraviolet (UV) Lamp Apparatus for Exposure of Nonmetallic Materials

Code of Federal Regulations (CFR)

40 CFR Part 60, Appendix A-7, Method 24	Determination of volatile matter content, water content, density, volume solids, and weight solids of surface coatings
29 CFR Part 1910.1200	Hazard Communication

Federal Specifications (FED SPEC)

FED SPEC TT-B-1325D Beads (Glass Spheres) Retro-Reflective

FED SPEC TT-P-1952F Paint, Traffic and Airfield Marking, Waterborne

FED STD 595 Colors used in Government Procurement

Commercial Item Description A-A-2886B Paint, Traffic, Solvent Based

Advisory Circulars (AC)

AC 150/5340-1 Standards for Airport Markings

C 150/5320-12 Measurement, Construction, and Maintenance of Skid Resistant Airport Pavement Surfaces

END OF ITEM P-620

APPENDIX A

CONSTRUCTION SAFETY AND PHASING PLAN

CONSTRUCTION SAFETY PHASING PLAN

for

REHABILITATE TIE-DOWN APRON

A.I.P. No. 3-06-0243-xxx-2025
County Project: # 22011

SANTA YNEZ AIRPORT

Santa Barbara County, CA

December 2024

Prepared by:

TARTAGLIA ENGINEERING

P.O. Box 476
Pismo Beach, CA 93449
(805) 466-5660

Contents

1. Introduction 4
2. Baseline Airport Facility 4
3. Project Description 4
A. General Scope of the Work 4
B. Location 5
C. Duration 5
4. Project Team 5
5. Emergency Response 6
6. Coordination 7
A. Construction Progress Meetings 7
B. Scope or Schedule Changes 7
C. FAA ATO / Facilities Coordination 7
D. Lines of Communication 7
E. Project Meetings and Representation 8
F. Coordination Procedures for FAA Facilities Shutdown and Restart 9
7. Phasing and Sequencing, Accomplishment 9
A. Phasing and Sequencing 9
B. Accomplishment 10
C. Construction Safety Drawings 10
D. Project Changes 10
8. Areas and Operations Affected by the Construction Activity 10
A. Areas Affected by Construction Activity 10
B. Operations Affected by Construction Activity 11
9. Protection of Navigation Aids (NAVAIDs) 12
10. Contractor Access 12
A. Airport Security Requirements 12
B. Vehicle Safety Requirements 12
C. Access and Driving on the Airport 12
D. Airfield Incursions 13
E. Fencing and Gates 13

F. Contractor Access and Haul Route Provisions 13
G. Radio Communications 14
H. Aircraft and Pedestrian Operations 15
I. Specific Safety Requirements 15
11. Wildlife Management 16
12. Foreign Object Debris (FOD) Management 16
13. Hazardous Materials (HAZMAT) Management 17
14. Notification of Construction Activity 18
15. Inspection Requirements 19
16. Underground Utilities 19
17. Penalties 20
18. Special Conditions 20
19. Runway and Taxiway Visual Aids 21
20. Marking and Signs for Access Routes 21
21. Hazard Marking and Lighting 21
22. Work Zone Lighting for Nighttime Construction 22
23. Protection of Specific and Individual Airport Safety Areas 22
A. Runway 8-26 22
B. Parallel and Connecting Taxiways to Runway 23
C. Apron and Taxilanes 23
24. Other Limitations on Construction 23
A. Prohibitions 23
B. Restrictions 23
C. Equipment Height 23
25. Third-Party Provider Obligations 24
26. Appendix 26
A. Figure 1: Project Layout Plan 26
B. Figure 2: Phasing Plan 26

1. Introduction

Aviation safety is the primary consideration at airports, especially during construction. This Construction Safety and Phasing Plan (CSPP) serves as a companion document to the project plans and specifications for the Terminal Improvements, at Santa Ynez Airport. The document has been prepared in compliance with FAA AC 150/5370-2G: Operational Safety on Airports During Construction, and with data and information taken from Santa Ynez Airport's Airport Layout Plan.

Phasing developed for this project is intended to minimize the impact the project will have on airport operations while providing a logical sequence of construction activities. The emphasis is safety to airport users and the traveling public, but also to all contractor forces including material delivery personnel, as well as team support members including airport and FAA staff, the engineer, and all quality assurance technicians.

The goal is a high-quality construction improvement completed in a safe manner with minimal impacts to the traveling public. All team members share responsibilities and obligations toward achieving this goal.

2. Baseline Airport Facility

Santa Ynez Valley Airport is a general aviation airport owned by Santa Barbara County. Administration and operation of the airport is by the Santa Ynez Valley Airport Authority through an agreement with the County. The airport is located in the unincorporated community of Santa Ynez, along the south side of State Highway 246. Santa Ynez is approximately 24 miles northwest of the city of Santa Barbara. The airport is at an elevation of 650 feet above mean sea level in the Santa Ynez Valley, occupying 130 acres. The facility includes one runway, Runway 8-26, 2812 feet long and 75 feet wide. The runway is served by a full-length parallel taxiway on the north side and four connecting taxiways. The airport includes several on-airport aviation related businesses, a general aviation terminal, a glider operation, a County of Santa Barbara air emergency response component, a fully staffed county fire station, and a seasonal U.S. Forest Service facility. Activity at the airport remains high with a vibrant hangar tenant group and other interests.

3. Project Description

A. General Scope of the Work

a. In general, the project includes the following major elements:
   - Surface treatment of approximately 71,000 square yards of apron.

b. The scope of actual construction work includes:
   - Airfield safety and security.
   - Construction site environmental compliance.
   - Temporary removal of tie down cables, chains, and fasteners.
   - Pavement cleaning.
   - Crack fill and seal.
   - Application of an emulsified asphalt seal coat.
   - Pavement markings.
   - Reinstallation of aircraft tie down cables, chains, and fasteners.

c. The work is presented in a single bid schedule.

d. Figure 1, the Project Layout Plan (sheet 3 of the project plan set) shows the extent and location of all work on this project.

B. Location

The work of this project is within the Airport Operations Area (AOA), and outside the all runway and taxiway object free areas.

C. Duration

The work is scheduled for 50 working days, according to the following phase breakdown:

Phase	Work Area	Activity	Duration (working days)
1	Taxilanes serving hangar rows E, F, & G	Crackfill and seal, application of emulsified asphalt seal coat, application of first coat of markings.	7
2	Taxilanes serving hangar rows A, B, C, & D		8
3	Main Apron: West	Same as taxilane areas, plus removal and reinstallation of tie-down cables, chains, and hardware.	15
4	Main Apron: East		15
5	Entire Project Area	Second coat of markings.	5
Total			**50**

A Notice to Proceed will be issued after the approval of all material submittals and all materials have been ordered and received. In general, the work is sensitive to temperature and weather. Additionally, it is anticipated that precipitation will result in non-work periods during rain events themselves and for a few days after, providing time for adequate pavement surface drying.

4. Project Team

Table 1 identifies key team members that have been and continue to be instrumental in the successful progress of this project to-date.

Design Contacts

Table 1

Organization	Point of Contact	Role	Contact Information
Santa Barbara County	John Green	Assistant Director, SBCO General Services	(805) 934-6229 jlgreen@countyofsb.org
Santa Barbara County	Diana Estorga	Capital Division Chief	(805) 934-6229 DiEstorga@countyofsb.org
Santa Barbara County	Steven Manuel	SBCO ACIP Manager	(805) 266-4176 stmanuel@countyofsb.org
Santa Ynez Airport	Jourdi de Werd	President, Airport Authority	(805) 688-8390 jourdi@dewerdcapital.com
FAA – Airports District Office	Justin Guan	Community Planner / Program Manager	(424) 405-7276 Justin.guan@faa.gov
Tartaglia Engineering	Jason Hargreaves	Lead Designer	(805) 466-5660 jason@tartaglia-engineering.com
	John Smith	Design Manager	(805) 466-5660 john@tartaglia-engineering.com
Earth Systems Pacific	Sydney Johnson	Project Manager / Quality Assurance / Materials	(805) 544-3276 sjohnson@earthsystems.com

Construction Team			
Table 2			
Organization	Role	Point of Contact	Contact Information
Santa Barbara County	Project Manager	Diana Estorga	(805) 934-6229
			diestorga@countyofsb.org
Santa Barbara County	Assistant Project Manager	Steve Manuel	(805) 934-6229
			stmanuel@countyofsb.org
Santa Ynez Airport	Airport Representative	Jourdi de Werd	(805) 688-8390
			jourdi@dewerdcapital.com
	On-Site Airport Representative	Dave Romero	(805) 688-8390
			syairportmanager@gmail.com
FAA – Airports District Office	Program Manager	Justin Guan	(424) 405-7276
			Justin.guan@faa.gov
Tartaglia Engineering	Lead Designer	Jason Hargreaves	(805) 466-5660
			jason@tartaglia-engineering.com
	Construction Manager	Michael Arms	(805) 466-5660
			michael@tartaglia-engineering.com
	Inspector	Brett Dolan	(805) 610-7816
			brett@tartaglia-engineering.com
General Contractor	Project Manager	TBD	Phone
			e-mail
	Project Superintendent	TBD	Phone
			e-mail
	Safety Manager	TBD	Phone
			e-mail
	Quality Control Manager	TBD	Phone
			e-mail
Subcontractor A	Project Manager	TBD	Phone
			e-mail
	Foreman	TBD	Phone
			e-mail
			e-mail

5. Emergency Response

Information in Table 3 has been updated to reflect the community where the Santa Ynez Airport resides.

Emergency Response			
Table 3			
Organization	Role	Point of Contact	Contact Information
Santa Ynez Valley Cottage Hospital 2050 Viborg Road, Solvang	Emergency Medical	N/A	(805) 682-7111
Marian Regional Medical Center 1400 E. Church, Santa Maria	Emergency Medical	N/A	(805) 739-3000
County of Santa Barbara Fire (Santa Ynez Airport - Station 32)	Fire Protection	N/A	911 or (805) 686-5058
Sheriff: Santa Barbara County (Buellton Office)	Public Safety	N/A	911 or (805) 686-8150
Hazardous Materials Management Services (HMMS)	Santa Barbara County Certified Unified Program Agency (CUPA)	N/A	911 or (805) 681-4900

6. Coordination

Coordination and communication are key to project success. Coordination between the airport and the design team has been instrumental in facilitating progress on the project to the point of public bidding and award of construction contract. The need for effective coordination and communication is heightened as the work moves out to the field, and the need for an emphasis on public safety becomes more acute.

A. Construction Progress Meetings

Periodic construction progress meetings will be scheduled to help facilitate communication between the Contractor, the Resident Project Representative (RPR) or the Project Engineer, and the Airport. These meetings are essential for sharing information on phasing and scheduling, and discussing issues related to airfield safety and improvement constructability. Minutes taken at each meeting will serve as the agenda for each subsequent meeting.

B. Scope or Schedule Changes

Scope or schedule changes, should they occur, will be well documented and agreed upon in advance of implementation. The FAA Program Manager will be kept informed as potential changes begin to materialize. All implemented changes will be proceeded with preparation, distribution, and approval of contract Change Orders.

C. FAA ATO / Facilities Coordination

There are no scheduled shut-down of FAA facilities required of this project. Additionally, there will be no re-certification flights of FAA navigation aids required after all work is complete. The local FAA Facilities representatives will be invited to the Pre-Construction Conference and all periodic progress meetings.

D. Lines of Communication

a. Santa Barbara County – General Services Department staff will serve and provide the following:
   - The Public Information Officer, disseminating information to the public and receiving concerns and communication from the public.
   - Communication with FAA – regarding project bidding, construction, grant management.
   - Communication with the Project Engineer regarding concerns and issues, possible changes to the project; scheduling, construction, scope of work, etc.
   - Communication with the contractor when immediate direction is warranted.

b. Santa Ynez Airport Representatives will serve and provide the following:
   - Primary point of contact with airport users and tenants.
   - On-site facilitation of contractor access to the airport.
   - Identification of issues to the Project Engineer related to the construction activity.

c. Project Engineer will serve and provide the following:
   - Communication with the airport regarding progress, issues, challenges, and opportunities, and input on schedule including certification flight tests.
   - Communication with the contractor regarding safety including any safety violations, quality assurance, work progress, periodic pay requests, field engineering including technical input and plan and specification interpretation, compliance with employee compensation, subcontractor issues, etc.
   - Communication with the FAA – Facilities regarding project schedule.

d. Contractor will serve and provide the following, through communication to the engineer:

- Schedule updates and other impacts to planned work progress.
- All material submittals and plan submittals.
- Look-ahead logic, seeking issues and challenges before they occur, providing questions and asking for input in a timely manner to facilitate uninterrupted progress.
- All required documentation for quality control, materials placed including weight tickets, certified payroll statements including compensation to DBE's, etc.

E. Project Meetings and Representation

Construction Team members are invited and expected to attend and provide active input at the following project meetings:

a. Pre-Construction Conference.
   - Identify / confirm the extent of award of contract.
   - Present detailed schedule.
   - Phasing and sequencing.
   - Review airport safety including the CSPP, with emphasis on:
     - No runway closures required or anticipated.
     - Runway and taxiway safety areas (imaginary areas centered on features).
     - Typical work window restrictions shall apply: nights/weekends, holidays, rain, etc.
     - Airfield facilities closing and re-opening procedures. No closures required.
   - Confirm all points of contact for team members including back-ups (update Table 2).
   - Project submittals.
   - Airport tenant and user concerns and issues, including charter service entities, emergency responder – tenants, FBO's, etc.
   - Neighbor / community concerns.
   - Construction activities and materials.
   - Quality control / quality assurance.
   - Project milestones.
   - Labor requirements, civil rights requirements, DBE goals and documentation.
   - Payroll records.
   - Pay requests; periodic and final.
   - Issuance of Notice to Proceed – Day 1.
   - Time for performance based on extent of contract award.

b. Construction Progress Meetings.
   - Meetings will be weekly until otherwise informed.
   - The primary venue for open discussion regarding all issues.
   - Team member to provide representation capable of providing active input.
   - Subjects at Pre-Construction Conference serve as the basis.
   - Discuss and review Requests for Information (RFI's), RFI Responses, Requests for Proposals (RFP's), Proposal Responses, Change Orders,
   - In the event of night work, meetings shall be held on the evening before the start of night work or the following morning immediately after the end of night work.
   - Engineer-prepared minutes shall be updated and serve as the agenda for next meeting.

c. Preliminary Final and Final Inspections.
   - Review progress to-date, including completed work and schedule.

- Establish final pay quantities, substantiated by field measurement, material weight ticket, or other.
- Status of all Contractor-provided closeout paperwork:
  - Marked up, as-built plans.
  - O&M Manuals.
  - Final certifications.
  - Permit closeout paperwork and confirmation.
  - All final certified payrolls, benefit statements, etc.
  - Documentation for final compensation to all DBE's including statement regarding compliance / achieving the goal.
- Identify all compensation deductions:
  - Based on contractor performance, in accordance with technical specifications.
  - Deductions due to waste material.
  - Financial penalties for CSPP violations.
- Receipt of all spare parts and elements and components to be salvaged to the Airport.
- Documentation of outstanding items and issues through generation of a Preliminary Punch List.
- Schedule for timely completion of all outstanding items, and for Final Inspection.

F. Coordination Procedures for FAA Facilities Shutdown and Restart

None. The scope of this project does not require any FAA involvement for shut-down, re-start, or flight verification of any facilities.

7. Phasing and Sequencing, Accomplishment

A. Phasing and Sequencing

The work of this project is subject to phasing, allowing time for airport users and tenants to prepare for and adjust their own activities to accommodate construction work.

Figure 1, the Project Layout Plan, identifies the following for the project:

- Extent of area of work.
- Contractor haul routes / path of travel for materials and equipment.
- Contractor yards.
- Airfield closure delineation (low-profile lighted delineators) for each phase.

Figure 2, the Phasing Plan, identifies the following for the project:

- Area and extent of the work area for each of the five (5) phases.
- The sequencing of work, providing advance indication to tenants and users of where the work will occur next.
- Phases 1 through 4 present individual work areas on the airport. Phase 5, the final phase, is global, focused on the type of work.

While the work could be accomplished in less phases, the phase approach provides a lower level of impact to airport users, in two ways:

- It shortens the duration of each individual phase.

- It reduces the extent of tenant impact, minimizing over-crowding through the temporary relocation of aircraft onto open tiedown areas.

B. Accomplishment

a. Airport to remain open for the duration of the project.
b. All work shall be accomplished between 0700 and 1600, local time.
c. Typical work windows will extend Monday morning through Friday afternoon.
d. Weekend and holiday work is not required or expected.
e. No impacts to runway or taxiways.
f. No impacts to navigation aids including beacon, wind cone, and PAPI.
g. The Contractor shall establish and maintain delineation for each work area as described, for the duration of each phase.
h. For Phases 1-4, once installed, delineation shall remain in-place, 24 hours a day, 7-days a week, until the phase is complete. The area is closed to tenants on foot, in vehicles, and in aircraft.
i. Phases 1-4 are to be accomplished in sequence. The closing of a phase area and the work of that area cannot begin until the phase before has been completed and accepted, and the area re-opened for public use.
j. The work of Phase 5, application of the second coat of pavement marking paint, extends throughout the entire project area. Delineation is not anticipated for this phase. Working with the RPR, the contractor shall proceed under radio authority, applying markings where necessary. The contractor shall anticipate a level of coordination of access to airfield areas, with consideration for aircraft traffic.

C. Construction Safety Drawings

Figures 1 and 2 provide clear indication of the individual work areas of this project, along with the location of closure delineation and contractor haul / access routes. These figures are included in the appendix of this CSPP.

D. Project Changes

If a project change occurs that affects either the project scope or project schedule, this CSPP will be updated accordingly. Revised or amended CSPP's involve approval from the FAA. Contractor will be required to modify the Safety Plan Compliance Document as necessary, after each modification to the CSPP.

8. Areas and Operations Affected by the Construction Activity

A. Areas Affected by Construction Activity

In general, the area of work of this project is along the north side of the Santa Ynez Airport, encompassing the main apron and taxilanes serving aircraft storage hangars, extending up to the parallel taxiway. All the work of this project is outside the Runway Safety Area (RSA) and the Runway Object Free Area (ROFA). In addition, the work of this project is outside the Taxiway Object Free Area (TOFA) and the Taxiway Safety Area (TSA). The extent of work, contractor yard, and contractor designated path of travel are clearly shown on the Project Layout Plan included in this document (Attachment 1).

Areas Affected For Duration of Phase					
Table 4					
	Phase 1	**Phase 2**	**Phase 3**	**Phase 4**	**Phase 5**
Runway 8-26	Open	Open	Open	Open	Open
Parallel & Connecting Taxiways	Open	Open	Open	Open	Open
Taxilane serving Row G	Closed	Open	Open	Open	Short-duration closure under radio authority. No delineation.
Taxilane serving Row F	Closed	Open	Open	Open	
Taxilane serving Row E	Closed	Open	Open	Open	
Taxilane serving Row D	Open	Closed	Open	Open	
Taxilane serving Row C	Open	Closed	Open	Open	
Taxilane serving Row B	Open	Closed	Open	Open	
Taxilane serving Row A	Open	Closed	Open	Open	
Tie-Down Apron: West	Open	Open	Closed	Open	
Tie-Down Apron: East	Open	Open	Open	Closed	

All areas of work will be delineated closed for the duration of each phase. There will be no re-opening of work areas after each work shift.

Table 5 identifies Airfield Safety Areas that are in force at Santa Ynez Airport. Contractor forces are to remain clear of Runway Object Free Area (ROFA) at all times.

Airfield Safety Areas			
Table 5			
Design Standards – General	Entity	Parameter	Dimension
Design Aircraft: B-I (small) Example Aircraft: Mooney	Runway 8 – 26	Runway Object Free Area (ROFA)	250 feet – centered
		Runway Safety Area (RSA)	120 feet – centered
	Taxiways	Taxiway Object Free Area (TOFA)	89 feet – centered
		Taxiway Safety Area (TSA)	49 feet – centered

B. Operations Affected by Construction Activity

Construction on this project is scheduled to occur during daylight hours (0700 – 1600), with work area phases delineated closed 24 hours a day, 7-days a week. These closures will impact and affect tenants and users through temporary denied access to hangars for the duration of each phase. Phase work areas have been kept small to help keep the duration of each closure to as short as practical.

It is anticipated tenants will temporarily relocate aircraft to open areas of the apron for the duration of a phase that impacts access to their specific hangar. Movement of aircraft to and from hangars and the tie-down aprons is anticipated during phase transition periods.

Access to and the functionality of the runway and taxiway network will never be impacted during this project. Aircraft use of Runway 8-26 and aircraft circulation around the airport between the hangars, taxiways and runway will be unrestricted due to contractor construction operations and contractor haul / access routes. Access to the airport office and fuel island will also be preserved.

The airport serves various air-attack entities, which operated in and around the area of construction. To preserve operations, the contractor is instructed to install temporary delineation (barricades) to create a

temporary air-attack operation area. The area, along with the delineation locations are clearly shown on the Project Layout Plan included in this document (Attachment 1).

9. Protection of Navigation Aids (NAVAIDs)

The Contractors operations shall remain clear of all navigation aids:

- Runway PAPI and VASI.
- Runway lighting.
- Airport beacon and primary wind cone.

NAVAIDS are anticipated to be unaffected by construction activities. However, the Contractor shall notify the Inspector immediately should Airport facilities be impacted or damaged during the work.

10. Contractor Access

Contractor access to and from the airport shall be per the provisions cited in this Construction Safety Phasing Plan, the project plans and specifications, and the contents of FAA Circular AC150/5370-2G, included in its entirety at the back of this document. In the field, contractor access shall be through one automatic vehicle access gate, designated on the Project Layout Plan.

A. Airport Security Requirements

a. All contractor forces shall wear and use OSHA-standard Personal Protective Equipment (PPE), appropriate for their individual tasks and for the environmental condition anticipated for this project in addition to safety wear and high-visibility outerwear.
b. All gates shall be unlocked and locked with each passage. No piggy-backing allowed.
c. All vehicles inside the fence shall be equipped with flashing beacons and/or orange and white checkered flags at all times.
d. Personal vehicles not allowed within the Airport Operations Area (AOA).
e. In the event of material delivery inside the fence, Contractor shall designate a flagman to accompany delivery vehicles to / from the gate and work site at all times.

B. Vehicle Safety Requirements

a. All vehicles will be equipped with either standard FAA orange and white checkered flags (day only) or amber rotating beacons / flashing lights (day or night), to be installed at the highest point on the equipment.
b. The company name or logo shall be displayed on both sides of the vehicles. Vehicle marking requirements are shown in the project specifications.
c. Employee parking shall be as designated by the Project Manager, outside the AOA.
d. Access to the job site shall be via specified Haul Routes as shown on the plans designated by and approved by the Project Engineer.

C. Access and Driving on the Airport

a. Contractor shall attend and participate in safety training / workshops organized and presented by the Airport in advance of driving within the AOA. Material delivery or occasional drivers need not receive training provided they have a trained escort while on airport property.
b. All vehicles and persons shall enter and exit the AOA through designated gates only.
c. Maximum vehicle speed shall be 15 MPH while on airport property.

d. No deviation from designated vehicle haul routes shall be allowed, unless previously approved by the Airport Project Manager. While in the AOA, all vehicles and persons shall remain within designated areas.
e. All private vehicles shall be parked outside the fence.
f. No vehicle shall be parked on or operated across any aircraft apron or transient aircraft tie-down row, whether they are vacant or occupied.

D. Airfield Incursions

a. An airfield incursion is an unauthorized entry into controlled space within the AOA. An incursion can be on foot or in a vehicle.
b. At towered airports, when the tower is open, unauthorized movement or entry into the Movement Area is considered an incursion.
c. At towered airports, when the tower is closed, unauthorized movement or entry into any Runway Object Free Area or Taxiway Object Free Area of a runway or taxiway that is open without adequate and proper announcement of your intent and confirmation of a safe condition, is considered an incursion.
d. There are four (4) categories of incursion, based on the level of risk or exposure, from most to least significant:
   - Category A: A serious incident in which a collision was narrowly avoided.
   - Category B: An incident in which separation decreases and there is a significant potential for collision, which may result in a time critical corrective / evasive response to avoid a collision.
   - Category C: An incident characterized by ample time and/or distance to avoid a collision.
   - Category D: An incident that meets the definition of airfield incursion such as incorrect presence of a single vehicle / person / aircraft on the protected area of a surface designated for the landing, take off, or taxiing of aircraft but with no immediate safety consequences.

E. Fencing and Gates

a. Throughout the duration of the project, security of the airport provided by the perimeter fence and access gates shall remain equal to or greater than pre-project condition. The integrity of the perimeter fence shall remain intact during construction. The work of this project does not modify the perimeter fence in any way.
b. Manual access gates normally closed will remain closed.
c. After entering the airport through a manual gate, the Contractor must lock himself in. All manual gates shall be locked after leaving the airport as well. During material import or export operations, the Contractor shall maintain a sentry at the access gate. The sentry shall be prepared to deny access to any unauthorized individuals. The gate shall be locked during all sentry breaks or lunch.
d. After entering or exiting the airport through an automatic gate, the Contractor shall remain near the gate until the gate is fully closed, prohibiting airport access to any other individual.

F. Contractor Access and Haul Route Provisions

a. The Contractor shall control his/her operations and the operations of his/her subcontractors and all suppliers while on airport property.
b. The Contractor's men and equipment shall be limited to the Construction areas shown on the project plans and in the specifications. The Contractor agrees to implement such security measures as are necessary to assure compliance with Federal Aviation Administration, State

and local airport regulations. The Contractor shall be responsible for clearly delineating the limits of his operation. Delineation shall be installed in accordance with the typical delineation details shown on the plans. Delineation left overnight shall be clearly and adequately lit. Batteries shall be replaced every two weeks at a minimum or more frequently as needed.

c. Haul routes will use existing vehicle service roads to bring in material or remove material at the worksite. Absolutely no deviations from designated routes will be allowed without prior written authorization of Airport Staff or the Project Engineer.
d. The Contractor directed to review the plans which show the fence, access gate, haul routes and areas available for the storage of materials and equipment as required. The restriction and control of persons and vehicles allowed on the Airport is of utmost importance. Therefore, the Contractor will be responsible for the persons and vehicles coming through the access gates during the time that they have it in their control. When the gates are unlocked, they shall have them in the "closed" position and guarded by a person on their staff who will allow only those persons known to them to be a part of the construction team. Additionally, only vehicles properly flagged or equipped with a rotating beacon will be allowed. At all times when the gates are not guarded by a person, they will be kept closed and locked.
e. It shall be the Contractor's responsibility to inform any and all delivery personnel of these requirements.
f. To avoid confusion with aircraft during the construction and to avoid damage to the existing pavement and to the adjacent property, the Contractor's equipment shall be restricted to the haul routes shown on the plans and in this document. The routes will be open to the Contractor depending on work area actively under construction. In most areas the routes coincide with or move across existing ramps or taxiways. It shall be the responsibility of the Contractor to provide adequate safeguards, including flagmen, so that the operation of the Airport will not be hindered.
g. All equipment storage areas shall be delineated as specified in the project specifications.
h. At the end of each workday, the active haul route shall be swept and cleared of any debris.
i. At the completion of work, all haul routes in paved or unpaved areas shall be restored to the conditions existing prior to the start of the work.

G. Radio Communications

a. Radio communications described in this section pertain to communication on radio frequencies employed by / at the airport for the purposes of informing and controlling the flying public regarding aircraft operations and airfield activities that could include maintenance and construction activities.
b. Air band radio communication is not for contractor-contractor communication, or contractor-project engineer communication.
c. There is no Air Traffic Control Tower (ATCT) at Santa Ynez Airport. Pilots operate into and out of the airport under non-towered procedures including standard communications procedures.
d. All air-band radio communications shall be between the construction contractor and individual aircraft pilots, on radio frequency 122.8 (Common Traffic Advisory Frequency (CTAF)).
e. Radio communications are required:
    - To broadcast contractor intent for the movement of men and equipment into or through active airport operations areas.

- To listen, understand, and communicate to others on the crew, information regarding active or near-term aircraft movements that can adversely impact contractor operations or pending contractor operations.
- To identify airfield conditions to pilots that will impact identified pilot intent.

f. Airband radio frequencies can be busy. Respectful radio protocol is essential. Prior to initiating radio communications, the Contractor's Radio Monitor shall listen for active communication and delay initiating communication until confident all previous communications are complete.
g. The Contractor shall have a designated, authorized, Radio Monitor on site the entire time work crews are present within the AOA. The Monitor shall have in his possession a working air-band radio tuned to the appropriate frequency, shall be in a physical position capable of hearing radio broadcasts (away from background noise), and shall be capable of initiating or responding to radio communications that are essential to the safety of the flying public and contractor forces.
h. Radio communication is essential for entering or crossing active airfield operations areas. The Contractor's radio monitor shall be capable of providing clear and concise direction regarding intent, and / or shall be capable of complete understanding of the location and intent of aircraft maneuvering on the airport.
i. Radio Monitor shall use cell phone, CB-radio, or other means to communicate between contractor forces including material delivery trucks, and not the airband radio.

H. Aircraft and Pedestrian Operations

Throughout the construction project, the following safety and operational practices shall be observed:

a. Airport runways and taxiways should remain in use by aircraft to the maximum extent possible.
b. Aircraft shall ***always*** have the right of way.
c. Aircraft use of areas near the contractor's work shall be controlled to minimize disturbance to the contractor's operation.
d. Contractor, subcontractor, and supplier employees are restricted from entering the airport area inside the fence except through the designated gates and along the routes shown on the Project Layout Plan.
e. Construction within the safety area of an active runway, taxiway, or apron and performed under normal operational conditions must be accomplished when the runway, taxiway, or apron is closed or use-restricted and initiated only with prior permission from the Airport Project Manager or Inspector.
f. Airport Project Manager, Engineer, RPR (Inspector), or other designated airport representative may order the contractor to suspend operations; move personnel, equipment, and materials to a safe location at any time the situation requires it.

I. Specific Safety Requirements

a. Aircraft, emergency vehicles, maintenance vehicles, operational vehicles and enplaning and deplaning passengers have right of way over all traffic. This includes passengers for general aviation aircraft as well as firefighting and emergency response aircraft.
b. No vehicles shall be left unattended within the AOA.
c. No spilling or littering of any substance onto any paved surface. Vehicle operators shall make sure that no loose object falls onto a paved surface or is allowed to become dispersed by either the wind or propeller or jet blast.

d. All hazardous conditions necessitated by construction or maintenance activities (trenches, excavations, stockpiles) shall be marked to render them readily visible, day and night.
e. Pollution by any substance, under any form, shall be properly controlled by means and methods acceptable to Airport Project Manager or RPR (Inspector).
f. No metal track vehicle shall be operated on any paved surface, unless prior approval has been secured from the Airport Project Manager or RPR (Inspector).
g. All accidents, incidents involving bodily injury or property damage, regardless of severity or property ownership, which occur on the airport, shall be immediately reported to the Airport Project Manager or RPR.

11. Wildlife Management

Throughout the duration of the project, Contractor and all subcontractors shall concern themselves with activities and site conditions that could, inadvertently, attract wildlife. To avoid such conditions, team members shall:

- Monitor construction water applications such that free water cannot stand for more than 30 hours, and more than 48 hours after the conclusion of a rain event.
- Implement pumps and other de-watering devices and techniques as necessary to eliminate standing water and the sheen associated with a wet surface.
- Maintain an effective solid waste program that keeps site trash including food waste to a minimum. Containers shall be conveniently placed, shall be securely closed or otherwise inaccessible to wildlife, and shall be serviced at a frequency that preserves their functionality.
- All airport access gates shall be kept securely closed when not in use to prevent public and wildlife access to the airport through an open gate.
- The Contractor shall maintain vegetation including grass to an acceptable level / condition within all contractor yards and material storage areas, to reduce wildlife attraction. Projects of long duration may demand a shift or temporary relocation of material stockpiles to facilitate vegetation control.
- Contractor wildlife management responsibilities including monitoring and addressing standing water extend over weekends, holidays, and extended non-work periods.
- The Contractor shall contact Airport Operations immediately in the event of a wildlife encounter, or at the time of recognition or identification of a condition that could be deemed an attraction to wildlife.

12. Foreign Object Debris (FOD) Management

It is the responsibility of the Contractor to maintain a clean project site free from FOD or the threat of FOD. The project site includes actual work areas, but also includes all haul routes, staging areas, all locations where delineation is placed, and any other airfield area occupied or affected by contractor operations.

FOD management also includes inspection of all vehicles before entering the AOA, looking for and addressing rock, loose construction materials, hand tools, hardware, etc., not stored securely within holding compartments (toolboxes, truck beds, etc.). In addition, vehicles shall be re-inspected when leaving the work area, heading out of the airport.

The Contractor and its employees will be held responsible for maintaining the project area and keeping it free from FOD whether it is generated from the project site or other airfield areas. This obligation also

applies to all material suppliers, equipment delivery and equipment servicing staff, quality control and quality assurance staff, etc. Everyone inside the AOA is responsible for the removal of FOD regardless of its origin. All parties associated and affiliated with this project are included in this obligation.

The Contractor is encouraged to limit his path of travel to narrow lanes, following the routes identified on the plans. in so doing, he narrows his area of focus when performing all cleaning and inspecting activities as the work shift ends.

The Contractor shall use water, brooms, blowers, street sweepers (no metal bristles), vacuum trucks, or any other industry-standard, effective means to clean airfield pavements within the project site prior to opening closed areas to air traffic. Airport Staff will have the final word on the acceptance of cleaned project areas for aircraft operations. The Contractor shall allow ample time for inspection of cleaned areas and re-cleaning if necessary, in advance of the end of any closure period.

13. Hazardous Materials (HAZMAT) Management

Hazardous Material Management applies to any material that is considered hazardous by the USEPA, either in character, quantity, condition, or any combination thereof. Hazardous materials can include construction materials, fuels, lubricants, coolants, binders, and coatings, but also can include waste products and blended products. The Contractor shall:

- Prepare, submit, and gain approval of a Hazardous Materials Management Plan (HMMP). The plan shall outline all anticipated hazardous materials to be used, employed, encountered, or generated by and at the necessity of this project, and shall include a complete library of Material Safety Data Sheets (MSDS). The document shall identify the Contractors Hazardous Materials Manager with 24-hour contact information. In addition, the plan shall address fuel and other material deliveries, material storage, and use. Lastly, the plan shall address spill prevention and control for all anticipated activities.
- Perform all maintenance, serving, and refueling of vehicles and equipment within the designated contractor yard(s).
- Keep all materials in original containers, labeled, to the extent possible, until use.
- Provide adequate and appropriate labeling of all waste product containers.
- Report any hazardous materials spills or related hazardous materials incidents to the following:
  - Call 911 immediately, for local emergency response.
  - Call Airport Operations.
  - Call 1-800-424-8802, the Environmental Protection Agency's (EPA), National Response Center.
  - Identify the caller, location, nearest point of access into airport (gate number), nature of the spill, current site condition, and specific hazardous substance and quantity if known, and how the spill or incident occurred.
  - For spills and incidents of potential significant impacts to the environment, identify date and time of spill, location of threatened waterway.
- Contractor's employees shall not attempt to clean the spill until it has been evaluated by the local emergency response agency. Only those employees with a Hazardous Material Certification shall be involved in the cleanup and then only under the direction of the local emergency response agency.

14. Notification of Construction Activity

1. The project contact list (Construction Team) will be made current at the conclusion of the Pre-Construction Conference, when all key team players have been identified. The contact list will be reviewed periodically at weekly construction progress meetings and updated as necessary throughout the duration of the project.

2. The Notice to Airman (NOTAM) system will be employed to provide project information including closure periods, out of service items, and scheduling updates, etc. The Airport Project Manager will provide active NOTAM management, uploading, and distribution of these to team members. NOTAM's must be issued and in-place before any airfield closures (and work) can occur. The Airport requires a minimum of 72 hours advance notice to publish a NOTAM. In the event a work period is canceled, the Airport can cancel a NOTAM immediately.

3. Local emergency responders including fire protection and law enforcement will be invited to attend the Pre-Construction Conference, to gain full knowledge of the extent and duration of the project. The Project Engineer will reach back out to these entities quarterly to remind them of the ongoing project, and to update any key members on the Construction team contact list.

4. Emergency Landing Procedures
   ****(No Runway closures with this project)****
   The most frequent event that can challenge airport work sites when runways are closed is the unplanned need for landing an aircraft. In the event the contractor's radio monitor is contacted by an aircraft requesting to land during construction hours, the contractor's radio monitor must engage the identifying aircraft and describe conditions on the ground at the airport (i.e. Runway 8-26 closed for construction).
   - He/she shall first confirm if an alternate runway is available and acceptable.
   - If no, then encourage the pilot to go elsewhere stating that "requested runway is closed" and identifying the two closest airports:
     - **Santa Maria Airport: 29.5 miles to the northwest**
     - **Santa Barbara Airport: 18 miles to the southeast**
     - **Lompoc Airport: 22 miles to the west**
   - Should the pilot insist on landing, the radio monitor shall ask the following questions:
     - "Are you declaring an emergency?"
     - "What is the nature of your emergency?"
     - "How much runway do you need?"
     - Followed by, "We will attempt to accommodate" and advising the pilot of any drop offs, loose debris, open trenches, or other possible hazards.

   The contractor shall temporally cease construction activities and clear the runway as quickly as possible. Time permitting, he shall turn on runway lights, following up to the aircraft specific characteristics about conditions on the ground and instructions for a preferred operation (ie: "first 2500 feet clear", "land early", "last 3,000 feet occupied with equipment", "equipment off right shoulder", etc. In all cases, the Radio Monitor to conclude each radio transmission to the pilot with **"Pilot Discretion".**

   Radio Monitor to contact emergency responders and identify the pending operation and nature of emergency and document the planes identification number (N number).

15. Inspection Requirements

The project RPR (Inspector) will be on-site full time, during all construction activities. Airport personnel will make periodic site visits to the project during construction to provide oversight and ensure the CSPP is being followed. The Project Engineer is responsible for ensuring the project is constructed in conformance with the contract, plans, and specifications. Should any deviations from the plans and specifications be observed, the Contractor will be required to immediately correct the deviations as instructed by the Project Engineer and/or Airport. Final acceptance of constructed improvements will be determined in accordance with the contract documents.

The Contractor shall identify a Construction Safety Officer in its Safety Plan Compliance Document (SPCD) as well as a single point of contact for each subcontractor involved on the project. These contacts will be incorporated into Table 2, Construction Team, in order to provide a comprehensive list of project contacts. The Contractor shall also outline in the SPCD its safety policy and internal inspection requirements to ensure airfield safety compliance.

During the re-opening of temporarily closed airfield pavements and facilities, Airport Personnel will have the final word on the acceptance of cleaned construction areas for aircraft operations. Refer to Section 12 for additional guidance on cleaning procedures prior to opening pavement.

Airport Personnel, Project Engineer, and RPR (Inspector) are not responsible for any escort, gate guard, placement of runway closure crosses and delineation, or other Contractor-required safety and security measures, duties, and responsibilities.

16. Underground Utilities

Utilities

Table 4

Organization	Role	Point of Contact	Contact Information
Airport Electrical	On-site airport electrical	Dave Romero	(805) 688-8390
Water: Santa Ynez River Water Conservation District	On-site water (including construction meter)	N/A	(805) 688-6015
PG&E	Power	N/A	
FAA	No on-airport facilities		
No other utilities on airfield			

The design team performed research into available records and as-built plans. All known underground utilities within the project footprint have been included / identified on the project plans and are shown to the best of our knowledge and ability. Facilities with the area of work are limited to Airport-Owned electrical infrastructure (conduits, conductors, junction boxes, edge lights, and guidance signs), and FAA-Owned electrical infrastructure (conduits, conductors, junction boxes, and above ground, visible navigation aids).

The contractor is required to investigate the site and become familiar with existing facilities. Such investigation includes potholing as necessary to confirm horizontal and vertical locations, especially at locations of potential conflict with designed underground facilities (electrical or storm drain).

All intentional interruptions or restorations of utilities, whether surface or underground, must be approved by and coordinated in advance with the Airport Manager.

All accidental interruptions of utilities must be immediately reported to Airport Operations and to the Project Engineer.

Certain utilities considered critical to the operations of the airport must be repaired immediately after any accidental interruption. In the event the party causing such interruption cannot perform the repair before the time limit as determined by the Airport Manager, the latter will have the option of having the repair done by either a private firm or Airport personnel. The resulting cost and expenses will be the sole responsibility of the party causing the interruption.

In the event of interruption or deactivation of waterlines, fire hydrants, or blocked and or rerouted emergency access routes Contractor shall immediately notify the Airport Manager and Airport Operations. The Airport Manager will in turn notify Emergency Response authorities. Procedures for this will be discussed at an Airport Safety Workshop put on by Tartaglia Engineering with the Contractor in attendance as part of the pre-construction conference.

17. Penalties

Table 6 identifies various CSPP and contract violations and associated consequences. Penalties apply to all team members on the field including the Project Engineer, Resident Project Representative, and Quality Assurance technicians.

Penalties for Noncompliance

Table 6

Violation	Consequence
Exceed work days allocation for construction: Overall contract	$500.00 per calendar day
Failure to facilitate runway opening at end of shift:	N/A. Runway remains open.
Access gate violation: Unattended gate, vehicle depart before fully closed, unauthorized third-party access	$2,000.00 per event
General airport perimeter security violation	$2,000 per event or per 24-hour period, as appropriate
Badge / escort violation: employees not under direct control of escort	1st occurrence: $500.00 fine & written warning
	2nd occurrence: $1,000.00 fine & permanent removal from project
Category A & B airfield incursion	**Construction Stand Down. All contractor (general and all sub's) activities stop immediately for the balance of the shift and the complete next shift. Time extension not granted for Stand Down. Mandatory Safety Meeting to review incident, CSPP and SPCD. Formulate plan to address issues. Revise SPCD.**
Category A & B airfield incursion	1st occurrence: $5,000.00 fine & permanent removal from project
	2nd occurrence: $10,000.00 fine, permanent removal from project of the offender and supervisor
Category C & D airfield incursion	1st occurrence: $2,000.00 fine & written warning
	2nd occurrence: $5,000.00 fine & permanent removal from project
Abnormal behavior deemed a risk to public safety	Permanent removal from project
General Safety Plan Violation	1st occurrence: $500.00 fine & written warning
	2nd occurrence: $1,000.00 fine & permanent removal from project

Financial penalties to be deducted from periodic pay requests when and if they occur, as appropriate.

18. Special Conditions

Airport operations take precedence over all work, especially if a question of safety is involved. Special conditions such as low visibility, aircraft in distress, aircraft accident, security breach, or work being

completed by others may require the rescheduling of Project Work to accomplish and preserve air safety. Full compensation for all costs involved in rescheduling and moving from one work area to another, including work stoppage caused by airport operations shall be considered as included in the contract prices paid for contract items of work and not additional compensation.

19. Runway and Taxiway Visual Aids

No modifications are anticipated to runway and taxiway visual aids.

20. Marking and Signs for Access Routes

The Contractor forces will recognize and acknowledge the airport will remain open during construction. “Runway Closed”, should that occur, does not mean “Airport Closed”.

Where access routes are on airfield pavements (runways, taxiways, aprons), Contractor to install low-profile barricades and / or delineators at periodic intervals along both sides of haul routes, from and between point of access (gate), yard, and work area. Emphasis shall be at all changes of direction where confusion regarding direction may exist. Delineators shall be installed at the start of each shift, maintained for the duration of each shift, and removed at the conclusion of each work period.

Delineators will be used as a means of traffic control, providing direction to contractor forces including material delivery vehicles, but also as an indication to pilots regarding active work areas and haul routes. At some closure locations, safety may be enhanced through the installation of two sets of closure delineators; one for aircraft that will help prevent aircraft from entering a taxiway that is closed at the other end, and one for contractor forces that will help prevent trucks and equipment from

Delineators are not required along those portions of access routes that are on airport perimeter roads outside active airport pavement areas. The Contractor shall, however, install delineation at locations where these routes enter airfield pavements and their respective object free areas. Signs shall also be installed and maintained at these locations stating, “Entering Active Airfield Area”, providing emphasis of the change of environment.

All access route delineation shall be removed from the site at the end of each shift unless placed outside object free areas or within object free areas of temporarily closed airfield facilities.

21. Hazard Marking and Lighting

Low profile barricades will be used as a method of traffic control. Barricades will be used to keep contractor forces including material delivery trucks within designated haul routes and within specific project work areas. In addition, these barricades will keep aircraft out of work zones.

Within the Safety Plan Compliance Document (SPCD), the Contractor shall identify additional means proposed to address those locations where haul / access routes cross open taxiways, including the establishment of contractor way points and radio-monitoring access / crossing guards.

Runway closure is not a part of this project. Runway closure crosses will not be employed during airfield facilities closures.

22. Work Zone Lighting for Nighttime Construction

Contractor forces shall install and maintain night shift area lighting for each night work period. Lights activated prior to closure shall be kept pointed down, below the horizontal plane, until after the runway is closed. During night shift operations that do not include runway closure, all work area lights shall remain pointed down below the horizontal plane for the duration of the shift. Balloon style lighting is acceptable (paving), when the runway(s) is/are closed. All work area lighting shall remain in the yard or outside the fence until after closure, then mobilized into position. Area lights to be removed from the work site back to the yard before any runway is re-opened.

Contractor shall comply with levels of illumination identified in Table 7 for the specific type and areas of work. Levels are considered minimums. Specific task or work areas may dictate enhanced night lighting for effective construction activities or increased safety.

Minimum Levels of Illumination

Table 7

Work Location or Type of Work	Illumination Level	Average Minimum Maintained Illuminance
• Contractor yard. • Contractor employee parking area. • Contractor point of access to airport (gate). • Within airport, haul route change of direction.	Level 1	2 foot-candles
• Haul route point of entry into specific work area. • Earthwork, grading, aggregate base. • Paving, chip seal, and slurry seal operations. • Pavement marking. • Rubber Removal • Crack fill and joint sealing	Level 2	5 foot-candles
• Electrical. • Drainage excavations, pipe placement, backfill. • Drainage structure placement / construction.	Level 3	10 foot-candles

Contractor to submit a Lighting Plan as a project submittal. The document shall identify how proposed minimum levels of illumination are to be met.

No night work required or anticipated for this project however the contractor may elect to work extended shifts, either starting early or continuing late, into periods of darkness. The contractor will only be required to prepare a Lighting Plan if work extends into darkness.

23. Protection of Specific and Individual Airport Safety Areas

A. Runway 8-26

All the work of this project is outside the Runway Object Free Area (ROFA) and the Runway Safety Area (RSA). Under no circumstances shall contractor personnel enter the ROFA and RSA.

B. Parallel and Connecting Taxiways to Runway

Portions of the work encroach into the Taxiway Object Free Area (TOFA) and Taxiway Safety Area (TSA) of parallel Taxiway A. The work on taxilane areas within the TOFA and TSA shall be identified in advance via NOTAM, and shall occur under radio authority. The RPR will coordinate and work with Contractor forces to facilitate short-term, temporary occupancy. In addition, all of the work of this project is on the main apron and hangar taxilanes.

C. Apron and Taxilanes

Work areas are to be phased based on activity, providing clear delineation to aircraft regarding acceptable paths of travel from and between hangar, taxiway, runway, terminal, and self-serve fuel. Contractor forces are to remain clear of the TOFA for Taxiway A. **Contractor encroachment into the ROFA, TOFA, RSA, and TSA is absolutely prohibited.**

24. Other Limitations on Construction

A. Prohibitions

a. No person (other than personnel so authorized) shall approach the scene of any emergency unless requested to do so by Airport personnel or as immediate lifesaving requires.
b. No torch-welding, open flame, material/equipment storage, or disposal of any waste material shall be authorized anywhere on the airport, except at designated locations and unless prior approval from Airport Staff or Project Engineer has been secured.

B. Restrictions

a. Construction inspection shall be full time anytime construction is taking place. All inspection and materials testing requirements are identified in the specifications and FAA advisory circulars.
b. All contractor forces shall comply with Cal-OSHA standards regarding protective headwear, footwear, and eyewear.
c. Appropriate markers acceptable to the Project Engineer shall be used to define the work area and hazardous condition within the “safety areas” of the “aircraft maneuvering area.”
d. Trench and excavation cover requirements are included in the specifications for this project. All open trenches, excavations, and stockpiled materials shall be prominently marked and lighted during the hours of restricted visibility and darkness. (Due to the nature of this project and tight physical relationship between areas of work, the runway, and taxiways, no open trenches allowed beyond each work window.)
e. All closed, deceptive, and hazardous areas resulting from construction activities shall be marked and lighted as appropriate.

C. Equipment Height

a. Prior to the start of construction, the Contractor shall provide a schedule of equipment anticipated to be serving this project to include specific heights. The Project Engineer shall review for confirmation that the equipment height identified in the Air-Space Analysis (FAA 7460-1) appropriately characterized the equipment to be used.

25. Third-Party Provider Obligations

In addition to general contractor forces, compliance with the requirements and obligations of the CSPP fall to all subcontractors, vendors, and service providers, collectively referred to as Third-Party Providers. Third Party Providers include, but are not necessarily limited to:

- Subcontractors
- Bulk material delivery entities (aggregate base, asphalt, concrete, pipe, pre-cast structures)
- Common carrier delivery entities (airfield electrical, signs, minor parts)
- Field mechanics
- Fuel delivery
- Equipment delivery
- Solid waste
- Sanitary service providers
- Field office housekeeping providers
- Field surveyors
- Quality Control and Quality Assurance materials testing entities
- Union representatives and sales forces

The general contractor is responsible for and shall manage 100% of all individuals and entities that enter the secured Airport Operations Area (AOA). This is an active management task, from initiation of project through final completion.

To facilitate and support general contractor management obligations, the contractor shall have on file and shall include in the Safety Plan Compliance Document (SPCD), the letter below, signed by at least two representatives of each Third-Party Provider, before each provider is allowed within the secured airport (electronic file to be provided for general contractor use). Additional, signed letters shall be forwarded to the RPR by third party providers as the need for them develops.

ABC General Contractor
Xxx Street
City, State, Zip

Date

Project: **Rehabilitate Apron and Taxilanes**
Airport: **Santa Ynez Airport, Santa Barbara County**
Subject: Construction Safety Phasing Plan Compliance

Dear Project Manager:

XYZ, a (subcontractor, vendor, service provider), will be working with and serving your firm on this project, to occur within the Airport Operations Area (AOA) of a general aviation airport. The airport will be open and active during our work. Preserving airport perimeter security and performing our tasks within the AOA in a safe manner is paramount to the overall success of the project with concurrent safe, ongoing airport operations.

A Construction Safety Phasing Plan (CSPP) has been prepared specifically for this project. We have reviewed and understand the CSPP, and fully intend to comply with its contents and requirements. We recognize the various financial penalties associated with failure to comply and acknowledge these obligations will be assessed to the general contractor, to be passed down to our firm in the event it is determined we were partially or fully responsible for an incident, accident, incursion, or breach of security.

Airfield Safety:

1. Private vehicles to remain outside the fence.
2. All vehicles to have a functioning amber beacon at night and a safety flag or beacon during the day.
3. Access on and around the airport is restricted. We are not to assume a clear, open path between our location and workers on the airfield.
4. We are to remain clear of all runway and taxiway object free areas unless they are closed or unless we are escorted by an individual maintaining radio contact with active aircraft.
5. Designated safety areas are larger than the pavements they serve and protect. Unauthorized access into a safety area is considered an incursion, subject to financial penalty.
6. We are to clean all active airfield pavements of dirt, dust, rock, or other debris after passing.
7. Aircraft have the right-of-way. Maximum vehicle speed on an airport is 15 miles per hour.

National Security:

1. Preserving the secured airport perimeter is a matter of national security.
2. Strict adherence to protocol is required when entering and exiting the airport.
3. Access to the airport and the work site is a privilege that can be revoked at any time.
4. When entering / exiting through an automatic / electric gate, we are required to remain in proximity until the gate comes to a complete close.
5. When entering / exiting through a manual gate, we are to close and fully lock the gate behind us.
6. At any time entering / exiting the airport, we are to be prepared and capable of denying access to anyone that is not in our charge.
7. Those with pre-existing authority to enter the airport will do-so on their own accord and will respect our insistence that they wait until we have completed our movement.

These summary requirements, along with the overall safety and security requirements of this project, as detailed in the CSPP, are understood and acknowledged.

Manager	Staff
Cell Phone	Cell Phone

No third-party provider shall be allowed within the secured airport area without first providing the signed letter to the general contractor. The general contractor shall create and maintain a list of Third-Party Providers that are current and authorized to access the airport.

26. Appendix

A. Figure 1: Project Layout Plan

B. Figure 2: Phasing Plan

End of Text.

LEGEND:

- CONTROL POINT
- AREA OF IMPROVEMENTS
- CONTRACTOR PATH OF TRAVEL
- BRL — BUILDING RESTRICTION LINE (BRL)
- HYDRANT
- ROFA — RUNWAY OBJECT FREE AREA (ROFA)
- PL — AIRPORT PROPERTY LINE
- B — TAXIWAY DESIGNATION
- CONTRACTOR YARD
- G — G — AIRPORT ACCESS GATE
- RUNWAY PROTECTION ZONE (RPZ)
- TOFA — TAXIWAY OBJECT FREE AREA (TOFA)

GRAPHIC SCALE

100 0 50 100 200 400

(IN FEET)
1 inch = 100 ft.

BASIS OF BEARING:

THE BASIS OF BEARINGS FOR THIS SURVEY IS THE CALIFORNIA COORDINATE SYSTEM, ZONE 5, NAD83–2011, EPOCH 2010.0000, HOLDING IZA A 1989 FOR POSITION AND THE BEARING BETWEEN IZA A 1989 AND IZA B 1989 FOR LINE.


BENCHMARK:

NORTH AMERICAN VERTICAL DATUM OF 1988 (NAVD88), HOLDING IZA A 1989 WITH AN ELEVATION OF 678.00' NAVD88.

CONTROL POINTS:

NAD83–2011 Epoch 2010.000
NAVD88

Pt. No.	Northing	Easting	Elev	Description
10	2049859.91	5938222.12	672.87	MAG & SHINER
11	2050066.99	5937897.19	673.30	SCRIBED X IN TC
1001	2050214.76	5937224.85	674.74	Set No.5 Rebar & Plastic Cap "Control Point"
1005	2049690.94	5938540.72	672.17	Set X in Concrete
1006	2049824.12	5938562.54	673.50	Set X in Concrete
1007	2049909.66	5938074.97	672.13	Set X in Concrete
1008	2050037.16	5937838.95	673.19	Set X in Concrete
1009	2050080.52	5937568.27	673.09	Set X in Concrete
1010	2050014.00	5937039.79	667.89	Set X in Concrete
1011	2050311.03	5937095.24	667.31	Set X in Concrete
1012	2050291.14	5936959.65	668.07	Set X in Concrete
1013	2050056.23	5936920.62	667.73	Set X in Concrete
1014	2050076.83	5936789.90	667.62	Set X in Concrete
1015	2050049.63	5936657.84	667.13	Set X in Concrete
1016	2050398.21	5936715.45	667.51	Set X in Concrete
1017	2050366.67	5936838.13	668.03	Set X in Concrete
1018	2049904.03	5936837.75	663.60	Set X in Concrete
1019	2049845.74	5937258.53	668.36	Set No.5 Rebar & Plastic Cap "Control Point"
1020	2049765.31	5937679.42	668.62	Set X in Concrete
1021	2049715.72	5938035.26	670.79	Set No.5 Rebar & Plastic Cap "Control Point"
1022	2050416.92	5936534.85	663.60	SET X
1023	2050088.43	5936480.62	663.030,	SET X
1024	2049997.94	5936498.98,	660.429,	SET X
1025	2050442.66	5936341.87	662.174,	SET X
1026	2050185.99	5936299.31	661.786,	SET X
1027	2050028.35,	5936151.86	657.508,	SET X
1028	2050355.66,	5936115.53	663.825,	SET X
1029	2050434.58	5936048.65	664.877,	SET MAG+TIN
1030	2050072.48	5936009.71	658.638,	SET X
6009	2048953.09	5939112.41	678.00	3" NOS Disk IZA A 1989
6010	2049568.95	5935431.17	661.30	3" NOS Disk IZA B 1989

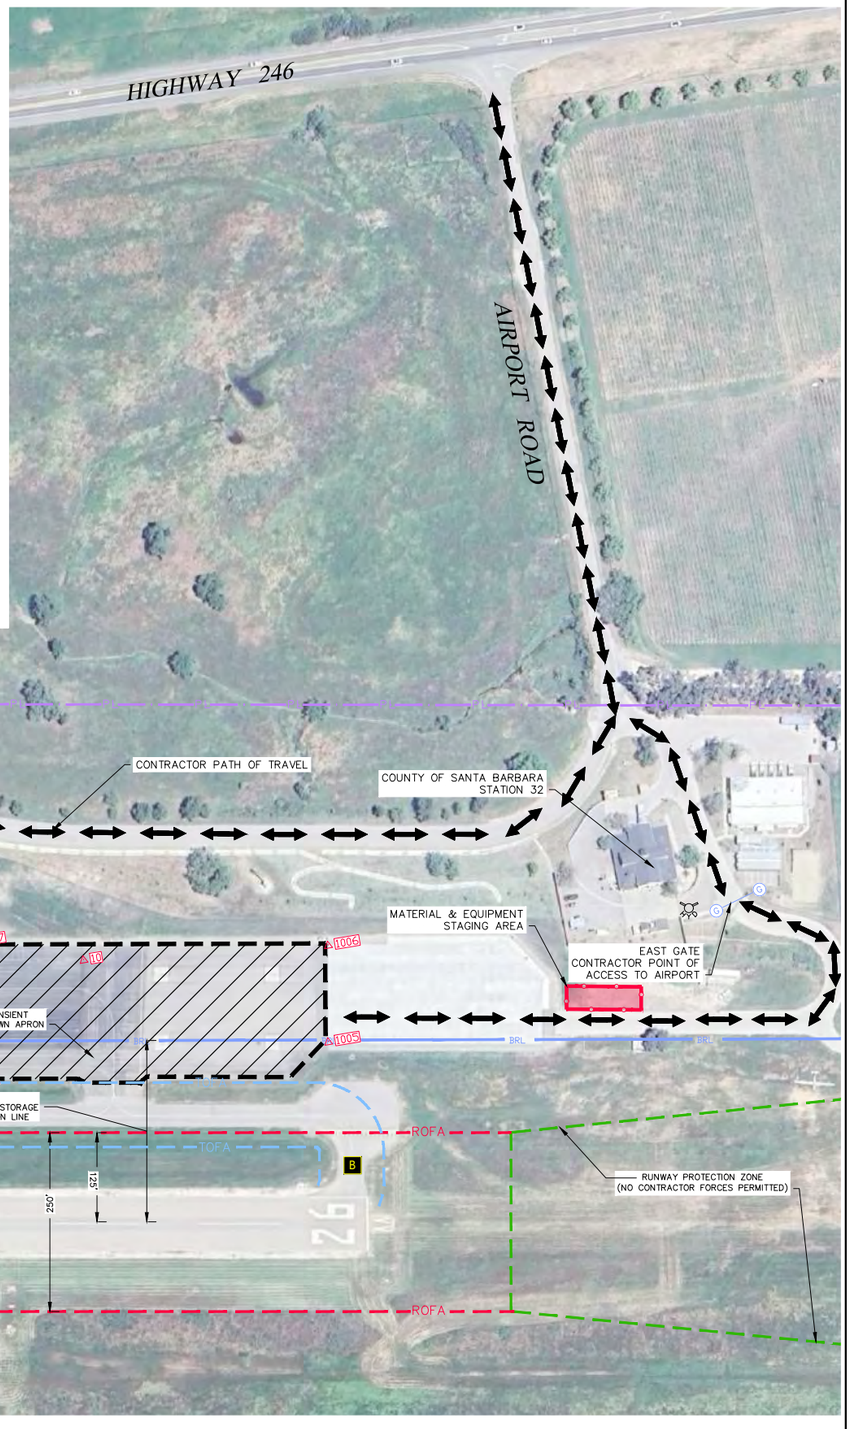

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

PROJECT LAYOUT PLAN

PLAN VIEW AND PROJECT CONTROL

REV.	DESCRIPTION	DATE	APP.
1	-	-	-

TARTAGLIA ENGINEERING


SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON


REGISTERED PROFESSIONAL ENGINEER — JOHN A. SMYTH — No. 46852 — EXP. 6-30-25 — CIVIL — STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22-55
DATE 8/10/2024
SHEET 3 of 14


PLOT DATE: 8/11/2025

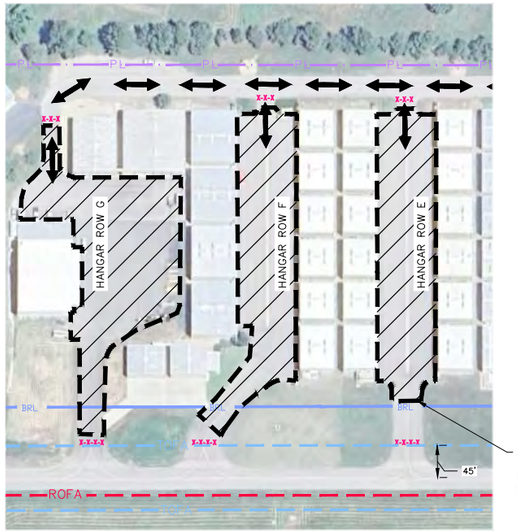


A/4 PHASE 1

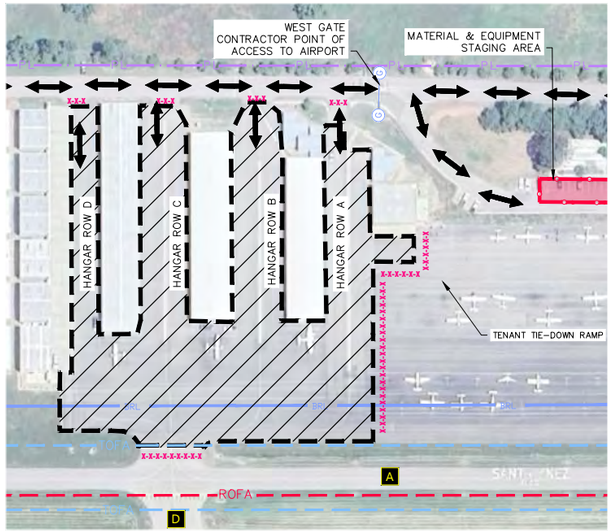

B/4 PHASE 2

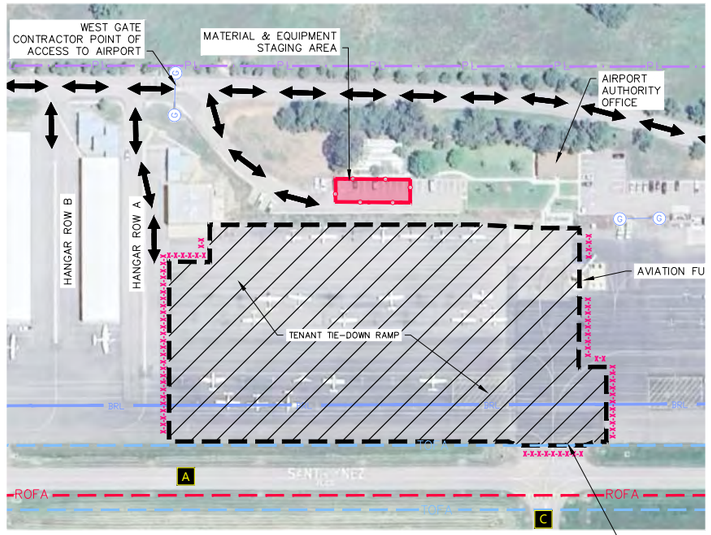

C/4 PHASE 3

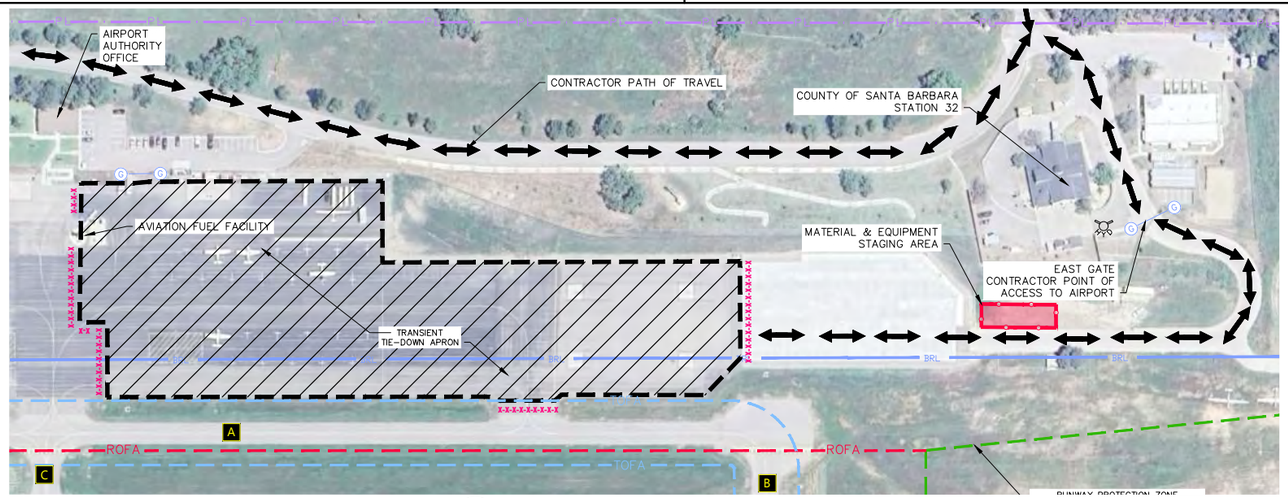

D/4 PHASE 4

LEGEND:

- LOW PROFILE DELINEATION (SEE DETAIL A, SHEET 2)
- AREA OF IMPROVEMENTS
- CONTRACTOR PATH OF TRAVEL
- BRL — BUILDING RESTRICTION LINE (BRL)
- HYDRANT
- ROFA — RUNWAY OBJECT FREE AREA (ROFA)
- PL — AIRPORT PROPERTY LINE
- B — TAXIWAY DESIGNATION
- CONTRACTOR YARD
- G — G — AIRPORT ACCESS GATE
- RUNWAY PROTECTION ZONE (RPZ)
- TOFA — TAXIWAY OBJECT FREE AREA (TOFA)

PHASING SUMMARY TABLE

PHASE	WORK AREAS	GENERAL WORK SUMMARY	DURATION
1	HANGAR ROWS E, F, & G	CRACK FILL & SEAL, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	7 WORKING DAYS
2	HANGAR ROWS A, B, C, & D	CRACK FILL & SEAL, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	8 WORKING DAYS
3	TENANT TIE-DOWN APRON	CRACK FILL & SEAL, REMOVAL & RE-INSTALLATION OF TIE-DOWN COMPONENTS, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	15 WORKING DAYS
TRANSITION		TRANSITION PERIOED TO ALLOW TENANTS TO RE-LOCATE AIRCRAFT BEFORE PHASE 4 BEGINS.	3 CALENDAR DAYS
4	TRANSIENT TIE-DOWN APRON	CRACK FILL & SEAL, REMOVAL & RE-INSTALLATION OF TIE-DOWN COMPONENTS, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	15 WORKING DAYS
5	ENTIRE PROJECT WORK AREA	SECOND COAT OF PAVEMENT MARKINGS	5 WORKING DAYS
TOTAL			50 WORKING DAYS

PHASING NOTES:

1. WORK SHALL BE ACCOMPLISHED IN A PHASED APPROACH. THE WORK OF ONE PHASE SHALL BE COMPLETE, THE WORK AREA CLEANED, AND ALL ACCEPTED BY THE INSPECTOR BEFORE PROCEEDING TO THE NEXT PHASE. THE ONLY EXCEPTION TO THIS IS THE APPLICATION OF THE SECOND COAT OF PERMANENT PAVEMENT MARKINGS.
2. ALL SECOND COAT OF PERMANENT PAVEMENT MARKINGS TO OCCUR IN ONE MOVE IN, 30 DAYS+ AFTER THE FIRST COAT OF MARKINGS APPLIED DURING PHASE 4. A CONTRACT TIME SUSPENSION WILL OCCUR BETWEEN PHASE 4 AND PHASE 5 TO ALLOW FOR THE 30 DAYS OF CURE BEFORE APPLICATION OF THE SECOND COAT OF MARKINGS.
3. CONTRACTOR TO PREPARE A WORK PLAN FOR PHASE 5; SECOND COAT OF PAVEMENT MARKINGS. ENGINEER SHALL APPROVE THE WORK PLAN BEFORE ANY WORK BEGINS IN THIS PHASE. WORK PLAN SHALL CONSIDER AIRCRAFT OPERATIONS: ALLOW AIRCRAFT TO ACCESS THE FUEL FARM, TWO OF THE THREE TAXIWAY CONNECTORS BETWEEN TAXIWAY ALPHA AND THE APRON SHALL BE OPEN AT ALL TIMES. IT IS ANTICIPATED THAT THE WORK AREAS WILL BE SPLIT UP INTO THREE OR FOUR AREAS. LOW PROFILE DELINEATION IS REQUIRED TO CLOSE DOWN THE WORK AREA UNTIL THE PAVEMENT MARKINGS ARE DRY, AND THE MARKINGS ARE ACCEPTED BY THE RPR, BEFORE PROCEEDING TO ANOTHER WORK AREA.
4. DEPENDING ON TIME OF CONSTRUCTION START DATE, THE ORDER OF PHASE 1, 2, 3 AND 4 WORK MAY SHIFT OR CHANGE.
5. A PHASE TRANSITION PERIOD OF 3 CALENDAR DAYS WILL OCCUR BETWEEN PHASES 3 & 4 TO ALLOW TENANTS TO RE-LOCATE AIRCRAFT TO FACILITATE WORK ON THE SUBSEQUENT PHASE. DURING THIS PERIOD, NO CONTRACT WORKING DAYS WILL BR COUNTED TOWARDS ANY SPECIFIC PHASE OR THE OVERALL CONTRACT DURATION.
6. LOW PROFILE BARRICADES SHALL BE PLACED AT LOCATIONS SHOWN ON THESE PHASING PLANS. BARRICADES FOR DELINEATION SHALL BE INSTALLED AT THE BEGINNING OF THE PHASE, REMAIN IN-PLACE FOR THE DURATION OF THE PHASE (24 HOURS, 7 DAYS A WEEK) AND REMOVED WHEN THE PHASE IS COMPLETE AND ACCEPTED BY THE INSPECTOR. REFER TO DETAIL A, SHEET 2 FOR LOW PROFILE BARRICADE DETAIL.

UNDERGROUND SERVICE ALERT
811
DIAL 811
TWO WORKING DAYS BEFORE YOU DIG

PHASING PLAN

PHASE 1 THROUGH 5

REV.	DESCRIPTION	DATE	APP.
1	-	-	-

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER — JOHN A. SMITH — No. 46852 — EXP. 6-30-25 — CIVIL — STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22-55
DATE 8/10/2024
SHEET 4 OF 14

PLOT DATE: 8/13/2025

APPENDIX B

ADVISORY CIRCULAR 150/5370-2G: OPERATIONAL SAFETY ON AIRPORTS DURING CONSTRUCTION

U.S. Department
of Transportation
Federal Aviation
Administration

Advisory Circular

Subject: Operational Safety on Airports During Construction	**Date:** 12/13/2017 **Initiated By:** AAS-100	**AC No:** 150/5370-2G **Change:**

1 **Purpose.**

This AC sets forth guidelines for operational safety on airports during construction.

2 **Cancellation.**

This AC cancels AC 150/5370-2F, *Operational Safety on Airports during Construction,* dated September 29, 2011.

3 **Application.**

This AC assists airport operators in complying with Title 14 Code of Federal Regulations (CFR) Part 139, *Certification of Airports*. For those certificated airports, this AC provides one way, but not the only way, of meeting those requirements. The use of this AC is mandatory for those airport construction projects receiving funds under the Airport Improvement Program (AIP). See Grant Assurance No. 34, *Policies, Standards, and Specifications*. While we do not require non-certificated airports without grant agreements or airports using Passenger Facility Charge (PFC) Program funds for construction projects to adhere to these guidelines, we recommend that they do so to help these airports maintain operational safety during construction.

4 **Related Documents.**

ACs and Orders referenced in the text of this AC do not include a revision letter, as they refer to the latest version. Appendix A contains a list of reading material on airport construction, design, and potential safety hazards during construction, as well as instructions for obtaining these documents.

5 **Principal Changes.**

The AC incorporates the following principal changes:

1. Notification about impacts to both airport owned and FAA-owned NAVAIDs was added. See paragraph 2.13.5.3, NAVAIDs.

2. Guidance for the use of orange construction signs was added. See paragraph 2.18.4.2, Temporary Signs.
3. Open trenches or excavations may be permitted in the taxiway safety area while the taxiway is open to aircraft operations, subject to restrictions. See paragraph 2.22.3.4, Excavations.
4. Guidance for temporary shortened runways and displaced thresholds has been enhanced. See Figure 2-1 and Figure 2-2.
5. Figures have been improved and a new Appendix F on the placement of orange construction signs has been added.

Hyperlinks (allowing the reader to access documents located on the internet and to maneuver within this document) are provided throughout this document and are identified with underlined text. When navigating within this document, return to the previously viewed page by pressing the "ALT" and " ←" keys simultaneously.

Figures in this document are schematic representations and are not to scale.

6 **Use of Metrics.**


Throughout this AC, U.S. customary units are used followed with "soft" (rounded) conversion to metric units. The U.S. customary units govern.

7 **Where to Find this AC.**

You can view a list of all ACs at http://www.faa.gov/regulations_policies/advisory_circulars/. You can view the Federal Aviation Regulations at http://www.faa.gov/regulations_policies/faa_regulations/.

8 **Feedback on this AC.**

If you have suggestions for improving this AC, you may use the Advisory Circular Feedback form at the end of this AC.



John R. Dermody
Director of Airport Safety and Standards

CONTENTS

Paragraph **Page**

Chapter 1. Planning an Airfield Construction Project 1-1
1.1 Overview. 1-1
1.2 Plan for Safety. 1-1
1.3 Develop a Construction Safety and Phasing Plan (CSPP). 1-3
1.4 Who Is Responsible for Safety During Construction? 1-4

Chapter 2. Construction Safety and Phasing Plans 2-1
2.1 Overview. 2-1
2.2 Assume Responsibility. 2-1
2.3 Submit the CSPP. 2-1
2.4 Meet CSPP Requirements. 2-2
2.5 Coordination. 2-6
2.6 Phasing. 2-7
2.7 Areas and Operations Affected by Construction Activity. 2-7
2.8 Navigation Aid (NAVAID) Protection. 2-11
2.9 Contractor Access. 2-11
2.10 Wildlife Management. 2-15
2.11 Foreign Object Debris (FOD) Management. 2-16
2.12 Hazardous Materials (HAZMAT) Management. 2-16
2.13 Notification of Construction Activities. 2-16
2.14 Inspection Requirements. 2-18
2.15 Underground Utilities. 2-19
2.16 Penalties. 2-19
2.17 Special Conditions. 2-19
2.18 Runway and Taxiway Visual Aids. 2-19
2.19 Marking and Signs for Access Routes. 2-29
2.20 Hazard Marking, Lighting and Signing. 2-30
2.21 Work Zone Lighting for Nighttime Construction. 2-32
2.22 Protection of Runway and Taxiway Safety Areas. 2-33
2.23 Other Limitations on Construction. 2-37

Chapter 3. Guidelines for Writing a CSPP 3-1
3.1 General Requirements. 3-1
3.2 Applicability of Subjects. 3-1
3.3 Graphical Representations. 3-1
3.4 Reference Documents. 3-2
3.5 Restrictions. 3-2
3.6 Coordination. 3-2
3.7 Phasing. 3-2
3.8 Areas and Operations Affected by Construction. 3-2
3.9 NAVAID Protection. 3-2
3.10 Contractor Access. 3-3
3.11 Wildlife Management. 3-4
3.12 FOD Management. 3-4
3.13 HAZMAT Management. 3-4
3.14 Notification of Construction Activities. 3-4
3.15 Inspection Requirements. 3-5
3.16 Underground Utilities. 3-5
3.17 Penalties. 3-5
3.18 Special Conditions. 3-5
3.19 Runway and Taxiway Visual Aids. 3-6
3.20 Marking and Signs for Access Routes. 3-6
3.21 Hazard Marking and Lighting. 3-6
3.22 Work Zone Lighting for Nighttime Construction. 3-6
3.23 Protection of Runway and Taxiway Safety Areas. 3-7
3.24 Other Limitations on Construction. 3-7

Appendix A. Related Reading Material A-1

Appendix B. Terms and Acronyms B-1

Appendix C. Safety and Phasing Plan Checklist C-1

Appendix D. Construction Project Daily Safety Inspection Checklist D-1

Appendix E. Sample Operational Effects Table E-1

Appendix F. Orange Construction Signs F-1

FIGURES

Number **Page**

Figure 2-1. Temporary Partially Closed Runway 2-9
Figure 2-2. Temporary Displaced Threshold 2-10
Figure 2-3. Markings for a Temporarily Closed Runway 2-21
Figure 2-4. Temporary Taxiway Closure 2-22
Figure 2-5. Temporary Outboard White Threshold Bars and Yellow Arrowheads 2-24
Figure 2-6. Lighted X in Daytime 2-26
Figure 2-7. Lighted X at Night 2-26
Figure 2-8. Interlocking Barricades 2-31
Figure 2-9. Low Profile Barricades 2-32
Figure E-1. Phase I Example E-1
Figure E-2. Phase II Example E-2
Figure E-3. Phase III Example E-3
Figure F-1. Approved Sign Legends F-1
Figure F-2. Orange Construction Sign Example 1 ..... F-2
Figure F-3. Orange Construction Sign Example 2 ..... F-3

TABLES

Number **Page**

Table A-1. FAA Publications A-1
Table A-2. Code of Federal Regulation A-3
Table B-1. Terms and Acronyms B-1
Table C-1. CSPP Checklist C-1
Table D-1. Potentially Hazardous Conditions D-1
Table E-1. Operational Effects Table E-4
Table E-2. Runway and Taxiway Edge Protection E-6
Table E-3. Protection Prior to Runway Threshold E-7

Page Intentionally Blank

CHAPTER 1. PLANNING AN AIRFIELD CONSTRUCTION PROJECT

1.1 Overview.

Airports are complex environments, and procedures and conditions associated with construction activities often affect aircraft operations and can jeopardize operational safety. Safety considerations are paramount and may make operational impacts unavoidable. However, careful planning, scheduling, and coordination of construction activities can minimize disruption of normal aircraft operations and avoid situations that compromise the airport's operational safety. The airport operator must understand how construction activities and aircraft operations affect one another to be able to develop an effective plan to complete the project. While the guidance in this AC is primarily used for construction operations, the concepts, methods and procedures described may also enhance the day-to-day airport maintenance operations, such as lighting maintenance and snow removal operations.

1.2 Plan for Safety.

Safety, maintaining aircraft operations, and construction costs are all interrelated. Since safety must not be compromised, the airport operator must strike a balance between maintaining aircraft operations and construction costs. This balance will vary widely depending on the operational needs and resources of the airport and will require early coordination with airport users and the FAA. As the project design progresses, the necessary construction locations, activities, and associated costs will be identified and their impact to airport operations must be assessed. Adjustments are made to the proposed construction activities, often by phasing the project, and/or to airport operations to maintain operational safety. This planning effort will ultimately result in a project Construction Safety and Phasing Plan (CSPP). The development of the CSPP takes place through the following five steps:

1.2.1 Identify Affected Areas.

The airport operator must determine the geographic areas on the airport affected by the construction project. Some, such as a runway extension, will be defined by the project. Others may be variable, such as the location of haul routes and material stockpiles.

1.2.2 Describe Current Operations.

Identify the normal airport operations in each affected area for each phase of the project. This becomes the baseline from which the impact on operations by construction activities can be measured. This should include a narrative of the typical users and aircraft operating within the affected areas. It should also include information related to airport operations: the Aircraft Approach Category (AAC) and Airplane Design Group (ADG) of the airplanes that operate on each runway; the ADG and Taxiway Design Group (TDG)[1] for each affected taxiway; designated approach visibility minimums;

[1] Find Taxiway Design Group information in AC 150/5300-13, *Airport Design.*

available approach and departure procedures; most demanding aircraft; declared distances; available air traffic control services; airport Surface Movement Guidance and Control System (SMGCS) plan; and others. The applicable seasons, days and times for certain operations should also be identified as applicable.

1.2.3 Allow for Temporary Changes to Operations.

To the extent practical, current airport operations should be maintained during the construction. In consultation with airport users, Aircraft Rescue and Fire Fighting (ARFF) personnel, and FAA Air Traffic Organization (ATO) personnel, the airport operator should identify and prioritize the airport's most important operations. The construction activities should be planned, through project phasing if necessary, to safely accommodate these operations. When the construction activities cannot be adjusted to safely maintain current operations, regardless of their importance, then the operations must be revised accordingly. Allowable changes include temporary revisions to approach procedures, restricting certain aircraft to specific runways and taxiways, suspension of certain operations, decreased weights for some aircraft due to shortened runways, and other changes. An example of a table showing temporary operations versus current operations is shown in Appendix E.

1.2.4 Take Required Measures to Revise Operations.

Once the level and type of aircraft operations to be maintained are identified, the airport operator must determine the measures required to safely conduct the planned operations during the construction. These measures will result in associated costs, which can be broadly interpreted to include not only direct construction costs, but also loss of revenue from impacted operations. Analysis of costs may indicate a need to reevaluate allowable changes to operations. As aircraft operations and allowable changes will vary widely among airports, this AC presents general guidance on those subjects.

1.2.5 Manage Safety Risk.

The FAA is committed to incorporating proactive safety risk management (SRM) tools into its decision-making processes. FAA Order 5200.11, *FAA Airports (ARP) Safety Management System (SMS)*, requires the FAA to conduct a Safety Assessment for certain triggering actions. Certain airport projects may require the airport operator to provide a Project Proposal Summary to help the FAA determine whether a Safety Assessment is required prior to FAA approval of the CSPP. The airport operator must coordinate with the appropriate FAA Airports Regional or District Office early in the development of the CSPP to determine the need for a Safety Risk Assessment. If the FAA requires an assessment, the airport operator must at a minimum:

1. Notify the appropriate FAA Airports Regional or District Office during the project "scope development" phase of any project requiring a CSPP.
2. Provide documents identified by the FAA as necessary to conduct SRM.
3. Participate in the SRM process for airport projects.
4. Provide a representative to participate on the SRM panel.

5. Ensure that all applicable SRM identified risks elements are recorded and mitigated within the CSPP.

1.3 Develop a Construction Safety and Phasing Plan (CSPP).

Development of an effective CSPP will require familiarity with many other documents referenced throughout this AC. See Appendix A for a list of related reading material.

1.3.1 List Requirements.

A CSPP must be developed for each on-airfield construction project funded by the Airport Improvement Program (AIP) or located on an airport certificated under Part 139. For on-airfield construction projects at Part 139 airports funded without AIP funds, the preparation of a CSPP represents an acceptable method the certificate holder may use to meet Part 139 requirements during airfield construction activity. As per FAA Order 5200.11, projects that require Safety Assessments do not include construction, rehabilitation, or change of any facility that is entirely outside the air operations area, does not involve any expansion of the facility envelope and does not involve construction equipment, haul routes or placement of material in locations that require access to the air operations area, increase the facility envelope, or impact line-of-sight. Such facilities may include passenger terminals and parking or other structures. However, extraordinary circumstances may trigger the need for a Safety Assessment and a CSPP. The CSPP is subject to subsequent review and approval under the FAA's Safety Risk Management procedures (see paragraph 1.2.5).

1.3.2 Prepare a Safety Plan Compliance Document (SPCD).

The Safety Plan Compliance Document (SPCD) details how the contractor will comply with the CSPP. Also, it will not be possible to determine all safety plan details (for example specific hazard equipment and lighting, contractor's points of contact, construction equipment heights) during the development of the CSPP. The successful contractor must define such details by preparing an SPCD that the airport operator reviews for approval prior to issuance of a notice-to-proceed. The SPCD is a subset of the CSPP, similar to how a shop drawing review is a subset to the technical specifications.

1.3.3 Assume Responsibility for the CSPP.

The airport operator is responsible for establishing and enforcing the CSPP. The airport operator may use the services of an engineering consultant to help develop the CSPP. However, writing the CSPP cannot be delegated to the construction contractor. Only those details the airport operator determines cannot be addressed before contract award are developed by the contractor and submitted for approval as the SPCD. The SPCD does not restate nor propose differences to provisions already addressed in the CSPP.

1.4 Who Is Responsible for Safety During Construction?

1.4.1 Establish a Safety Culture.

Everyone has a role in operational safety on airports during construction: the airport operator, the airport's consultants, the construction contractor and subcontractors, airport users, airport tenants, ARFF personnel, Air Traffic personnel, including Technical Operations personnel, FAA Airports Division personnel, and others, such as military personnel at any airport supporting military operations (e.g. national guard or a joint use facility). Close communication and coordination between all affected parties is the key to maintaining safe operations. Such communication and coordination should start at the project scoping meeting and continue through the completion of the project. The airport operator and contractor should conduct onsite safety inspections throughout the project and immediately remedy any deficiencies, whether caused by negligence, oversight, or project scope change.

1.4.2 Assess Airport Operator's Responsibilities.

An airport operator has overall responsibility for all activities on an airport, including construction. This includes the predesign, design, preconstruction, construction, and inspection phases. Additional information on the responsibilities listed below can be found throughout this AC. The airport operator must:

1.4.2.1 Develop a CSPP that complies with the safety guidelines of Chapter 2, Construction Safety and Phasing Plans, and Chapter 3, Guidelines for Writing a CSPP. The airport operator may develop the CSPP internally or have a consultant develop the CSPP for approval by the airport operator. For tenant sponsored projects, approve a CSPP developed by the tenant or its consultant.

1.4.2.2 Require, review and approve the SPCD by the contractor that indicates how it will comply with the CSPP and provides details that cannot be determined before contract award.

1.4.2.3 Convene a preconstruction meeting with the construction contractor, consultant, airport employees and, if appropriate, tenant sponsor and other tenants to review and discuss project safety before beginning construction activity. The appropriate FAA representatives should be invited to attend the meeting. See AC 150/5370-12, *Quality Management for Federally Funded Airport Construction Projects.* (Note "FAA" refers to the Airports Regional or District Office, the Air Traffic Organization, Flight Standards Service, and other offices that support airport operations, flight regulations, and construction/environmental policies.)

1.4.2.4 Ensure contact information is accurate for each representative/point of contact identified in the CSPP and SPCD.

1.4.2.5 Hold weekly or, if necessary, daily safety meetings with all affected parties to coordinate activities.

1.4.2.6 Notify users, ARFF personnel, and FAA ATO personnel of construction and conditions that may adversely affect the operational safety of the airport via Notices to Airmen (NOTAM) and other methods, as appropriate. Convene a meeting for review and discussion if necessary.

1.4.2.7 Ensure construction personnel know applicable airport procedures and changes to those procedures that may affect their work.

1.4.2.8 Ensure that all temporary construction signs are located per the scheduled list for each phase of the project.

1.4.2.9 Ensure construction contractors and subcontractors undergo training required by the CSPP and SPCD.

1.4.2.10 Ensure vehicle and pedestrian operations addressed in the CSPP and SPCD are coordinated with airport tenants, the airport traffic control tower (ATCT), and construction contractors.

1.4.2.11 At certificated airports, ensure each CSPP and SPCD is consistent with Part 139.

1.4.2.12 Conduct inspections sufficiently frequently to ensure construction contractors and tenants comply with the CSPP and SPCD and that there are no altered construction activities that could create potential safety hazards.

1.4.2.13 Take immediate action to resolve safety deficiencies.

1.4.2.14 At airports subject to 49 CFR Part 1542, *Airport Security*, ensure construction access complies with the security requirements of that regulation.

1.4.2.15 Notify appropriate parties when conditions exist that invoke provisions of the CSPP and SPCD (for example, implementation of low-visibility operations).

1.4.2.16 Ensure prompt submittal of a Notice of Proposed Construction or Alteration (Form 7460-1) for conducting an aeronautical study of potential obstructions such as tall equipment (cranes, concrete pumps, other), stock piles, and haul routes. A separate form may be filed for each potential obstruction, or one form may be filed describing the entire construction area and maximum equipment height. In the latter case, a separate form must be filed for any object beyond or higher than the originally evaluated area/height. The FAA encourages online submittal of forms for expediency at https://oeaaa.faa.gov/oeaaa/external/portal.jsp. The appropriate FAA Airports Regional or District Office can provide assistance in determining which objects require an aeronautical study.

1.4.2.17 Ensure prompt transmission of the Airport Sponsor Strategic Event Submission, FAA Form 6000-26, located at https://oeaaa.faa.gov/oeaaa/external/content/AIRPORT_SPONSOR_STRATEGIC_EVENT_SUBMISSION_FORM.pdf, to assure proper coordination for NAS Strategic Interruption per Service Level Agreement with ATO.

1.4.2.18 Promptly notify the FAA Airports Regional or District Office of any proposed changes to the CSPP prior to implementation of the change. Changes to the CSPP require review and approval by the airport operator and the FAA. The FAA Airports Regional or District office will determine if further coordination within the FAA is needed. Coordinate with appropriate local and other federal government agencies, such as Environmental Protection Agency (EPA), Occupational Safety and Health Administration (OSHA), Transportation Security Administration (TSA), and the state environmental agency.

1.4.3 Define Construction Contractor's Responsibilities.

The contractor is responsible for complying with the CSPP and SPCD. The contractor must:

1.4.3.1 Submit a Safety Plan Compliance Document (SPCD) to the airport operator describing how it will comply with the requirements of the CSPP and supply any details that could not be determined before contract award. The SPCD must include a certification statement by the contractor, indicating an understanding of the operational safety requirements of the CSPP and the assertion of compliance with the approved CSPP and SPCD unless written approval is granted by the airport operator. Any construction practice proposed by the contractor that does not conform to the CSPP and SPCD may impact the airport's operational safety and will require a revision to the CSPP and SPCD and re-coordination with the airport operator and the FAA in advance.

1.4.3.2 Have available at all times copies of the CSPP and SPCD for reference by the airport operator and its representatives, and by subcontractors and contractor employees.

1.4.3.3 Ensure that construction personnel are familiar with safety procedures and regulations on the airport. Provide a point of contact who will coordinate an immediate response to correct any construction-related activity that may adversely affect the operational safety of the airport. Many projects will require 24-hour coverage.

1.4.3.4 Identify in the SPCD the contractor's on-site employees responsible for monitoring compliance with the CSPP and SPCD during construction. At least one of these employees must be on-site when active construction is taking place.

1.4.3.5 Conduct sufficient inspections to ensure construction personnel comply with the CSPP and SPCD and that there are no altered construction activities that could create potential safety hazards.

1.4.3.6 Restrict movement of construction vehicles and personnel to permitted construction areas by flagging, barricading, erecting temporary fencing, or providing escorts, as appropriate, and as specified in the CSPP and SPCD.

1.4.3.7 Ensure that no contractor employees, employees of subcontractors or suppliers, or other persons enter any part of the air operations area (AOA) from the construction site unless authorized.

1.4.3.8 Ensure prompt submittal through the airport operator of Form 7460-1 for the purpose of conducting an aeronautical study of contractor equipment such as tall equipment (cranes, concrete pumps, and other equipment), stock piles, and haul routes when different from cases previously filed by the airport operator. The FAA encourages online submittal of forms for expediency at https://oeaaa.faa.gov/oeaaa/external/portal.jsp.

1.4.3.9 Ensure that all necessary safety mitigations are understood by all parties involved, and any special requirements of each construction phase will be fulfilled per the approved timeframe.

1.4.3.10 Participate in pre-construction meetings to review construction limits, safety mitigations, NOTAMs, and understand all special airport operational needs during each phase of the project.

1.4.4 Define Tenant's Responsibilities.

If planning construction activities on leased property, Airport tenants, such as airline operators, fixed base operators, and FAA ATO/Technical Operations sponsoring construction are strongly encouraged to:

1. Develop, or have a consultant develop, a project specific CSPP and submit it to the airport operator. The airport operator may forgo a complete CSPP submittal and instead incorporate appropriate operational safety principles and measures addressed in the advisory circular within their tenant lease agreements.
2. In coordination with its contractor, develop an SPCD and submit it to the airport operator for approval issued prior to issuance of a Notice to Proceed.
3. Ensure that construction personnel are familiar with safety procedures and regulations on the airport during all phases of the construction.
4. Provide a point of contact of who will coordinate an immediate response to correct any construction-related activity that may adversely affect the operational safety of the airport.
5. Identify in the SPCD the contractor's on-site employees responsible for monitoring compliance with the CSPP and SPCD during construction. At least one of these employees must be on-site when active construction is taking place.
6. Ensure that no tenant or contractor employees, employees of subcontractors or suppliers, or any other persons enter any part of the AOA from the construction site unless authorized.
7. Restrict movement of construction vehicles to construction areas by flagging and barricading, erecting temporary fencing, or providing escorts, as appropriate, as specified in the CSPP and SPCD.
8. Ensure prompt submittal through the airport operator of Form 7460-1 for conducting an aeronautical study of contractor equipment such as tall equipment (cranes, concrete pumps, other), stock piles, and haul routes. The FAA encourages online submittal of forms for expediency at https://oeaaa.faa.gov/oeaaa/external/portal.jsp.
9. Participate in pre-construction meetings to review construction limits, safety mitigations, NOTAMs, and understand all special airport operational needs during each phase of the project.

CHAPTER 2. CONSTRUCTION SAFETY AND PHASING PLANS

2.1 Overview.

Aviation safety is the primary consideration at airports, especially during construction. The airport operator's CSPP and the contractor's Safety Plan Compliance Document (SPCD) are the primary tools to ensure safety compliance when coordinating construction activities with airport operations. These documents identify all aspects of the construction project that pose a potential safety hazard to airport operations and outline respective mitigation procedures for each hazard. They must provide information necessary for the Airport Operations department to conduct airfield inspections and expeditiously identify and correct unsafe conditions during construction. All aviation safety provisions included within the project drawings, contract specifications, and other related documents must also be reflected in the CSPP and SPCD.

2.2 Assume Responsibility.

Operational safety on the airport remains the airport operator's responsibility at all times. The airport operator must develop, certify, and submit for FAA approval each CSPP. It is the airport operator's responsibility to apply the requirements of the FAA approved CSPP. The airport operator must revise the CSPP when conditions warrant changes and must submit the revised CSPP to the FAA for approval. The airport operator must also require and approve a SPCD from the project contractor.

2.3 Submit the CSPP.

Construction Safety and Phasing Plans should be developed concurrently with the project design. Milestone versions of the CSPP should be submitted for review and approval as follows. While these milestones are not mandatory, early submission will help to avoid delays. Submittals are preferred in 8.5 × 11 inch or 11 × 17 inch format for compatibility with the FAA's Obstruction Evaluation / Airport Airspace Analysis (OE / AAA) process.

2.3.1 Submit an Outline/Draft.

By the time approximately 25% to 30% of the project design is completed, the principal elements of the CSPP should be established. Airport operators are encouraged to submit an outline or draft, detailing all CSPP provisions developed to date, to the FAA for review at this stage of the project design.

2.3.2 Submit a CSPP.

The CSPP should be formally submitted for FAA approval when the project design is 80 percent to 90 percent complete. Since provisions in the CSPP will influence contract costs, it is important to obtain FAA approval in time to include all such provisions in the procurement contract.

2.3.3 Submit an SPCD.

The contractor should submit the SPCD to the airport operator for approval to be issued prior to the Notice to Proceed.

2.3.4 Submit CSPP Revisions.

All revisions to a previously approved CSPP must be re-submitted to the FAA for review and approval/disapproval action.

2.4 Meet CSPP Requirements.

2.4.1 To the extent possible, the CSPP should address the following as outlined in Chapter 3, Guidelines for Writing a CSPP. Details that cannot be determined at this stage are to be included in the SPCD.

1. Coordination.
    a. Contractor progress meetings.
    b. Scope or schedule changes.
    c. FAA ATO coordination.
2. Phasing.
    a. Phase elements.
    b. Construction safety drawings.
3. Areas and operations affected by the construction activity.
    a. Identification of affected areas.
    b. Mitigation of effects.
4. Protection of navigation aids (NAVAIDs).
5. Contractor access.
    a. Location of stockpiled construction materials.
    b. Vehicle and pedestrian operations.
6. Wildlife management.
    a. Trash.
    b. Standing water.
    c. Tall grass and seeds.
    d. Poorly maintained fencing and gates.
    e. Disruption of existing wildlife habitat.
7. Foreign Object Debris (FOD) management.
8. Hazardous materials (HAZMAT) management.
9. Notification of construction activities.

a. Maintenance of a list of responsible representatives/ points of contact.

b. NOTAM.

c. Emergency notification procedures.

d. Coordination with ARFF Personnel.

e. Notification to the FAA.

10. Inspection requirements.

a. Daily (or more frequent) inspections.

b. Final inspections.

11. Underground utilities.

12. Penalties.

13. Special conditions.

14. Runway and taxiway visual aids. Marking, lighting, signs, and visual NAVAIDs.

a. General.

b. Markings.

c. Lighting and visual NAVAIDs.

d. Signs, temporary, including orange construction signs, and permanent signs.

15. Marking and signs for access routes.

16. Hazard marking and lighting.

a. Purpose.

b. Equipment.

17. Work zone lighting for nighttime construction (if applicable).

18. Protection of runway and taxiway safety areas, object free areas, obstacle free zones, and approach/departure surfaces.

a. Runway Safety Area (RSA).

b. Runway Object Free Area (ROFA).

c. Taxiway Safety Area (TSA). Provide details for any adjustments to Taxiway Safety Area width to allow continued operation of smaller aircraft. See paragraph 2.22.3.

d. Taxiway Object Free Area (TOFA). Provide details for any continued aircraft operations while construction occurs within the TOFA. See paragraph 2.22.4.

e. Obstacle Free Zone (OFZ).

f. Runway approach/departure surfaces.

19. Other limitations on construction.

a. Prohibitions.

b. Restrictions.

2.4.2 The Safety Plan Compliance Document (SPCD) should include a general statement by the construction contractor that he/she has read and will abide by the CSPP. In addition, the SPCD must include all supplemental information that could not be included in the CSPP prior to the contract award. The contractor statement should include the name of the contractor, the title of the project CSPP, the approval date of the CSPP, and a reference to any supplemental information (that is, "I, (Name of Contractor), have read the (Title of Project) CSPP, approved on (Date), and will abide by it as written and with the following additions as noted:"). The supplemental information in the SPCD should be written to match the format of the CSPP indicating each subject by corresponding CSPP subject number and title. If no supplemental information is necessary for any specific subject, the statement, "No supplemental information," should be written after the corresponding subject title. The SPCD should not duplicate information in the CSPP:

1. Coordination. Discuss details of proposed safety meetings with the airport operator and with contractor employees and subcontractors.
2. Phasing. Discuss proposed construction schedule elements, including:
   a. Duration of each phase.
   b. Daily start and finish of construction, including "night only" construction.
   c. Duration of construction activities during:
      i. Normal runway operations.
      ii. Closed runway operations.
      iii. Modified runway "Aircraft Reference Code" usage.
3. Areas and operations affected by the construction activity. These areas and operations should be identified in the CSPP and should not require an entry in the SPCD.
4. Protection of NAVAIDs. Discuss specific methods proposed to protect operating NAVAIDs.
5. Contractor access. Provide the following:
   a. Details on how the contractor will maintain the integrity of the airport security fence (gate guards, daily log of construction personnel, and other).
   b. Listing of individuals requiring driver training (for certificated airports and as requested).
   c. Radio communications.
      i. Types of radios and backup capabilities.
      ii. Who will be monitoring radios.
      iii. Who to contact if the ATCT cannot reach the contractor's designated person by radio.

d. Details on how the contractor will escort material delivery vehicles.

6. Wildlife management. Discuss the following:
   a. Methods and procedures to prevent wildlife attraction.
   b. Wildlife reporting procedures.
7. Foreign Object Debris (FOD) management. Discuss equipment and methods for control of FOD, including construction debris and dust.
8. Hazardous Materials (HAZMAT) management. Discuss equipment and methods for responding to hazardous spills.
9. Notification of construction activities. Provide the following:
   a. Contractor points of contact.
   b. Contractor emergency contact.
   c. Listing of tall or other requested equipment proposed for use on the airport and the timeframe for submitting 7460-1 forms not previously submitted by the airport operator.
   d. Batch plant details, including 7460-1 submittal.
10. Inspection requirements. Discuss daily (or more frequent) inspections and special inspection procedures.
11. Underground utilities. Discuss proposed methods of identifying and protecting underground utilities.
12. Penalties. Penalties should be identified in the CSPP and should not require an entry in the SPCD.
13. Special conditions. Discuss proposed actions for each special condition identified in the CSPP.
14. Runway and taxiway visual aids. Including marking, lighting, signs, and visual NAVAIDs. Discuss proposed visual aids including the following:
   a. Equipment and methods for covering signage and airfield lights.
   b. Equipment and methods for temporary closure markings (paint, fabric, other).
   c. Temporary orange construction signs.
   d. Types of temporary Visual Guidance Slope Indicators (VGSI).
15. Marking and signs for access routes. Discuss proposed methods of demarcating access routes for vehicle drivers.
16. Hazard marking and lighting. Discuss proposed equipment and methods for identifying excavation areas.
17. Work zone lighting for nighttime construction (if applicable). Discuss proposed equipment, locations, aiming, and shielding to prevent interference with air traffic control and aircraft operations.

18. Protection of runway and taxiway safety areas, object free areas, obstacle free zones, and approach/departure surfaces. Discuss proposed methods of identifying, demarcating, and protecting airport surfaces including:
    a. Equipment and methods for maintaining Taxiway Safety Area standards.
    b. Equipment and methods to ensure the safe passage of aircraft where Taxiway Safety Area or Taxiway Object Free Area standards cannot be maintained.
    c. Equipment and methods for separation of construction operations from aircraft operations, including details of barricades.
19. Other limitations on construction should be identified in the CSPP and should not require an entry in the SPCD.

2.5 **Coordination.**

Airport operators, or tenants responsible for design, bidding and conducting construction on their leased properties, should ensure at all project developmental stages, such as predesign, prebid, and preconstruction conferences, they capture the subject of airport operational safety during construction (see AC 150/5370-12, *Quality Management for Federally Funded Airport Construction Projects*). In addition, the following should be coordinated as required:

2.5.1 Progress Meetings.

Operational safety should be a standing agenda item for discussion during progress meetings throughout the project developmental stages.

2.5.2 Scope or Schedule Changes.

Changes in the scope or duration at any of the project stages may require revisions to the CSPP and review and approval by the airport operator and the FAA (see paragraph 1.4.2.17).

2.5.3 FAA ATO Coordination.

Early coordination with FAA ATO is highly recommended during the design phase and is required for scheduling Technical Operations shutdowns prior to construction. Coordination is critical to restarts of NAVAID services and to the establishment of any special procedures for the movement of aircraft. Formal agreements between the airport operator and appropriate FAA offices are recommended. All relocation or adjustments to NAVAIDs, or changes to final grades in critical areas, should be coordinated with FAA ATO and may require an FAA flight inspection prior to restarting the facility. Flight inspections must be coordinated and scheduled well in advance of the intended facility restart. Flight inspections may require a reimbursable agreement between the airport operator and FAA ATO. Reimbursable agreements should be coordinated a minimum of 12 months prior to the start of construction. (See paragraph 2.13.5.3.2 for required FAA notification regarding FAA-owned NAVAIDs.)

2.6 **Phasing.**

Once it has been determined what types and levels of airport operations will be maintained, the most efficient sequence of construction may not be feasible. In this case, the sequence of construction may be phased to gain maximum efficiency while allowing for the required operations. The development of the resulting construction phases should be coordinated with local Air Traffic personnel and airport users. The sequenced construction phases established in the CSPP must be incorporated into the project design and must be reflected in the contract drawings and specifications.

2.6.1 Phase Elements.

For each phase the CSPP should detail:

- Areas closed to aircraft operations.
- Duration of closures.
- Taxi routes and/or areas of reduced TSA and TOFA to reflect reduced ADG use.
- ARFF access routes.
- Construction staging, disposal, and cleanout areas.
- Construction access and haul routes.
- Impacts to NAVAIDs.
- Lighting, marking, and signing changes.
- Available runway length and/or reduced RSA and ROFA to reflect reduced ADG use.
- Declared distances (if applicable).
- Required hazard marking, lighting, and signing.
- Work zone lighting for nighttime construction (if applicable).
- Lead times for required notifications.

2.6.2 Construction Safety Drawings.

Drawings specifically indicating operational safety procedures and methods in affected areas (i.e., construction safety drawings) should be developed for each construction phase. Such drawings should be included in the CSPP as referenced attachments and should also be included in the contract drawing package.

2.7 **Areas and Operations Affected by Construction Activity.**

Runways and taxiways should remain in use by aircraft to the maximum extent possible without compromising safety. Pre-meetings with the FAA ATO will support operational simulations. See Appendix E for an example of a table showing temporary operations versus current operations. The tables in Appendix E can be useful for coordination among all interested parties, including FAA Lines of Business.

2.7.1 Identification of Affected Areas.

Identifying areas and operations affected by the construction helps to determine possible safety problems. The affected areas should be identified in the construction safety drawings for each construction phase. (See paragraph 2.6.2.) Of particular concern are:

2.7.1.1 **Closing, or Partial Closing, of Runways, Taxiways and Aprons, and Displaced Thresholds.**

When a runway is partially closed, a portion of the pavement is unavailable for any aircraft operation, meaning taxiing, landing, or takeoff in either direction on that pavement is prohibited. A displaced threshold, by contrast, is established to ensure obstacle clearance and adequate safety area for landing aircraft. The pavement prior to the displaced threshold is normally available for take-off in the direction of the displacement and for landing and takeoff in the opposite direction. Misunderstanding this difference, may result in issuance of an inaccurate NOTAM, and can lead to a hazardous condition.

2.7.1.1.1 Partially Closed Runways.

The temporarily closed portion of a partially closed runway will generally extend from the threshold to a taxiway that may be used for entering and exiting the runway. If the closed portion extends to a point between taxiways, pilots will have to back-taxi on the runway, which is an undesirable operation. See Figure 2-1 for a desirable configuration.

2.7.1.1.2 Displaced Thresholds.

Since the portion of the runway pavement between the permanent threshold and a standard displaced threshold is available for takeoff and for landing in the opposite direction, the temporary displaced threshold need not be located at an entrance/exit taxiway. See Figure 2-2.

2.7.1.2 Closing of aircraft rescue and fire fighting access routes.

2.7.1.3 Closing of access routes used by airport and airline support vehicles.

2.7.1.4 Interruption of utilities, including water supplies for fire fighting.

2.7.1.5 Approach/departure surfaces affected by heights of objects.

2.7.1.6 Construction areas, storage areas, and access routes near runways, taxiways, aprons, or helipads.

Figure 2-1. Temporary Partially Closed Runway


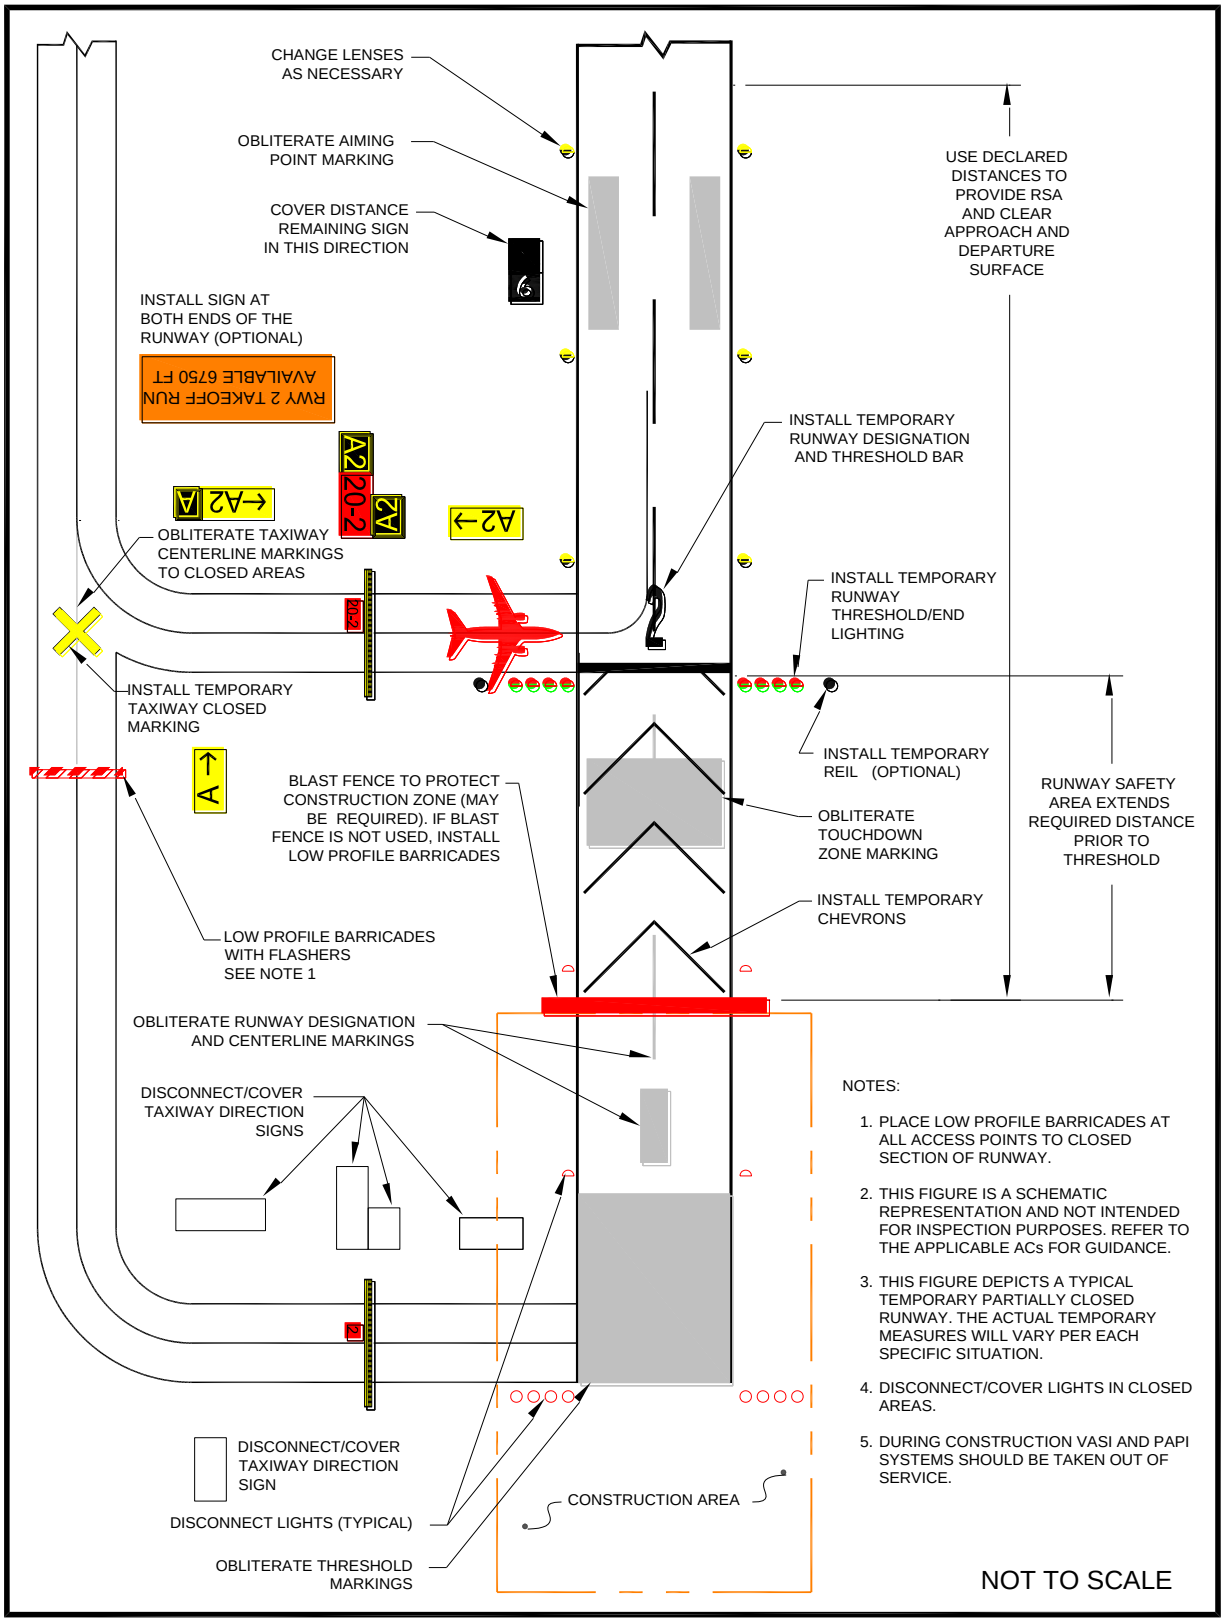


Figure 2-2. Temporary Displaced Threshold

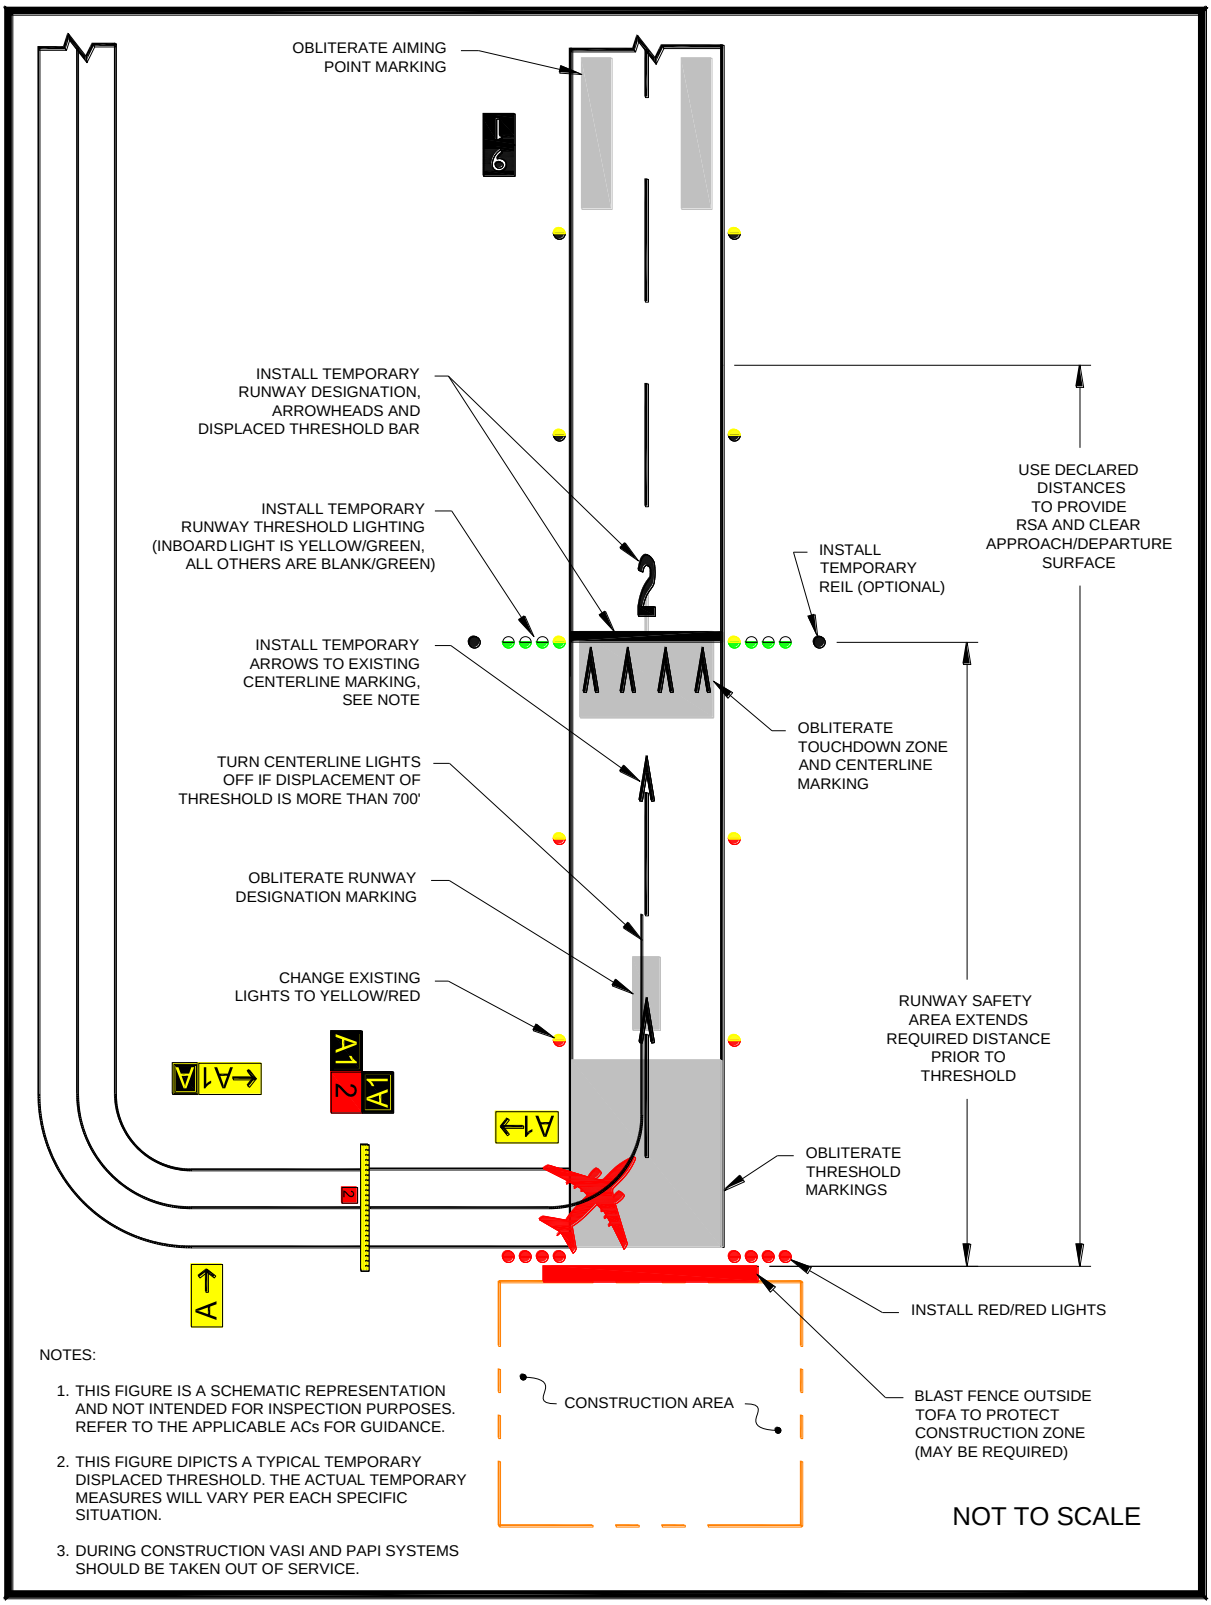

Note: See paragraph 2.18.2.5.

2.7.2 Mitigation of Effects.

Establishment of specific procedures is necessary to maintain the safety and efficiency of airport operations. The CSPP must address:

2.7.2.1 Temporary changes to runway and/or taxi operations.

2.7.2.2 Detours for ARFF and other airport vehicles.

2.7.2.3 Maintenance of essential utilities.

2.7.2.4 Temporary changes to air traffic control procedures. Such changes must be coordinated with the ATO.

2.8 Navigation Aid (NAVAID) Protection.

Before commencing construction activity, parking vehicles, or storing construction equipment and materials near a NAVAID, coordinate with the appropriate FAA ATO/Technical Operations office to evaluate the effect of construction activity and the required distance and direction from the NAVAID. (See paragraph 2.13.5.3.) Construction activities, materials/equipment storage, and vehicle parking near electronic NAVAIDs require special consideration since they may interfere with signals essential to air navigation. If any NAVAID may be affected, the CSPP and SPCD must show an understanding of the "critical area" associated with each NAVAID and describe how it will be protected. Where applicable, the operational critical areas of NAVAIDs should be graphically delineated on the project drawings. Pay particular attention to stockpiling material, as well as to movement and parking of equipment that may interfere with line of sight from the ATCT or with electronic emissions. Interference from construction equipment and activities may require NAVAID shutdown or adjustment of instrument approach minimums for low visibility operations. This condition requires that a NOTAM be filed (see paragraph 2.13.2). Construction activities and materials/equipment storage near a NAVAID must not obstruct access to the equipment and instruments for maintenance. Submittal of a 7460-1 form is required for construction vehicles operating near FAA NAVAIDs. (See paragraph 2.13.5.3.)

2.9 Contractor Access.

The CSPP must detail the areas to which the contractor must have access, and explain how contractor personnel will access those areas. Specifically address:

2.9.1 Location of Stockpiled Construction Materials.

Stockpiled materials and equipment storage are not permitted within the RSA and OFZ, and if possible should not be permitted within the Object Free Area (OFA) of an operational runway. Stockpiling material in the OFA requires submittal of a 7460-1 form and justification provided to the appropriate FAA Airports Regional or District Office for approval. The airport operator must ensure that stockpiled materials and equipment adjacent to these areas are prominently marked and lighted during hours of restricted visibility or darkness. (See paragraph 2.18.2.) This includes determining and

verifying that materials are stabilized and stored at an approved location so as not to be a hazard to aircraft operations and to prevent attraction of wildlife and foreign object damage from blowing or tracked material. See paragraphs 2.10 and 2.11.

2.9.2 Vehicle and Pedestrian Operations.

The CSPP should include specific vehicle and pedestrian requirements. Vehicle and pedestrian access routes for airport construction projects must be controlled to prevent inadvertent or unauthorized entry of persons, vehicles, or animals onto the AOA. The airport operator should coordinate requirements for vehicle operations with airport tenants, contractors, and the FAA air traffic manager. In regard to vehicle and pedestrian operations, the CSPP should include the following, with associated training requirements:

2.9.2.1 **Construction Site Parking.**

Designate in advance vehicle parking areas for contractor employees to prevent any unauthorized entry of persons or vehicles onto the AOA. These areas should provide reasonable contractor employee access to the job site.

2.9.2.2 **Construction Equipment Parking.**

Contractor employees must park and service all construction vehicles in an area designated by the airport operator outside the OFZ and never in the safety area of an active runway or taxiway. Unless a complex setup procedure makes movement of specialized equipment infeasible, inactive equipment must not be parked on a closed taxiway or runway. If it is necessary to leave specialized equipment on a closed taxiway or runway at night, the equipment must be well lighted. Employees should also park construction vehicles outside the OFA when not in use by construction personnel (for example, overnight, on weekends, or during other periods when construction is not active). Parking areas must not obstruct the clear line of sight by the ATCT to any taxiways or runways under air traffic control nor obstruct any runway visual aids, signs, or navigation aids. The FAA must also study those areas to determine effects on airport design criteria, surfaces established by 14 CFR Part 77, Safe, Efficient Use, and Preservation of the Navigable Airspace (Part 77), and on NAVAIDs and Instrument Approach Procedures (IAP). See paragraph 2.13.1 for further information.

2.9.2.3 **Access and Haul Roads.**

Determine the construction contractor’s access to the construction sites and haul roads. Do not permit the construction contractor to use any access or haul roads other than those approved. Access routes used by contractor vehicles must be clearly marked to prevent inadvertent entry to areas open to airport operations. Pay special attention to ensure that if construction traffic is to share or cross any ARFF routes that ARFF right of way is not impeded at any time, and that construction traffic on haul

roads does not interfere with NAVAIDs or approach surfaces of operational runways. Address whether access gates will be blocked or inoperative or if a rally point will be blocked or inaccessible.

2.9.2.4 Marking and lighting of vehicles in accordance with AC 150/5210-5, *Painting, Marking, and Lighting of Vehicles Used on an Airport.*

2.9.2.5 Description of proper vehicle operations on various areas under normal, lost communications, and emergency conditions.

2.9.2.6 Required escorts.

2.9.2.7 **Training Requirements for Vehicle Drivers to Ensure Compliance with the Airport Operator's Vehicle Rules and Regulations.**

Specific training should be provided to vehicle operators, including those providing escorts. See AC 150/5210-20, *Ground Vehicle Operations on Airports*, for information on training and records maintenance requirements.

2.9.2.8 **Situational Awareness.**

Vehicle drivers must confirm by personal observation that no aircraft is approaching their position (either in the air or on the ground) when given clearance to cross a runway, taxiway, or any other area open to airport operations. In addition, it is the responsibility of the escort vehicle driver to verify the movement/position of all escorted vehicles at any given time. At non-towered airports, all aircraft movements and flight operations rely on aircraft operators to self-report their positions and intentions. However, there is no requirement for an aircraft to have radio communications. Because aircraft do not always broadcast their positions or intentions, visual checking, radio monitoring, and situational awareness of the surroundings is critical to safety.

2.9.2.9 **Two-Way Radio Communication Procedures.**

2.9.2.9.1 General.

The airport operator must ensure that tenant and construction contractor personnel engaged in activities involving unescorted operation on aircraft movement areas observe the proper procedures for communications, including using appropriate radio frequencies at airports with and without ATCT. When operating vehicles on or near open runways or taxiways, construction personnel must understand the critical importance of maintaining radio contact, as directed by the airport operator, with:

1. Airport operations
2. ATCT

3. Common Traffic Advisory Frequency (CTAF), which may include UNICOM, MULTICOM.
4. Automatic Terminal Information Service (ATIS). This frequency is useful for monitoring conditions on the airport. Local air traffic will broadcast information regarding construction related runway closures and "shortened" runways on the ATIS frequency.

2.9.2.9.2 Areas Requiring Two-Way Radio Communication with the ATCT.

Vehicular traffic crossing active movement areas must be controlled either by two-way radio with the ATCT, escort, flagman, signal light, or other means appropriate for the particular airport.

2.9.2.9.3 Frequencies to be Used.

The airport operator will specify the frequencies to be used by the contractor, which may include the CTAF for monitoring of aircraft operations. Frequencies may also be assigned by the airport operator for other communications, including any radio frequency in compliance with Federal Communications Commission requirements. At airports with an ATCT, the airport operator will specify the frequency assigned by the ATCT to be used between contractor vehicles and the ATCT.

2.9.2.9.4 Proper radio usage, including read back requirements.

2.9.2.9.5 Proper phraseology, including the International Phonetic Alphabet.

2.9.2.9.6 Light Gun Signals.

Even though radio communication is maintained, escort vehicle drivers must also familiarize themselves with ATCT light gun signals in the event of radio failure. See the FAA safety placard "Ground Vehicle Guide to Airport Signs and Markings." This safety placard may be downloaded through the Runway Safety Program Web site at http://www.faa.gov/airports/runway_safety/publications/ (see "Signs & Markings Vehicle Dashboard Sticker") or obtained from the FAA Airports Regional Office.

2.9.2.10 **Maintenance of the secured area of the airport, including:**

2.9.2.10.1 Fencing and Gates.

Airport operators and contractors must take care to maintain security during construction when access points are created in the security fencing to permit the passage of construction vehicles or personnel. Temporary gates should be equipped so they can be securely closed and locked to prevent access by animals and unauthorized people. Procedures should be in place to ensure that only authorized persons and vehicles have access to the AOA and to prohibit "piggybacking" behind another person or vehicle. The Department of Transportation (DOT) document DOT/FAA/AR-

00/52, *Recommended Security Guidelines for Airport Planning and Construction*, provides more specific information on fencing. A copy of this document can be obtained from the Airport Consultants Council, Airports Council International, or American Association of Airport Executives.

2.9.2.10.2 Badging Requirements.

Airports subject to 49 CFR Part 1542, *Airport Security*, must meet standards for access control, movement of ground vehicles, and identification of construction contractor and tenant personnel.

2.10 Wildlife Management.

The CSPP and SPCD must be in accordance with the airport operator's wildlife hazard management plan, if applicable. See AC 150/5200-33, *Hazardous Wildlife Attractants On or Near Airports,* and CertAlert 98-05, *Grasses Attractive to Hazardous Wildlife.* Construction contractors must carefully control and continuously remove waste or loose materials that might attract wildlife. Contractor personnel must be aware of and avoid construction activities that can create wildlife hazards on airports, such as:

2.10.1 Trash.

Food scraps must be collected from construction personnel activity.

2.10.2 Standing Water.

2.10.3 Tall Grass and Seeds.

Requirements for turf establishment can be at odds with requirements for wildlife control. Grass seed is attractive to birds. Lower quality seed mixtures can contain seeds of plants (such as clover) that attract larger wildlife. Seeding should comply with the guidance in AC 150/5370-10, *Standards for Specifying Construction of Airports,* Item T-901, Seeding. Contact the local office of the United Sates Department of Agriculture Soil Conservation Service or the State University Agricultural Extension Service (County Agent or equivalent) for assistance and recommendations. These agencies can also provide liming and fertilizer recommendations.

2.10.4 Poorly Maintained Fencing and Gates.

See paragraph 2.9.2.10.1.

2.10.5 Disruption of Existing Wildlife Habitat.

While this will frequently be unavoidable due to the nature of the project, the CSPP should specify under what circumstances (location, wildlife type) contractor personnel should immediately notify the airport operator of wildlife sightings.

2.11 Foreign Object Debris (FOD) Management.

Waste and loose materials, commonly referred to as FOD, are capable of causing damage to aircraft landing gears, propellers, and jet engines. Construction contractors must not leave or place FOD on or near active aircraft movement areas. Materials capable of creating FOD must be continuously removed during the construction project. Fencing (other than security fencing) or covers may be necessary to contain material that can be carried by wind into areas where aircraft operate. See AC 150/5210-24, *Foreign Object Debris (FOD) Management.*

2.12 Hazardous Materials (HAZMAT) Management.

Contractors operating construction vehicles and equipment on the airport must be prepared to expeditiously contain and clean-up spills resulting from fuel or hydraulic fluid leaks. Transport and handling of other hazardous materials on an airport also requires special procedures. See AC 150/5320-15, *Management of Airport Industrial Waste.*

2.13 Notification of Construction Activities.

The CSPP and SPCD must detail procedures for the immediate notification of airport users and the FAA of any conditions adversely affecting the operational safety of the airport. It must address the notification actions described below, as applicable.

2.13.1 List of Responsible Representatives/points of contact for all involved parties, and procedures for contacting each of them, including after hours.

2.13.2 NOTAMs.

Only the airport operator may initiate or cancel NOTAMs on airport conditions, and is the only entity that can close or open a runway. The airport operator must coordinate the issuance, maintenance, and cancellation of NOTAMs about airport conditions resulting from construction activities with tenants and the local air traffic facility (control tower, approach control, or air traffic control center), and must either enter the NOTAM into NOTAM Manager, or provide information on closed or hazardous conditions on airport movement areas to the FAA Flight Service Station (FSS) so it can issue a NOTAM. The airport operator must file and maintain a list of authorized representatives with the FSS. Refer to AC 150/5200-28, *Notices to Airmen (NOTAMs) for Airport Operators,* for a sample NOTAM form. Only the FAA may issue or cancel NOTAMs on shutdown or irregular operation of FAA owned facilities. Any person having reason to believe that a NOTAM is missing, incomplete, or inaccurate must notify the airport operator. See paragraph 2.7.1.1 about issuing NOTAMs for partially closed runways versus runways with displaced thresholds.

2.13.3 Emergency notification procedures for medical, fire fighting, and police response.

2.13.4 Coordination with ARFF.

The CSPP must detail procedures for coordinating through the airport sponsor with ARFF personnel, mutual aid providers, and other emergency services if construction requires:

1. The deactivation and subsequent reactivation of water lines or fire hydrants, or
2. The rerouting, blocking and restoration of emergency access routes, or
3. The use of hazardous materials on the airfield.

2.13.5 Notification to the FAA.

2.13.5.1 **Part 77.**

Any person proposing construction or alteration of objects that affect navigable airspace, as defined in Part 77, must notify the FAA. This includes construction equipment and proposed parking areas for this equipment (i.e., cranes, graders, other equipment) on airports. FAA Form 7460-1, *Notice of Proposed Construction or Alteration*, can be used for this purpose and submitted to the appropriate FAA Airports Regional or District Office. See Appendix A to download the form. Further guidance is available on the FAA web site at oeaaa.faa.gov.

2.13.5.2 **Part 157.**

With some exceptions, Title 14 CFR Part 157, *Notice of Construction, Alteration, Activation, and Deactivation of Airports*, requires that the airport operator notify the FAA in writing whenever a non-Federally funded project involves the construction of a new airport; the construction, realigning, altering, activating, or abandoning of a runway, landing strip, or associated taxiway; or the deactivation or abandoning of an entire airport. Notification involves submitting FAA Form 7480-1, *Notice of Landing Area Proposal*, to the nearest FAA Airports Regional or District Office. See Appendix A to download the form.

2.13.5.3 **NAVAIDs.**

For emergency (short-notice) notification about impacts to both airport owned and FAA owned NAVAIDs, contact: 866-432-2622.

2.13.5.3.1 Airport Owned/FAA Maintained.

If construction operations require a shutdown of 24 hours or greater in duration, or more than 4 hours daily on consecutive days, of a NAVAID owned by the airport but maintained by the FAA, provide a 45-day minimum notice to FAA ATO/Technical Operations prior to facility shutdown, using Strategic Event Coordination (SEC) Form 6000.26 contained within FAA Order 6000.15, *General Maintenance Handbook for National Airspace System (NAS) Facilities*.

2.13.5.3.2 FAA Owned.

1. The airport operator must notify the appropriate FAA ATO Service Area Planning and Requirements (P&R) Group a minimum of 45 days prior to implementing an event that causes impacts to NAVAIDs, using SEC Form 6000.26.
2. Coordinate work for an FAA owned NAVAID shutdown with the local FAA ATO/Technical Operations office, including any necessary reimbursable agreements and flight checks. Detail procedures that address unanticipated utility outages and cable cuts that could impact FAA NAVAIDs. Refer to active Service Level Agreement with ATO for specifics.

2.14 **Inspection Requirements.**

2.14.1 Daily Inspections.

Inspections should be conducted at least daily, but more frequently if necessary to ensure conformance with the CSPP. A sample checklist is provided in Appendix D, Construction Project Daily Safety Inspection Checklist. See also AC 150/5200-18, *Airport Safety Self-Inspection.* Airport operators holding a Part 139 certificate are required to conduct self-inspections during unusual conditions, such as construction activities, that may affect safe air carrier operations.

2.14.2 Interim Inspections.

Inspections should be conducted of all areas to be (re)opened to aircraft traffic to ensure the proper operation of lights and signs, for correct markings, and absence of FOD. The contractor should conduct an inspection of the work area with airport operations personnel. The contractor should ensure that all construction materials have been secured, all pavement surfaces have been swept clean, all transition ramps have been properly constructed, and that surfaces have been appropriately marked for aircraft to operate safely. Only if all items on the list meet with the airport operator's approval should the air traffic control tower be notified to open the area to aircraft operations. The contractor should be required to retain a suitable workforce and the necessary equipment at the work area for any last minute cleanup that may be requested by the airport operator prior to opening the area.

2.14.3 Final Inspections.

New runways and extended runway closures may require safety inspections at certificated airports prior to allowing air carrier service. Coordinate with the FAA Airport Certification Safety Inspector (ACSI) to determine if a final inspection will be necessary.

2.15 **Underground Utilities.**

The CSPP and/or SPCD must include procedures for locating and protecting existing underground utilities, cables, wires, pipelines, and other underground facilities in excavation areas. This may involve coordinating with public utilities and FAA ATO/Technical Operations. Note that "One Call" or "Miss Utility" services do not include FAA ATO/Technical Operations.

2.16 **Penalties.**

The CSPP should detail penalty provisions for noncompliance with airport rules and regulations and the safety plans (for example, if a vehicle is involved in a runway incursion). Such penalties typically include rescission of driving privileges or access to the AOA.

2.17 **Special Conditions.**

The CSPP must detail any special conditions that affect the operation of the airport and will require the activation of any special procedures (for example, low-visibility operations, snow removal, aircraft in distress, aircraft accident, security breach, Vehicle / Pedestrian Deviation (VPD) and other activities requiring construction suspension/resumption).

2.18 **Runway and Taxiway Visual Aids.**

This includes marking, lighting, signs, and visual NAVAIDs. The CSPP must ensure that areas where aircraft will be operating are clearly and visibly separated from construction areas, including closed runways. Throughout the duration of the construction project, verify that these areas remain clearly marked and visible at all times and that marking, lighting, signs, and visual NAVAIDs that are to continue to perform their functions during construction remain in place and operational. Visual NAVAIDs that are not serving their intended function during construction must be temporarily disabled, covered, or modified as necessary. The CSPP must address the following, as appropriate:

2.18.1 General.

Airport markings, lighting, signs, and visual NAVAIDs must be clearly visible to pilots, not misleading, confusing, or deceptive. All must be secured in place to prevent movement by prop wash, jet blast, wing vortices, and other wind currents and constructed of materials that will minimize damage to an aircraft in the event of inadvertent contact. Items used to secure such markings must be of a color similar to the marking.

2.18.2 Markings.

During the course of construction projects, temporary pavement markings are often required to allow for aircraft operations during or between work periods. During the design phase of the project, the designer should coordinate with the project manager,

airport operations, airport users, the FAA Airports project manager, and Airport Certification Safety Inspector for Part 139 airports to determine minimum temporary markings. The FAA Airports project manager will, wherever a runway is closed, coordinate with the appropriate FAA Flight Standards Office and disseminate findings to all parties. Where possible, the temporary markings on finish grade pavements should be placed to mirror the dimensions of the final markings. Markings must be in compliance with the standards of AC 150/5340-1, *Standards for Airport Markings,* except as noted herein. Runways and runway exit taxiways closed to aircraft operations are marked with a yellow X. The preferred visual aid to depict temporary runway closure is the lighted X signal placed on or near the runway designation numbers. (See paragraph 2.18.2.1.2.)

2.18.2.1 **Closed Runways and Taxiways.**

2.18.2.1.1 Permanently Closed Runways.

For runways, obliterate the threshold marking, runway designation marking, and touchdown zone markings, and place an X at each end and at 1,000-foot (300 m) intervals. For a multiple runway environment, if the lighted X on a designated number will be located in the RSA of an adjacent active runway, locate the lighted X farther down the closed runway to clear the RSA of the active runway. In addition, the closed runway numbers located in the RSA of an active runway must be marked with a flat yellow X.

2.18.2.1.2 Temporarily Closed Runways.

For runways that have been temporarily closed, place an X at each end of the runway directly on or as near as practicable to the runway designation numbers. For a multiple runway environment, if the lighted X on a designated number will be located in the RSA of an adjacent active runway, locate the lighted X farther down the closed runway to clear the RSA of the active runway. In addition, the closed runway numbers located in the RSA of an active runway must be marked with a flat yellow X. See Figure 2-3. See also paragraph 2.18.3.3.

2.18.2.1.3 Partially Closed Runways and Displaced Thresholds.

When threshold markings are needed to identify the temporary beginning of the runway that is available for landing, the markings must comply with AC 150/5340-1. An X is not used on a partially closed runway or a runway with a displaced threshold. See paragraph 2.7.1.1 for the difference between partially closed runways and runways with displaced thresholds. Because of the temporary nature of threshold displacement due to construction, it is not necessary to re-adjust the existing runway centerline markings to meet standard spacing for a runway with a visual approach. Some of the requirements below may be waived in the cases of low-activity airports and/or short duration changes that are measured in days rather than weeks. Consider whether the presence of an airport traffic

control tower allows for the development of special procedures. Contact the appropriate FAA Airports Regional or District Office for assistance.

Figure 2-3. Markings for a Temporarily Closed Runway




1. **Partially Closed Runways.** Pavement markings for temporary closed portions of the runway consist of a runway threshold bar, runway designation, and yellow chevrons to identify pavement areas that are unsuitable for takeoff or landing (see AC 150/5340-1). Obliterate or cover markings prior to the moved threshold. Existing touchdown zone markings beyond the moved threshold may remain in place. Obliterate aiming point markings. Issue appropriate NOTAMs regarding any nonstandard markings. See Figure 2-4.
2. **Displaced Thresholds.** Pavement markings for a displaced threshold consist of a runway threshold bar, runway designation, and white arrowheads with and without arrow shafts. These markings are required to identify the portion of the runway before the displaced threshold to provide centerline guidance for pilots during approaches, takeoffs, and landing rollouts from the opposite direction. See AC 150/5340-1. Obliterate markings prior to the displaced threshold. Existing touchdown zone markings beyond the displaced threshold may remain in place. Obliterate aiming point markings. Issue appropriate NOTAMs regarding any nonstandard markings. See Figure 2-2.

2.18.2.1.4 Taxiways.

1. **Permanently Closed Taxiways.** AC 150/5300-13 *Airport Design*, notes that it is preferable to remove the pavement, but for pavement that is to remain, place an X at the entrance to both ends of the closed section. Obliterate taxiway centerline markings, including runway leadoff lines, leading to the closed taxiway. See Figure 2-4.

Figure 2-4. Temporary Taxiway Closure

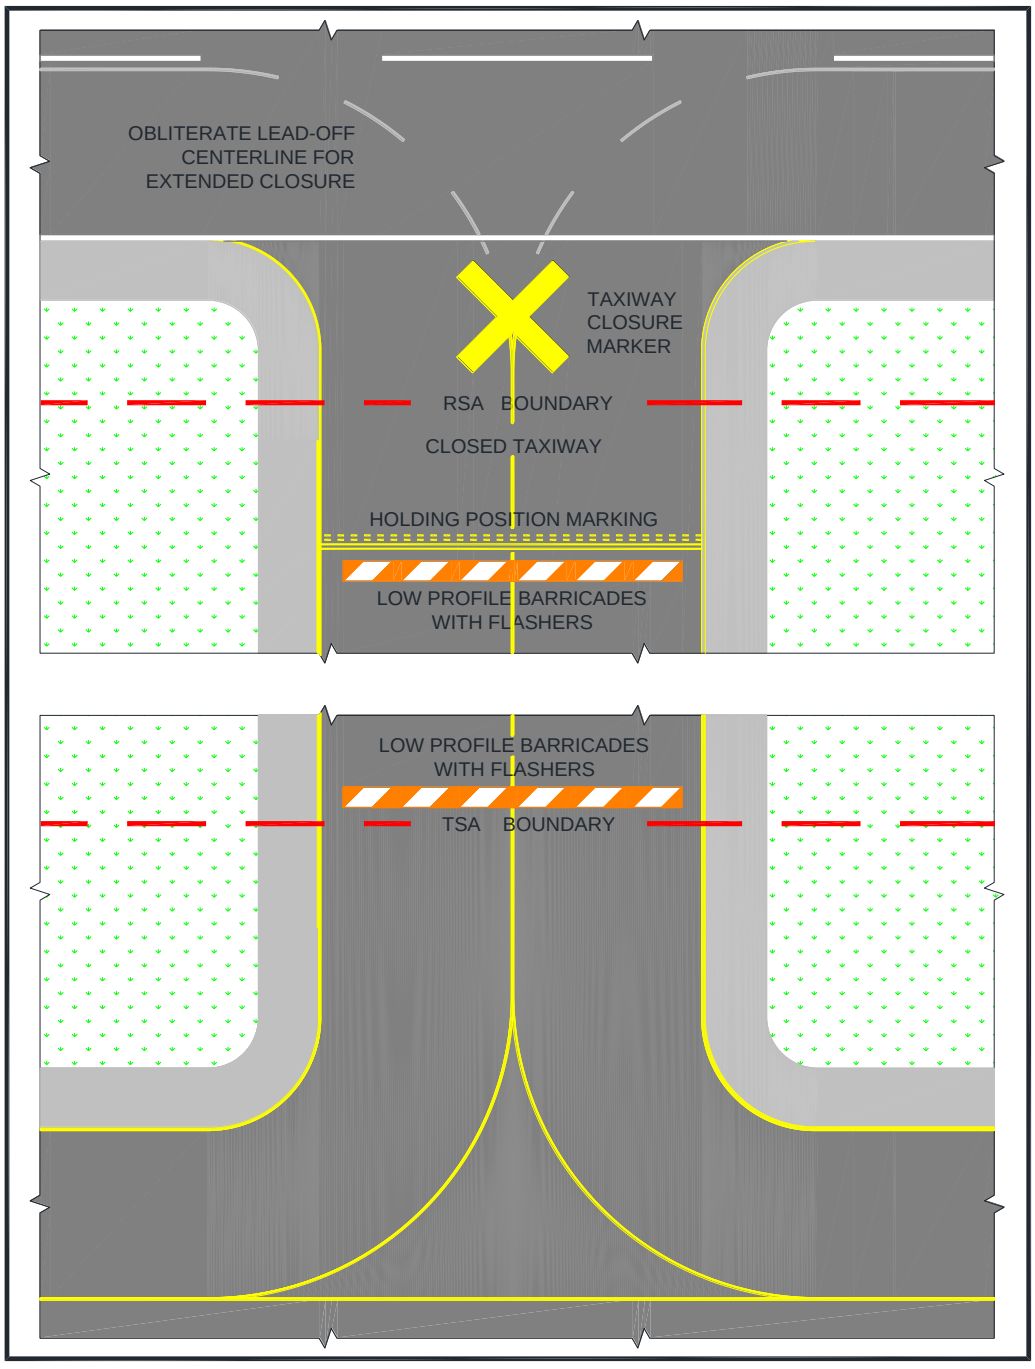

2. **Temporarily Closed Taxiways.** Place barricades outside the safety area of intersecting taxiways. For runway/taxiway intersections, place an X at the entrance to the closed taxiway from the runway. If the taxiway will be closed for an extended period, obliterate taxiway centerline markings, including runway leadoff lines and taxiway to taxiway turns, leading to the closed section. Always obliterate runway lead-off lines for high speed exits, regardless of the duration of the closure. If the centerline markings will be reused upon reopening the taxiway, it is preferable to paint over the marking. This will result in less damage to the pavement when the upper layer of paint is ultimately removed. See Figure 2-4.

2.18.2.1.5 Temporarily Closed Airport.

When the airport is closed temporarily, mark all the runways as closed.

2.18.2.2 If unable to paint temporary markings on the pavement, construct them from any of the following materials: fabric, colored plastic, painted sheets of plywood, or similar materials. They must be properly configured and appropriately secured to prevent movement by prop wash, jet blast, or other wind currents. Items used to secure such markings must be of a color similar to the marking.


2.18.2.3 It may be necessary to remove or cover runway markings, including but not limited to, runway designation markings, threshold markings, centerline markings, edge stripes, touchdown zone markings and aiming point markings, depending on the length of construction and type of activity at the airport. When removing runway markings, apply the same treatment to areas between stripes or numbers, as the cleaned area will appear to pilots as a marking in the shape of the treated area.

2.18.2.4 If it is not possible to install threshold bars, chevrons, and arrows on the pavement, "temporary outboard white threshold bars and yellow arrowheads", see Figure 2-5, may be used. Locate them outside of the runway pavement surface on both sides of the runway. The dimensions must be as shown in Figure 2-5. If the markings are not discernible on grass or snow, apply a black background with appropriate material over the ground to ensure they are clearly visible.

2.18.2.5 The application rate of paint to mark a short-term temporary runway and taxiway markings may deviate from the standard (see Item P-620, "Runway and Taxiway Painting," in AC 150/5370-10), but the dimensions must meet the existing standards. When applying temporary markings at night, it is recommended that the fast curing, Type II paint be used to help offset the higher humidity and cooler temperatures often experienced at night. Diluting the paint will substantially increase cure time and is not recommended. Glass beads are not recommended for temporary markings. Striated markings may also be used for certain temporary markings. AC

150/5340-1, *Standards for Airport Markings*, has additional guidance on temporary markings.

Figure 2-5. Temporary Outboard White Threshold Bars and Yellow Arrowheads

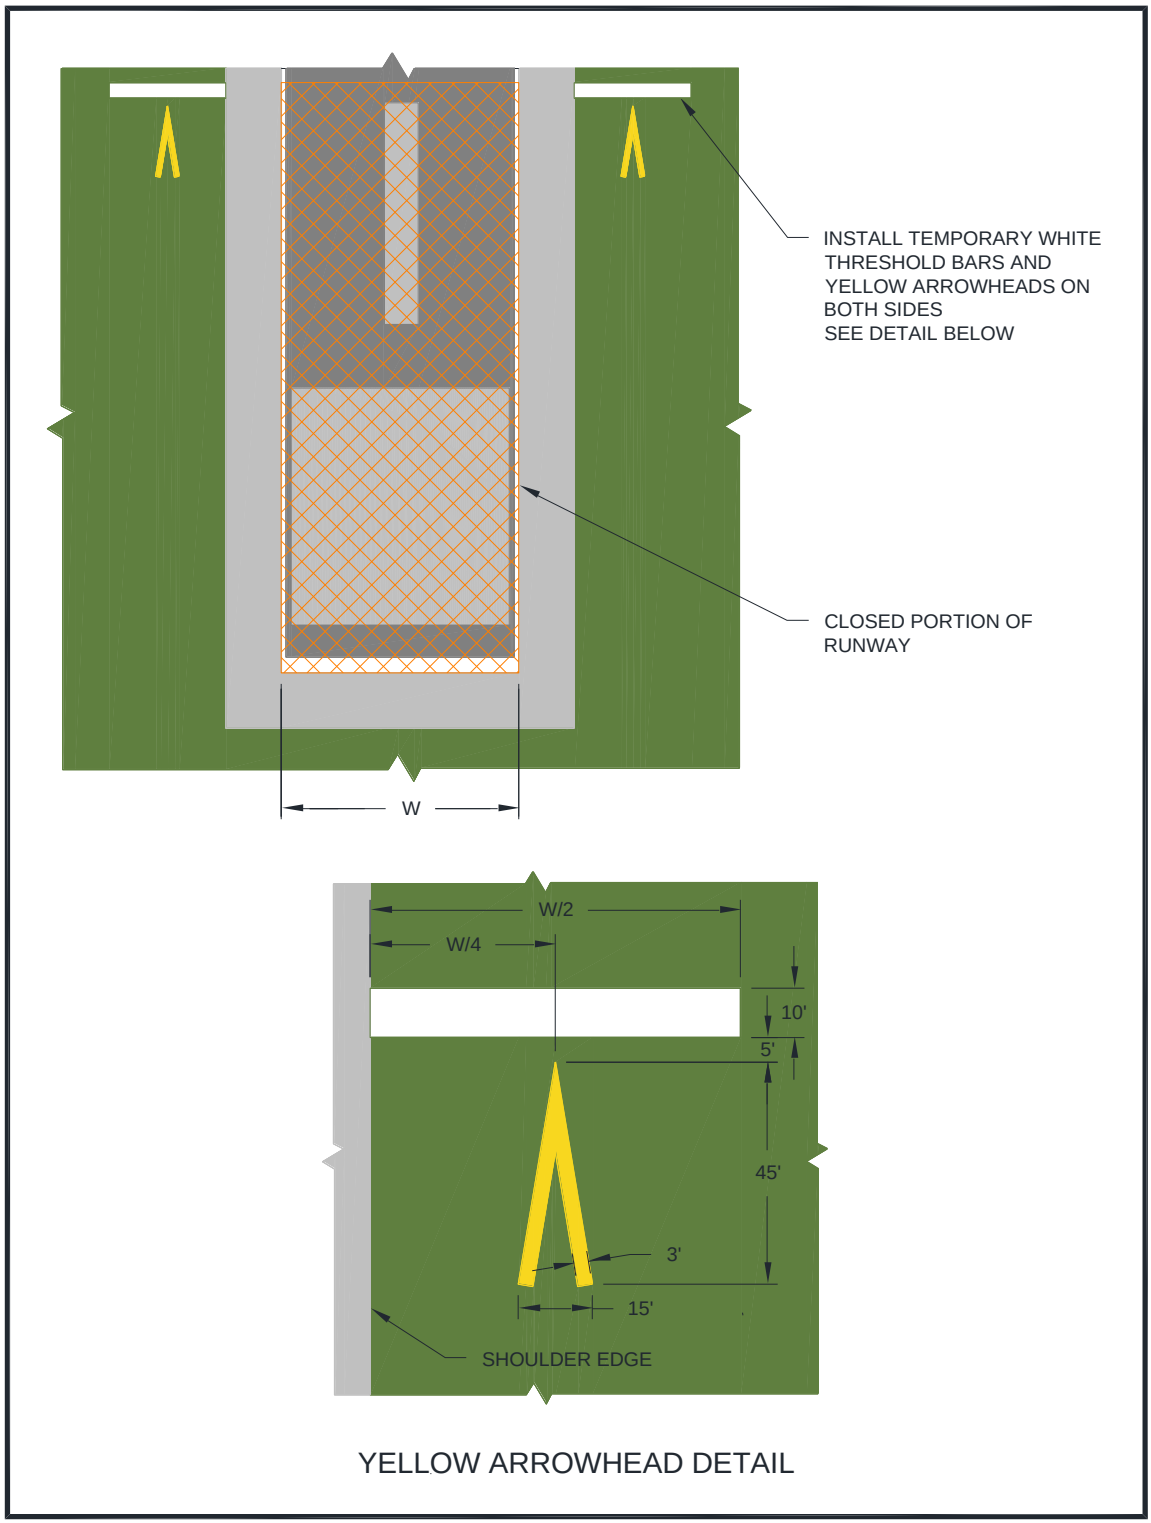

2.18.3 Lighting and Visual NAVAIDs.

This paragraph refers to standard runway and taxiway lighting systems. See below for hazard lighting. Lighting installation must be in conformance with AC 150/5340-30, *Design and Installation Details for Airport Visual Aids,* and fixture design in conformance with AC 150/5345-50, *Specification for Portable Runway and Taxiway Lights.* When disconnecting runway and taxiway lighting fixtures, disconnect the associated isolation transformers. See AC 150/5340-26, *Maintenance of Airport Visual Aid Facilities*, for disconnect procedures and safety precautions. Alternately, cover the light fixture in such a way as to prevent light leakage. Avoid removing the lamp from energized fixtures because an excessive number of isolation transformers with open secondaries may damage the regulators and/or increase the current above its normal value. Secure, identify, and place any above ground temporary wiring in conduit to prevent electrocution and fire ignition sources. Maintain mandatory hold signs to operate normally in any situation where pilots or vehicle drivers could mistakenly be in that location. At towered airports certificated under Part 139, holding position signs are required to be illuminated on open taxiways crossing to closed or inactive runways. If the holding position sign is installed on the runway circuit for the closed runway, install a jumper to the taxiway circuit to provide power to the holding position sign for nighttime operations. Where it is not possible to maintain power to signs that would normally be operational, install barricades to exclude aircraft. Figure 2-1, Figure 2-2, Figure 2-3, and Figure 2-4 illustrate temporary changes to lighting and visual NAVAIDs.

2.18.3.1 **Permanently Closed Runways and Taxiways.**

For runways and taxiways that have been permanently closed, disconnect the lighting circuits.

2.18.3.2 **Temporarily Closed Runways and New Runways Not Yet Open to Air Traffic.**

If available, use a lighted X, both at night and during the day, placed at each end of the runway on or near the runway designation numbers facing the approach. (Note that the lighted X must be illuminated at all times that it is on a runway.) The use of a lighted X is required if night work requires runway lighting to be on. See AC 150/5345-55, *Specification for L-893, Lighted Visual Aid to Indicate Temporary Runway Closure.* For runways that have been temporarily closed, but for an extended period, and for those with pilot controlled lighting, disconnect the lighting circuits or secure switches to prevent inadvertent activation. For runways that will be opened periodically, coordinate procedures with the FAA air traffic manager or, at airports without an ATCT, the airport operator. Activate stop bars if available. Figure 2-6 shows a lighted X by day. Figure 2-7 shows a lighted X at night.

Figure 2-6. Lighted X in Daytime



Figure 2-7. Lighted X at Night



2.18.3.3 **Partially Closed Runways and Displaced Thresholds.**

When a runway is partially closed, a portion of the pavement is unavailable for any aircraft operation, meaning taxiing and landing or taking off in either direction. A displaced threshold, by contrast, is put in place to ensure obstacle clearance by landing aircraft. The pavement prior to the displaced threshold is available for takeoff in the direction of the displacement, and for landing and takeoff in the opposite direction. Misunderstanding this difference and issuance of a subsequently inaccurate NOTAM can result in a hazardous situation. For both partially

closed runways and displaced thresholds, approach lighting systems at the affected end must be placed out of service.

2.18.3.3.1 Partially Closed Runways.

Disconnect edge and threshold lights on that part of the runway at and behind the threshold (that is, the portion of the runway that is closed). Alternately, cover the light fixtures in such a way as to prevent light leakage. See Figure 2-1.

2.18.3.3.2 Temporary Displaced Thresholds.

Edge lighting in the area of the displacement emits red light in the direction of approach and yellow light (white for visual runways) in the opposite direction. If the displacement is 700 feet or less, blank out centerline lights in the direction of approach or place the centerline lights out of service. If the displacement is over 700 feet, place the centerline lights out of service. See AC 150/5340-30 for details on lighting displaced thresholds. See Figure 2-2.

2.18.3.3.3 Temporary runway thresholds and runway ends must be lighted if the runway is lighted and it is the intended threshold for night landings or instrument meteorological conditions.

2.18.3.3.4 A temporary threshold on an unlighted runway may be marked by retroreflective, elevated markers in addition to markings noted in paragraph 2.18.2.1.3. Markers seen by aircraft on approach are green. Markers at the rollout end of the runway are red. At certificated airports, temporary elevated threshold markers must be mounted with a frangible fitting (see 14 CFR Part 139.309). At non-certificated airports, the temporary elevated threshold markings may either be mounted with a frangible fitting or be flexible. See AC 150/5345-39, *Specification for L-853, Runway and Taxiway Retroreflective Markers.*

2.18.3.3.5 Temporary threshold lights and runway end lights and related visual NAVAIDs are installed outboard of the edges of the full-strength pavement only when they cannot be installed on the pavement. They are installed with bases at grade level or as low as possible, but not more than 3 inch (7.6 cm) above ground. (The standard above ground height for airport lighting fixtures is 14 inches (35 cm)). When any portion of a base is above grade, place properly compacted fill around the base to minimize the rate of gradient change so aircraft can, in an emergency, cross at normal landing or takeoff speeds without incurring significant damage. See AC 150/5370-10.

2.18.3.3.6 Maintain threshold and edge lighting color and spacing standards as described in AC 150/5340-30. Battery powered, solar, or portable lights that meet the criteria in AC 150/5345-50 may be used. These systems are intended primarily for visual flight rules (VFR) aircraft operations but may

be used for instrument flight rules (IFR) aircraft operations, upon individual approval from the Flight Standards Division of the applicable FAA Regional Office.

2.18.3.3.7 When runway thresholds are temporarily displaced, reconfigure yellow lenses (caution zone), as necessary, and place the centerline lights out of service.

2.18.3.3.8 Relocate the Visual Glide Slope Indicator (VGSI), such as Visual Approach Slope Indicator (VASI) and Precision Approach Path Indicator (PAPI); other airport lights, such as Runway End Identifier Lights (REIL); and approach lights to identify the temporary threshold. Another option is to disable the VGSI or any equipment that would give misleading indications to pilots as to the new threshold location. Installation of temporary visual aids may be necessary to provide adequate guidance to pilots on approach to the affected runway. If the FAA owns and operates the VGSI, coordinate its installation or disabling with the local ATO/Technical Operations Office. Relocation of such visual aids will depend on the duration of the project and the benefits gained from the relocation, as this can result in great expense. See FAA JO 6850.2, *Visual Guidance Lighting Systems*, for installation criteria for FAA owned and operated NAVAIDs.

2.18.3.3.9 Issue a NOTAM to inform pilots of temporary lighting conditions.

2.18.3.4 **Temporarily Closed Taxiways.**

If possible, deactivate the taxiway lighting circuits. When deactivation is not possible (for example other taxiways on the same circuit are to remain open), cover the light fixture in a way as to prevent light leakage.

2.18.4 Signs.

To the extent possible, signs must be in conformance with AC 150/5345-44, *Specification for Runway and Taxiway Signs,* and AC 150/5340-18, *Standard for Airport Sign Systems.*

2.18.4.1 **Existing Signs.**

Runway exit signs are to be covered for closed runway exits. Outbound destination signs are to be covered for closed runways. Any time a sign does not serve its normal function or would provide conflicting information, it must be covered or removed to prevent misdirecting pilots. Note that information signs identifying a crossing taxiway continue to perform their normal function even if the crossing taxiway is closed. For long term construction projects, consider relocating signs, especially runway distance remaining signs.

2.18.4.2 **Temporary Signs.**

Orange construction signs comprise a message in black on an orange background. Orange construction signs may help pilots be aware of changed conditions. The airport operator may choose to introduce these signs as part of a movement area construction project to increase situational awareness when needed. Locate signs outside the taxiway safety limits and ahead of construction areas so pilots can take timely action. Use temporary signs judiciously, striking a balance between the need for information and the increase in pilot workload. When there is a concern of pilot "information overload," the applicability of mandatory hold signs must take precedence over orange construction signs recommended during construction. Temporary signs must meet the standards for such signs in Engineering Brief 93, *Guidance for the Assembly and Installation of Temporary Orange Construction Signs.* Many criteria in AC 150/5345-44, *Specification for Runway and Taxiway Signs,* are referenced in the Engineering Brief. Permissible sign legends are:

1. CONSTRUCTION AHEAD,
2. CONSTRUCTION ON RAMP, and
3. RWY XX TAKEOFF RUN AVAILABLE XXX FT.

Phasing, supported by drawings and sign schedule, for the installation of orange construction signs must be included in the CSPP or SPCD.

2.18.4.2.1 Takeoff Run Available (TORA) signs.

Recommended: Where a runway has been shortened for takeoff, install orange TORA signs well before the hold lines, such as on a parallel taxiway prior to a turn to a runway hold position. See EB 93 for sign size and location.

2.18.4.2.2 Sign legends are shown in Figure F-1.

Note: See Figure E-1, Figure E-2, Figure E-3, Figure F-2, and Figure F-3 for examples of orange construction sign locations.

2.19 **Marking and Signs for Access Routes.**

The CSPP should indicate that pavement markings and signs for construction personnel will conform to AC 150/5340-18 and, to the extent practicable, with the Federal Highway Administration Manual on Uniform Traffic Control Devices (MUTCD) and/or State highway specifications. Signs adjacent to areas used by aircraft must comply with the frangibility requirements of AC 150/5220-23, *Frangible Connections,* which may require modification to size and height guidance in the MUTCD.

2.20 **Hazard Marking, Lighting and Signing.**

2.20.1 Hazard marking, lighting, and signing prevent pilots from entering areas closed to aircraft, and prevent construction personnel from entering areas open to aircraft. The CSPP must specify prominent, comprehensible warning indicators for any area affected by construction that is normally accessible to aircraft, personnel, or vehicles. Hazard marking and lighting must also be specified to identify open manholes, small areas under repair, stockpiled material, waste areas, and areas subject to jet blast. Also consider less obvious construction-related hazards and include markings to identify FAA, airport, and National Weather Service facilities cables and power lines; instrument landing system (ILS) critical areas; airport surfaces, such as RSA, OFA, and OFZ; and other sensitive areas to make it easier for contractor personnel to avoid these areas.

2.20.2 Equipment.

2.20.2.1 **Barricades.**

Low profile barricades, including traffic cones, (weighted or sturdily attached to the surface) are acceptable methods used to identify and define the limits of construction and hazardous areas on airports. Careful consideration must be given to selecting equipment that poses the least danger to aircraft but is sturdy enough to remain in place when subjected to typical winds, prop wash and jet blast. The spacing of barricades must be such that a breach is physically prevented barring a deliberate act. For example, if barricades are intended to exclude aircraft, gaps between barricades must be smaller than the wingspan of the smallest aircraft to be excluded; if barricades are intended to exclude vehicles, gaps between barricades must be smaller than the width of the excluded vehicles, generally 4 feet (1.2 meters). Provision must be made for ARFF access if necessary. If barricades are intended to exclude pedestrians, they must be continuously linked. Continuous linking may be accomplished through the use of ropes, securely attached to prevent FOD.

2.20.2.2 **Lights.**

Lights must be red, either steady burning or flashing, and must meet the luminance requirements of the State Highway Department. Batteries powering lights will last longer if lights flash. Lights must be mounted on barricades and spaced at no more than 10 feet (3 meters). Lights must be operated between sunset and sunrise and during periods of low visibility whenever the airport is open for operations. They may be operated by photocell, but this may require that the contractor turn them on manually during periods of low visibility during daytime hours.

2.20.2.3 **Supplement Barricades with Signs (for example) As Necessary.**

Examples are “No Entry” and “No Vehicles.” Be aware of the increased effects of wind and jet blast on barricades with attached signs.

2.20.2.4 **Air Operations Area – General.**

Barricades are not permitted in any active safety area or on the runway side of a runway hold line. Within a runway or taxiway object free area, and on aprons, use orange traffic cones, flashing or steady burning red lights as noted above, highly reflective collapsible barricades marked with diagonal, alternating orange and white stripes; and/or signs to separate all construction/maintenance areas from the movement area. Barricades may be supplemented with alternating orange and white flags at least 20 by 20 inch (50 by 50 cm) square and securely fastened to eliminate FOD. All barricades adjacent to any open runway or taxiway / taxilane safety area, or apron must be as low as possible to the ground, and no more than 18 inches high, exclusive of supplementary lights and flags. Barricades must be of low mass; easily collapsible upon contact with an aircraft or any of its components; and weighted or sturdily attached to the surface to prevent displacement from prop wash, jet blast, wing vortex, and other surface wind currents. If affixed to the surface, they must be frangible at grade level or as low as possible, but not to exceed 3 inch (7.6 cm) above the ground. Figure 2-8 and Figure 2-9 show sample barricades with proper coloring and flags.

Figure 2-8. Interlocking Barricades



Figure 2-9. Low Profile Barricades



2.20.2.5 **Air Operations Area – Runway/Taxiway Intersections.**

Use highly reflective barricades with lights to close taxiways leading to closed runways. Evaluate all operating factors when determining how to mark temporary closures that can last from 10 to 15 minutes to a much longer period of time. However, even for closures of relatively short duration, close all taxiway/runway intersections with barricades. The use of traffic cones is appropriate for short duration closures.

2.20.2.6 **Air Operations Area – Other.**

Beyond runway and taxiway object free areas and aprons, barricades intended for construction vehicles and personnel may be many different shapes and made from various materials, including railroad ties, sawhorses, jersey barriers, or barrels.

2.20.2.7 **Maintenance.**

The construction specifications must include a provision requiring the contractor to have a person on call 24 hours a day for emergency maintenance of airport hazard lighting and barricades. The contractor must file the contact person's information with the airport operator. Lighting should be checked for proper operation at least once per day, preferably at dusk.

2.21 Work Zone Lighting for Nighttime Construction.

Lighting equipment must adequately illuminate the work area if the construction is to be performed during nighttime hours. Refer to AC 150/5370-10 for minimum illumination levels for nighttime paving projects. Additionally, it is recommended that all support equipment, except haul trucks, be equipped with artificial illumination to safely

illuminate the area immediately surrounding their work areas. The lights should be positioned to provide the most natural color illumination and contrast with a minimum of shadows. The spacing must be determined by trial. Light towers should be positioned and adjusted to aim away from ATCT cabs and active runways to prevent blinding effects. Shielding may be necessary. Light towers should be removed from the construction site when the area is reopened to aircraft operations. Construction lighting units should be identified and generally located on the construction phasing plans in relationship to the ATCT and active runways and taxiways.

2.22 **Protection of Runway and Taxiway Safety Areas.**

Runway and taxiway safety areas, OFZs, OFAs, and approach surfaces are described in AC 150/5300-13. Protection of these areas includes limitations on the location and height of equipment and stockpiled material. An FAA airspace study may be required. Coordinate with the appropriate FAA Airports Regional or District Office if there is any doubt as to requirements or dimensions (see paragraph 2.13.5) as soon as the location and height of materials or equipment are known. The CSPP should include drawings showing all safety areas, object free areas, obstacle free zones and approach departure surfaces affected by construction.

2.22.1 Runway Safety Area (RSA).

A runway safety area is the defined surface surrounding the runway prepared or suitable for reducing the risk of damage to airplanes in the event of an undershoot, overshoot, or excursion from the runway (see AC 150/5300-13). Construction activities within the existing RSA are subject to the following conditions:

2.22.1.1 No construction may occur within the existing RSA while the runway is open for aircraft operations. The RSA dimensions may be temporarily adjusted if the runway is restricted to aircraft operations requiring an RSA that is equal to the RSA width and length beyond the runway ends available during construction. (See AC 150/5300-13). The temporary use of declared distances and/or partial runway closures may provide the necessary RSA under certain circumstances. Coordinate with the appropriate FAA Airports Regional or District Office to have declared distances information published, and appropriate NOTAMs issued. See AC 150/5300-13 for guidance on the use of declared distances.

2.22.1.2 The airport operator must coordinate the adjustment of RSA dimensions as permitted above with the appropriate FAA Airports Regional or District Office and the local FAA air traffic manager and issue a NOTAM.

2.22.1.3 The CSPP and SPCD must provide procedures for ensuring adequate distance for protection from blasting operations, if required by operational considerations.

2.22.1.4 **Excavations.**

2.22.1.4.1 Open trenches or excavations are not permitted within the RSA while the runway is open. Backfill trenches before the runway is opened. If backfilling excavations before the runway must be opened is impracticable, cover the excavations appropriately. Covering for open trenches must be designed to allow the safe operation of the heaviest aircraft operating on the runway across the trench without damage to the aircraft.

2.22.1.4.2 Construction contractors must prominently mark open trenches and excavations at the construction site with red or orange flags, as approved by the airport operator, and light them with red lights during hours of restricted visibility or darkness.

2.22.1.5 **Erosion Control.**

Soil erosion must be controlled to maintain RSA standards, that is, the RSA must be cleared and graded and have no potentially hazardous ruts, humps, depressions, or other surface variations, and capable, under dry conditions, of supporting snow removal equipment, aircraft rescue and fire fighting equipment, and the occasional passage of aircraft without causing structural damage to the aircraft.

2.22.2 Runway Object Free Area (ROFA).

Construction, including excavations, may be permitted in the ROFA. However, equipment must be removed from the ROFA when not in use, and material should not be stockpiled in the ROFA if not necessary. Stockpiling material in the OFA requires submittal of a 7460-1 form and justification provided to the appropriate FAA Airports Regional or District Office for approval.

2.22.3 Taxiway Safety Area (TSA).

2.22.3.1 A taxiway safety area is a defined surface alongside the taxiway prepared or suitable for reducing the risk of damage to an airplane unintentionally departing the taxiway. (See AC 150/5300-13.) Since the width of the TSA is equal to the wingspan of the design aircraft, no construction may occur within the TSA while the taxiway is open for aircraft operations. The TSA dimensions may be temporarily adjusted if the taxiway is restricted to aircraft operations requiring a TSA that is equal to the TSA width available during construction. Give special consideration to TSA dimensions at taxiway turns and intersections. (see AC 150/5300-13).

2.22.3.2 The airport operator must coordinate the adjustment of the TSA width as permitted above with the appropriate FAA Airports Regional or District Office and the FAA air traffic manager and issue a NOTAM.

2.22.3.3 The CSPP and SPCD must provide procedures for ensuring adequate distance for protection from blasting operations.

2.22.3.4 **Excavations.**

1. Curves. Open trenches or excavations are not permitted within the TSA while the taxiway is open. Trenches should be backfilled before the taxiway is opened. If backfilling excavations before the taxiway must be opened is impracticable, cover the excavations appropriately. Covering for open trenches must be designed to allow the safe operation of the heaviest aircraft operating on the taxiway across the trench without damage to the aircraft.
2. Straight Sections. Open trenches or excavations are not permitted within the TSA while the taxiway is open for unrestricted aircraft operations. Trenches should be backfilled before the taxiway is opened. If backfilling excavations before the taxiway must be opened is impracticable, cover the excavations to allow the safe passage of ARFF equipment and of the heaviest aircraft operating on the taxiway across the trench without causing damage to the equipment or aircraft. In rare circumstances where the section of taxiway is indispensable for aircraft movement, open trenches or excavations may be permitted in the TSA while the taxiway is open to aircraft operations, subject to the following restrictions:
   a. Taxiing speed is limited to 10 mph.
   b. Appropriate NOTAMs are issued.
   c. Marking and lighting meeting the provisions of paragraphs 2.18 and 2.20 are implemented.
   d. Low mass, low-profile lighted barricades are installed.
   e. Appropriate temporary orange construction signs are installed.
3. Construction contractors must prominently mark open trenches and excavations at the construction site with red or orange flags, as approved by the airport operator, and light them with red lights during hours of restricted visibility or darkness.

2.22.3.5 **Erosion control.**

Soil erosion must be controlled to maintain TSA standards, that is, the TSA must be cleared and graded and have no potentially hazardous ruts, humps, depressions, or other surface variations, and capable, under dry conditions, of supporting snow removal equipment, aircraft rescue and firefighting equipment, and the occasional passage of aircraft without causing structural damage to the aircraft.

2.22.4 Taxiway Object Free Area (TOFA).

Unlike the Runway Object Free Area, aircraft wings regularly penetrate the taxiway object free area during normal operations. Thus, the restrictions are more stringent. Except as provided below, no construction may occur within the taxiway object free area while the taxiway is open for aircraft operations.

2.22.4.1 The taxiway object free area dimensions may be temporarily adjusted if the taxiway is restricted to aircraft operations requiring a taxiway object free area that is equal to the taxiway object free area width available. Give special consideration to TOFA dimensions at taxiway turns and intersections.

2.22.4.2 Offset taxiway centerline and edge pavement markings (do not use glass beads) may be used as a temporary measure to provide the required taxiway object free area. Where offset taxiway pavement markings are provided, centerline lighting, centerline reflectors, or taxiway edge reflectors are required. Existing lighting that does not coincide with the temporary markings must be taken out of service.

2.22.4.3 Construction activity, including open excavations, may be accomplished without adjusting the width of the taxiway object free area, subject to the following restrictions:

2.22.4.3.1 Taxiing speed is limited to 10 mph.

2.22.4.3.2 NOTAMs issued advising taxiing pilots of hazard and recommending reduced taxiing speeds on the taxiway.

2.22.4.3.3 Marking and lighting meeting the provisions of paragraphs 2.18 and 2.20 are implemented.

2.22.4.3.4 If desired, appropriate orange construction signs are installed. See paragraph 2.18.4.2 and Appendix F.

2.22.4.3.5 Five-foot clearance is maintained between equipment and materials and any part of an aircraft (includes wingtip overhang). If such clearance can only be maintained if an aircraft does not have full use of the entire taxiway width (with its main landing gear at the edge of the usable pavement), then it will be necessary to move personnel and equipment for the passage of that aircraft.

2.22.4.3.6 Flaggers furnished by the contractor must be used to direct and control construction equipment and personnel to a pre-established setback distance for safe passage of aircraft, and airline and/or airport personnel. Flaggers must also be used to direct taxiing aircraft. Due to liability issues, the airport operator should require airlines to provide flaggers for directing taxiing aircraft.

2.22.5 Obstacle Free Zone (OFZ).

In general, personnel, material, and/or equipment may not penetrate the OFZ while the runway is open for aircraft operations. If a penetration to the OFZ is necessary, it may be possible to continue aircraft operations through operational restrictions. Coordinate with the FAA through the appropriate FAA Airports Regional or District Office.

2.22.6 Runway Approach/Departure Areas and Clearways.

All personnel, materials, and/or equipment must remain clear of the applicable threshold siting surfaces, as defined in AC 150/5300-13. Objects that do not penetrate these surfaces may still be obstructions to air navigation and may affect standard instrument approach procedures. Coordinate with the FAA through the appropriate FAA Airports Regional or District Office.

2.22.6.1 Construction activity in a runway approach/departure area may result in the need to partially close a runway or displace the existing runway threshold. Partial runway closure, displacement of the runway threshold, as well as closure of the complete runway and other portions of the movement area also require coordination through the airport operator with the appropriate FAA air traffic manager (FSS if non-towered) and ATO/Technical Operations (for affected NAVAIDS) and airport users.

2.22.6.2 **Caution About Partial Runway Closures.**

When filing a NOTAM for a partial runway closure, clearly state that the portion of pavement located prior to the threshold is not available for landing and departing traffic. In this case, the threshold has been moved for both landing and takeoff purposes (this is different than a displaced threshold). There may be situations where the portion of closed runway is available for taxiing only. If so, the NOTAM must reflect this condition).

2.22.6.3 **Caution About Displaced Thresholds.**

Implementation of a displaced threshold affects runway length available for aircraft landing over the displacement. Depending on the reason for the displacement (to provide obstruction clearance or RSA), such a displacement may also require an adjustment in the landing distance available and accelerate-stop distance available in the opposite direction. If project scope includes personnel, equipment, excavation, or other work within the existing RSA of any usable runway end, do not implement a displaced threshold unless arrivals and departures toward the construction activity are prohibited. Instead, implement a partial closure.

2.23 **Other Limitations on Construction.**

The CSPP must specify any other limitations on construction, including but not limited to:

2.23.1 Prohibitions.

2.23.1.1 No use of tall equipment (cranes, concrete pumps, and so on) unless a 7460-1 determination letter is issued for such equipment.

2.23.1.2 No use of open flame welding or torches unless fire safety precautions are provided and the airport operator has approved their use.

2.23.1.3 No use of electrical blasting caps on or within 1,000 feet (300 meters) of the airport property. See AC 150/5370-10.

2.23.2 Restrictions.

2.23.2.1 Construction suspension required during specific airport operations.

2.23.2.2 Areas that cannot be worked on simultaneously.

2.23.2.3 Day or night construction restrictions.

2.23.2.4 Seasonal construction restrictions.

2.23.2.5 Temporary signs not approved by the airport operator.

2.23.2.6 Grades changes that could result in unplanned effects on NAVAIDs.

CHAPTER 3. GUIDELINES FOR WRITING A CSPP

3.1 General Requirements.

The CSPP is a standalone document written to correspond with the subjects outlined in paragraph 2.4. The CSPP is organized by numbered sections corresponding to each subject listed in paragraph 2.4, and described in detail in paragraphs 2.5 - 2.23. Each section number and title in the CSPP matches the corresponding subject outlined in paragraph 2.4 (for example, 1. Coordination, 2. Phasing, 3. Areas and Operations Affected by the Construction Activity, and so on). With the exception of the project scope of work outlined in Section 2. Phasing, only subjects specific to operational safety during construction should be addressed.

3.2 Applicability of Subjects.

Each section should, to the extent practical, focus on the specific subject. Where an overlapping requirement spans several sections, the requirement should be explained in detail in the most applicable section. A reference to that section should be included in all other sections where the requirement may apply. For example, the requirement to protect existing underground FAA ILS cables during trenching operations could be considered FAA ATO coordination (Coordination, paragraph 2.5.3), an area and operation affected by the construction activity (Areas and Operations Affected by the Construction Activity, paragraph 2.7.1.4), a protection of a NAVAID (Protection of Navigational Aids (NAVAIDs), paragraph 2.8), or a notification to the FAA of construction activities (Notification of Construction Activities, paragraph 2.13.5.3.2). However, it is more specifically an underground utility requirement (Underground Utilities, paragraph 2.15). The procedure for protecting underground ILS cables during trenching operations should therefore be described in 2.4.2.11: “The contractor must coordinate with the local FAA System Support Center (SSC) to mark existing ILS cable routes along Runway 17-35. The ILS cables will be located by hand digging whenever the trenching operation moves within 10 feet of the cable markings.” All other applicable sections should include a reference to 2.4.2.11: “ILS cables shall be identified and protected as described in 2.4.2.11” or “See 2.4.2.11 for ILS cable identification and protection requirements.” Thus, the CSPP should be considered as a whole, with no need to duplicate responses to related issues.

3.3 Graphical Representations.

Construction safety drawings should be included in the CSPP as attachments. When other graphical representations will aid in supporting written statements, the drawings, diagrams, and/or photographs should also be attached to the CSPP. References should be made in the CSPP to each graphical attachment and may be made in multiple sections.

3.4 **Reference Documents.**

The CSPP must not incorporate a document by reference unless reproduction of the material in that document is prohibited. In that case, either copies of or a source for the referenced document must be provided to the contractor. Where this AC recommends references (e.g. as in paragraph 3.9) the intent is to include a reference to the corresponding section in the CSPP, not to this Advisory Circular.

3.5 **Restrictions.**

The CSPP should not be considered as a project design review document. The CSPP should also avoid mention of permanent ("as-built") features such as pavements, markings, signs, and lighting, except when such features are intended to aid in maintaining operational safety during the construction.

3.6 **Coordination.**

Include in this section a detailed description of conferences and meetings to be held both before and during the project. Include appropriate information from AC 150/5370-12. Discuss coordination procedures and schedules for each required FAA ATO Technical Operations shutdown and restart and all required flight inspections.

3.7 **Phasing.**

Include in this section a detailed scope of work description for the project as a whole and each phase of work covered by the CSPP. This includes all locations and durations of the work proposed. Attach drawings to graphically support the written scope of work. Detail in this section the sequenced phases of the proposed construction. Include a reference to paragraph 3.8, as appropriate.

3.8 **Areas and Operations Affected by Construction.**

Focus in this section on identifying the areas and operations affected by the construction. Describe corresponding mitigation that is not covered in detail elsewhere in the CSPP. Include references to paragraphs below as appropriate. Attach drawings as necessary to graphically describe affected areas and mechanisms proposed. See Appendix F for sample operational effects tables and figures.

3.9 **NAVAID Protection.**

List in this section all NAVAID facilities that will be affected by the construction. Identify NAVAID facilities that will be placed out of service at any time prior to or during construction activities. Identify individuals responsible for coordinating each shutdown and when each facility will be out of service. Include a reference to paragraph 3.6 for FAA ATO NAVAID shutdown, restart, and flight inspection coordination. Outline in detail procedures to protect each NAVAID facility remaining in service from interference by construction activities. Include a reference to paragraph 3.14 for the

issuance of NOTAMs as required. Include a reference to paragraph 3.16 for the protection of underground cables and piping serving NAVAIDs. If temporary visual aids are proposed to replace or supplement existing facilities, include a reference to paragraph 3.19. Attach drawings to graphically indicate the affected NAVAIDS and the corresponding critical areas.

3.10 **Contractor Access.**

This will necessarily be the most extensive section of the CSPP. Provide sufficient detail so that a contractor not experienced in working on airports will understand the unique restrictions such work will require. Due to this extent, it should be broken down into subsections as described below:

3.10.1 Location of Stockpiled Construction Materials.

Describe in this section specific locations for stockpiling material. Note any height restrictions on stockpiles. Include a reference to paragraph 3.21 for hazard marking and lighting devices used to identify stockpiles. Include a reference to paragraph 3.11 for provisions to prevent stockpile material from becoming wildlife attractants. Include a reference to paragraph 3.12 for provisions to prevent stockpile material from becoming FOD. Attach drawings to graphically indicate the stockpile locations.

3.10.2 Vehicle and Pedestrian Operations.

While there are many items to be addressed in this major subsection of the CSPP, all are concerned with one main issue: keeping people and vehicles from areas of the airport where they don't belong. This includes preventing unauthorized entry to the AOA and preventing the improper movement of pedestrians or vehicles on the airport. In this section, focus on mechanisms to prevent construction vehicles and workers traveling to and from the worksite from unauthorized entry into movement areas. Specify locations of parking for both employee vehicles and construction equipment, and routes for access and haul roads. In most cases, this will best be accomplished by attaching a drawing. Quote from AC 150/5210-5 specific requirements for contractor vehicles rather than referring to the AC as a whole, and include special requirements for identifying HAZMAT vehicles. Quote from, rather than incorporate by reference, AC 150/5210-20 as appropriate to address the airport's rules for ground vehicle operations, including its training program. Discuss the airport's recordkeeping system listing authorized vehicle operators.

3.10.3 Two-Way Radio Communications.

Include a special section to identify all individuals who are required to maintain communications with Air Traffic (AT) at airports with active towers, or monitor CTAF at airports without or with closed ATCT. Include training requirements for all individuals required to communicate with AT. Individuals required to monitor AT frequencies should also be identified. If construction employees are also required to communicate by radio with Airport Operations, this procedure should be described in detail. Usage of vehicle mounted radios and/or portable radios should be addressed. Communication procedures for the event of disabled radio communication (that is, light

signals, telephone numbers, others) must be included. All radio frequencies should by identified (Tower, Ground Control, CTAF, UNICOM, ATIS, and so on).

3.10.4 Airport Security.

Address security as it applies to vehicle and pedestrian operations. Discuss TSA requirements, security badging requirements, perimeter fence integrity, gate security, and other needs. Attach drawings to graphically indicate secured and/or Security Identification Display Areas (SIDA), perimeter fencing, and available access points.

3.11 **Wildlife Management.**

Discuss in this section wildlife management procedures. Describe the maintenance of existing wildlife mitigation devices, such as perimeter fences, and procedures to limit wildlife attractants. Include procedures to notify Airport Operations of wildlife encounters. Include a reference to paragraph 3.10 for security (wildlife) fence integrity maintenance as required.

3.12 **FOD Management.**

In this section, discuss methods to control and monitor FOD: worksite housekeeping, ground vehicle tire inspections, runway sweeps, and so on. Include a reference to paragraph 3.15 for inspection requirements as required.

3.13 **HAZMAT Management.**

Describe in this section HAZMAT management procedures: fuel deliveries, spill recovery procedures, Safety Data Sheet (SDS), Material Safety Data Sheet (MSDS) or Product Safety Data Sheet (PSDS) availability, and other considerations. Any specific airport HAZMAT restrictions should also be identified. Include a reference to paragraph 3.10 for HAZMAT vehicle identification requirements. Quote from, rather than incorporate by reference, AC 150/5320-15.

3.14 **Notification of Construction Activities.**

List in this section the names and telephone numbers of points of contact for all parties affected by the construction project. We recommend a single list that includes all telephone numbers required under this section. Include emergency notification procedures for all representatives of all parties potentially impacted by the construction. Identify individual representatives – and at least one alternate – for each party. List both on-duty and off-duty contact information for each individual, including individuals responsible for emergency maintenance of airport construction hazard lighting and barricades. Describe procedures to coordinate immediate response to events that might adversely affect the operational safety of the airport (such as interrupted NAVAID service). Explain requirements for and the procedures for the issuance of Notices to Airmen (NOTAMs), notification to FAA required by 14 CFR Part 77 and Part 157 and in the event of affected NAVAIDs. For NOTAMs, identify an individual, and at least one alternate, responsible for issuing and cancelling each specific type of Notice to

Airmen (NOTAM) required. Detail notification methods for police, fire fighting, and medical emergencies. This may include 911, but should also include direct phone numbers of local police departments and nearby hospitals. Identify the E911 address of the airport and the emergency access route via haul roads to the construction site. Require the contractor to have this information available to all workers. The local Poison Control number should be listed. Procedures regarding notification of Airport Operations and/or the ARFF Department of such emergencies should be identified, as applicable. If airport radio communications are identified as a means of emergency notification, include a reference to paragraph 3.10. Differentiate between emergency and nonemergency notification of ARFF personnel, the latter including activities that affect ARFF water supplies and access roads. Identify the primary ARFF contact person and at least one alternate. If notification is to be made through Airport Operations, then detail this procedure. Include a method of confirmation from the ARFF department.

3.15 **Inspection Requirements.**

Describe in this section inspection requirements to ensure airfield safety compliance. Include a requirement for routine inspections by the resident engineer (RE) or other airport operator's representative and the construction contractors. If the engineering consultants and/or contractors have a Safety Officer who will conduct such inspections, identify this individual. Describe procedures for special inspections, such as those required to reopen areas for aircraft operations. Part 139 requires daily airfield inspections at certificated airports, but these may need to be more frequent when construction is in progress. Discuss the role of such inspections on areas under construction. Include a requirement to immediately remedy any deficiencies, whether caused by negligence, oversight, or project scope change.

3.16 **Underground Utilities.**

Explain how existing underground utilities will be located and protected. Identify each utility owner and include contact information for each company/agency in the master list. Address emergency response procedures for damaged or disrupted utilities. Include a reference to paragraph 3.14 for notification of utility owners of accidental utility disruption as required.

3.17 **Penalties.**

Describe in this section specific penalties imposed for noncompliance with airport rules and regulations, including the CSPP: SIDA violations, VPD, and others.

3.18 **Special Conditions.**

Identify any special conditions that may trigger specific safety mitigation actions outlined in this CSPP: low visibility operations, snow removal, aircraft in distress, aircraft accident, security breach, VPD, and other activities requiring construction suspension/resumption. Include a reference to paragraph 3.10 for compliance with airport safety and security measures and for radio communications as required. Include

a reference to paragraph 3.14 for emergency notification of all involved parties, including police/security, ARFF, and medical services.

3.19 **Runway and Taxiway Visual Aids.**

Include marking, lighting, signs, and visual NAVAIDS. Detail temporary runway and taxiway marking, lighting, signs, and visual NAVAIDs required for the construction. Discuss existing marking, lighting, signs, and visual NAVAIDs that are temporarily, altered, obliterated, or shut down. Consider non-federal facilities and address requirements for reimbursable agreements necessary for alteration of FAA facilities and for necessary flight checks. Identify temporary TORA signs or runway distance remaining signs if appropriate. Identify required temporary visual NAVAIDs such as REIL or PAPI. Quote from, rather than incorporate by reference, AC 150/5340-1, *Standards for Airport Markings;* AC 150/5340-18, *Standards for Airport Sign Systems;* and AC 150/5340-30, as required. Attach drawings to graphically indicate proposed marking, lighting, signs, and visual NAVAIDs.

3.20 **Marking and Signs for Access Routes.**

Detail plans for marking and signs for vehicle access routes. To the extent possible, signs should be in conformance with the Federal Highway Administration MUTCD and/or State highway specifications, not hand lettered. Detail any modifications to the guidance in the MUTCD necessary to meet frangibility/height requirements.

3.21 **Hazard Marking and Lighting.**

Specify all marking and lighting equipment, including when and where each type of device is to be used. Specify maximum gaps between barricades and the maximum spacing of hazard lighting. Identify one individual and at least one alternate responsible for maintenance of hazard marking and lighting equipment in the master telephone list. Include a reference to paragraph 3.14. Attach drawings to graphically indicate the placement of hazard marking and lighting equipment.

3.22 **Work Zone Lighting for Nighttime Construction.**

If work is to be conducted at night, specify all lighting equipment, including when and where each type of device is to be used. Indicate the direction lights are to be aimed and any directions that aiming of lights is prohibited. Specify any shielding necessary in instances where aiming is not sufficient to prevent interference with air traffic control and aircraft operations. Attach drawings to graphically indicate the placement and aiming of lighting equipment. Where the plan only indicates directions that aiming of lights is prohibited, the placement and positioning of portable lights must be proposed by the Contractor and approved by the airport operator’s representative each time lights are relocated or repositioned.

3.23 **Protection of Runway and Taxiway Safety Areas.**

This section should focus exclusively on procedures for protecting all safety areas, including those altered by the construction: methods of demarcation, limit of access, movement within safety areas, stockpiling and trenching restrictions, and so on. Reference AC 150/5300-13, as required. Include a reference to paragraph 3.10 for procedures regarding vehicle and personnel movement within safety areas. Include a reference to paragraph 3.10 for material stockpile restrictions as required. Detail requirements for trenching, excavations, and backfill. Include a reference to paragraph 3.21 for hazard marking and lighting devices used to identify open excavations as required. If runway and taxiway closures are proposed to protect safety areas, or if temporary displaced thresholds and/or revised declared distances are used to provide the required Runway Safety Area, include a reference to paragraphs 3.14 and 3.19. Detail procedures for protecting the runway OFZ, runway OFA, taxiway OFA and runway approach surfaces including those altered by the construction: methods of demarcation, limit of cranes, storage of equipment, and so on. Quote from, rather than incorporate by reference, AC 150/5300-13, as required. Include a reference to paragraph 3.24 for height (i.e., crane) restrictions as required. One way to address the height of equipment that will move during the project is to establish a three-dimensional "box" within which equipment will be confined that can be studied as a single object. Attach drawings to graphically indicate the safety area, OFZ, and OFA boundaries.

3.24 **Other Limitations on Construction.**

This section should describe what limitations must be applied to each area of work and when each limitation will be applied: limitations due to airport operations, height (i.e., crane) restrictions, areas which cannot be worked at simultaneously, day/night work restrictions, winter construction, and other limitations. Include a reference to paragraph 3.7 for project phasing requirements based on construction limitations as required.

Page Intentionally Blank

APPENDIX A. RELATED READING MATERIAL

Obtain the latest version of the following free publications from the FAA on its Web site at http://www.faa.gov/airports/.

Table A-1. FAA Publications

Number	Title and Description
AC 150/5200-28	*Notices to Airmen (NOTAMs) for Airport Operators* Guidance for using the NOTAM System in airport reporting.
AC 150/5200-30	*Airport Field Condition Assessments and Winter Operations Safety* Guidance for airport owners/operators on the development of an acceptable airport snow and ice control program and on appropriate field condition reporting procedures.
AC 150/5200-33	*Hazardous Wildlife Attractants On or Near Airports* Guidance on locating certain land uses that might attract hazardous wildlife to public-use airports.
AC 150/5210-5	*Painting, Marking, and Lighting of Vehicles Used on an Airport* Guidance, specifications, and standards for painting, marking, and lighting vehicles operating in the airport air operations areas.
AC 150/5210-20	*Ground Vehicle Operations to include Taxiing or Towing an Aircraft on Airports* Guidance to airport operators on developing ground vehicle operation training programs.
AC 150/5300-13	*Airport Design* FAA standards and recommendations for airport design. Establishes approach visibility minimums as an airport design parameter, and contains the Object Free area and the obstacle free-zone criteria.
AC 150/5210-24	*Airport Foreign Object Debris (FOD) Management* Guidance for developing and managing an airport foreign object debris (FOD) program

Number	Title and Description
AC 150/5320-15	*Management of Airport Industrial Waste* Basic information on the characteristics, management, and regulations of industrial wastes generated at airports. Guidance for developing a Storm Water Pollution Prevention Plan (SWPPP) that applies best management practices to eliminate, prevent, or reduce pollutants in storm water runoff with particular airport industrial activities.
AC 150/5340-1	*Standards for Airport Markings* FAA standards for the siting and installation of signs on airport runways and taxiways.
AC 150/5340-18	*Standards for Airport Sign Systems* FAA standards for the siting and installation of signs on airport runways and taxiways.
AC 150/5345-28	*Precision Approach Path Indicator (PAPI) Systems* FAA standards for PAPI systems, which provide pilots with visual glide slope guidance during approach for landing.
AC 150/5340-30	*Design and Installation Details for Airport Visual Aids* Guidance and recommendations on the installation of airport visual aids.
AC 150/5345-39	*Specification for L-853, Runway and Taxiway Retroreflective Markers*
AC 150/5345-44	*Specification for Runway and Taxiway Signs* FAA specifications for unlighted and lighted signs for taxiways and runways.
AC 150/5345-53	*Airport Lighting Equipment Certification Program* Details on the Airport Lighting Equipment Certification Program (ALECP).
AC 150/5345-50	*Specification for Portable Runway and Taxiway Lights* FAA standards for portable runway and taxiway lights and runway end identifier lights for temporary use to permit continued aircraft operations while all or part of a runway lighting system is inoperative.
AC 150/5345-55	*Specification for L-893, Lighted Visual Aid to Indicate Temporary Runway Closure*

Number	Title and Description
AC 150/5370-10	*Standards for Specifying Construction of Airports* Standards for construction of airports, including earthwork, drainage, paving, turfing, lighting, and incidental construction.
AC 150/5370-12	*Quality Management for Federally Funded Airport Construction Projects*
EB 93	*Guidance for the Assembly and Installation of Temporary Orange Construction Signs*
FAA Order 5200.11	FAA Airports (ARP) Safety Management System (SMS) Basics for implementing SMS within ARP. Includes roles and responsibilities of ARP management and staff as well as other FAA lines of business that contribute to the ARP SMS.
FAA Certalert 98-05	*Grasses Attractive to Hazardous Wildlife* Guidance on grass management and seed selection.
FAA Form 7460-1	Notice of Proposed Construction or Alteration
FAA Form 7480-1	Notice of Landing Area Proposal
FAA Form 6000.26	National NAS Strategic Interruption Service Level Agreement, Strategic Events Coordination, Airport Sponsor Form

Obtain the latest version of the following free publications from the Electronic Code of Federal Regulations at http://www.ecfr.gov/.

Table A-2. Code of Federal Regulation

Number	Title
Title 14 CFR Part 77	Safe, Efficient Use and Preservation of the Navigable Airspace
Title 14 CFR Part 139	Certification of Airports
Title 49 CFR Part 1542	Airport Security

Obtain the latest version of the Manual on Uniform Traffic Control Devices from the Federal Highway Administration at http://mutcd.fhwa.dot.gov/.

Page Intentionally Blank

APPENDIX B. TERMS AND ACRONYMS

Table B-1. Terms and Acronyms

Term	Definition
Form 7460-1	Notice of Proposed Construction or Alteration. For on-airport projects, the form submitted to the FAA regional or airports division office as formal written notification of any kind of construction or alteration of objects that affect navigable airspace, as defined in 14 CFR Part 77, *Safe, Efficient Use, and Preservation of the Navigable Airspace*. (See guidance available on the FAA web site at https://oeaaa.faa.gov.) The form may be downloaded at http://www.faa.gov/airports/resources/forms/, or filed electronically at: https://oeaaa.faa.gov.
Form 7480-1	Notice of Landing Area Proposal. Form submitted to the FAA Airports Regional Division Office or Airports District Office as formal written notification whenever a project without an airport layout plan on file with the FAA involves the construction of a new airport; the construction, realigning, altering, activating, or abandoning of a runway, landing strip, or associated taxiway; or the deactivation or abandoning of an entire airport The form may be downloaded at http://www.faa.gov/airports/resources/forms/.
Form 6000-26	Airport Sponsor Strategic Event Submission Form
AC	Advisory Circular
ACSI	Airport Certification Safety Inspector
ADG	Airplane Design Group
AIP	Airport Improvement Program
ALECP	Airport Lighting Equipment Certification Program
ANG	Air National Guard
AOA	Air Operations Area, as defined in 14 CFR Part 107. Means a portion of an airport, specified in the airport security program, in which security measures are carried out. This area includes aircraft movement areas, aircraft parking areas, loading ramps, and safety areas, and any adjacent areas (such as general aviation areas) that are not separated by adequate security systems, measures, or procedures. This area does not include the secured area of the airport terminal building.
ARFF	Aircraft Rescue and Fire Fighting
ARP	FAA Office of Airports
ASDA	Accelerate-Stop Distance Available
AT	Air Traffic
ATCT	Airport Traffic Control Tower
ATIS	Automatic Terminal Information Service
ATO	Air Traffic Organization
Certificated Airport	An airport that has been issued an Airport Operating Certificate by the FAA under

Term	Definition
	the authority of 14 CFR Part 139, *Certification of Airports*.
CFR	Code of Federal Regulations
Construction	The presence of construction-related personnel, equipment, and materials in any location that could infringe upon the movement of aircraft.
CSPP	Construction Safety and Phasing Plan. The overall plan for safety and phasing of a construction project developed by the airport operator, or developed by the airport operator's consultant and approved by the airport operator. It is included in the invitation for bids and becomes part of the project specifications.
CTAF	Common Traffic Advisory Frequency
Displaced Threshold	A threshold that is located at a point on the runway other than the designated beginning of the runway. The portion of pavement behind a displaced threshold is available for takeoffs in either direction or landing from the opposite direction.
DOT	Department of Transportation
EPA	Environmental Protection Agency
FAA	Federal Aviation Administration
FOD	Foreign Object Debris/Damage
FSS	Flight Service Station
GA	General Aviation
HAZMAT	Hazardous Materials
HMA	Hot Mix Asphalt
IAP	Instrument Approach Procedures
IFR	Instrument Flight Rules
ILS	Instrument Landing System
LDA	Landing Distance Available
LOC	Localizer antenna array
Movement Area	The runways, taxiways, and other areas of an airport that are used for taxiing or hover taxiing, air taxiing, takeoff, and landing of aircraft, exclusive of loading aprons and aircraft parking areas (reference 14 CFR Part 139).
MSDS	Material Safety Data Sheet
MUTCD	Manual on Uniform Traffic Control Devices
NAVAID	Navigation Aid
NAVAID Critical Area	An area of defined shape and size associated with a NAVAID that must remain clear and graded to avoid interference with the electronic signal.
Non-Movement Area	The area inside the airport security fence exclusive of the Movement Area. It is important to note that the non-movement area includes pavement traversed by aircraft.

Term	Definition
NOTAM	Notices to Airmen
Obstruction	Any object/obstacle exceeding the obstruction standards specified by 14 CFR Part 77, subpart C.
OCC	Operations Control Center
OE / AAA	Obstruction Evaluation / Airport Airspace Analysis
OFA	Object Free Area. An area on the ground centered on the runway, taxiway, or taxi lane centerline provided to enhance safety of aircraft operations by having the area free of objects except for those objects that need to be located in the OFA for air navigation or aircraft ground maneuvering purposes. (See AC 150/5300-13 for additional guidance on OFA standards and wingtip clearance criteria.)
OFZ	Obstacle Free Zone. The airspace below 150 ft (45 m) above the established airport elevation and along the runway and extended runway centerline that is required to be clear of all objects, except for frangible visual NAVAIDs that need to be located in the OFZ because of their function, in order to provide clearance protection for aircraft landing or taking off from the runway and for missed approaches. The OFZ is subdivided as follows: Runway OFZ, Inner Approach OFZ, Inner Transitional OFZ, and Precision OFZ. Refer to AC 150/5300-13 for guidance on OFZ.
OSHA	Occupational Safety and Health Administration
OTS	Out of Service
P&R	Planning and Requirements Group
NPI	NAS Planning & Integration
PAPI	Precision Approach Path Indicator
PFC	Passenger Facility Charge
PLASI	Pulse Light Approach Slope Indicator
Project Proposal Summary	A clear and concise description of the proposed project or change that is the object of Safety Risk Management.
RA	Reimbursable Agreement
RE	Resident Engineer
REIL	Runway End Identifier Lights
RNAV	Area Navigation
ROFA	Runway Object Free Area
RSA	Runway Safety Area. A defined surface surrounding the runway prepared or suitable for reducing the risk of damage to airplanes in the event of an undershoot, overshoot, or excursion from the runway, in accordance with AC 150/5300-13.
SDS	Safety Data Sheet
SIDA	Security Identification Display Area
SMS	Safety Management System

Term	Definition
SPCD	Safety Plan Compliance Document. Details developed and submitted by a contractor to the airport operator for approval providing details on how the performance of a construction project will comply with the CSPP.
SRM	Safety Risk Management
SSC	System Support Center
Taxiway Safety Area	A defined surface alongside the taxiway prepared or suitable for reducing the risk of damage to an airplane unintentionally departing the taxiway, in accordance with AC 150/5300-13.
TDG	Taxiway Design Group
Temporary	Any condition that is not intended to be permanent.
Temporary Runway End	The beginning of that portion of the runway available for landing and taking off in one direction, and for landing in the other direction. Note the difference from a displaced threshold.
Threshold	The beginning of that portion of the runway available for landing. In some instances, the landing threshold may be displaced.
TODA	Takeoff Distance Available
TOFA	Taxiway Object Free Area
TORA	Takeoff Run Available. The length of the runway less any length of runway unavailable and/or unsuitable for takeoff run computations. See AC 150/5300-13 for guidance on declared distances.
TSA	Taxiway Safety Area, or Transportation Security Administration
UNICOM	A radio communications system of a type used at small airports.
VASI	Visual Approach Slope Indicator
VGSI	Visual Glide Slope Indicator. A device that provides a visual glide slope indicator to landing pilots. These systems include precision approach path indicator (PAPI), visual approach slope indicator (VASI), and pulse light approach slope indicator (PLASI).
VFR	Visual Flight Rules
VOR	Very High Frequency Omnidirectional Radio Range
VPD	Vehicle / Pedestrian Deviation

APPENDIX C. SAFETY AND PHASING PLAN CHECKLIST

This appendix is keyed to Chapter 2. In the electronic version of this AC, clicking on the paragraph designation in the Reference column will access the applicable paragraph. There may be instances where the CSPP requires provisions that are not covered by the list in this appendix.

This checklist is intended as an aid, not a required submittal.

Table C-1. CSPP Checklist

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
General Considerations					
Requirements for predesign, prebid, and preconstruction conferences to introduce the subject of airport operational safety during construction are specified.	2.5				
Operational safety is a standing agenda item for construction progress meetings.	2.5				
Scheduling of the construction phases is properly addressed.	2.6				
Any formal agreements are established.	2.5.3				
Areas and Operations Affected by Construction Activity					
Drawings showing affected areas are included.	2.7.1				
Closed or partially closed runways, taxiways, and aprons are depicted on drawings.	2.7.1.1				
Access routes used by ARFF vehicles affected by the project are addressed.	2.7.1.2				
Access routes used by airport and airline support vehicles affected by the project are addressed.	2.7.1.3				
Underground utilities, including water supplies for firefighting and drainage.	2.7.1.4				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
Approach/departure surfaces affected by heights of temporary objects are addressed.	2.7.1.5				
Construction areas, storage areas, and access routes near runways, taxiways, aprons, or helipads are properly depicted on drawings.	2.7.1				
Temporary changes to taxi operations are addressed.	2.7.2.1				
Detours for ARFF and other airport vehicles are identified.	2.7.2.2				
Maintenance of essential utilities and underground infrastructure is addressed.	2.7.2.3				
Temporary changes to air traffic control procedures are addressed.	2.7.2.4				
NAVAIDs					
Critical areas for NAVAIDs are depicted on drawings.	2.8				
Effects of construction activity on the performance of NAVAIDS, including unanticipated power outages, are addressed.	2.8				
Protection of NAVAID facilities is addressed.	2.8				
The required distance and direction from each NAVAID to any construction activity is depicted on drawings.	2.8				
Procedures for coordination with FAA ATO/Technical Operations, including identification of points of contact, are included.	2.8, 2.13.1, 2.13.5.3.1, 2.18.1				
Contractor Access					
The CSPP addresses areas to which contractor will have access and how	2.9				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
the areas will be accessed.					
The application of 49 CFR Part 1542 Airport Security, where appropriate, is addressed.	2.9				
The location of stockpiled construction materials is depicted on drawings.	2.9.1				
The requirement for stockpiles in the ROFA to be approved by FAA is included.	2.9.1				
Requirements for proper stockpiling of materials are included.	2.9.1				
Construction site parking is addressed.	2.9.2.1				
Construction equipment parking is addressed.	2.9.2.2				
Access and haul roads are addressed.	2.9.2.3				
A requirement for marking and lighting of vehicles to comply with AC 150/5210-5, *Painting, Marking and Lighting of Vehicles Used on an Airport,* is included.	2.9.2.4				
Proper vehicle operations, including requirements for escorts, are described.	2.9.2.5, 2.9.2.6				
Training requirements for vehicle drivers are addressed.	2.9.2.7				
Two-way radio communications procedures are described.	2.9.2.9				
Maintenance of the secured area of the airport is addressed.	2.9.2.10				
Wildlife Management					
The airport operator's wildlife management procedures are addressed.	2.10				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
Foreign Object Debris Management					
The airport operator's FOD management procedures are addressed.	2.11				
Hazardous Materials Management					
The airport operator's hazardous materials management procedures are addressed.	2.12				
Notification of Construction Activities					
Procedures for the immediate notification of airport user and local FAA of any conditions adversely affecting the operational safety of the airport are detailed.	2.13				
Maintenance of a list by the airport operator of the responsible representatives/points of contact for all involved parties and procedures for contacting them 24 hours a day, seven days a week is specified.	2.13.1				
A list of local ATO/Technical Operations personnel is included.	2.13.1				
A list of ATCT managers on duty is included.	2.13.1				
A list of authorized representatives to the OCC is included.	2.13.2				
Procedures for coordinating, issuing, maintaining and cancelling by the airport operator of NOTAMS about airport conditions resulting from construction are included.	2.8, 2.13.2, 2.18.3.3.9				
Provision of information on closed or hazardous conditions on airport movement areas by the airport operator to the OCC is specified.	2.13.2				
Emergency notification procedures for medical, fire fighting, and police	2.13.3				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
response are addressed.					
Coordination with ARFF personnel for non-emergency issues is addressed.	2.13.4				
Notification to the FAA under 14 CFR parts 77 and 157 is addressed.	2.13.5				
Reimbursable agreements for flight checks and/or design and construction for FAA owned NAVAIDs are addressed.	2.13.5.3.2				
Inspection Requirements					
Daily and interim inspections by both the airport operator and contractor are specified.	2.14.1, 2.14.2				
Final inspections at certificated airports are specified when required.	2.14.3				
Underground Utilities					
Procedures for protecting existing underground facilities in excavation areas are described.	2.15				
Penalties					
Penalty provisions for noncompliance with airport rules and regulations and the safety plans are detailed.	2.16				
Special Conditions					
Any special conditions that affect the operation of the airport or require the activation of any special procedures are addressed.	2.17				
Runway and Taxiway Visual Aids - Marking, Lighting, Signs, and Visual NAVAIDs					
The proper securing of temporary airport markings, lighting, signs, and visual NAVAIDs is addressed.	2.18.1				
Frangibility of airport markings, lighting, signs, and visual NAVAIDs is specified.	2.18.1, 2.18.3, 2.18.4.2, 2.20.2.4				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
The requirement for markings to be in compliance with AC 150/5340-1, *Standards for Airport Markings,* is specified.	2.18.2				
Detailed specifications for materials and methods for temporary markings are provided.	2.18.2				
The requirement for lighting to conform to AC 150/5340-30, *Design and Installation Details for Airport Visual Aids;* AC 150/5345-50, *Specification for Portable Runway and Taxiway Lights;* and AC 150/5345-53, *Airport Lighting Certification Program,* is specified.	2.18.3				
The use of a lighted X is specified where appropriate.	2.18.2.1.2, 2.18.3.2				
The requirement for signs to conform to AC 150/5345-44, *Specification for Runway and Taxiway Signs;* AC 50/5340-18, *Standards for Airport Sign Systems;* and AC 150/5345-53, *Airport Lighting Certification Program,* is specified.	2.18.4				
Marking and Signs For Access Routes					
The CSPP specifies that pavement markings and signs intended for construction personnel should conform to AC 150/5340-18 and, to the extent practicable, with the MUTCD and/or State highway specifications.	2.18.4.2				
Hazard Marking and Lighting					
Prominent, comprehensible warning indicators for any area affected by construction that is normally accessible to aircraft, personnel, or vehicles are specified.	2.20.1				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
Hazard marking and lighting are specified to identify open manholes, small areas under repair, stockpiled material, and waste areas.	2.20.1				
The CSPP considers less obvious construction-related hazards.	2.20.1				
Equipment that poses the least danger to aircraft but is sturdy enough to remain in place when subjected to typical winds, prop wash and jet blast is specified.	2.20.2.1				
The spacing of barricades is specified such that a breach is physically prevented barring a deliberate act.	2.20.2.1				
Red lights meeting the luminance requirements of the State Highway Department are specified.	2.20.2.2				
Barricades, temporary markers, and other objects placed and left in areas adjacent to any open runway, taxiway, taxi lane, or apron are specified to be as low as possible to the ground, and no more than 18 inch high.	2.20.2.3				
Barricades are specified to indicate construction locations in which no part of an aircraft may enter.	2.20.2.3				
Highly reflective barriers with lights are specified to barricade taxiways leading to closed runways.	2.20.2.5				
Markings for temporary closures are specified.	2.20.2.5				
The provision of a contractor's representative on call 24 hours a day for emergency maintenance of airport hazard lighting and barricades is specified.	2.20.2.7				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
Work Zone Lighting for Nighttime Construction					
If work is to be conducted at night, the CSPP identifies construction lighting units and their general locations and aiming in relationship to the ATCT and active runways and taxiways.	2.21				
Protection of Runway and Taxiway Safety Areas					
The CSPP clearly states that no construction may occur within a safety area while the associated runway or taxiway is open for aircraft operations.	2.22.1.1, 2.22.3.1				
The CSPP specifies that the airport operator coordinates the adjustment of RSA or TSA dimensions with the ATCT and the appropriate FAA Airports Regional or District Office and issues a local NOTAM.	2.22.1.2, 2.22.3.2				
Procedures for ensuring adequate distance for protection from blasting operations, if required by operational considerations, are detailed.	2.22.3.3				
The CSPP specifies that open trenches or excavations are not permitted within a safety area while the associated runway or taxiway is open, subject to approved exceptions.	2.22.1.4				
Appropriate covering of excavations in the RSA or TSA that cannot be backfilled before the associated runway or taxiway is open is detailed.	2.22.1.4				
The CSPP includes provisions for prominent marking of open trenches and excavations at the construction site.	2.22.1.4				
Grading and soil erosion control to maintain RSA/TSA standards are	2.22.3.5				

Coordination	Reference	Addressed?			Remarks
		Yes	No	NA	
addressed.					
The CSPP specifies that equipment is to be removed from the ROFA when not in use.	2.22.2				
The CSPP clearly states that no construction may occur within a taxiway safety area while the taxiway is open for aircraft operations.	2.22.3				
Appropriate details are specified for any construction work to be accomplished in a taxiway object free area.	2.22.4				
Measures to ensure that personnel, material, and/or equipment do not penetrate the OFZ or threshold siting surfaces while the runway is open for aircraft operations are included.	2.22.4.3.6				
Provisions for protection of runway approach/departure areas and clearways are included.	2.22.6				
Other Limitations on Construction					
The CSPP prohibits the use of open flame welding or torches unless adequate fire safety precautions are provided and the airport operator has approved their use.	2.23.1.2				
The CSPP prohibits the use of electrical blasting caps on or within 1,000 ft (300 m) of the airport property.	2.23.1.3				

APPENDIX D. CONSTRUCTION PROJECT DAILY SAFETY INSPECTION CHECKLIST

The situations identified below are potentially hazardous conditions that may occur during airport construction projects. Safety area encroachments, unauthorized and improper ground vehicle operations, and unmarked or uncovered holes and trenches near aircraft operating surfaces pose the most prevalent threats to airport operational safety during airport construction projects. The list below is one tool that the airport operator or contractor may use to aid in identifying and correcting potentially hazardous conditions. It should be customized as appropriate for each project including information such as the date, time and name of the person conducting the inspection.

Table D-1. Potentially Hazardous Conditions

Item	Action Required (Describe)	No Action Required (Check)
Excavation adjacent to runways, taxiways, and aprons improperly backfilled.		
Mounds of earth, construction materials, temporary structures, and other obstacles near any open runway, taxiway, or taxi lane; in the related Object Free area and aircraft approach or departure areas/zones; or obstructing any sign or marking.		
Runway resurfacing projects resulting in lips exceeding 3 inch (7.6 cm) from pavement edges and ends.		
Heavy equipment (stationary or mobile) operating or idle near AOA, in runway approaches and departures areas, or in OFZ.		
Equipment or material near NAVAIDs that may degrade or impair radiated signals and/or the monitoring of navigation and visual aids. Unauthorized or improper vehicle operations in localizer or glide slope critical areas, resulting in electronic interference and/or facility shutdown.		
Tall and especially relatively low visibility units (that is, equipment with slim profiles) — cranes, drills, and similar objects — located in critical areas, such as OFZ and		

Item	Action Required (Describe)	No Action Required (Check)
approach zones.		
Improperly positioned or malfunctioning lights or unlighted airport hazards, such as holes or excavations, on any apron, open taxiway, or open taxi lane or in a related safety, approach, or departure area.		
Obstacles, loose pavement, trash, and other debris on or near AOA. Construction debris (gravel, sand, mud, paving materials) on airport pavements may result in aircraft propeller, turbine engine, or tire damage. Also, loose materials may blow about, potentially causing personal injury or equipment damage.		
Inappropriate or poorly maintained fencing during construction intended to deter human and animal intrusions into the AOA. Fencing and other markings that are inadequate to separate construction areas from open AOA create aviation hazards.		
Improper or inadequate marking or lighting of runways (especially thresholds that have been displaced or runways that have been closed) and taxiways that could cause pilot confusion and provide a potential for a runway incursion. Inadequate or improper methods of marking, barricading, and lighting of temporarily closed portions of AOA create aviation hazards.		
Wildlife attractants — such as trash (food scraps not collected from construction personnel activity), grass seeds, tall grass, or standing water — on or near airports.		
Obliterated or faded temporary markings on active operational areas.		
Misleading or malfunctioning obstruction lights. Unlighted or unmarked obstructions in the approach to any open runway pose aviation hazards.		

Item	Action Required (Describe)	No Action Required (Check)
Failure to issue, update, or cancel NOTAMs about airport or runway closures or other construction related airport conditions.		
Failure to mark and identify utilities or power cables. Damage to utilities and power cables during construction activity can result in the loss of runway / taxiway lighting; loss of navigation, visual, or approach aids; disruption of weather reporting services; and/or loss of communications.		
Restrictions on ARFF access from fire stations to the runway / taxiway system or airport buildings.		
Lack of radio communications with construction vehicles in airport movement areas.		
Objects, regardless of whether they are marked or flagged, or activities anywhere on or near an airport that could be distracting, confusing, or alarming to pilots during aircraft operations.		
Water, snow, dirt, debris, or other contaminants that temporarily obscure or derogate the visibility of runway/taxiway marking, lighting, and pavement edges. Any condition or factor that obscures or diminishes the visibility of areas under construction.		
Spillage from vehicles (gasoline, diesel fuel, oil) on active pavement areas, such as runways, taxiways, aprons, and airport roadways.		
Failure to maintain drainage system integrity during construction (for example, no temporary drainage provided when working on a drainage system).		

Item	Action Required (Describe)	No Action Required (Check)
Failure to provide for proper electrical lockout and tagging procedures. At larger airports with multiple maintenance shifts/workers, construction contractors should make provisions for coordinating work on circuits.		
Failure to control dust. Consider limiting the amount of area from which the contractor is allowed to strip turf.		
Exposed wiring that creates an electrocution or fire ignition hazard. Identify and secure wiring, and place it in conduit or bury it.		
Site burning, which can cause possible obscuration.		
Construction work taking place outside of designated work areas and out of phase.		


APPENDIX E. SAMPLE OPERATIONAL EFFECTS TABLE

E.1 **Project Description.**

Runway 15-33 is currently 7820 feet long, with a 500 foot stopway on the north end. This project will remove the stopway and extend the runway 1000 feet to the north and 500 feet to the south. Finally, the existing portion of the runway will be repaved. The runway 33 glide slope will be relocated. The new runway 33 localizer has already been installed by FAA Technical Operations and only needs to be switched on. Runway 15 is currently served only by a localizer, which will remain in operation as it will be beyond the future RSA. Appropriate NOTAMS will be issued throughout the project.

E.1.1 During Phase I, the runway 15 threshold will be displaced 1000 feet to keep construction equipment below the approach surface. The start of runway 15 takeoff and the departure end of runway 33 will also be moved 500 feet to protect workers from jet blast. Declared distances for runway 33 will be adjusted to provide the required RSA and applicable departure surface. Excavation near Taxiway G will require its ADG to be reduced from IV to III. See Figure E-1.

Figure E-1. Phase I Example

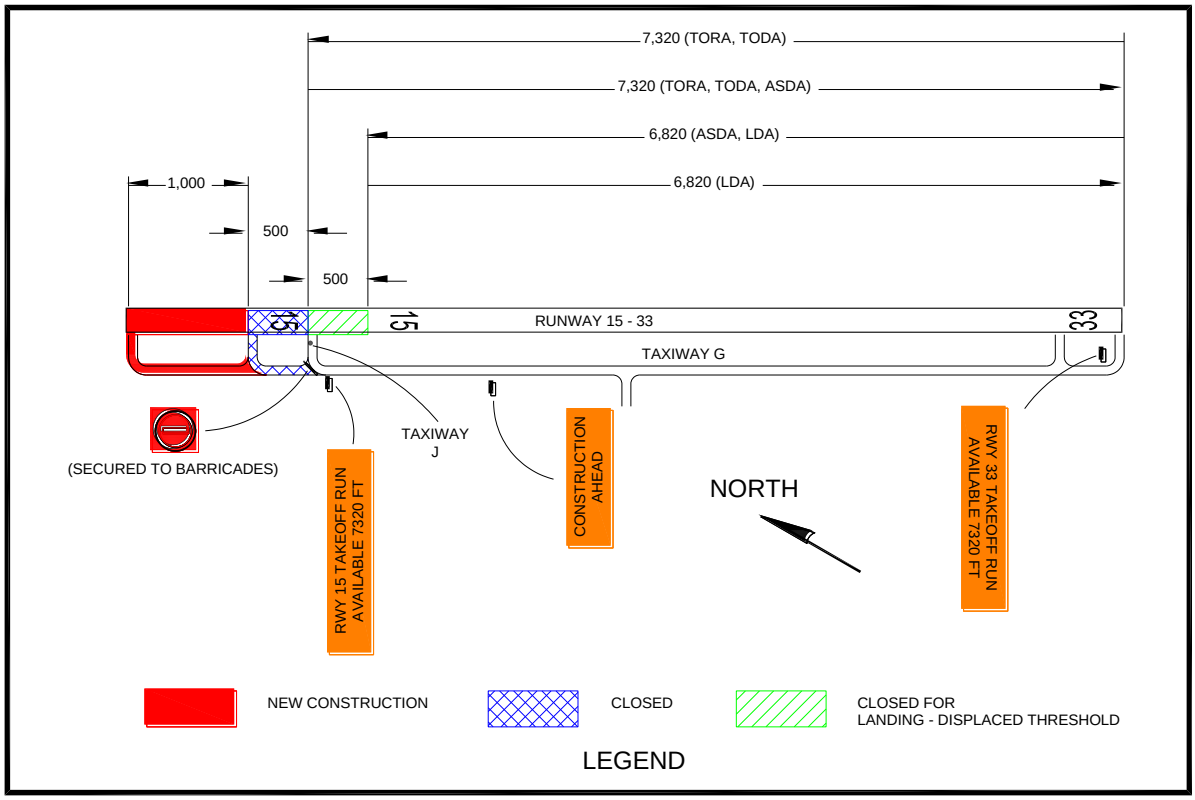


Note 1: Where hold signs are installed on both sides of a taxiway, install the TORA sign on the left side of the taxiway before the final turn to the runway intersection.

Note 2: Based on the declared distances for Runway 33 departures, the maximum equipment height in the construction area is 12.5 feet (500/40 = 12.5).

E.2 During Phase II, the runway 33 threshold will be displaced 1000 feet to keep construction equipment below the approach surface. The start of runway 33 takeoff and the departure end of runway 15 will also be moved 500 feet to protect workers from jet blast. Declared distances for runway 15 will be adjusted to provide the required RSA and applicable departure surface. See Figure E-2.

Figure E-2. Phase II Example

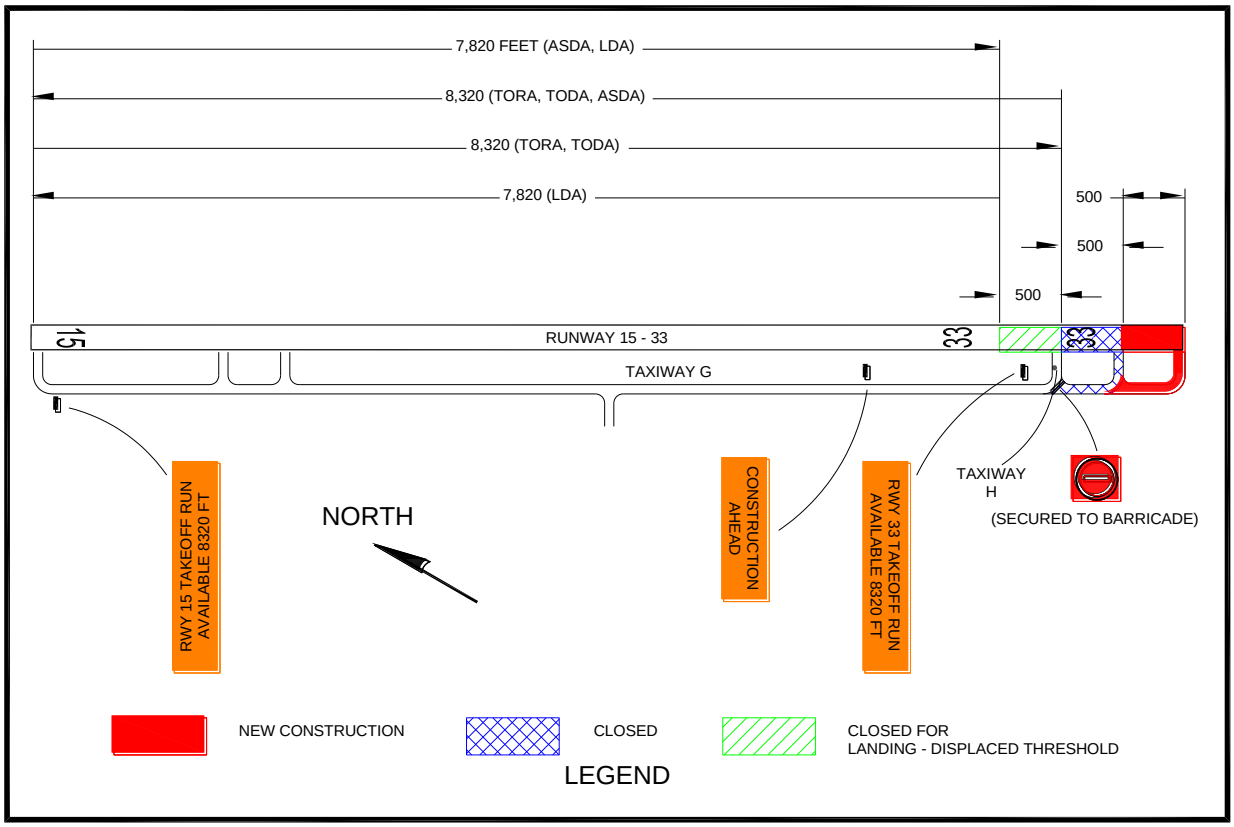

Note 1: Where hold signs are installed on both sides of a taxiway, install the TORA sign on the left side of the taxiway before the final turn to the runway intersection.

Note 2: Based on the declared distances for Runway 15 departures, the maximum equipment height in the construction area is 12.5 feet (500/40 = 12.5).

E.3 During Phase III, the existing portion of the runway will be repaved with Hot Mix Asphalt (HMA) and the runway 33 glide slope will be relocated. Construction will be accomplished between the hours of 8:00 pm and 5:00 am, during which the runway will be closed to operations.

Figure E-3. Phase III Example

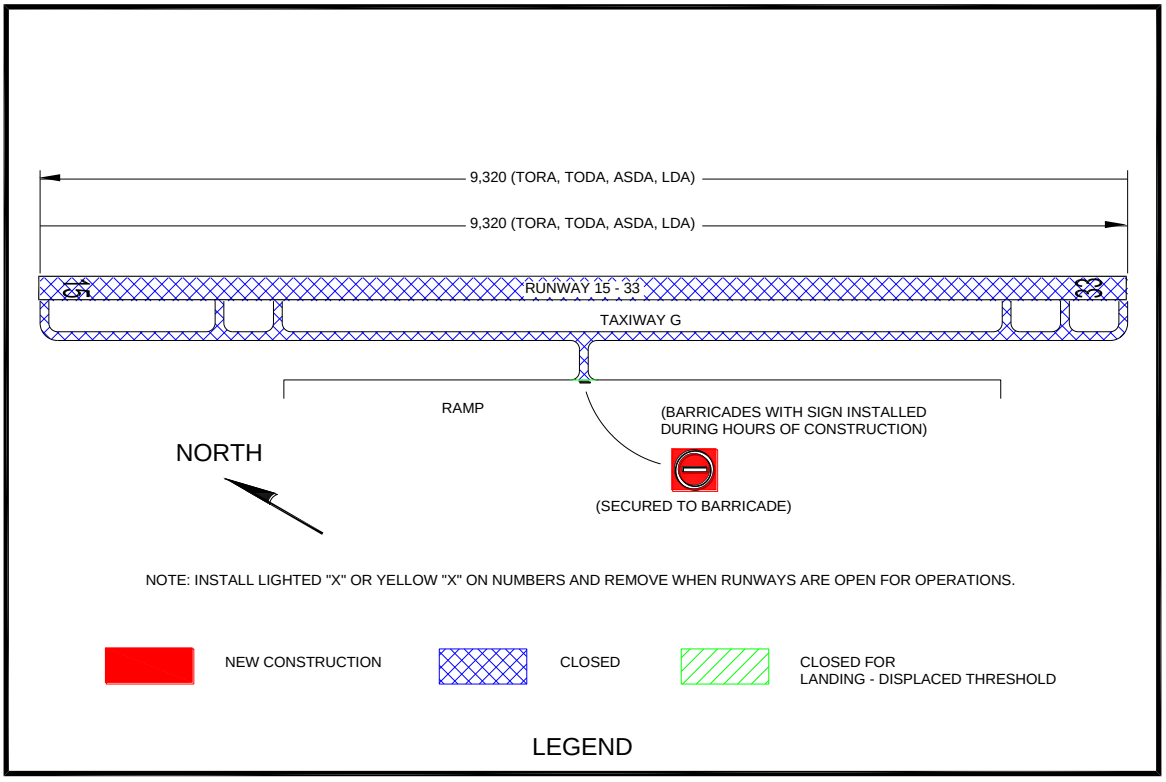


Table E-1. Operational Effects Table

Project	Runway 15-33 Extension and Repaving			
Phase	**Normal (Existing)**	**Phase I: Extend Runway 15 End**	**Phase II: Extend Runway 33 End**	**Phase III: Repave Runway**
Scope of Work	N/A	Extend Runway 15-33 1,000 ft on north end with Hot Mix Asphaltic Concrete (HMA).	Extend Runway 15-33 500 ft on south end with Hot Mix Asphaltic Concrete (HMA).	Repave existing runway with HMA Relocate Runway 33 Glide Slope
Effects of Construction Operations	N/A	Existing North 500 ft closed	Existing South 500 ft closed	Runway closed between 8:00 pm and 5:00 am Edge lighting out of service
Construction Phase	N/A	Phase I (Anticipated)	Phase II (Anticipated)	Phase III (Anticipated)
Runway 15 Average Aircraft Operations	Carrier: 52 /day GA: 26 /day Military: 11 /day	Carrier: 40 /day GA: 26 /day Military: 0 /day	Carrier: 45 /day GA: 26 /day Military: 5 /day	Carrier: 45 / day GA: 20 / day Military: 0 /day
Runway 33 Average Aircraft Operations	Carrier: 40 /day GA: 18 /day Military: 10 /day	Carrier: 30 /day GA: 18 /day Military: 0 /day	Carrier: 25 /day GA: 18 /day Military: 5 /day	Carrier: 20 /day GA: 5 /day Military: 0 /day
Runway 15-33 Aircraft Category	C-IV	C-IV	C-IV	C-IV
Runway 15 Approach Visibility Minimums	1 mile	1 mile	1 mile	1 mile
Runway 33 Approach Visibility Minimums	¾ mile	¾ mile	¾ mile	1 mile

Note: Proper coordination with Flight Procedures group is necessary to maintain instrument approach procedures during construction.

Project		Runway 15-33 Extension and Repaving			
Phase		Normal (Existing)	Phase I: Extend Runway 15 End	Phase II: Extend Runway 33 End	Phase III: Repave Runway
Runway 15 Declared Distances	TORA	7,820	7,320	8,320	9,320
	TODA	7,820	7,320	8,320	9,320
	ASDA	7,820	7,320	7,820	9,320
	LDA	7,820	6,820	7,820	9,320
Runway 33 Declared Distances	TORA	7,820	7,320	8,320	9,320
	TODA	7,820	7,320	8,320	9,320
	ASDA	8,320	6,820	8,320	9,320
	LDA	7,820	6,820	7,820	9,320
Runway 15 Approach Procedures		LOC only	LOC only	LOC only	LOC only
		RNAV	RNAV	RNAV	RNAV
		VOR	VOR	VOR	VOR
Runway 33 Approach Procedures		ILS	ILS	ILS	LOC only
		RNAV	RNAV	RNAV	RNAV
		VOR	VOR	VOR	VOR
Runway 15 NAVAIDs		LOC	LOC	LOC	LOC
Runway 33 NAVAIDs		ILS, MALSR	ILS, MALSR	ILS, MALSR	LOC, MALSR
Taxiway G ADG		IV	III	IV	IV
Taxiway G TDG		4	4	4	4
ATCT (hours open)		24 hours	24 hours	24 hours	0500 - 2000
ARFF Index		D	D	D	D

Project	Runway 15-33 Extension and Repaving			
Phase	**Normal (Existing)**	**Phase I: Extend Runway 15 End**	**Phase II: Extend Runway 33 End**	**Phase III: Repave Runway**
Special Conditions	Air National Guard (ANG) military operations	All military aircraft relocated to alternate ANG Base	Some large military aircraft relocated to alternate ANG Base	All military aircraft relocated to alternate ANG Base
Information for NOTAMs		Refer above for applicable declared distances. Taxiway G limited to 118 ft wingspan	Refer above for applicable declared distances.	Refer above for applicable declared distances. Airport closed 2000 – 0500. Runway 15 glide slope OTS.

Note: This table is one example. It may be advantageous to develop a separate table for each project phase and/or to address the operational status of the associated NAVAIDs per construction phase.

Complete the following chart for each phase to determine the area that must be protected along the runway and taxiway edges:

Table E-2. Runway and Taxiway Edge Protection

Runway/Taxiway	Aircraft Approach Category* A, B, C, or D	Airplane Design Group* I, II, III, or IV	Safety Area Width in Feet Divided by 2*

*See AC 150/5300-13 to complete the chart for a specific runway/taxiway.

Complete the following chart for each phase to determine the area that must be protected before the runway threshold:

Table E-3. Protection Prior to Runway Threshold

Runway End Number	Airplane Design Group* I, II, III, or IV	Aircraft Approach Category* A, B, C, or D	Minimum Safety Area Prior to the Threshold*	Minimum Distance to Threshold Based on Required Approach Slope*	
			ft	ft	: 1
			ft	ft	: 1
			ft	ft	: 1
			ft	ft	: 1

*See AC 150/5300-13 to complete the chart for a specific runway.


Page Intentionally Blank

APPENDIX F. ORANGE CONSTRUCTION SIGNS

Figure F-1. Approved Sign Legends




Figure F-2. Orange Construction Sign Example 1

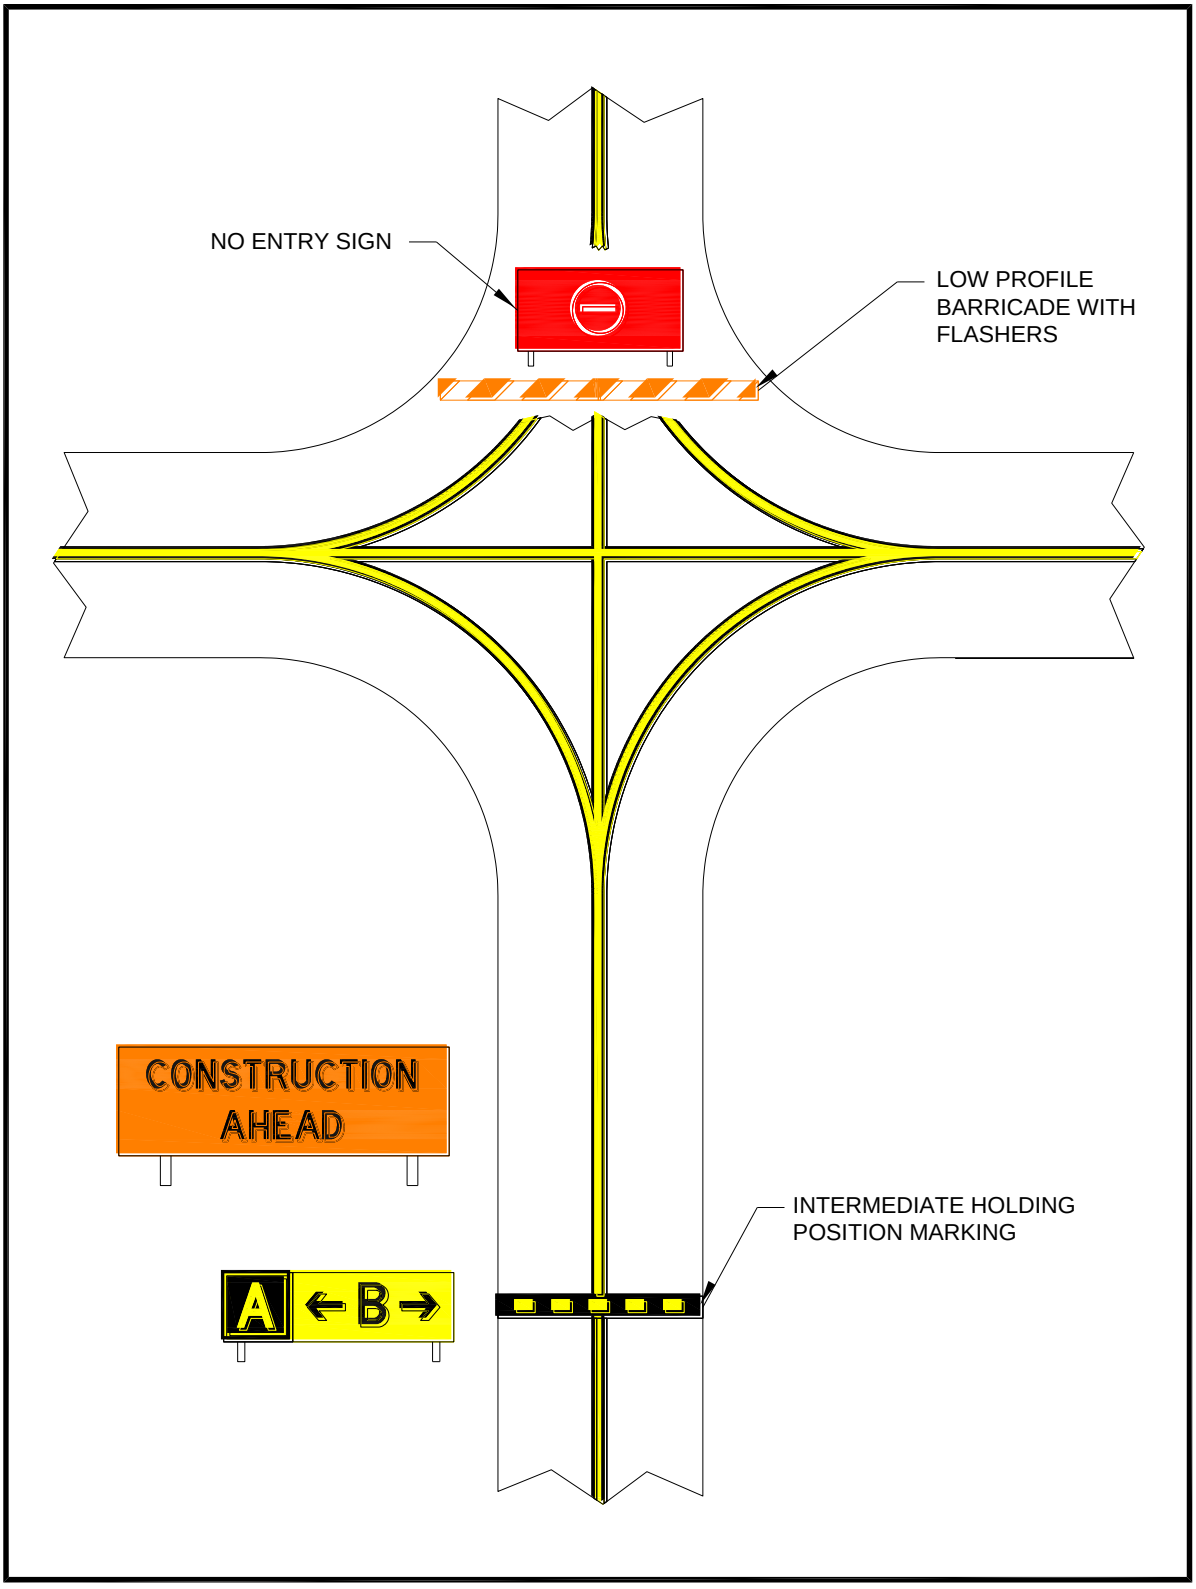

Note: For proper placement of signs, refer to EB 93.

Figure F-3. Orange Construction Sign Example 2

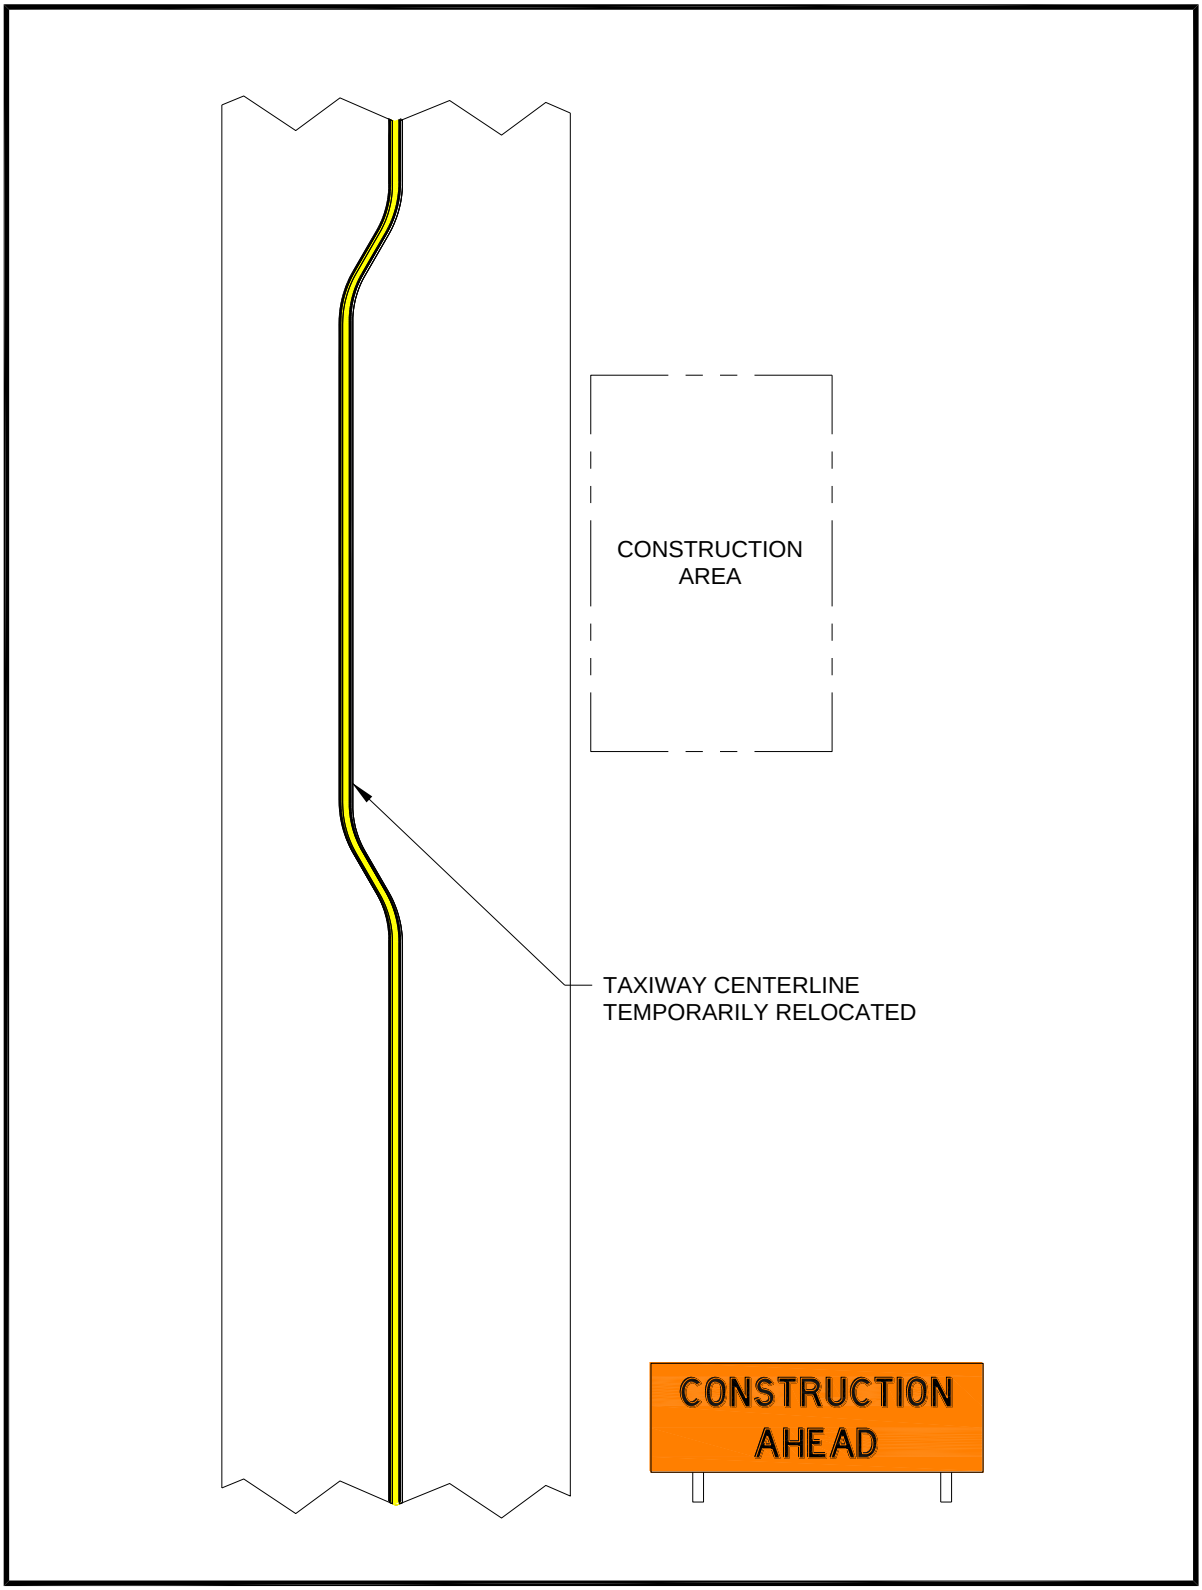

Note: For proper placement of signs, refer to EB 93.

Page Intentionally Blank

Advisory Circular Feedback

If you find an error in this AC, have recommendations for improving it, or have suggestions for new items/subjects to be added, you may let us know by (1) mailing this form to Manager, Airport Engineering Division, Federal Aviation Administration ATTN: AAS-100, 800 Independence Avenue SW, Washington DC 20591 or (2) faxing it to the attention of the Office of Airport Safety and Standards at (202) 267-5383.

Subject: AC 150/5370-2G Date: _____

Please check all appropriate line items:

☐ An error (procedural or typographical) has been noted in paragraph _____ on page _____.

☐ Recommend paragraph _____ on page _____ be changed as follows:

_____
_____
_____

☐ In a future change to this AC, please cover the following subject:
(Briefly describe what you want added.)

_____
_____
_____

☐ Other comments:

_____
_____
_____

☐ I would like to discuss the above. Please contact me at (phone number, email address).

_____

Submitted by: _____ Date: _____

Page Intentionally Blank

APPENDIX C

FAA CONTRACT PROVISIONS

ACCESS TO RECORDS AND REPORTS

The Contractor must maintain an acceptable cost accounting system. The Contractor agrees to provide the Owner, the Federal Aviation Administration and the Comptroller General of the United States or any of their duly authorized representatives access to any books, documents, papers and records of the Contractor which are directly pertinent to the specific contract for the purpose of making audit, examination, excerpts and transcriptions. The Contractor agrees to maintain all books, records and reports required under this contract for a period of not less than three years after final payment is made and all pending matters are closed.

AFFIRMATIVE ACTION REQUIREMENT

NOTICE OF REQUIREMENT FOR AFFIRMATIVE ACTION to ENSURE EQUAL EMPLOYMENT OPPORTUNITY

1. The Offeror's or Bidder's attention is called to the "Equal Opportunity Clause" and the "Standard Federal Equal Employment Opportunity Construction Contract Specifications" set forth herein.

2. The goals and timetables for minority and female participation, expressed in percentage terms for the Contractor's aggregate workforce in each trade on all construction work in the covered area, are as follows:

Timetables

Goals for minority participation for each trade: 19.7%

Goals for female participation in each trade: 6.9%

These goals are applicable to all of the Contractor's construction work (whether or not it is Federal or federally assisted) performed in the covered area. If the Contractor performs construction work in a geographical area located outside of the covered area, it shall apply the goals established for such geographical area where the work is actually performed. With regard to this second area, the Contractor also is subject to the goals for both its federally involved and non-federally involved construction.

The Contractor's compliance with the Executive Order and the regulations in 41 CFR Part 60-4 shall be based on its implementation of the Equal Opportunity Clause, specific affirmative action obligations required by the specifications set forth in 41 CFR 60-4.3(a) and its efforts to meet the goals. The hours of minority and female employment and training must be substantially uniform throughout the length of the contract, and in each trade, and the Contractor shall make a good faith effort to employ minorities and women evenly on each of its projects. The transfer of minority or female employees or trainees from Contractor to Contractor or from project to project for the sole purpose of meeting the Contractor's goals shall be a violation of the contract, the Executive Order and the regulations in 41 CFR Part 60-4. Compliance with the goals will be measured against the total work hours performed.

3. The Contractor shall provide written notification to the Director of the Office of Federal Contract Compliance Programs (OFCCP) within 10 working days of award of any construction subcontract in excess of $10,000 at any tier for construction work under the contract resulting from this solicitation. The notification shall list the name, address, and telephone number of the subcontractor; employer identification number of the subcontractor; estimated dollar amount of the subcontract; estimated starting and completion dates of the subcontract; and the geographical area in which the subcontract is to be performed.

4. As used in this notice and in the contract resulting from this solicitation, the "covered area" **Santa Barbara County, California**,

BREACH OF CONTRACT TERMS

Any violation or breach of terms of this contract on the part of the Contractor or its subcontractors may result in the suspension or termination of this contract or such other action that may be necessary to enforce the rights of the parties of this agreement.

Owner will provide Contractor written notice that describes the nature of the breach and corrective actions the Contractor must undertake in order to avoid termination of the contract. Owner reserves the right to withhold payments to Contractor until such time the Contractor corrects the breach or the Owner elects to terminate the contract. The Owner's notice will identify a specific date by which the Contractor must correct the breach. Owner may proceed with termination of the contract if the Contractor fails to correct the breach by the deadline indicated in the Owner's notice.

The duties and obligations imposed by the Contract Documents and the rights and remedies available thereunder are in addition to, and not a limitation of, any duties, obligations, rights and remedies otherwise imposed or available by law.

BUY AMERICAN PREFERENCE

The Contractor agrees to comply with 49 USC § 50101, which provides that Federal funds may not be obligated unless all steel and manufactured goods used in AIP funded projects are produced in the United States, unless the Federal Aviation Administration has issued a waiver for the product; the product is listed as an Excepted Article, Material Or Supply in Federal Acquisition Regulation subpart 25.108; or is included in the FAA Nationwide Buy American Waivers Issued list.

A bidder or offeror must complete and submit the Buy America certification included herein with their bid or offer. The Owner will reject as nonresponsive any bid or offer that does not include a completed Certificate of Buy American Compliance.

CERTIFICATE OF BUY AMERICAN COMPLIANCE FOR TOTAL FACILITY

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with its proposal. The bidder or offeror must indicate how it intends to comply with 49 USC § 50101 by selecting one of the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (i.e. not both) by inserting a checkmark (✓) or the letter "X".

☐ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101 by:

a) Only installing steel and manufactured products produced in the United States; or
b) Installing manufactured products for which the Federal Aviation Administration (FAA) has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing; or
c) Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

- To provide to the Owner evidence that documents the source and origin of the steel and manufactured product.
- To faithfully comply with providing U.S. domestic products.
- To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

☐ The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for either a Type 3 or Type 4 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:

a) To the submit to the Owner within 15 calendar days of the bid opening, a formal waiver request and required documentation that supports the type of waiver being requested.
b) That failure to submit the required documentation within the specified timeframe is cause for a non-responsive determination that may result in rejection of the proposal.

c) To faithfully comply with providing U.S. domestic products at or above the approved U.S. domestic content percentage as approved by the FAA.
d) To furnish U.S. domestic product for any waiver request that the FAA rejects.
e) To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

Required Documentation

Type 3 Waiver – The cost of components and subcomponents produced in the United States is more than 60 percent of the cost of all components and subcomponents of the "facility". The required documentation for a Type 3 waiver is:

a) Listing of all manufactured products that are not comprised of 100 percent U.S. domestic content (excludes products listed on the FAA Nationwide Buy American Waivers Issued listing and products excluded by Federal Acquisition Regulation Subpart 25.108; products of unknown origin must be considered as non-domestic products in their entirety).
b) Cost of non-domestic components and subcomponents, excluding labor costs associated with final assembly and installation at project location.
c) Percentage of non-domestic component and subcomponent cost as compared to total "facility" component and subcomponent costs, excluding labor costs associated with final assembly and installation at project location.

Type 4 Waiver – Total cost of project using U.S. domestic source product exceeds the total project cost using non-domestic product by 25 percent. The required documentation for a Type 4 of waiver is:

a) Detailed cost information for total project using U.S. domestic product
b) Detailed cost information for total project using non-domestic product

False Statements: Per 49 USC § 47126, this certification concerns a matter within the jurisdiction of the Federal Aviation Administration and the making of a false, fictitious or fraudulent certification may render the maker subject to prosecution under Title 18, United States Code.

Date	Signature
Company Name	Title

Certificate of Buy American Compliance for Manufactured Products

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with their proposal. The bidder or offeror must indicate how they intend to comply with 49 USC § 50101 by selecting one on the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (not both) by inserting a checkmark (✓) or the letter "X".

☐ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101 by:

a) Only installing steel and manufactured products produced in the United States;
b) Installing manufactured products for which the Federal Aviation Administration (FAA) has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing; or
c) Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

1. To provide to the Owner evidence that documents the source and origin of the steel and manufactured product.
2. To faithfully comply with providing U.S. domestic product.
3. To furnish U.S. domestic product for any waiver request that the FAA rejects
4. To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

☐ The bidder or offeror hereby certifies it cannot comply with the 100 percent Buy American Preferences of 49 USC § 50101(a) but may qualify for either a Type 3 or Type 4 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:

1. To the submit to the Owner within 15 calendar days of the bid opening, a formal waiver request and required documentation that supports the type of waiver being requested.
2. That failure to submit the required documentation within the specified timeframe is cause for a non-responsive determination may result in rejection of the proposal.
3. To faithfully comply with providing U.S. domestic products at or above the approved U.S. domestic content percentage as approved by the FAA.
4. To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

Required Documentation

Type 3 Waiver – The cost of the item components and subcomponents produced in the United States is more that 60 percent of the cost of all components and subcomponents of the "item". The required documentation for a Type 3 waiver is:

a) Listing of all product components and subcomponents that are not comprised of 100 percent U.S. domestic content (Excludes products listed on the FAA Nationwide Buy American Waivers Issued listing and products excluded by Federal Acquisition

Regulation Subpart 25.108; products of unknown origin must be considered as non-domestic products in their entirety).

b) Cost of non-domestic components and subcomponents, excluding labor costs associated with final assembly at place of manufacture.
c) Percentage of non-domestic component and subcomponent cost as compared to total "item" component and subcomponent costs, excluding labor costs associated with final assembly at place of manufacture.

Type 4 Waiver – Total cost of project using U.S. domestic source product exceeds the total project cost using non-domestic product by 25 percent. The required documentation for a Type 4 of waiver is:

a) Detailed cost information for total project using U.S. domestic product
b) Detailed cost information for total project using non-domestic product

False Statements: Per 49 USC § 47126, this certification concerns a matter within the jurisdiction of the Federal Aviation Administration and the making of a false, fictitious or fraudulent certification may render the maker subject to prosecution under Title 18, United States Code.

Date	Signature
Company Name	Title

CIVIL RIGHTS - GENERAL

GENERAL CIVIL RIGHTS PROVISIONS

The Contractor agrees to comply with pertinent statutes, Executive Orders and such rules as are promulgated to ensure that no person shall, on the grounds of race, creed, color, national origin, sex, age, or disability be excluded from participating in any activity conducted with or benefiting from Federal assistance.

This provision binds the Contractor and subcontractors from the bid solicitation period through the completion of the contract. This provision is in addition to that required by Title VI of the Civil Rights Act of 1964.

GENERAL CIVIL RIGHTS PROVISIONS

The (tenant/concessionaire/lessee) agrees to comply with pertinent statutes, Executive Orders and such rules as are promulgated to ensure that no person shall, on the grounds of race, creed, color, national origin, sex, age, or disability be excluded from participating in any activity conducted with or benefiting from Federal assistance. If the (tenant/concessionaire/lessee) transfers its obligation to another, the transferee is obligated in the same manner as the (tenant/concessionaire/lessor).

This provision obligates the (tenant/concessionaire/lessee) for the period during which the property is owned, used or possessed by the (tenant/concessionaire/lessee) and the airport remains obligated to the Federal Aviation Administration. This provision is in addition to that required by Title VI of the Civil Rights Act of 1964.

CIVIL RIGHTS – TITLE VI ASSURANCE

Title VI Solicitation Notice:

The **County**, in accordance with the provisions of Title VI of the Civil Rights Act of 1964 (78 Stat. 252, 42 USC §§ 2000d to 2000d-4) and the Regulations, hereby notifies all bidders or offerors that it will affirmatively ensure that any contract entered into pursuant to this advertisement, [select disadvantaged business enterprises or airport concession disadvantaged business enterprises] will be afforded full and fair opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award.

Compliance with Nondiscrimination Requirements:

During the performance of this contract, the Contractor, for itself, its assignees, and successors in interest (hereinafter referred to as the "Contractor"), agrees as follows:

1. **Compliance with Regulations:** The Contractor (hereinafter includes consultants) will comply with the Title VI List of Pertinent Nondiscrimination Acts and Authorities, as they may be amended from time to time, which are herein incorporated by reference and made a part of this contract.
2. **Nondiscrimination:** The Contractor, with regard to the work performed by it during the contract, will not discriminate on the grounds of race, color, or national origin in the selection and retention of subcontractors, including procurements of materials and leases of equipment. The Contractor will not participate directly or indirectly in the discrimination prohibited by the Nondiscrimination Acts and Authorities, including employment practices when the contract covers any activity, project, or program set forth in Appendix B of 49 CFR part 21.
3. **Solicitations for Subcontracts, including Procurements of Materials and Equipment:** In all solicitations, either by competitive bidding or negotiation made by the Contractor for work to be performed under a subcontract, including procurements of materials, or leases of equipment, each potential subcontractor or supplier will be notified by the Contractor of the contractor's obligations under this contract and the Nondiscrimination Acts and Authorities on the grounds of race, color, or national origin.
4. **Information and Reports:** The Contractor will provide all information and reports required by the Acts, the Regulations, and directives issued pursuant thereto and will permit access to its books, records, accounts, other sources of information, and its facilities as may be determined by the sponsor or the Federal Aviation Administration to be pertinent to ascertain compliance with such Nondiscrimination Acts and Authorities and instructions. Where any information required of a contractor is in the exclusive possession of another who fails or refuses to furnish the information, the Contractor will so certify to the sponsor or the Federal Aviation Administration, as appropriate, and will set forth what efforts it has made to obtain the information.
5. **Sanctions for Noncompliance:** In the event of a Contractor's noncompliance with the non-discrimination provisions of this contract, the sponsor will impose such contract sanctions as it or the Federal Aviation Administration may determine to be appropriate, including, but not limited to:
    a. Withholding payments to the Contractor under the contract until the Contractor complies; and/or
    b. Cancelling, terminating, or suspending a contract, in whole or in part.

6. **Incorporation of Provisions:** The Contractor will include the provisions of paragraphs one through six in every subcontract, including procurements of materials and leases of equipment, unless exempt by the Acts, the Regulations, and directives issued pursuant thereto. The Contractor will take action with respect to any subcontract or procurement as the sponsor or the Federal Aviation Administration may direct as a means of enforcing such provisions including sanctions for noncompliance. Provided, that if the Contractor becomes involved in, or is threatened with litigation by a subcontractor, or supplier because of such direction, the Contractor may request the sponsor to enter into any litigation to protect the interests of the sponsor. In addition, the Contractor may request the United States to enter into the litigation to protect the interests of the United States.

•

CLEAN AIR AND WATER POLLUTION CONTROL

Contractor agrees to comply with all applicable standards, orders, and regulations issued pursuant to the Clean Air Act (42 USC § 740-7671q) and the Federal Water Pollution Control Act as amended (33 USC § 1251-1387). The Contractor agrees to report any violation to the Owner immediately upon discovery. The Owner assumes responsibility for notifying the Environmental Protection Agency (EPA) and the Federal Aviation Administration.

Contractor must include this requirement in all subcontracts that exceeds $150,000.

CONTRACT WORKHOURS AND SAFETY STANDARDS ACT REQUIREMENTS

1. Overtime Requirements.

No contractor or subcontractor contracting for any part of the contract work which may require or involve the employment of laborers or mechanics shall require or permit any such laborer or mechanic, including watchmen and guards, in any workweek in which he or she is employed on such work to work in excess of forty hours in such workweek unless such laborer or mechanic receives compensation at a rate not less than one and one-half times the basic rate of pay for all hours worked in excess of forty hours in such workweek.

2. Violation; Liability for Unpaid Wages; Liquidated Damages.

In the event of any violation of the clause set forth in paragraph (1) of this clause, the Contractor and any subcontractor responsible therefor shall be liable for the unpaid wages. In addition, such contractor and subcontractor shall be liable to the United States (in the case of work done under contract for the District of Columbia or a territory, to such District or to such territory), for liquidated damages. Such liquidated damages shall be computed with respect to each individual laborer or mechanic, including watchmen and guards, employed in violation of the clause set forth in paragraph (1) of this clause, in the sum of $10 for each calendar day on which such individual was required or permitted to work in excess of the standard workweek of forty hours without payment of the overtime wages required by the clause set forth in paragraph (1) of this clause.

3. Withholding for Unpaid Wages and Liquidated Damages.

The Federal Aviation Administration (FAA) or the Owner shall upon its own action or upon written request of an authorized representative of the Department of Labor withhold or cause to be withheld, from any moneys payable on account of work performed by the contractor or subcontractor under any such contract or any other Federal contract with the same prime contractor, or any other federally assisted contract subject to the Contract Work Hours and Safety Standards Act, which is held by the same prime contractor, such sums as may be determined to be necessary to satisfy any liabilities of such contractor or subcontractor for unpaid wages and liquidated damages as provided in the clause set forth in paragraph (2) of this clause.

4. Subcontractors.

The Contractor or subcontractor shall insert in any subcontracts the clauses set forth in paragraphs (1) through (4) and also a clause requiring the subcontractor to include these clauses in any lower tier subcontracts. The prime contractor shall be responsible for compliance by any subcontractor or lower tier subcontractor with the clauses set forth in paragraphs (1) through (4) of this clause.

COPELAND "ANTI-KICKBACK" ACT

Contractor must comply with the requirements of the Copeland "Anti-Kickback" Act (18 USC 874 and 40 USC 3145), as supplemented by Department of Labor regulation 29 CFR part 3. Contractor and subcontractors are prohibited from inducing, by any means, any person employed on the project to give up any part of the compensation to which the employee is entitled. The Contractor and each Subcontractor must submit to the Owner, a weekly statement on the wages paid to each employee performing on covered work during the prior week. Owner must report any violations of the Act to the Federal Aviation Administration.

DAVIS-BACON REQUIREMENTS

1. Minimum Wages.

(i) All laborers and mechanics employed or working upon the site of the work will be paid unconditionally and not less often than once a week, and without subsequent deduction or rebate on any account (except such payroll deductions as are permitted by the Secretary of Labor under the Copeland Act (29 CFR Part 3)), the full amount of wages and bona fide fringe benefits (or cash equivalent thereof) due at time of payment computed at rates not less than those contained in the wage determination of the Secretary of Labor which is attached hereto and made a part hereof, regardless of any contractual relationship which may be alleged to exist between the Contractor and such laborers and mechanics.

Contributions made or costs reasonably anticipated for bona fide fringe benefits under section 1(b)(2) of the Davis-Bacon Act on behalf of laborers or mechanics are considered wages paid to such laborers or mechanics, subject to the provisions of paragraph (1)(iv) of this section; also, regular contributions made or costs incurred for more than a weekly period (but not less often than quarterly) under plans, funds, or programs which cover the particular weekly period, are deemed to be constructively made or incurred during such weekly period. Such laborers and mechanics shall be paid the appropriate wage rate and fringe benefits on the wage determination for the classification of work actually performed, without regard to skill, except as provided in 29 CFR Part 5.5(a)(4). Laborers or mechanics performing work in more than one classification may be compensated at the rate specified for each classification for the time actually worked therein: *Provided* that the employer's payroll records accurately set forth the time spent in each classification in which work is performed. The wage determination (including any additional classification and wage rates conformed under (1)(ii) of this section) and the Davis-Bacon poster (WH-1321) shall be posted at all times by the Contractor and its subcontractors at the site of the work in a prominent and accessible place where it can easily be seen by the workers.

(ii)(A) The contracting officer shall require that any class of laborers or mechanics, including helpers, which is not listed in the wage determination and which is to be employed under the contract shall be classified in conformance with the wage determination. The contracting officer shall approve an additional classification and wage rate and fringe benefits therefore only when the following criteria have been met:

(1) The work to be performed by the classification requested is not performed by a classification in the wage determination;

(2) The classification is utilized in the area by the construction industry; and

(3) The proposed wage rate, including any bona fide fringe benefits, bears a reasonable relationship to the wage rates contained in the wage determination.

(B) If the Contractor and the laborers and mechanics to be employed in the classification (if known), or their representatives, and the contracting officer agree on the classification and wage rate (including the amount designated for fringe benefits where appropriate), a report of the action taken shall be sent by the contracting officer to the Administrator of the Wage and Hour Division, Employment Standards Administration, U.S. Department of Labor, Washington, DC 20210. The Administrator, or an authorized representative, will approve, modify, or disapprove every additional classification action

within 30 days of receipt and so advise the contracting officer or will notify the contracting officer within the 30-day period that additional time is necessary.

(C) In the event the Contractor, the laborers, or mechanics to be employed in the classification, or their representatives, and the contracting officer do not agree on the proposed classification and wage rate (including the amount designated for fringe benefits where appropriate), the contracting officer shall refer the questions, including the views of all interested parties and the recommendation of the contracting officer, to the Administrator for determination. The Administrator, or an authorized representative, will issue a determination within 30 days of receipt and so advise the contracting officer or will notify the contracting officer within the 30-day period that additional time is necessary.

(D) The wage rate (including fringe benefits where appropriate) determined pursuant to subparagraphs (1)(ii) (B) or (C) of this paragraph, shall be paid to all workers performing work in the classification under this contract from the first day on which work is performed in the classification.

(iii) Whenever the minimum wage rate prescribed in the contract for a class of laborers or mechanics includes a fringe benefit which is not expressed as an hourly rate, the contractor shall either pay the benefit as stated in the wage determination or shall pay another bona fide fringe benefit or an hourly cash equivalent thereof.

(iv) If the Contractor does not make payments to a trustee or other third person, the Contractor may consider as part of the wages of any laborer or mechanic the amount of any costs reasonably anticipated in providing bona fide fringe benefits under a plan or program: *Provided* that the Secretary of Labor has found, upon the written request of the Contractor, that the applicable standards of the Davis-Bacon Act have been met. The Secretary of Labor may require the Contractor to set aside in a separate account assets for the meeting of obligations under the plan or program.

2. Withholding.

The Federal Aviation Administration or the sponsor shall upon its own action or upon written request of an authorized representative of the Department of Labor withhold or cause to be withheld from the Contractor under this contract or any other Federal contract with the same prime contractor, or any other federally-assisted contract subject to Davis-Bacon prevailing wage requirements, which is held by the same prime contractor, so much of the accrued payments or advances as may be considered necessary to pay laborers and mechanics, including apprentices, trainees, and helpers, employed by the Contractor or any subcontractor the full amount of wages required by the contract. In the event of failure to pay any laborer or mechanic, including any apprentice, trainee, or helper, employed or working on the site of work, all or part of the wages required by the contract, the Federal Aviation Administration may, after written notice to the Contractor, Sponsor, Applicant, or Owner, take such action as may be necessary to cause the suspension of any further payment, advance, or guarantee of funds until such violations have ceased.

3. Payrolls and Basic Records.

(i) Payrolls and basic records relating thereto shall be maintained by the Contractor during the course of the work and preserved for a period of three years thereafter for all laborers and mechanics working at the site of the work. Such records shall contain the name, address, and social security number of each such worker; his or her correct classification; hourly rates of wages paid (including rates of contributions or costs anticipated for bona fide fringe benefits or cash equivalents thereof of the types

described in 1(b)(2)(B) of the Davis-Bacon Act); daily and weekly number of hours worked; deductions made; and actual wages paid. Whenever the Secretary of Labor has found under 29 CFR 5.5(a)(1)(iv) that the wages of any laborer or mechanic include the amount of any costs reasonably anticipated in providing benefits under a plan or program described in section 1(b)(2)(B) of the Davis-Bacon Act, the Contractor shall maintain records that show that the commitment to provide such benefits is enforceable, that the plan or program is financially responsible, and that the plan or program has been communicated in writing to the laborers or mechanics affected, and that show the costs anticipated or the actual costs incurred in providing such benefits. Contractors employing apprentices or trainees under approved programs shall maintain written evidence of the registration of apprenticeship programs and certification of trainee programs, the registration of the apprentices and trainees, and the ratios and wage rates prescribed in the applicable programs.

(ii)(A) The Contractor shall submit weekly for each week in which any contract work is performed a copy of all payrolls to the Federal Aviation Administration if the agency is a party to the contract, but if the agency is not such a party, the Contractor will submit the payrolls to the applicant, Sponsor, or Owner, as the case may be, for transmission to the Federal Aviation Administration. The payrolls submitted shall set out accurately and completely all of the information required to be maintained under 29 CFR 5.5(a)(3)(i), except that full social security numbers and home addresses shall not be included on weekly transmittals. Instead the payrolls shall only need to include an individually identifying number for each employee (*e.g.* the last four digits of the employee's social security number). The required weekly payroll information may be submitted in any form desired. Optional Form WH–347 is available for this purpose from the Wage and Hour Division Web site at *www.dol.gov/whd/forms/wh347instr.htm* or its successor site. The prime contractor is responsible for the submission of copies of payrolls by all subcontractors. Contractors and subcontractors shall maintain the full social security number and current address of each covered worker and shall provide them upon request to the Federal Aviation Administration if the agency is a party to the contract, but if the agency is not such a party, the Contractor will submit them to the applicant, sponsor, or Owner, as the case may be, for transmission to the Federal Aviation Administration, the Contractor, or the Wage and Hour Division of the Department of Labor for purposes of an investigation or audit of compliance with prevailing wage requirements. It is not a violation of this section for a prime contractor to require a subcontractor to provide addresses and social security numbers to the prime contractor for its own records, without weekly submission to the sponsoring government agency (or the applicant, Sponsor, or Owner).

(B) Each payroll submitted shall be accompanied by a "Statement of Compliance," signed by the Contractor or subcontractor or his or her agent who pays or supervises the payment of the persons employed under the contract and shall certify the following:

(1) The payroll for the payroll period contains the information required to be provided under 29 CFR § 5.5(a)(3)(ii), the appropriate information is being maintained under 29 CFR § 5.5 (a)(3)(i), and that such information is correct and complete;

(2) Each laborer and mechanic (including each helper, apprentice, and trainee) employed on the contract during the payroll period has been paid the full weekly wages earned, without rebate, either directly or indirectly, and that no deductions have been made either directly or indirectly from the full wages earned, other than permissible deductions as set forth in Regulations 29 CFR Part 3;

(3) Each laborer or mechanic has been paid not less than the applicable wage rates and fringe benefits or cash equivalents for the classification of work performed, as specified in the applicable wage determination incorporated into the contract.

(C) The weekly submission of a properly executed certification set forth on the reverse side of Optional Form WH-347 shall satisfy the requirement for submission of the "Statement of Compliance" required by paragraph (3)(ii)(B) of this section.

(D) The falsification of any of the above certifications may subject the Contractor or subcontractor to civil or criminal prosecution under Section 1001 of Title 18 and Section 231 of Title 31 of the United States Code.

(iii) The Contractor or subcontractor shall make the records required under paragraph (3)(i) of this section available for inspection, copying, or transcription by authorized representatives of the sponsor, the Federal Aviation Administration, or the Department of Labor and shall permit such representatives to interview employees during working hours on the job. If the Contractor or subcontractor fails to submit the required records or to make them available, the Federal agency may, after written notice to the Contractor, Sponsor, applicant, or Owner, take such action as may be necessary to cause the suspension of any further payment, advance, or guarantee of funds. Furthermore, failure to submit the required records upon request or to make such records available may be grounds for debarment action pursuant to 29 CFR 5.12.

4. Apprentices and Trainees.

(i) Apprentices. Apprentices will be permitted to work at less than the predetermined rate for the work they performed when they are employed pursuant to and individually registered in a bona fide apprenticeship program registered with the U.S. Department of Labor, Employment and Training Administration, Bureau of Apprenticeship and Training, or with a State Apprenticeship Agency recognized by the Bureau, or if a person is employed in his or her first 90 days of probationary employment as an apprentice in such an apprenticeship program, who is not individually registered in the program, but who has been certified by the Bureau of Apprenticeship and Training or a State Apprenticeship Agency (where appropriate) to be eligible for probationary employment as an apprentice. The allowable ratio of apprentices to journeymen on the job site in any craft classification shall not be greater than the ratio permitted to the contractor as to the entire work force under the registered program. Any worker listed on a payroll at an apprentice wage rate, who is not registered or otherwise employed as stated above, shall be paid not less than the applicable wage rate on the wage determination for the classification of work actually performed. In addition, any apprentice performing work on the job site in excess of the ratio permitted under the registered program shall be paid not less than the applicable wage rate on the wage determination for the work actually performed. Where a contractor is performing construction on a project in a locality other than that in which its program is registered, the ratios and wage rates (expressed in percentages of the journeyman's hourly rate) specified in the Contractor's or subcontractor's registered program shall be observed. Every apprentice must be paid at not less than the rate specified in the registered program for the apprentice's level of progress, expressed as a percentage of the journeymen hourly rate specified in the applicable wage determination. Apprentices shall be paid fringe benefits in accordance with the provisions of the apprenticeship program. If the apprenticeship program does not specify fringe benefits, apprentices must be paid the full amount of fringe benefits listed on the wage determination for the applicable

classification. If the Administrator determines that a different practice prevails for the applicable apprentice classification, fringes shall be paid in accordance with that determination. In the event the Bureau of Apprenticeship and Training, or a State Apprenticeship Agency recognized by the Bureau, withdraws approval of an apprenticeship program, the Contractor will no longer be permitted to utilize apprentices at less than the applicable predetermined rate for the work performed until an acceptable program is approved.

(ii) Trainees. Except as provided in 29 CFR 5.16, trainees will not be permitted to work at less than the predetermined rate for the work performed unless they are employed pursuant to and individually registered in a program which has received prior approval, evidenced by formal certification by the U.S. Department of Labor, Employment and Training Administration. The ratio of trainees to journeymen on the job site shall not be greater than permitted under the plan approved by the Employment and Training Administration. Every trainee must be paid at not less than the rate specified in the approved program for the trainee's level of progress, expressed as a percentage of the journeyman hourly rate specified in the applicable wage determination. Trainees shall be paid fringe benefits in accordance with the provisions of the trainee program. If the trainee program does not mention fringe benefits, trainees shall be paid the full amount of fringe benefits listed on the wage determination unless the Administrator of the Wage and Hour Division determines that there is an apprenticeship program associated with the corresponding journeyman wage rate on the wage determination that provides for less than full fringe benefits for apprentices. Any employee listed on the payroll at a trainee rate that is not registered and participating in a training plan approved by the Employment and Training Administration shall be paid not less than the applicable wage rate on the wage determination for the classification of work actually performed. In addition, any trainee performing work on the job site in excess of the ratio permitted under the registered program shall be paid not less than the applicable wage rate on the wage determination for the work actually performed. In the event the Employment and Training Administration withdraws approval of a training program, the Contractor will no longer be permitted to utilize trainees at less than the applicable predetermined rate for the work performed until an acceptable program is approved.

(iii) Equal Employment Opportunity. The utilization of apprentices, trainees, and journeymen under this part shall be in conformity with the equal employment opportunity requirements of Executive Order 11246, as amended, and 29 CFR Part 30.

5. Compliance with Copeland Act Requirements.

The Contractor shall comply with the requirements of 29 CFR Part 3, which are incorporated by reference in this contract.

6. Subcontracts.

The Contractor or subcontractor shall insert in any subcontracts the clauses contained in 29 CFR Part 5.5(a)(1) through (10) and such other clauses as the Federal Aviation Administration may by appropriate instructions require, and also a clause requiring the subcontractors to include these clauses in any lower tier subcontracts. The prime contractor shall be responsible for the compliance by any subcontractor or lower tier subcontractor with all the contract clauses in 29 CFR Part 5.5.

7. Contract Termination: Debarment.

A breach of the contract clauses in paragraph 1 through 10 of this section may be grounds for termination of the contract, and for debarment as a contractor and a subcontractor as provided in 29 CFR 5.12.

8. Compliance with Davis-Bacon and Related Act Requirements.

All rulings and interpretations of the Davis-Bacon and Related Acts contained in 29 CFR Parts 1, 3, and 5 are herein incorporated by reference in this contract.

9. Disputes Concerning Labor Standards.

Disputes arising out of the labor standards provisions of this contract shall not be subject to the general disputes clause of this contract. Such disputes shall be resolved in accordance with the procedures of the Department of Labor set forth in 29 CFR Parts 5, 6, and 7. Disputes within the meaning of this clause include disputes between the Contractor (or any of its subcontractors) and the contracting agency, the U.S. Department of Labor, or the employees or their representatives.

10. Certification of Eligibility.

(i) By entering into this contract, the Contractor certifies that neither it (nor he or she) nor any person or firm who has an interest in the Contractor's firm is a person or firm ineligible to be awarded Government contracts by virtue of section 3(a) of the Davis-Bacon Act or 29 CFR 5.12(a)(1).

(ii) No part of this contract shall be subcontracted to any person or firm ineligible for award of a Government contract by virtue of section 3(a) of the Davis-Bacon Act or 29 CFR 5.12(a)(1).

(iii) The penalty for making false statements is prescribed in the U.S. Criminal Code, 18 USC 1001.

DEBARMENT AND SUSPENSION

CERTIFICATION OF OFFERER/BIDDER REGARDING DEBARMENT

By submitting a bid/proposal under this solicitation, the bidder or offeror certifies that neither it nor its principals are presently debarred or suspended by any Federal department or agency from participation in this transaction.

CERTIFICATION OF LOWER TIER CONTRACTORS REGARDING DEBARMENT

The successful bidder, by administering each lower tier subcontract that exceeds $25,000 as a "covered transaction", must verify each lower tier participant of a "covered transaction" under the project is not presently debarred or otherwise disqualified from participation in this federally assisted project. The successful bidder will accomplish this by:

1. Checking the System for Award Management at website: http://www.sam.gov.
2. Collecting a certification statement similar to the Certification of Offerer /Bidder Regarding Debarment, above.
3. Inserting a clause or condition in the covered transaction with the lower tier contract.

If the Federal Aviation Administration later determines that a lower tier participant failed to disclose to a higher tier participant that it was excluded or disqualified at the time it entered the covered transaction, the FAA may pursue any available remedies, including suspension and debarment of the non-compliant participant.

DISADVANTAGED BUSINESS ENTERPRISE

Information Submitted as a matter of bidder responsiveness:

The Owner's award of this contract is conditioned upon Bidder or Offeror satisfying the good faith effort requirements of 49 CFR §26.53.

As a condition of bid responsiveness, the Bidder or Offeror must submit the following information with its proposal on the forms provided herein:

1) The names and addresses of Disadvantaged Business Enterprise (DBE) firms that will participate in the contract;
2) A description of the work that each DBE firm will perform;
3) The dollar amount of the participation of each DBE firm listed under (1)
4) Written statement from Bidder or Offeror that attests their commitment to use the DBE firm(s) listed under (1) to meet the Owner's project goal; and
5) If Bidder or Offeror cannot meet the advertised project DBE goal, evidence of good faith efforts undertaken by the Bidder or Offeror as described in appendix A to 49 CFR part 26.

Information submitted as a matter of bidder responsibility:

The Owner's award of this contract is conditioned upon Bidder or Offeror satisfying the good faith effort requirements of 49 CFR §26.53.

The successful Bidder or Offeror must provide written confirmation of participation from each of the DBE firms the Bidder or Offeror lists in its commitment within five days after bid opening.

1) The names and addresses of Disadvantaged Business Enterprise (DBE) firms that will participate in the contract;
2) A description of the work that each DBE firm will perform;
3) The dollar amount of the participation of each DBE firm listed under (1)
4) Written statement from Bidder or Offeror that attests their commitment to use the DBE firm(s) listed under (1) to meet the Owner's project goal; and
5) If Bidder or Offeror cannot meet the advertised project DBE goal, evidence of good faith efforts undertaken by the Bidder or Offeror as described in appendix A to 49 CFR part 26.

The requirements of 49 CFR part 26 apply to this contract. It is the policy of the [Insert Name of Owner] to practice nondiscrimination based on race, color, sex, or national origin in the award or performance of this contract. The Owner encourages participation by all firms qualifying under this solicitation regardless of business size or ownership.

DISADVANTAGED BUSINESS ENTERPRISES

Contract Assurance (§ 26.13) –

The Contractor or subcontractor shall not discriminate on the basis of race, color, national origin, or sex in the performance of this contract. The Contractor shall carry out applicable requirements of 49 CFR part 26 in the award and administration of Department of Transportation-assisted contracts. Failure by the Contractor to carry out these requirements is a material breach of this contract, which may result in

the termination of this contract or such other remedy as the Owner deems appropriate, which may include, but is not limited to:

1) Withholding monthly progress payments;
2) Assessing sanctions;
3) Liquidated damages; and/or
4) Disqualifying the Contractor from future bidding as non-responsible.

Prompt Payment (§26.29) – The prime contractor agrees to pay each subcontractor under this prime contract for satisfactory performance of its contract no later than [specify number] days from the receipt of each payment the prime contractor receives from [Name of recipient]. The prime contractor agrees further to return retainage payments to each subcontractor within [specify the same number as above] days after the subcontractor's work is satisfactorily completed. Any delay or postponement of payment from the above referenced time frame may occur only for good cause following written approval of the [Name of Recipient]. This clause applies to both DBE and non-DBE subcontractors.

DISTRACTED DRIVING

TEXTING WHEN DRIVING

In accordance with Executive Order 13513, "Federal Leadership on Reducing Text Messaging While Driving", (10/1/2009) and DOT Order 3902.10, "Text Messaging While Driving", (12/30/2009), the Federal Aviation Administration encourages recipients of Federal grant funds to adopt and enforce safety policies that decrease crashes by distracted drivers, including policies to ban text messaging while driving when performing work related to a grant or subgrant.

In support of this initiative, the Owner encourages the Contractor to promote policies and initiatives for its employees and other work personnel that decrease crashes by distracted drivers, including policies that ban text messaging while driving motor vehicles while performing work activities associated with the project. The Contractor must include the substance of this clause in all sub-tier contracts exceeding $3,500 that involve driving a motor vehicle in performance of work activities associated with the project.

PROHIBITION ON CERTAIN TELECOMMUNICATIONS AND VIDEO SURVEILLANCE SERVICES OR EQUIPMENT

Contractor and Subcontractor agree to comply with mandatory standards and policies relating to use and procurement of certain telecommunications and video surveillance services or equipment in compliance with the National Defense Authorization Act [Public Law 115-232 § 889(f)(1)].

DRUG FREE WORKPLACE REQUIREMENTS

The Drug-Free Workplace Act of 1988 requires some Federal contractors and *all* Federal grantees to agree that they will provide drug-free workplaces as a condition of receiving a contract or grant from a Federal agency. The Act does ***not*** apply to contractors, subcontractors, or subgrantees, although the Federal grantees workplace may be where the contractors, subcontractors, or subgrantees are working.

Contract Types – This provision applies to all AIP funded projects, but not to the contracts between the grantee (the sponsor) and a contractor, subcontractors, suppliers, or subgrantees.

Use of Provision – No mandatory or recommended text provided because the requirements do not extend beyond the sponsor level.

EQUAL EMPLOYMENT OPPORTUNITY (EEO)

EQUAL OPPORTUNITY CLAUSE

During the performance of this contract, the Contractor agrees as follows:

(1) The Contractor will not discriminate against any employee or applicant for employment because of race, color, religion, sex, or national origin. The Contractor will take affirmative action to ensure that applicants are employed, and that employees are treated during employment, without regard to their race, color, religion, sex, sexual orientation, gender identify, or national origin. Such action shall include, but not be limited to, the following: employment, upgrading, demotion, or transfer; recruitment or recruitment advertising; layoff, or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship. The Contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices to be provided setting forth the provisions of this nondiscrimination clause.

(2) The Contractor will, in all solicitations or advertisements for employees placed by or on behalf of the Contractor, state that all qualified applicants will receive considerations for employment without regard to race, color, religion, sex, or national origin.

(3) The Contractor will send to each labor union or representative of workers with which it has a collective bargaining agreement or other contract or understanding, a notice to be provided advising the said labor union or workers' representatives of the Contractor's commitments under this section and shall post copies of the notice in conspicuous places available to employees and applicants for employment.

(4) The Contractor will comply with all provisions of Executive Order 11246 of September 24, 1965, and of the rules, regulations, and relevant orders of the Secretary of Labor.

(5) The Contractor will furnish all information and reports required by Executive Order 11246 of September 24, 1965, and by rules, regulations, and orders of the Secretary of Labor, or pursuant thereto, and will permit access to his books, records, and accounts by the administering agency and the Secretary of Labor for purposes of investigation to ascertain compliance with such rules, regulations, and orders.

(6) In the event of the Contractor's noncompliance with the nondiscrimination clauses of this contract or with any of the said rules, regulations, or orders, this contract may be canceled, terminated, or suspended in whole or in part and the Contractor may be declared ineligible for further Government contracts or federally assisted construction contracts in accordance with procedures authorized in Executive Order 11246 of September 24, 1965, and such other sanctions may be imposed and remedies invoked as provided in Executive Order 11246 of September 24, 1965, or by rule, regulation, or order of the Secretary of Labor, or as otherwise provided by law.

(7) The Contractor will include the portion of the sentence immediately preceding paragraph (1) and the provisions of paragraphs (1) through (7) in every subcontract or purchase order unless exempted by rules, regulations, or orders of the Secretary of Labor issued pursuant to section 204 of Executive Order 11246 of September 24, 1965, so that such provisions will be binding upon each subcontractor or vendor. The Contractor will take such action with respect to any subcontract or purchase order as the administering agency may direct as a means of enforcing such provisions, including sanctions for

noncompliance*: Provided, however*, that in the event a contractor becomes involved in, or is threatened with, litigation with a subcontractor or vendor as a result of such direction by the administering agency the Contractor may request the United States to enter into such litigation to protect the interests of the United States.

STANDARD FEDERAL EQUAL EMPLOYMENT OPPORTUNITY
CONSTRUCTION CONTRACT SPECIFICATIONS

1. As used in these specifications:

a. "Covered area" means the geographical area described in the solicitation from which this contract resulted;

b. "Director" means Director, Office of Federal Contract Compliance Programs (OFCCP), U.S. Department of Labor, or any person to whom the Director delegates authority;

c. "Employer identification number" means the Federal social security number used on the Employer's Quarterly Federal Tax Return, U.S. Treasury Department Form 941;

d. "Minority" includes:

(1) Black (all persons having origins in any of the Black African racial groups not of Hispanic origin);

(2) Hispanic (all persons of Mexican, Puerto Rican, Cuban, Central or South American, or other Spanish culture or origin regardless of race);

(3) Asian and Pacific Islander (all persons having origins in any of the original peoples of the Far East, Southeast Asia, the Indian Subcontinent, or the Pacific Islands); and

(4) American Indian or Alaskan native (all persons having origins in any of the original peoples of North America and maintaining identifiable tribal affiliations through membership and participation or community identification).

2. Whenever the Contractor, or any subcontractor at any tier, subcontracts a portion of the work involving any construction trade, it shall physically include in each subcontract in excess of $10,000 the provisions of these specifications and the Notice which contains the applicable goals for minority and female participation and which is set forth in the solicitations from which this contract resulted.

3. If the Contractor is participating (pursuant to 41 CFR part 60-4.5) in a Hometown Plan approved by the U.S. Department of Labor in the covered area either individually or through an association, its affirmative action obligations on all work in the Plan area (including goals and timetables) shall be in accordance with that Plan for those trades which have unions participating in the Plan. Contractors shall be able to demonstrate their participation in and compliance with the provisions of any such Hometown Plan. Each contractor or subcontractor participating in an approved plan is individually required to comply with its obligations under the EEO clause and to make a good faith effort to achieve each goal under the Plan in each trade in which it has employees. The overall good faith performance by other contractors or subcontractors toward a goal in an approved Plan does not excuse any covered contractor's or subcontractor's failure to take good faith efforts to achieve the Plan goals and timetables.

4. The Contractor shall implement the specific affirmative action standards provided in paragraphs 7a through 7p of these specifications. The goals set forth in the solicitation from which this contract

resulted are expressed as percentages of the total hours of employment and training of minority and female utilization the Contractor should reasonably be able to achieve in each construction trade in which it has employees in the covered area. Covered construction contractors performing construction work in a geographical area where they do not have a Federal or federally assisted construction contract shall apply the minority and female goals established for the geographical area where the work is being performed. Goals are published periodically in the Federal Register in notice form, and such notices may be obtained from any Office of Federal Contract Compliance Programs office or from Federal procurement contracting officers. The Contractor is expected to make substantially uniform progress in meeting its goals in each craft during the period specified.

5. Neither the provisions of any collective bargaining agreement nor the failure by a union with whom the Contractor has a collective bargaining agreement to refer either minorities or women shall excuse the Contractor's obligations under these specifications, Executive Order 11246, or the regulations promulgated pursuant thereto.

6. In order for the non-working training hours of apprentices and trainees to be counted in meeting the goals, such apprentices and trainees shall be employed by the Contractor during the training period and the Contractor shall have made a commitment to employ the apprentices and trainees at the completion of their training, subject to the availability of employment opportunities. Trainees shall be trained pursuant to training programs approved by the U.S. Department of Labor.

7. The Contractor shall take specific affirmative actions to ensure equal employment opportunity. The evaluation of the Contractor's compliance with these specifications shall be based upon its effort to achieve maximum results from its actions. The Contractor shall document these efforts fully and shall implement affirmative action steps at least as extensive as the following:

a. Ensure and maintain a working environment free of harassment, intimidation, and coercion at all sites, and in all facilities at which the Contractor's employees are assigned to work. The Contractor, where possible, will assign two or more women to each construction project. The Contractor shall specifically ensure that all foremen, superintendents, and other onsite supervisory personnel are aware of and carry out the Contractor's obligation to maintain such a working environment, with specific attention to minority or female individuals working at such sites or in such facilities.

b. Establish and maintain a current list of minority and female recruitment sources, provide written notification to minority and female recruitment sources and to community organizations when the Contractor or its unions have employment opportunities available, and maintain a record of the organizations' responses.

c. Maintain a current file of the names, addresses, and telephone numbers of each minority and female off-the-street applicant and minority or female referral from a union, a recruitment source, or community organization and of what action was taken with respect to each such individual. If such individual was sent to the union hiring hall for referral and was not referred back to the Contractor by the union or, if referred, not employed by the Contractor, this shall be documented in the file with the reason therefore along with whatever additional actions the Contractor may have taken.

d. Provide immediate written notification to the Director when the union or unions with which the Contractor has a collective bargaining agreement has not referred to the Contractor a minority

person or female sent by the Contractor, or when the Contractor has other information that the union referral process has impeded the Contractor's efforts to meet its obligations.

e. Develop on-the-job training opportunities and/or participate in training programs for the area which expressly include minorities and women, including upgrading programs and apprenticeship and trainee programs relevant to the Contractor's employment needs, especially those programs funded or approved by the Department of Labor. The Contractor shall provide notice of these programs to the sources compiled under 7b above.

f. Disseminate the Contractor's EEO policy by providing notice of the policy to unions and training programs and requesting their cooperation in assisting the Contractor in meeting its EEO obligations; by including it in any policy manual and collective bargaining agreement; by publicizing it in the company newspaper, annual report, etc.; by specific review of the policy with all management personnel and with all minority and female employees at least once a year; and by posting the company EEO policy on bulletin boards accessible to all employees at each location where construction work is performed.

g. Review, at least annually, the company's EEO policy and affirmative action obligations under these specifications with all employees having any responsibility for hiring, assignment, layoff, termination, or other employment decisions, including specific review of these items, with onsite supervisory personnel such superintendents, general foremen, etc., prior to the initiation of construction work at any job site. A written record shall be made and maintained identifying the time and place of these meetings, persons attending, subject matter discussed, and disposition of the subject matter.

h. Disseminate the Contractor's EEO policy externally by including it in any advertising in the news media, specifically including minority and female news media, and providing written notification to and discussing the Contractor's EEO policy with other contractors and subcontractors with whom the Contractor does or anticipates doing business.

i. Direct its recruitment efforts, both oral and written, to minority, female, and community organizations, to schools with minority and female students; and to minority and female recruitment and training organizations serving the Contractor's recruitment area and employment needs. Not later than one month prior to the date for the acceptance of applications for apprenticeship or other training by any recruitment source, the Contractor shall send written notification to organizations, such as the above, describing the openings, screening procedures, and tests to be used in the selection process.

j. Encourage present minority and female employees to recruit other minority persons and women and, where reasonable, provide after school, summer, and vacation employment to minority and female youth both on the site and in other areas of a contractor's workforce.

k. Validate all tests and other selection requirements where there is an obligation to do so under 41 CFR part 60-3.

l. Conduct, at least annually, an inventory and evaluation at least of all minority and female personnel, for promotional opportunities and encourage these employees to seek or to prepare for, through appropriate training, etc., such opportunities.

m. Ensure that seniority practices, job classifications, work assignments, and other personnel practices do not have a discriminatory effect by continually monitoring all personnel and employment related activities to ensure that the EEO policy and the Contractor's obligations under these specifications are being carried out.

n. Ensure that all facilities and company activities are non-segregated except that separate or single user toilet and necessary changing facilities shall be provided to assure privacy between the sexes.

o. Document and maintain a record of all solicitations of offers for subcontracts from minority and female construction contractors and suppliers, including circulation of solicitations to minority and female contractor associations and other business associations.

p. Conduct a review, at least annually, of all supervisor's adherence to and performance under the Contractor's EEO policies and affirmative action obligations.

8. Contractors are encouraged to participate in voluntary associations, which assist in fulfilling one or more of their affirmative action obligations (7a through 7p). The efforts of a contractor association, joint contractor union, contractor community, or other similar groups of which the Contractor is a member and participant may be asserted as fulfilling any one or more of its obligations under 7a through 7p of these specifications provided that the Contractor actively participates in the group, makes every effort to assure that the group has a positive impact on the employment of minorities and women in the industry, ensures that the concrete benefits of the program are reflected in the Contractor's minority and female workforce participation, makes a good faith effort to meet its individual goals and timetables, and can provide access to documentation which demonstrates the effectiveness of actions taken on behalf of the Contractor. The obligation to comply, however, is the Contractor's and failure of such a group to fulfill an obligation shall not be a defense for the Contractor's noncompliance.

9. A single goal for minorities and a separate single goal for women have been established. The Contractor, however, is required to provide equal employment opportunity and to take affirmative action for all minority groups, both male and female, and all women, both minority and non-minority. Consequently, if the particular group is employed in a substantially disparate manner (for example, even though the Contractor has achieved its goals for women generally), the Contractor may be in violation of the Executive Order if a specific minority group of women is underutilized.

10. The Contractor shall not use the goals and timetables or affirmative action standards to discriminate against any person because of race, color, religion, sex, or national origin.

11. The Contractor shall not enter into any subcontract with any person or firm debarred from Government contracts pursuant to Executive Order 11246.

12. The Contractor shall carry out such sanctions and penalties for violation of these specifications and of the Equal Opportunity Clause, including suspension, termination, and cancellation of existing subcontracts as may be imposed or ordered pursuant to Executive Order 11246, as amended, and its implementing regulations, by the Office of Federal Contract Compliance Programs. Any contractor who fails to carry out such sanctions and penalties shall be in violation of these specifications and Executive Order 11246, as amended.

13. The Contractor, in fulfilling its obligations under these specifications, shall implement specific affirmative action steps, at least as extensive as those standards prescribed in paragraph 7 of these

specifications, so as to achieve maximum results from its efforts to ensure equal employment opportunity. If the Contractor fails to comply with the requirements of the Executive Order, the implementing regulations, or these specifications, the Director shall proceed in accordance with 41 CFR part 60-4.8.

14. The Contractor shall designate a responsible official to monitor all employment related activity to ensure that the company EEO policy is being carried out, to submit reports relating to the provisions hereof as may be required by the Government, and to keep records. Records shall at least include for each employee, the name, address, telephone number, construction trade, union affiliation if any, employee identification number when assigned, social security number, race, sex, status (e.g., mechanic, apprentice, trainee, helper, or laborer), dates of changes in status, hours worked per week in the indicated trade, rate of pay, and locations at which the work was performed. Records shall be maintained in an easily understandable and retrievable form; however, to the degree that existing records satisfy this requirement, contractors shall not be required to maintain separate records.

15. Nothing herein provided shall be construed as a limitation upon the application of other laws which establish different standards of compliance or upon the application of requirements for the hiring of local or other area residents (e.g. those under the Public Works Employment Act of 1977 and the Community Development Block Grant Program).

FEDERAL FAIR LABOR STANDARDS ACT (FEDERAL MINIMUM WAGE)

All contracts and subcontracts that result from this solicitation incorporate by reference the provisions of 29 CFR part 201, the Federal Fair Labor Standards Act (FLSA), with the same force and effect as if given in full text. The FLSA sets minimum wage, overtime pay, recordkeeping, and child labor standards for full and part-time workers.

The Contractor has full responsibility to monitor compliance to the referenced statute or regulation. The Contractor must address any claims or disputes that arise from this requirement directly with the U.S. Department of Labor – Wage and Hour Division.

LOBBYING AND INFLUENCING FEDERAL EMPLOYEES

CERTIFICATION REGARDING LOBBYING

The Bidder or Offeror certifies by signing and submitting this bid or proposal, to the best of his or her knowledge and belief, that:

(1) No Federal appropriated funds have been paid or will be paid, by or on behalf of the Bidder or Offeror, to any person for influencing or attempting to influence an officer or employee of an agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with the awarding of any Federal contract, the making of any Federal grant, the making of any Federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment, or modification of any Federal contract, grant, loan, or cooperative agreement.

(2) If any funds other than Federal appropriated funds have been paid or will be paid to any person for influencing or attempting to influence an officer or employee of any agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with this Federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form-LLL, "Disclosure Form to Report Lobbying," in accordance with its instructions.

(3) The undersigned shall require that the language of this certification be included in the award documents for all sub-awards at all tiers (including subcontracts, subgrants, and contracts under grants, loans, and cooperative agreements) and that all sub-recipients shall certify and disclose accordingly.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by section 1352, title 31, U.S. Code. Any person who fails to file the required certification shall be subject to a civil penalty of not less than $10,000 and not more than $100,000 for each such failure.

PROHIBITION OF SEGREGATED FACILITIES

(a) The Contractor agrees that it does not and will not maintain or provide for its employees any segregated facilities at any of its establishments, and that it does not and will not permit its employees to perform their services at any location under its control where segregated facilities are maintained. The Contractor agrees that a breach of this clause is a violation of the Equal Employment Opportunity clause in this contract.

(b) "Segregated facilities," as used in this clause, means any waiting rooms, work areas, rest rooms and wash rooms, restaurants and other eating areas, time clocks, locker rooms and other storage or dressing areas, parking lots, drinking fountains, recreation or entertainment areas, transportation, and housing facilities provided for employees that are segregated by explicit directive or are in fact segregated on the basis of race, color, religion, sex, or national origin because of written or oral policies or employee custom. The term does not include separate or single-user rest rooms or necessary dressing or sleeping areas provided to assure privacy between the sexes.

(c) The Contractor shall include this clause in every subcontract and purchase order that is subject to the Equal Employment Opportunity clause of this contract.

OCCUPATIONAL SAFETY AND HEALTH ACT OF 1970

All contracts and subcontracts that result from this solicitation incorporate by reference the requirements of 29 CFR Part 1910 with the same force and effect as if given in full text. The employer must provide a work environment that is free from recognized hazards that may cause death or serious physical harm to the employee. The employer retains full responsibility to monitor its compliance and their subcontractor's compliance with the applicable requirements of the Occupational Safety and Health Act of 1970 (20 CFR Part 1910). The employer must address any claims or disputes that pertain to a referenced requirement directly with the U.S. Department of Labor – Occupational Safety and Health Administration.

PROCUREMENT OF RECOVERED MATERIALS

Contractor and subcontractor agree to comply with Section 6002 of the Solid Waste Disposal Act, as amended by the Resource Conservation and Recovery Act, and the regulatory provisions of 40 CFR Part 247. In the performance of this contract and to the extent practicable, the Contractor and subcontractors are to use products containing the highest percentage of recovered materials for items designated by the Environmental Protection Agency (EPA) under 40 CFR Part 247 whenever:

1) The contract requires procurement of $10,000 or more of a designated item during the fiscal year; or
2) The contractor has procured $10,000 or more of a designated item using Federal funding during the previous fiscal year.

The list of EPA-designated items is available at www.epa.gov/smm/comprehensive-procurement-guidelines-construction-products.

Section 6002(c) establishes exceptions to the preference for recovery of EPA-designated products if the contractor can demonstrate the item is:

a) Not reasonably available within a timeframe providing for compliance with the contract performance schedule;
b) Fails to meet reasonable contract performance requirements; or
c) Is only available at an unreasonable price.

RIGHTS TO INVENTIONS

Contracts or agreements that include the performance of experimental, developmental, or research work must provide for the rights of the Federal Government and the Owner in any resulting invention as established by 37 CFR part 401, Rights to Inventions Made by Non-profit Organizations and Small Business Firms under Government Grants, Contracts, and Cooperative Agreements. This contract incorporates by reference the patent and inventions rights as specified within 37 CFR §401.14. Contractor must include this requirement in all sub-tier contracts involving experimental, developmental, or research work.

SEISMIC SAFETY

In the performance of design services, the Consultant agrees to furnish a building design and associated construction specification that conform to a building code standard that provides a level of seismic safety substantially equivalent to standards as established by the National Earthquake Hazards Reduction Program (NEHRP). Local building codes that model their building code after the current version of the International Building Code (IBC) meet the NEHRP equivalency level for seismic safety. At the conclusion of the design services, the Consultant agrees to furnish the Owner a "certification of compliance" that attests conformance of the building design and the construction specifications with the seismic standards of NEHRP or an equivalent building code.

Construction Contracts

SEISMIC SAFETY

The Contractor agrees to ensure that all work performed under this contract, including work performed by subcontractors, conforms to a building code standard that provides a level of seismic safety substantially equivalent to standards established by the National Earthquake Hazards Reduction Program (NEHRP). Local building codes that model their code after the current version of the International Building Code (IBC) meet the NEHRP equivalency level for seismic safety.

TAX DELINQUENCY AND FELONY CONVICTIONS

CERTIFICATION OF OFFERER/BIDDER REGARDING TAX DELINQUENCY AND FELONY CONVICTIONS

The applicant must complete the following two certification statements. The applicant must indicate its current status as it relates to tax delinquency and felony conviction by inserting a checkmark (✓) in the space following the applicable response. The applicant agrees that, if awarded a contract resulting from this solicitation, it will incorporate this provision for certification in all lower tier subcontracts.

Certifications

1) The applicant represents that it is (✓) is not (✓) a corporation that has any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.

2) The applicant represents that it is (✓) is not (✓) is not a corporation that was convicted of a criminal violation under any Federal law within the preceding 24 months.

Note

If an applicant responds in the affirmative to either of the above representations, the applicant is ineligible to receive an award unless the sponsor has received notification from the agency suspension and debarment official (SDO) that the SDO has considered suspension or debarment and determined that further action is not required to protect the Government's interests. The applicant therefore must provide information to the owner about its tax liability or conviction to the Owner, who will then notify the FAA Airports District Office, which will then notify the agency's SDO to facilitate completion of the required considerations before award decisions are made.

Term Definitions

Felony conviction: Felony conviction means a conviction within the preceding twentyfour (24) months of a felony criminal violation under any Federal law and includes conviction of an offense defined in a section of the U.S. code that specifically classifies the offense as a felony and conviction of an offense that is classified as a felony under 18 U.S.C. § 3559.

Tax Delinquency: A tax delinquency is any unpaid Federal tax liability that has been assessed, for which all judicial and administrative remedies have been exhausted, or have lapsed, and that is not being paid in a timely manner pursuant to an agreement with the authority responsible for collecting the tax liability.

TERMINATION OF CONTRACT

TERMINATION FOR CONVENIENCE (CONSTRUCTION & EQUIPMENT CONTRACTS)

The Owner may terminate this contract in whole or in part at any time by providing written notice to the Contractor. Such action may be without cause and without prejudice to any other right or remedy of Owner. Upon receipt of a written notice of termination, except as explicitly directed by the Owner, the Contractor shall immediately proceed with the following obligations regardless of any delay in determining or adjusting amounts due under this clause:

1. Contractor must immediately discontinue work as specified in the written notice.
2. Terminate all subcontracts to the extent they relate to the work terminated under the notice.
3. Discontinue orders for materials and services except as directed by the written notice.
4. Deliver to the Owner all fabricated and partially fabricated parts, completed and partially completed work, supplies, equipment and materials acquired prior to termination of the work, and as directed in the written notice.
5. Complete performance of the work not terminated by the notice.
6. Take action as directed by the Owner to protect and preserve property and work related to this contract that Owner will take possession.

Owner agrees to pay Contractor for:

1) completed and acceptable work executed in accordance with the contract documents prior to the effective date of termination;

2) documented expenses sustained prior to the effective date of termination in performing work and furnishing labor, materials, or equipment as required by the contract documents in connection with uncompleted work;

3) reasonable and substantiated claims, costs, and damages incurred in settlement of terminated contracts with Subcontractors and Suppliers; and

4) reasonable and substantiated expenses to the Contractor directly attributable to Owner's termination action.

Owner will not pay Contractor for loss of anticipated profits or revenue or other economic loss arising out of or resulting from the Owner's termination action.

The rights and remedies this clause provides are in addition to any other rights and remedies provided by law or under this contract.

TERMINATION FOR CONVENIENCE (PROFESSIONAL SERVICES)

The Owner may, by written notice to the Consultant, terminate this Agreement for its convenience and without cause or default on the part of Consultant. Upon receipt of the notice of termination, except as explicitly directed by the Owner, the Contractor must immediately discontinue all services affected.

Upon termination of the Agreement, the Consultant must deliver to the Owner all data, surveys, models, drawings, specifications, reports, maps, photographs, estimates, summaries, and other documents and materials prepared by the Engineer under this contract, whether complete or partially complete.

Owner agrees to make just and equitable compensation to the Consultant for satisfactory work completed up through the date the Consultant receives the termination notice. Compensation will not include anticipated profit on non-performed services.

Owner further agrees to hold Consultant harmless for errors or omissions in documents that are incomplete as a result of the termination action under this clause.

TERMINATION FOR DEFAULT (CONSTRUCTION)

Section 80-09 of FAA Advisory Circular 150/5370-10 establishes conditions, rights, and remedies associated with Owner termination of this contract due to default of the Contractor.

TERMINATION FOR DEFAULT (EQUIPMENT)

The Owner may, by written notice of default to the Contractor, terminate all or part of this Contract if the Contractor:

1. Fails to commence the Work under the Contract within the time specified in the Notice- to-Proceed;
2. Fails to make adequate progress as to endanger performance of this Contract in accordance with its terms;
3. Fails to make delivery of the equipment within the time specified in the Contract, including any Owner approved extensions;
4. Fails to comply with material provisions of the Contract;
5. Submits certifications made under the Contract and as part of their proposal that include false or fraudulent statements; or
6. Becomes insolvent or declares bankruptcy.

If one or more of the stated events occur, the Owner will give notice in writing to the Contractor and Surety of its intent to terminate the contract for cause. At the Owner's discretion, the notice may allow the Contractor and Surety an opportunity to cure the breach or default.

If within [10] days of the receipt of notice, the Contractor or Surety fails to remedy the breach or default to the satisfaction of the Owner, the Owner has authority to acquire equipment by other procurement action. The Contractor will be liable to the Owner for any excess costs the Owner incurs for acquiring such similar equipment.

Payment for completed equipment delivered to and accepted by the Owner shall be at the Contract price. The Owner may withhold from amounts otherwise due the Contractor for such completed equipment, such sum as the Owner determines to be necessary to protect the Owner against loss because of Contractor default.

Owner will not terminate the Contractor's right to proceed with the Work under this clause if the delay in completing the work arises from unforeseeable causes beyond the control and without the fault or negligence of the Contractor. Examples of such acceptable causes include: acts of God, acts of the Owner, acts of another Contractor in the performance of a contract with the Owner, and severe weather events that substantially exceed normal conditions for the location.

If, after termination of the Contractor's right to proceed, the Owner determines that the Contractor was not in default, or that the delay was excusable, the rights and obligations of the parties will be the same as if the Owner issued the termination for the convenience the Owner.

The rights and remedies of the Owner in this clause are in addition to any other rights and remedies provided by law or under this contract.

TERMINATION FOR DEFAULT (PROFESSIONAL SERVICES)

Either party may terminate this Agreement for cause if the other party fails to fulfill its obligations that are essential to the completion of the work per the terms and conditions of the Agreement. The party initiating the termination action must allow the breaching party an opportunity to dispute or cure the breach.

The terminating party must provide the breaching party [7] days advance written notice of its intent to terminate the Agreement. The notice must specify the nature and extent of the breach, the conditions necessary to cure the breach, and the effective date of the termination action. The rights and remedies in this clause are in addition to any other rights and remedies provided by law or under this agreement.

a) **Termination by Owner**: The Owner may terminate this Agreement in whole or in part, for the failure of the Consultant to:
   1. Perform the services within the time specified in this contract or by Owner approved extension;
   2. Make adequate progress so as to endanger satisfactory performance of the Project; or
   3. Fulfill the obligations of the Agreement that are essential to the completion of the Project.

   Upon receipt of the notice of termination, the Consultant must immediately discontinue all services affected unless the notice directs otherwise. Upon termination of the Agreement, the Consultant must deliver to the Owner all data, surveys, models, drawings, specifications, reports, maps, photographs, estimates, summaries, and other documents and materials prepared by the Engineer under this contract, whether complete or partially complete.

   Owner agrees to make just and equitable compensation to the Consultant for satisfactory work completed up through the date the Consultant receives the termination notice. Compensation will not include anticipated profit on non-performed services.

   Owner further agrees to hold Consultant harmless for errors or omissions in documents that are incomplete as a result of the termination action under this clause.

   If, after finalization of the termination action, the Owner determines the Consultant was not in default of the Agreement, the rights and obligations of the parties shall be the same as if the Owner issued the termination for the convenience of the Owner.

b) **Termination by Consultant**: The Consultant may terminate this Agreement in whole or in part, if the Owner:
   1. Defaults on its obligations under this Agreement;
   2. Fails to make payment to the Consultant in accordance with the terms of this Agreement;
   3. Suspends the Project for more than [180] days due to reasons beyond the control of the Consultant.

   Upon receipt of a notice of termination from the Consultant, Owner agrees to cooperate with Consultant for the purpose of terminating the agreement or portion thereof, by mutual consent. If

Owner and Consultant cannot reach mutual agreement on the termination settlement, the Consultant may, without prejudice to any rights and remedies it may have, proceed with terminating all or parts of this Agreement based upon the Owner's breach of the contract.

In the event of termination due to Owner breach, the Engineer is entitled to invoice Owner and to receive full payment for all services performed or furnished in accordance with this Agreement and all justified reimbursable expenses incurred by the Consultant through the effective date of termination action. Owner agrees to hold Consultant harmless for errors or omissions in documents that are incomplete as a result of the termination action under this clause.

TRADE RESTRICTION CERTIFICATION

By submission of an offer, the Offeror certifies that with respect to this solicitation and any resultant contract, the Offeror –

1) is not owned or controlled by one or more citizens of a foreign country included in the list of countries that discriminate against U.S. firms as published by the Office of the United States Trade Representative (USTR);

2) has not knowingly entered into any contract or subcontract for this project with a person that is a citizen or national of a foreign country included on the list of countries that discriminate against U.S. firms as published by the USTR; and

3) has not entered into any subcontract for any product to be used on the Federal project that is produced in a foreign country included on the list of countries that discriminate against U.S. firms published by the USTR.

This certification concerns a matter within the jurisdiction of an agency of the United States of America and the making of a false, fictitious, or fraudulent certification may render the maker subject to prosecution under Title 18 USC Section 1001.

The Offeror/Contractor must provide immediate written notice to the Owner if the Offeror/Contractor learns that its certification or that of a subcontractor was erroneous when submitted or has become erroneous by reason of changed circumstances. The Contractor must require subcontractors provide immediate written notice to the Contractor if at any time it learns that its certification was erroneous by reason of changed circumstances.

Unless the restrictions of this clause are waived by the Secretary of Transportation in accordance with 49 CFR 30.17, no contract shall be awarded to an Offeror or subcontractor:

1) who is owned or controlled by one or more citizens or nationals of a foreign country included on the list of countries that discriminate against U.S. firms published by the USTR or
2) whose subcontractors are owned or controlled by one or more citizens or nationals of a foreign country on such USTR list or
3) who incorporates in the public works project any product of a foreign country on such USTR list.

Nothing contained in the foregoing shall be construed to require establishment of a system of records in order to render, in good faith, the certification required by this provision. The knowledge and information of a contractor is not required to exceed that which is normally possessed by a prudent person in the ordinary course of business dealings.

The Offeror agrees that, if awarded a contract resulting from this solicitation, it will incorporate this provision for certification without modification in all lower tier subcontracts. The Contractor may rely on the certification of a prospective subcontractor that it is not a firm from a foreign country included on the list of countries that discriminate against U.S. firms as published by USTR, unless the Offeror has knowledge that the certification is erroneous.

This certification is a material representation of fact upon which reliance was placed when making an award. If it is later determined that the Contractor or subcontractor knowingly rendered an erroneous

certification, the Federal Aviation Administration (FAA) may direct through the Owner cancellation of the contract or subcontract for default at no cost to the Owner or the FAA.

VETERAN'S PREFERENCE

In the employment of labor (excluding executive, administrative, and supervisory positions), the Contractor and all sub-tier contractors must give preference to covered veterans as defined within Title 49 United States Code Section 47112. Covered veterans include Vietnam-era veterans, Persian Gulf veterans, Afghanistan-Iraq war veterans, disabled veterans, and small business concerns (as defined by 15 USC 632) owned and controlled by disabled veterans. This preference only applies when there are covered veterans readily available and qualified to perform the work to which the employment relates.

DOMESTIC PREFERENCES FOR PROCUREMENTS

The Bidder or Offeror certifies by signing and submitting this bid or proposal that, to the greatest extent practicable, the Bidder or Offeror has provided a preference for the purchase, acquisition, or use of goods, products, or materials produced in the United States (including, but not limited to, iron, aluminum, steel, cement, and other manufactured products) in compliance with 2 CFR § 200.322.

APPENDIX D

COUNTY OF SANTA BARBARA GENERAL CONDITIONS

General Conditions

County of Santa Barbara
Santa Ynez Valley Airport
Pavement Rehabilitation
Project #22011
May 2025

GENERAL CONDITIONS

GENERAL CONDITIONS

Table of Contents

CONTRACT DOCUMENTS 5
- **1.1 DEFINITIONS** 5
- **1.2 ABBREVIATIONS** 6
- **1.3 EXECUTION, CORRELATION AND INTENT** 6
- **1.4 OWNERSHIP AND USE OF DOCUMENTS** 7

OWNER 7
- **2.1 DEFINITION** 7
- **2.2 INFORMATION AND SERVICES FURNISHED BY THE OWNER** 7
- **2.3 DELEGATION** 7
- **2.4 AUTHORITY OF BOARD AND INSPECTION** 8

ARCHITECT/ENGINEER 8
- **3.1 DEFINITIONS** 8
- **3.2 ARCHITECT/ENGINEER'S DUTIES DURING CONSTRUCTION** 8

DESIGNATED REPRESENTATIVE 10
- **4.1 DEFINITION** 10
- **4.2 ADMINISTRATION OF THE CONTRACT** 10
- **4.3 OWNER'S AND DESIGNATED REPRESENTATIVE'S RIGHT TO STOP WORK** 11

CONTRACTOR 11
- **5.1 DEFINITION** 11
- **5.2 REVIEW OF CONTRACT DOCUMENTS** 12
- **5.3 SUPERVISION AND CONSTRUCTION PROCEDURES** 12
- **5.4 LABOR AND MATERIALS** 12
- **5.5 WARRANTIES AND GUARANTEES** 14
- **5.6 CONTROL OF OPERATIONS AND EMPLOYEES** 15
- **5.7 PERMITS, FEES AND NOTICES** 16
- **5.8 ALLOWANCES** 16
- **5.9 SUPERINTENDENT** 16
- **5.10 CONSTRUCTION SCHEDULE** 17

Submission of Schedule and Format 17
Updating of the Schedule 18
Revision of the Schedule 18
Minor Changes of the Schedule 18
Extensions of Contract Time 18
During Construction 18
Owner Directed Schedule 19
5.11 SUBMITTAL SCHEDULE 19
5.12 DRAWINGS AND SPECIFICATIONS AT THE SITE 20
5.13 USE OF SITE 20
5.14 CUTTING AND PATCHING WORK 20
5.15 DAILY AND FINAL CLEAN UP 21
5.16 COMMUNICATIONS 21
5.17 ROYALTIES AND PATENTS 21
5.18 INSURANCE 21
Insurance Requirements for Contractor 21
Subcontractors 22
5.19 CONTRACTOR QUALITY CONTROL SYSTEM 22
5.21 WARRANTY OF CONSTRUCTION 25
5.22 SUBCONTRACTS 26
5.23 LAWS TO BE OBSERVED 26

SUBCONTRACTORS 27
6.1 DEFINITION 27
6.2 SUB-CONTRACTUAL RELATIONS 27

SEPARATE CONTRACTS 27
7.1 OTHER CONTRACTORS 27
7.2 CONTRACTOR TO INSPECT OTHER WORK 27
7.3 COORDINATION AND COOPERATION 27
7.4 OWNER'S RIGHT TO CLEAN UP 28
7.5 DAMAGES TO WORK 28

MISCELLANEOUS PROVISIONS 28
8.1 GOVERNING LAW 29
8.2 SUCCESSORS AND ASSIGNS 29
8.3 WRITTEN NOTICE 29
8.4 CLAIMS FOR DAMAGES 29
8.5 PERFORMANCE BOND AND LABOR MATERIAL PAYMENT BOND 29
8.6 RIGHTS AND REMEDIES 29
8.7 TESTS 29
8.8 ORDER OF PRECEDENCE 31

TIME 31
9.1 DEFINITIONS 31
9.2 PROGRESS AND COMPLETION 31
9.3 DELAYS AND EXTENSIONS OF TIME 32

PAYMENTS AND COMPLETION 33
10.1 CONTRACT SUM 33
10.2 SCHEDULE OF VALUES 33
10.3 APPLICATION FOR PAYMENT 33
10.4 PROGRESS PAYMENTS 34
10.5 PAYMENTS WITHHELD 35
10.6 FAILURE OF PAYMENT 35
10.7 SUBSTANTIAL COMPLETION 35
10.8 FINAL COMPLETION AND FINAL PAYMENT 36
10.9 MEASUREMENT OF QUANTITIES FOR UNIT PRICE WORK 37

PROTECTION OF PERSONS AND PROPERTY 37
11.1 SAFETY PRECAUTIONS AND PROGRAMS 37
11.2 SAFETY OF PERSONS AND PROPERTY 38
11.3 EMERGENCIES 39

UTILITIES 39
12.1 LOCATION 39
12.2 PROTECTION 39
12.3 EXCAVATIONS 40
12.4 REMOVAL 40
12.5 RELOCATION 40
12.6 DELAYS 40
12.7 COOPERATION 41

CHANGES IN THE WORK 41
13.1 CHANGE ORDERS 41
13.2 CONCEALED CONDITIONS 43
13.3 CLAIMS FOR ADDITIONAL COST 43
13.4 MINOR CHANGES IN THE WORK 43

UNCOVERING AND CORRECTION OF WORK 44
14.1 UNCOVERING OF WORK 44
14.2 CORRECTION OF WORK 44
14.3 ACCEPTANCE OF DEFECTIVE OR NONCONFORMING WORK 44

TERMINATION OF THE CONTRACT 45
15.1 TERMINATION BY THE CONTRACTOR 45
15.2 TERMINATION BY THE OWNER 45

PROJECT REQUIREMENTS 45
16.1 PROJECT REPORTS 45
16.2 DRAWINGS, PRODUCT DATA AND SAMPLES 46
16.3 TEMPORARY SERVICES, SYSTEMS AND FACILITIES 49
16.4 SAFETY 52

ARTICLE 1: CONTRACT DOCUMENTS

1.1 DEFINITIONS

1.1.1 The Contract Documents: The Contract Documents consist of the Agreement between the Owner and the Contractor, the Conditions of the Contract (General Conditions, General Requirements, Special Provisions and other Conditions), the Drawings, the Specifications, all Addenda, Supplements, Invitations to Bid and Proposal Forms issued prior to execution of the Contract and all Modifications issued after the execution of the Contract. A Modification is (1) a written amendment to the Contract signed by both parties (2) a Change Order, (3) a written interpretation issued by the Architect/Engineer pursuant to Subparagraph 3.2.2 or (4) a written order for a minor change in the Work issued on the Owner's behalf pursuant to Paragraph 13.4.1.

1.1.2 The Contract: The Contract Documents form the Contract with the Contractor. This Contract represents the entire and integrated agreement and supersedes all prior negotiations, representations, or agreements, either written or oral. The Contract may be amended or modified only by a Modification as defined in Subparagraph 1.1.1. The Contract Documents shall not be construed to create any contractual relationship of any kind between the Architect/Engineer and the Contractor or between the Architect/Engineer and the Designated Representative but the Architect/Engineer and the Designated Representative shall be entitled to performance of the obligations of the Contractor intended for their benefit and to enforcement thereof. Nothing contained in the Contract Documents shall create any contractual relationship between the Owner, the Designated Representative or the Architect/Engineer and any Subcontractor or Sub-subcontractor.

1.1.3 The Work: The term "Work" means the construction and services required by the Contract Documents, whether completed or partially completed, and includes all other labor, materials, equipment and services provided or to be provided by the Contractor to fulfill the Contractor's obligations. The Work may constitute the whole or part of the project.

The Project: The "Project" is the total construction of which the Work performed under the Contract Documents may be the whole or a part and which may include construction by the Owner or by separate contractors.

1.1.5 The Owner: As defined in Article 2 of the General Conditions, the Owner for this project is:
Santa Barbara County, through its
Board of Supervisors

1.1.6 Architect/Engineer: As defined in Article 3 of the General Conditions.

1.1.7 Designated Representative: As defined in Article 4 of the General Conditions, the Designated Representative is also the Labor Compliance Coordinator for the Work.

1.1.8 Contractor: As defined in Article 5 of the General Conditions.

1.1.9 Product: The term "product" shall include materials, equipment and systems.

1.1.10 The Drawings: The Drawings are the graphic and pictorial portions of the Contract Documents, wherever located and whenever issued, showing the design, location and dimensions of the Work, generally including plans, elevations, sections, details, schedules, and diagrams.

1.1.11 The Specifications: The Specifications are that portion of the Contract Documents consisting of the written requirements for materials, equipment, construction systems, standards and workmanship for the Work and performance of related services.

1.1.12 The Bid Package: The Bid Package is the volume usually assembled for the Work which may include the bidding requirements, sample forms, conditions of the Contracts and Specifications.

1.1.13 As Approved: Where used in conjunction with the Designated Representative or the Architect/Engineer's response to submittal's, requests, applications, inquiries, reports and claims by the Contractor, the meaning of the term "approved" shall not exceed the limitations of the Designated Representative or the Architect/Engineer's responsibilities and duties as established in these General Conditions.

1.1.13.1 In no case shall "approval" by the Designated Representative or the Architect/Engineer be interpreted as a release of the Contractor from the responsibilities to fulfill the requirements of the Contract Documents.

1.1.13.2 Approval, where required for an item, shall be obtained from the Architect/Engineer through the Designated Representative in writing.

1.1.14 Indicated: The term "indicated" is a cross reference to details, notes or schedules on the drawings, other paragraphs

or schedules in the Specifications and similar means of recording requirements in the Contract Documents.

1.1.14.1 Where terms such as "shown", "noted", "scheduled", and "specified" are used instead of "indicated", it is for the purpose of helping the reader accomplish the cross reference and no limitation of locations is intended except as specifically noted.

1.1.14.2 Directed, Requested, Etc.: Where not otherwise explained, terms such as "directed", "requested", "authorized", "selected:, "approved", "required", "accepted", and "permitted" mean "directed by the Architect/Engineer, Designated Representative or Owner's Representative", "requested by the Architect/Engineer, Designated Representative or the Owner's Representative", etc. However, no such implied meaning will be interpreted to extend to the Architect/Engineer's or Designated Representative's responsibility in the Contractor's area of construction supervision.

1.1.15 Installer: The person or entity engaged by the Contractor or its Subcontractor or Sub-subcontractor for the performance of a particular unit of Work at the project site, including installation, erection, application and similar required operations. It is a General Requirement that installers be recognized as experienced and competent in the Work that they are engaged to perform.

1.1.16 Suitable, Reasonable, Proper, Correct, and Necessary: Such terms shall mean as suitable, reasonable, proper, correct or necessary for the purpose intended as required by the Contract Documents, subject to the judgment of the Architect/Engineer or the Designated Representative.

1.1.17 Including, Such As: The Terms "including" and "such as" shall always be taken in the most inclusive sense, namely, "including, but not limited to", and "such as, but not limited to."

1.1.18 Option: The term "option" shall mean a choice from the specified products which shall be made by the Contractor. The choice is not "whether" the Work is to be performed, but "which" product or "which" procedure is to be used. The product or procedure chosen by the Contractor shall be provided at no increase in the cost to the Owner or the Designated Representative and with no lessening of the Contractor's responsibility for its performance. All or any options selected or proposed are still subject to all requirements for submittals and for approval of same.

1.1.19 Exposed: The term "exposed" shall mean any item or surface, exterior or interior, which can be seen by a person outside the building, or seen by a person inside any usable space within the building during normal activity.

1.1.20 At No Additional Cost: The term "at no additional cost" shall mean at no additional cost to the Owner and at no cost to the Architect/Engineer or the Designated Representative.

1.1.21 Testing Laboratory: An independent entity engaged to perform specific inspections or tests of the Work, either at the project site or elsewhere; and to report and interpret the results of those inspections or tests.

1.1.22 Record Documents: Construction Documents revised to show changes made during the construction process, usually based on marked-up prints, drawings and other data furnished by the Contractor to the Designated Representative.

1.1.23 Compliance Group Representative: The person or entity representing a third-party observer whose sole purpose on the PROJECT is to interview contractor employees, including any subcontractor for prevailing wage compliance consistent with federal and state prevailing wage requirements as set forth in the David-Bacon Act and other related codes, laws or regulations.

1.2 ABBREVIATIONS

1.2.1 The language of the specifications and elsewhere in the Contract Documents is of the abbreviated type in certain instances and implies words and meanings which will be appropriately interpreted.

1.2.2 Actual word abbreviations of a self-explanatory nature have been included in the Specifications and Drawings. These are generally defined in the Specifications Section at the first instance of use of each term so abbreviated. They are generally summarized in a list on the Drawings.

1.2.3 Singular words will be interpreted as plural and plural words will be interpreted as singular where applicable and the full context of the requirements so indicates.

1.3 EXECUTION, CORRELATION AND INTENT

1.3.1 By executing this Agreement, the Contractor represents that he has visited the site, familiarized himself with the local conditions under which the Work is to be performed and correlated its observations with the requirements of the Contract Documents. Claims, as a result of failure to do so, will not be considered.

1.3.2 The contract agreement shall be signed in triplicate by the Owner and Contractor. Original copies are to be provided to Owner, Contractor, and Designated Representative. Digital signatures, as of 2021, are acceptable by the County of Santa Barbara

1.3.3 The intent of the Contract Documents is to include all items necessary for the proper execution and completion of

the Work. The Contract Documents are complementary and what is required by any one shall be as binding as if required by all. Work not covered in the Contract Documents will not be required unless it is consistent therewith and is reasonably inferable therefrom as being necessary to produce the intended results. Words and abbreviations in the Contract Documents which have well-known technical or trade meanings are used in accordance with such recognized meanings.

1.3.4 The organization of the Specification into divisions, sections and articles and the arrangements of Drawings shall not control the Contractor in dividing the Work among Subcontractors or in establishing the extent of Work to be performed by any Trade.

1.3.5 All indications or notations which apply to one or a number of similar situations, materials or processes shall be deemed to apply to all such situations, materials or processes wherever they appear in the Work, unless otherwise indicated in the Contract Documents.

1.3.5.1 Where the word "similar" appears on the drawings, it shall be interpreted in its general sense and not as meaning identical and all details shall be worked out in relations to their location and connection with other parts of the Work.

1.3.5.2 Where, on any drawings, a portion of the Work is drawn out and the remainder is indicated in outline, the parts drawn out shall also apply to parts outlined.

1.3.6 All manufactured articles, materials and equipment shall be applied, installed, connected, erected, used, cleaned and conditioned in accordance with the manufacturer's written or printed directions and instructions unless otherwise indicated in the Contract Documents.

1.3.7 The Contract Documents should be read as one package and are dependent on one another for interpretation. If there is an ambiguity or conflict between documents, the Contractor or its Subcontractor has the duty of inquiring with the Designated Representative and the Architect/Engineer before he bids on the job. Conflicts and discrepancies discovered during the process of the Work shall be referred to the Architect/Engineer and Owner via the Designated Representative for resolution.

1.3.8 Any noted discrepancies between the Contract Documents shall be promptly called to the attention of the Designated Representative and the Architect/Engineer and no Work so affected shall be undertaken in advance of the Designated Representative's and the Architect/Engineer's decision, except at the Contractor's own risk.

1.4 OWNERSHIP AND USE OF DOCUMENTS

1.4.1 Unless otherwise provided in the Contract Documents, the Contractor will be furnished, free of charge, up to eight (8) sets of approved Working Drawings and Specifications for the execution of the Work.

1.4.2 All Drawings, Specifications and copies thereof furnished by the Owner are and shall remain its property. They are to be used only with respect to this project and are not to be used on any other project. With the exception of one contract set for each party, such documents are to be returned or suitably accounted for to the Owner on request at the completion of the Work.

ARTICLE 2: OWNER

2.1 DEFINITION

2.1.1 The Owner is the person or entity identified as such in the Agreement between the Owner and the Contractor and is referred to throughout the Contract Documents as if singular in number and masculine in gender. The term Owner means the Owner or its authorized representative.

2.2 INFORMATION AND SERVICES FURNISHED BY THE OWNER

2.2.1 The Owner will furnish all surveys describing the physical characteristics and approximate known utility locations for the site of the Project.

2.2.2 Except as provided in Subparagraph 5.7.1, the Owner will secure and pay for necessary approvals, easements, assessments and charges required for the construction, use, or occupancy of permanent structures or for permanent changes in existing facilities unless otherwise noted.

2.2.3 Information or services under the Owner's control will be furnished by the Owner with reasonable promptness to avoid delay in the orderly progress of the Work.

2.2.4 The Owner shall forward all instructions to the Contractor through the Designated Representative.

2.2.5 The Owner shall at all times have access to the Work for inspection, wherever it is in preparation or in progress. When directed by the Designated Representative, the Contractor shall provide facilities for such access and inspection at the Contractor's cost.

2.3 DELEGATION

2.3.1 The Board of Supervisors delegates to the County Director of General Services the authority to act on its behalf in the administration of this contract.

2.3.2 The Director of General Services has the authority to change the Designated Representative when the Designated Representative is an employee of the County.

2.3.3 If the Designated Representative is a person or entity other than an employee of the County, the Director of General Services shall recommend to the Board of Supervisors a replacement for the Designated Representative whenever such replacement is in the best interest of the County. An affirmative majority vote by the Board of Supervisors is required to complete the replacement of the Designated Representative.

2.3.4 The Director of General Services may execute Change Orders in accordance with Article 13 in a cumulative amount not to exceed 10% of the first $250,000 of the base contract amount plus 5% of the base contract amount over $250,000, and for time extensions as the director may deem equitable. Any Change Orders in excess of 10% of the first $250,000 of the base contract amount plus 5% of the base contract amount over $250,000 shall be approved by a majority vote of the Board of Supervisors.

2.4 AUTHORITY OF BOARD AND INSPECTION

2.4.1 The Board of Supervisors has the final authority in all matters affecting the work covered by the plans and specifications. Within the scope of the contract, the Designated Representative has the authority to enforce compliance with the plans and specifications. The Contractor shall promptly comply with instructions from the Designated Representative.

2.4.2 On all questions relating to quantities, the acceptability of material, equipment, or work, the execution, progress or sequence of work, and the interpretation of specifications or drawings, the decision of the Designated Representative is final and binding, and shall be precedent to any payment under the contract, unless otherwise ordered by the Board.

2.4.3 Labor Compliance Monitoring: To ensure compliance with prevailing wage requirements in the WORK, the Board of Supervisors has adopted a *Joint Labor Compliance Monitoring Program.* This program monitors labor compliance by conducting interviews with CONTRACTOR employees and subcontractors at the project site. A copy of the *Joint Labor Compliance Monitoring Program* is available at the Capital Projects Division Office. A copy of the *Joint Labor Compliance Monitoring Program* will be provided upon request. The Contractor, and all subcontractors, shall cooperate by allowing approved Compliance Group Representatives access to its employees on the project site for the purpose of conducting prevailing wage compliance interviews. The Compliance Group Representative shall restrict their on-site activities to prevailing wage compliance interviews only. Promotion, advertising or other related activities of the Compliance Group Representative is strictly prohibited. Any additional effort required by the Contractor in compliance with this Article shall be incorporated into the Bid Scope of Work and no additional compensation will be considered.

2.4.4 The Designated Representative (or its designee) may accompany any Compliance Group Representative when conducting prevailing wage compliance interviews. The Compliance Group Representative will display in plain view a county-issued identification card when conducting prevailing wage compliance interviews at the project site.

ARTICLE 3: ARCHITECT/ENGINEER

3.1 DEFINITIONS

3.1.1 The Architect/Engineer is the person lawfully licensed to practice architecture or engineering or an entity lawfully practicing architecture or engineering who has entered into an Agreement with the Owner to serve as Architect/Engineer and is referred to throughout the Contract Documents as if singular in number and masculine in gender. The term Architect/Engineer means the Architect/Engineer or its authorized representative.

3.1.2 Architect/Engineer shall be entitled to performance by the Contractor of any obligations expressly set forth which are intended for the Architect/Engineer's benefit and to enforcement thereof.

3.1.3 In the case of the termination of the employment of the Architect/Engineer, the Owner shall appoint a capable and reputable Architect/Engineer. The status under the Contract of the Architect/Engineer so appointed shall be that of the former Architect/Engineer. The Owner shall notify the Contractor whenever the Architect/Engineer is replaced.

3.1.4 The Architect/Engineer may be an employee of the County or other governmental entity.

3.2 ARCHITECT/ENGINEER'S DUTIES DURING CONSTRUCTION

3.2.1 The Architect/Engineer shall at all times have access to the Work wherever it is in preparation and progress. When directed by the Designated Representative, the Contractor shall provide facilities for such access at the Contractor's cost so the Architect/Engineer may perform its functions under the Contract Documents.

3.2.2 The Architect/Engineer will be the interpreter of the requirements of the Drawings and Specifications. Written

interpretations necessary for the proper execution or progress of the Work, in the form of drawings or otherwise, will be issued with reasonable promptness by the Architect/Engineer through the Designated Representative and in accordance with any schedule agreed upon. The Contractor or Owner shall make written dated request through the Designated Representative to the Architect/Engineer for such interpretations. Such interpretations shall be consistent with and reasonably inferable from the Contract Documents. The Contractor or Owner shall execute and complete the Work in accordance with such interpretations. The Architect/Engineer shall not be liable to the Contractor for the result of any interpretation or decisions rendered in good faith in such capacity.

3.2.2.1 The Architect/Engineer shall interpret the requirements of Change Orders and he shall decide all other questions of design intent in connection with the Work.

3.2.2.2 It shall be the responsibility of the Architect/Engineer to make interpretations and render opinions in regard to all claims to the Owner or Designated Representative involving questions of interpretation of the intent of the drawings and specifications. Such opinions and interpretations, together with the reasons therefore, shall be furnished in writing by the Architect/Engineer to the Owner, Designated Representative and Contractor within ten (10) days after a request is made thereof.

3.2.2.3 Neither the Contractor, the Designated Representative nor the Owner shall be bound by any determination, interpretation or opinion of the Architect/Engineer if it is determined that such is not in accord with the true intent of the Contract Documents. The party taking issue with the determination, interpretation, or decision of the Architect/Engineer shall give the other party or parties, as the case may be, written notice of such fact within ten (10) days after the determination, interpretation, or opinion is rendered by the Architect/Engineer. However, it is the intent of this Paragraph 3.2 that in the actual performance of the Work, the Contractor and the Designated Representative shall, in the first instance, proceed in accordance with the instruction given by the Architect/Engineer unless the Owner and the Designated Representative mutually agree that the Contractor and the Designated Representative shall proceed otherwise.

3.2.3 The Architect/Engineer's decisions in matters relating to artistic effect will be final if consistent with the intent of the Contract Documents.

3.2.4 The Architect/Engineer will have the authority to reject Work which does not conform to the Contract Documents. Whenever, in its opinion, he considers it necessary or advisable for the implementation of the intent of the Contract Documents, he will have authority to require special inspection or testing of the Work in accordance with Subparagraph 8.7.2 whether or not such Work be then fabricated, installed or completed. However, neither the Architect/Engineer's authority to act under this Subparagraph 3.2.4, nor any decision made by him in good faith either to exercise or not to exercise such authority, shall give rise to any duty or responsibility of the Architect/Engineer to the Contractor, any Subcontractor, any of their agents or employees, or any other person performing any of the Work.

3.2.4.1 The Architect/Engineer will be the judge of the performance of the Work and will use its powers under the Contract to enforce its faithful performance. The Architect/Engineer will determine the amount, quality, acceptability and fitness of all parts of the Work.

3.2.4.2 The Architect/Engineer will recommend suspension of the Work whenever suspension may be necessary to ensure the proper execution of the Work.

3.2.5 The Architect/Engineer will review and approve or take other appropriate action upon Contractor's submittals such as Shop Drawings, Product Data and Samples, but only for conformance with the design concept of the Work and with the information given in the Contract Documents. Such action shall be taken with reasonable promptness so as to cause no delay. The Architect/Engineer approval of a specific item shall not indicate approval of an assembly of which item is a component.

3.2.6 The Architect/Engineer along with the Designated Representative will conduct inspections to determine the dates of Substantial Completion and Final Completion and will receive and review written warranties and related documents required by the Contract and assembled by the Contractor.

3.2.7 Architect/Engineer shall prepare and deliver to the Owner a set of reproducible mylar record construction drawings and record construction specifications showing significant changes in the Work during the construction process based upon marked up prints of drawings and other data provided by the Contractor through the Designated Representative.

3.2.8 The Architect/Engineer will communicate with the Contractor through the Designated Representative.

3.2.9 The Architect/Engineer will visit the site at intervals appropriate to the stage of construction to become generally familiar with the progress and quality of Work and to determine in general if the Work is being performed in a manner indicating that the Work, when completed, will be in accordance with the Contract Documents. However, the Architect/Engineer will not be required to make exhaustive or continuous on-site inspections to check quality or quantity of the Work. On the basis of on-site observations as an Architect/Engineer, the Architect/Engineer will keep the Owner informed of progress of the Work and will endeavor to guard the Owner against defects and deficiencies in the Work.

3.2.10 The Architect/Engineer will not have control over or charge of and will not be responsible for construction means,

methods, techniques, sequences or procedures, or for safety precautions and programs in connection with the Work, since these are solely the Contractor's responsibility as provided in Paragraph 5.3. The Architect/Engineer will not be responsible for the Contractor's failure to carry out the Work in accordance with the Contract Documents. The Architect/Engineer will not have control or charge of and will not be responsible for acts or omissions of the Contractor, Subcontractor, or their agents or employees, or of any other persons performing portions of the Work.

3.2.11 The Architect/Engineer has no authority to issue change orders. All requests for proposals shall be prepared by the Architect/Engineer, shall be approved by the Owner or Director of General Services, and shall be issued to the Contractor through the Designated Representative.

ARTICLE 4: DESIGNATED REPRESENTATIVE

4.1 DEFINITION

4.1.1 The Designated Representative is the person or entity who has been identified in writing by the Owner to serve as Designated Representative and is referred to throughout the Contract Documents. When the Designated Representative is an entity, the term Designated Representative includes the Designated Representative acting through its authorized representatives as indicated to the Contractor in writing at the preconstruction meeting or whenever changes in personnel assignments occur.

4.2 ADMINISTRATION OF THE CONTRACT

4.2.1 The Designated Representative will provide, as the Owner's authorized representative, the general administration of the Project as herein described.

4.2.2 The Designated Representative will be the Owner's construction representative during the construction until final payment and shall have the responsibility to monitor the Work of the Contractor.

4.2.3 The Designated Representative shall monitor the Work to be performed through completion. The Designated Representative's activities shall in no way supersede or dilute the Contractor's obligation to perform the Work in conformance with all contract requirements, but s/he is empowered, by the Owner, to act on its behalf with respect to the proper execution of the Work and shall give instructions to require such corrective measures as may be necessary, in its opinion, to ensure the proper execution of the contract or to protect the Owner's interest. The Designated Representative shall have the authority to require prompt execution of Work whenever such action may be necessary, in its opinion, to ensure the proper execution of the Work or to protect the interests of the Owner. Except as otherwise provided herein, the Designated Representative shall determine the amount, quality, acceptability, fitness and progress of the Work covered by the Contract without, however, assuming any of the Architect/Engineer's statutory or customary obligations.

4.2.4 The Designated Representative shall be deemed to be the Owner's Representative to the extent set forth below and elsewhere in this Contract. The Designated Representative shall have no authority to obligate or otherwise bind the Owner.

4.2.5 The Designated Representative shall review and monitor the Contractor's Work and construction schedule and establish specific measures and actions which the Contractor shall take to maintain the current approved schedule.

4.2.6 The Designated Representative shall examine the Contractor's Work to determine if the construction conforms to the requirements of this Contract (provided, however, that such action by the Designated Representative shall not supersede or diminish the Contractor's obligation to furnish materials and perform the Work in conformity with all requirements of this Contract).

4.2.7 The Designated Representative shall determine any corrective measures which may be necessary to bring the Contractor's performance into conformity with Contract requirements.

4.2.8 The Designated Representative shall monitor the Contractor's performance in coordinating the Contractor's Work under this Contract with the Work being performed or to be performed by other separate contractors.

4.2.9 The Designated Representative shall assist the Owner and the Architect/Engineer in the resolution of questions of Contract interpretation. If the Contractor either disagrees with the Designated Representative's interpretation or considers that such interpretation constitutes a constructive change in Contract requirements, the question shall be referred to the Owner for contract interpretation.

4.2.10 The Designated Representative shall establish and recommend administrative procedures for coordinating the activities of the Contractor, the Designated Representative, the Architect/Engineer and the Owner.

4.2.11 The Designated Representative shall monitor the Contractor's submittal schedule.

4.2.12 The Designated Representative shall coordinate the activities of the Testing Agencies with the activities of the Contractor.

4.2.13 The Designated Representative shall review all requests or recommendations for changes affecting this Contract, review proposals, assist in negotiating and submit recommendations thereon to the Owner.

4.2.14 The Designated Representative shall make recommendations, together with the Architect/Engineer where appropriate, to the Owner as to the qualifications of Subcontractors or Suppliers wherever submittals of Subcontractors and Suppliers are required to be furnished under this contract.

4.2.15 The Designated Representative shall transmit to the Owner all written guarantees and warranties which the Contractor is required to furnish under this contract.

4.2.16 The Designated Representative may call meetings which shall be attended by the Contractor, Subcontractors and Material Suppliers, as the Designated Representative may deem necessary.

4.2.17 The Designated Representative shall have the authority to reject Work which does not conform to the Contract Documents and to require any Special Inspection and Testing in accordance with Subparagraph 8.7.2.

4.2.18 The Designated Representative shall review all applications by the Contractor for progress payments and final payment and make recommendations to the Architect/Engineer and Owner for approval thereof in accordance with the Owner's procedures.

4.2.19 The Designated Representative along with the Architect/Engineer will conduct inspections to determine the dates of Substantial Completion and Final Completion and will receive and review written warranties and related documents required by the Contract and assembled by the Contractor.

4.2.20 In the event any claim is made or any action brought in any way relating to the design or construction of the Project, the Designated Representative will render to the Owner any and all assistance required of it.

4.2.21 The Owner may, at his option, designate the Designated Representative as its representative to perform additional functions, including functions for which other authorized representatives may be designated by the provisions of this contract.

4.2.22 It shall be the duty of the Contractor to comply with all procedures established and implemented by the Designated Representative and approved by the Owner as stated above. In the event any such procedures are at a variance with other provisions of the Contract Documents, such procedures shall prevail.

4.2.23 The Designated Representative shall, at all times, have access to the Work wherever it is in preparation and progress. When directed by the Designated Representative, the Contractor shall provide facilities for such access so the Designated Representative may perform its functions under the Contract Documents.

4.2.24 In no event shall any act or omission on the part of the Designated Representative relieve the Contractor from its obligation to perform its Work in full compliance with the Contract.

4.3 OWNER'S AND DESIGNATED REPRESENTATIVE'S RIGHT TO STOP WORK

4.3.1 If the Contractor fails to correct defective Work as required by Paragraph 14.2 or persistently fails to carry out the Work in accordance with the Contract Documents, the Designated Representative or the Owner through the Designated Representative may order the Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated.

4.3.1.1 The Contractor shall bear all costs of such Work stoppage unless it is determined that no fault existed in the Contractor's Work. Any Work stoppage for the correction of defective Work or removal and replacement of unacceptable materials and equipment will not be considered as the basis for any time extension.

4.3.2 If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Document and fails within 48 hours after receipt of written notice from the Designated Representative to commence and continue correction of such default or neglect with diligence and promptness, the Designated Representative may, by written notice and without prejudice to any other remedy he or the Owner may have, make good such deficiencies. In such case an appropriate Change Order shall be issued deducting from the payments then or thereafter due the Contractor the cost of correcting such deficiencies, including compensation for the Architect/Engineer's and the Designated Representative's additional services made necessary by such default, neglect or failure.

4.3.3 The relationship of the Designated Representative to the Owner may be that of an independent contractor and the Designated Representative shall have no authority to bind the Owner in any way with the Contractor, its subcontractors, materials suppliers or any third parties.

ARTICLE 5: CONTRACTOR

5.1 DEFINITION

5.1.1 A Contractor is the person or entity identified as such in the Agreement between the Owner and a Contractor and is referred to throughout the Contract Document as if singular in number and masculine in gender. The term Contractor means the Contractor or its authorized representative.

5.1.2 It is the duty of the Contractor to comply with all procedures established and implemented by the Designated Representative and approved by the Owner as stated herein.

5.2 REVIEW OF CONTRACT DOCUMENTS

5.2.1 The Contractor shall carefully study and compare the Contract Documents, shall investigate existing site conditions, and shall at once report to the Designated Representative any error, inconsistency or omission he may or reasonably should discover.

5.2.2 All soil and test borehole data, water table elevations, and soil analyses shown on the drawings or included in the specifications apply only at the locations of the test holes and to the depths indicated. Soil test reports for the test holes which have been drilled are available for inspection at the office of the Director of General Services. Any additional subsurface exploration shall be done by bidders or the Contractor at their own expense.

5.2.3 The indicated elevation of the water table is that existing at the date the test hole was determined. It is the Contractor's responsibility to determine and allow for the elevation of groundwater at the date of project construction. A difference in elevations between groundwater shown in soil boring logs and groundwater actually encountered during construction will not be considered as a basis for extra work.

5.3 SUPERVISION AND CONSTRUCTION PROCEDURES

5.3.1 The Contractor shall supervise and direct the Work, using the best skill and attention. He shall be solely responsible for all construction means, methods, techniques, sequences and procedures and for coordinating all portions of the Work under the Contract.

5.3.1.1 The Designated Representative may reject any means, methods, techniques, sequences or procedures proposed by the Contractor, which might constitute or create a hazard to the Work or to persons or property, or which will not provide Work in accordance with the Contract Documents. However, neither the Designated Representative's acceptance of nor its failure to reject any means, methods, techniques, sequences and procedures shall relieve the Contractor of its responsibilities to safely and properly complete the Work.

5.3.2 The Contractor shall be responsible to the Owner and the Designated Representative for the acts and omissions of its employees and all its Subcontractors and their agents and employees and other persons performing any of the Work under a contract with the Contractor.

5.3.3 Neither observations, inspections, tests or approvals by persons other than the Contractor shall relieve the Contractor from its obligations to perform the Work in accordance with the Contract Documents.

5.3.4 The Contractor shall do and be responsible for the correct horizontal and vertical layout out and completion of the Work as per the drawings and written instruction of the Designated Representative including all necessary leveling and checking. The Contractor shall protect and preserve all permanent survey monuments or bench marks and shall bear the expense of replacing any that may be disturbed without permission of the Designated Representative. Replacement of damaged permanent survey monuments or benchmarks shall be performed by a licensed land surveyor hired by the Owner.

5.3.5 The Contractor shall keep the Designated Representative informed of the plan and progress of its Work. No Work shall be closed or covered until it has been duly inspected and approved. Should uninspected Work be covered, the Contractor shall, at its own expense, uncover all such Work so that it can be properly inspected; and after such inspection, he shall properly repair and replace all such Work.

5.4 LABOR AND MATERIALS

5.4.1 The Contractor shall provide and pay for all labor, equipment, tools, construction equipment and machinery, transportation and other facilities and services necessary for the proper execution and completion of the Work, whether temporary or permanent and whether or not incorporated or to be incorporated in the Work.

5.4.1.1 The Contractor shall accept delivery and store, protect and provide security for any Owner-purchased materials, systems and equipment which are a part of the Work until such items are incorporated into the Work. The Contractor shall document receipt of such materials, systems and equipment on forms acceptable to the Designated Representative.

5.4.1.2 The Contractor shall furnish, install, connect, make operable, and test all heating, ventilating and air conditioning equipment, plumbing fixtures, lighting fixtures, kitchen equipment, and any other mechanical or electrical equipment shown on the plans or called for in the specifications or change orders. In connection therewith, the Contractor shall also furnish and install all necessary devices, hardware, and systems required to make said equipment properly and safely operable including, but not limited to, mounting hardware and framing, insulation, vibration control devices, duct systems, gas piping systems, hot and cold water systems, venting ducts, control systems, and electrical circuits.

5.4.1.3 The Contractor shall furnish and install complete utility systems ready for use and shall pay any special fees, permits or assessments required by the serving utility.

5.4.2 The Contractor shall at all times enforce strict discipline and good order among its employees and shall not employ on the Work any unfit person or anyone not skilled in the task assigned to him.

5.4.2.1 Any person employed, who is found to be incompetent, intemperate, troublesome, disorderly or otherwise objectionable, or who fails or refuses to perform its work properly and acceptably, shall be immediately removed from the work by the Contractor and not be re-employed on the work.

5.4.2.2 The Owner may remove and may order the Contractor to remove any person who is incompetent or otherwise objectionable from the site of the Work.

5.4.3 Approval of the Architect/Engineer under any substitution clause shall be obtained in writing before any substitution is made. In the event of the Contractor failing to obtain such approval, no consideration will be given to any appeal from the decision of the Architect/Engineer condemning any materials furnished.

5.4.4 Pursuant to the Public Contract Code, any reference in the specifications and plans to any brand name, article, device, product, materials, fixture, form or type of construction by brand name, make, or catalog number, such references shall be interpreted as establishing a standard of quality and shall not be construed as limiting competition; and the Contractor, in such cases, may at its option use any article, device, product, materials fixture, form or type of construction which in the judgment of the Architect/Engineer expressed in writing is equal to that specified. The Contractor must within forty (40) days after award of the Contract submit data substantiating a request for substitution.

5.4.5 If the Contractor proposed to use a material which, while suitable for the intended use, deviates in any way from the detailed requirements of the Contract Documents he shall inform the Architect/Engineer through the Designated Representative in writing of the nature of such deviations at the time that the materials are submitted for approval and shall request a written approval of the deviation from the requirements of the Contract Documents.

5.4.6 In requesting approval of deviations or substitutions, the Contractor shall provide evidence leading to a reasonable certainty that the proposed substitutions or deviation will provide a quality of result at least equal to that otherwise attainable. If, in the opinion of the Architect/Engineer, the evidence presented by the Contractor does not provide a sufficient basis for such reasonable certainty, the Architect/Engineer may reject such substitution or deviation without further investigation.

5.4.7 The Architect/Engineer will judge the design and appearance of proposed substitutes on the basis of their suitability in relation to the overall design of the project, as well as for their intrinsic merits. The Architect/Engineer will not approve proposed substitutes as equal to items specified which, in its opinion, would be unharmonious, or otherwise inconsistent with the character or quality of design of the project.

5.4.8 Any additional cost, or any loss or damage, arising from the substitution of any material or method for those originally specified or drawn shall be borne by the Contractor, notwithstanding approval or acceptance of such substitution by the Owner or Architect/Engineer, unless such substitution was made at the written request or direction of the Owner or Architect/Engineer.

5.4.9 The investigation, review and approval of substitute materials requires a minimum of 30 calendar days additional time more than for specified items. The Contractor is required to assure the time impact will not delay its or other Contractor's Work when submitting (proposing) a substitution. Submittal of a substitution will be promptly rejected if the Contractor does not accept the delay responsibility in making its submittal.

5.4.10 The Contractor, its agents and employees shall be bound by and comply with all applicable provisions of the California Labor Code, and with Federal, State, and local laws related to labor.

5.4.11 The Contractor shall strictly adhere to the provisions of the California Labor Code regarding minimum wages, the eight-hour day and the forty-hour week, overtime, Saturday, Sunday, and holiday work and non-discrimination because of race, color, national origin, religion, sex, age, or physically handicapped when otherwise qualified. The Contractor shall forfeit to the Owner the penalties prescribed in the California Labor Code for violations.

5.4.12 The Contractor, as required by the California Labor Code, Sections 1770 et seq., the Contractor shall pay not less than the prevailing rate of per diem wages for each classification of worker employed as determined by the Director of the California Department of Industrial Relations. A copy of the general prevailing rate of per diem wages is available at the General Services Department to be viewed upon request. The Contractor shall post a copy of such wage determination at each job site.

5.4.13 As provided in Section 1775 of the California Labor Code, as a penalty, the Contractor shall forfeit twenty-five dollars ($25.00) for each calendar day, or portion thereof, for each worker paid less than the prevailing rates for such work or craft in which such worker is employed for any public work done under the Contract by the Contractor or any Subcontractor under him.

5.4.14 The Contractor shall submit completed Payroll Reporting Forms for all Tradesmen employed on the Work with the monthly Progress Payment Application.

5.4.15 Payroll Reporting Forms shall be the forms prescribed by the Owner or computer generated payroll reporting forms

which have been approved in writing by the Owner or the Designated Representative.

5.4.16 The Contractor's attention is directed to Sections 1777.5, 1777.6, and 1777.7 of the California Labor Code and Title 8, California Administrative Code Section 200 et seq.

5.4.17 To ensure compliance and complete understanding of the law regarding apprentices, and specifically the required ratio thereunder, the Contractor and Subcontractors should, where some question exists, contact the Division of Apprenticeship Standards prior to commencement of the Work. Responsibility for compliance with the law lies with the Contractor.

5.4.18 The Owner's policy is to encourage the employment and training of apprentices in its construction contracts as may be permitted under local apprenticeship standards.

5.4.19 As required by Section 1773.8 of the California Labor Code, the Contractor shall pay travel and subsistence payments to each worker needed to execute the Work, as such travel and subsistence payments are defined in the applicable collective bargaining agreements filed in accordance with this section.

5.4.20 To establish such travel and subsistence payments, the representative of any craft, classification, or type of workman needed to execute the Work shall file with the Department of Industrial Relations fully executed copies of collective bargaining agreements for the particular craft classification or type of work involved. Such agreements shall be filed within ten (10) days after their execution and thereafter shall establish such travel and subsistence payments whenever filed thirty (30) days prior to the call for bids.

5.4.21 The Contractor shall comply with all applicable provisions of Sections 1810 to 1815, inclusive of the California Labor Code relating to working hours. As a penalty, the Contractor shall forfeit twenty-five dollars ($25.00) for each worker employed in the execution of the Work by the Contractor or by any Subcontractor for each calendar day during which such work is required or permitted to work more than eight (8) hours in any one calendar day and forty (40) hours in any one calendar week, unless such worker receives compensation for all hours worked in excess of these limits at not less than one and one half (1.5) times the basic rate of pay.

5.5 WARRANTIES AND GUARANTEES

5.5.1 The Contractor, prior to or at the time of Substantial Completion for the Work and during administrative closeout of the project, shall submit one (1) digital copy of all warranties and guarantees to the Designated Representative for subsequent transmittal to the Architect/Engineer and Owner. All guarantees and warranties shall be in writing on guarantors'/warrantors' stationery or official forms and signed by a responsible company official, and shall be submitted in full force and effect by the Contractor.

5.5.1.1 The Contractor warrants to the Owner and the Designated Representative that all installed materials and equipment will be new unless otherwise specified and that all Work will be of good quality, free from faults and defects and in conformance with the Contract Documents. All Work not conforming to these requirements, including substitutions not properly approved or authorized, shall be considered defective unless specifically accepted by the Owner. If required by the Designated Representative, the Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment. This warranty is not limited by the provisions of Paragraph 14.2.

5.5.1.2 The warranty of materials, equipment and workmanship defined in 5.5.1 is separate from, independent of and in addition to any other guarantees in this contract or any other warranties required by the Contract Documents.

5.5.1.3 Except as otherwise specified, all Work shall be guaranteed by the Contractor against defects resulting from the use of inferior materials, equipment or workmanship for one year from the date of Substantial Completion of the Project and acceptance/occupancy by the Owner in writing, provided that if prior to the acceptance of the entire project, the Owner occupies or uses any separate unit of Work, the guarantee period shall, as to the unit so occupied or used, commence on the date of such occupancy or use, with the further provision that the Owner shall have first agreed in writing that the separate unit shall be occupied or used by the Owner until such certificate has been given. Equipment and facilities, which have seasonal limitations on their operations, shall be guaranteed for one full year from the date of test and acceptance in writing by the Owner.

5.5.1.4 If within any guarantee period, repairs or changes are required in connection the guaranteed Work, as the result of the use of materials, equipment or workmanship which are defective or inferior or not in accordance with the terms of the Contract, the Contractor shall, promptly, within 48 hours after receipt of notice from the Designated Representative or Owner and without expense to the Owner or the Designated Representative, commence and continue to effect such repairs or changes.

(a.) The Contractor shall place in satisfactory condition, in every particular, all of such guaranteed Work and correct all defects therein.

(b.) The Contractor shall make good all changes to the structure or site or equipment or contents thereof, which, in the opinion of the Architect/Engineer and the Designated Representative is the result of the use of materials, equipment or workmanship which are inferior, defective or not in accordance with the terms of the Contract. The Contractor shall make good any Work or materials, or the equipment and contents of structures or site disturbed in fulfilling such guarantee.

(c.) Notifications by Owner of defects shall stop the warranty time period. The guarantee or warranty period for that replaced or restored Work shall be reinstated for the remaining time period, starting on the date of acceptance of the replaced or restored Work.

5.5.1.5 In any case, where in fulfilling the requirement of the Contract or of any guarantee embraced in or required thereby, the Contractor disturbs any Work guaranteed under another contract, he shall restore such Work to a condition satisfactory to the Architect/Engineer and the Designated Representative and guarantee such restored Work to the same extent as it was guaranteed under such other contract.

5.5.1.6 If the Contractor, after notice, fails to proceed within 48 hours to commence and continue to comply with the terms of the guarantee, the Owner or Designated Representative may have the defect corrected in which case the Contractor and its surety shall be liable for all expenses incurred.

5.5.1.7 All special guarantees or warranties applicable to definite parts of the Work that may be stipulated in the Specifications or other papers forming a part of the Contract shall be subject to the terms of the Subparagraph 5.5.1.2 during the first year of the life of such special guarantee.

5.5.1.8 Nothing contained in Subparagraph 5.5.1 shall be construed to establish a period of limitation with respect to any other obligation which the Contractor might have under the Contract Documents, including liability for defective Work under Subparagraph 5.5.1. Subparagraph 5.5.1 relates to the specific obligation of the Contractor to correct the Work and does not limit the time within which its obligation to comply with the Contract Documents may be sought to be enforced, nor of the time within which proceedings may be commenced to establish the Contractor's Liability with respect to its other obligations under this contract.

5.5.1.9 In the event the Work of the Contractor is to be modified by another Contractor, either before or after the Inspection provided for in Subparagraph 10.7.1, the first Contractor shall remain responsible in all respects under the warranty given in Paragraph 5.5 and under any other warranties provided in the General Conditions or by law. However, the first Contractor shall not be responsible for any defects in materials or workmanship introduced by the Contractor modifying its Work. Both the first Contractor and the Contractor making the modifications shall be responsible solely for the Work done by each. The Contractor modifying the earlier Work shall be responsible for any damage to or defect introduced into the Work which it is modifying.

5.5.1.10 Warranties and guarantees shall clearly define what is to be guaranteed; the extent, terms, conditions, time and effective dates.

5.5.1.11 Copies of the same warranties and guarantees shall be included in the "Owner's Maintenance Manual" as specified herein.

5.5.2 The Owner shall schedule an end of warranty review meeting with the Designated Representative, Architect/Engineer, and Contractor prior to the end of one year warranty to determine any work requiring correction.

5.6 CONTROL OF OPERATIONS AND EMPLOYEES

5.6.1 The Contractor shall not use any of the existing Owner's facilities, such as, but not limited to, toilets, cafeteria, parking areas, power hookup, except with the Owner's written approval.

5.6.2 The Contractor shall confine and perform its operations in those areas where construction is required. Contractor shall protect the contiguous non-construction property. The Contractor shall protect from damage all existing trees, utilities, or other improvements at the site. Should damage result from the Contractor's failure to exercise reasonable care in the performance of its Work, the Contractor shall repair or restore any such damage at its own expense.

5.6.3 Obnoxious behavior or possession or consumption of alcoholic beverages or drugs on the premises is strictly prohibited. Violators shall be promptly discharged from the site and may be subject to prosecution.

5.6.4 All vehicular aisles and walking paths at the site where Work under the Contract is being performed are for the general use and the Contractor's operations must conform to the Owners regulations and requirements to keep areas free of obstructions. If the Work of a Contractor requires that such aisles and paths be temporarily discontinued, after obtaining Designated Representative's approval, the Work shall be done expeditiously and alternate vehicular routes and paths of travel shall be identified by such Contractor and maintained as directed.

5.6.4.1 To minimize public inconvenience and possible hazards and to restore work areas to their original condition and former state of usefulness as soon as practicable, the Contractor shall diligently prosecute the work to completion. If, in the Designated Representative's opinion the Contractor fails to prosecute the work to the extent that the above purposes are not being accomplished, the Contractor shall, upon orders from the Designated Representative, immediately take the steps necessary to fully accomplish said purposes. All costs of prosecuting the work as described herein shall be borne by the Contractor. Should the Contractor fail to take the necessary steps to fully accomplish said purposes, after orders of the Designated Representative to do so, the Owner may suspend the work in whole or in part, until the Contractor takes said steps.

5.6.4.2 If work is suspended through no fault of the Owner, all expenses and losses incurred by the Contractor during such suspensions shall be borne by him. If the Contractor fails to properly provide for public safety, traffic, and protection

of the work during periods of suspension, the Owner may elect to do so, and deduct the cost thereof from monies due the Contractor. Such action will not relieve the Contractor from liability.

5.6.5 The Contractor shall not disturb any existing structure, piping, apparatus or other Work unless expressly required by the contract. Where cutting, drilling or removals are required in existing walls, floor or roof construction, the Work shall be done in such a manner to safeguard and not endanger the structure and shall in all cases be as approved by the Owner and Designated Representative. Prior to any cutting, drilling or removals, the Contractor shall investigate both sides of the surface involved, shall determine the exact location of adjacent structural members by visual examination and shall avoid interference with such members. No structural members, such as joists, beams or columns supporting Work that are to remain shall be cut, drilled or removed unless such conditions are shown in detail on the Drawings and reinforcing of members affected or new members to compensate for such cutting, drilling and removals are shown. If unforeseen obstructions are encountered, the Contractor shall take all precautions necessary to prevent damage and shall apply for and obtain full instructions from the Designated Representative, in writing, before proceeding with the Work.

5.6.6 Rights of way or easements for the improvement as shown on the plans will be provided by the Owner. Unless otherwise provided, the Contractor shall make its own arrangements, pay for, and assume all responsibility for acquiring, using, and disposing of additional work areas and facilities temporarily required by him. The Contractor shall indemnify and hold the Owner, Designated Representative, and Architect/Engineer harmless from all claims for damages occasioned by such actions.

5.6.7 The Contractor shall remove and dispose at no cost to the Owner and with the Owner's approval, existing improvements for which no specific disposition is made on the plans but which could interfere with the work.

5.7 PERMITS, FEES AND NOTICES

5.7.1 Unless otherwise provided in the Contract Documents, the Contractor shall secure and pay for all permits including encroachment permits, governmental fees, licenses and inspections necessary for the proper execution and completion of this Work, which are customarily secured after execution of the contract and which are legally required at the time bids or proposals are received.

5.7.1.1 The Project pays County Building Permit Fees.

5.7.1.2 The Owner will pay for building permits required by other governmental entities.

5.7.1.3 The Contractor shall sign for all building permits and shall be responsible for all inspections required.

5.7.2 The Contractor shall give all notices and comply with all laws, ordinances, rules, regulations and orders of any public authority bearing on the performance of the Work.

5.7.3 Unless otherwise provided in the Contract Documents, it is the responsibility of the Contractor to make certain that the Contract Documents are in accordance with the applicable laws, statutes, building codes and regulations. If the Contractor observes that any of the Contract Documents are at variance therewith in any respect, he shall promptly notify the Designated Representative in writing and any necessary changes shall be by appropriate Modification.

5.7.4 If the Contractor performs any Work knowing it to be contrary to such laws, ordinances, rules and regulations and without such notices to the Designated Representative he shall assume full responsibility therefore and shall bear all costs attributable thereto.

5.8 ALLOWANCES

5.8.1 The Contractor shall include in the Contract Sum as defined in Subparagraph 10.1.1, all allowances stated in the Contract Documents. Items covered by these allowances shall be supplied for such amounts and by such persons as the Designated Representative may direct, but the Contractor will not be required to employ persons against whom he makes a reasonable objection.

5.8.2 Unless otherwise provided in the Contract Documents, all allowances shall cover the cost to the Contractor, less applicable trade discount, of the materials and equipment required by the allowances delivered at the site and all applicable taxes.

5.8.3 Unless otherwise provided in the Contract Documents, the Contractor's costs for unloading and handling (including hoisting) on the site, labor, installation costs, overhead, profit and other expenses contemplated for the original allowance shall be included in the Contract Sum and not in the allowance.

5.8.4 Unless otherwise provided in the Contract Documents, whenever the cost is more than or less than the allowance, the Contract Sum shall be adjusted accordingly by Change Order, the amount of which recognizes changes, if any, in handling costs on the site, labor, installation costs, overhead, profit and other expenses.

5.9 SUPERINTENDENT

5.9.1 The Contractor shall employ an experienced, competent superintendent and necessary assistants who shall be in attendance at the Project site full time during the progress of the Work until the date of Substantial Completion and

for such additional time thereafter as the Designated Representative may deem necessary for the expeditious completion of the Work. The superintendent shall be satisfactory to the Designated Representative and shall not be changed without the consent of the Designated Representative, unless the superintendent proves to be unsatisfactory to the Contractor or ceases to be in its employ. The superintendent shall represent the Contractor and all communications given to the superintendent shall be as binding as if given to the Contractor. Important communications shall be confirmed in writing. Other communications shall be so confirmed on written request in each case.

5.9.2 The Contractor shall submit a job organization chart and resumes which identify the key personnel he intends to assign to the project, to the Designated Representative within 48 hours after receipt of the Notice to Proceed. The Owner, acting through the Designated Representative, reserves the right to approve the Contractor's proposed personnel and anyone not so approved shall be immediately replaced by someone acceptable. If in the course of construction, the Owner, on advice of the Designated Representative, determines that it would be in its best interest to request a change in the Contractor's personnel, he may do so; and the Contractor shall immediately assign a suitable replacement who is acceptable to the Owner and the Designated Representative at no additional cost.

5.9.2.1 A duly authorized representative of the Contractor shall be available for emergency telephone communication from the Owner or Designated Representative on a 24 hour basis, seven days a week during the performance of the Work.

5.10 CONSTRUCTION SCHEDULE

5.10.1 Submission of Schedule and Format

5.10.1.1 Within Five **(5) calendar days** of the Notice to Proceed, the Contractor shall submit to the Designated Representative a construction Schedule covering the entire project.

5.10.1.2 The Schedule shall be prepared utilizing the critical path method of scheduling. The Schedule will show the Contractor's plan for construction in sufficient detail to indicate the sequence of construction and planned dates for achieving major milestones.

5.10.1.3 The maximum duration for any single activity will be twenty (20) working days, with the exception of "Fabrication and Delivery" activities. Although portions of the Work may take longer than 20 working days, all work shall be presented in the schedule to allow for monitoring of progress through completion of incremental activities with a duration not exceeding 5 days.

5.10.1.4 A sufficient number of activities will be carried in the schedule so that each subcontract subdivision is represented and the planned start and completion of each Subcontractor's Work can be determined.

5.10.1.5 All submittals required by the specifications will be scheduled along with the approval period (fifteen calendar days minimum) and fabrication and delivery periods.

5.10.1.6 The Contractor shall submit to the Designated Representative for approval a computer-generated critical path schedule and bar charts. The schedule shall contain the following information and shall be presented in a legible format acceptable to the Designated Representative.

(a.) The critical path schedule shall indicate for each activity:

Description
Original Duration
Remaining Duration
Percentage Complete
Total Float (critical path highlighted)
Responsibility Code (who will perform the work)
Early Start/Finish Dates (current update)
Late Start/Finish Dates (current update)
Predecessor and Successor Activities to the activity (arrow connections)

(b.) The Contractor shall submit a bar chart schedule listing all activities in the schedule as organized by responsibility, area or date as approved by the Designated Representative. The bar chart shall include all the information listed in paragraph (a.) above for each activity except the listing of predecessor and successor activities.

5.10.1.7 If construction must commence during Schedule preparation and approval period, the Contractor shall prepare a **twenty (20) calendar day schedule** to cover the initial field construction and submittals. Activities on this Schedule should have maximum durations of five (5) days to allow for monitoring of progress through completion of the incremental activities.

5.10.1.8 A copy of the Schedule shall be submitted via email to the Designated Representative for review. At the time of submittal, The Contractor's lead on-site manager or superintendent will make a presentation to the Designated Representative on the planned construction sequence/schedule. Within **Fifteen (15) calendar days** of receipt, the Designated Representative will notify the Contractor, in writing, as to any objections to the Schedule submitted. If the Schedule is deemed objectionable, the Contractor will have **five (5) calendar days** from receipt to revise the

schedule and resubmit it as above. The Contractor's presentation will include, but not be limited to:

(a.) Describing the sequence and phasing of work.
(b.) Delineating any area subdivision used to plan the work sequence/schedule.
(c.) Identifying the critical path.
(d.) Identifying when the milestone events specified herein are planned to be achieved (earliest and latest times).
(e.) Any plans for shift work, weekend work, or extended work weeks and non-work days (i.e. holidays observed).
(f.) Any planned interruptions of building power, water, communications, or other utilities.
(g.) Any assumptions used in planning and sequencing the work.
(h.) Long lead fabrication items.
(i.) Manpower projections for the project.
(j.) Noise/dust control measures.
(k.) Safety plan.
(l.) Plans for moving materials into the building and removing refuse and debris.
(m.) Any other planning information requested by the Owner or its Designated Representative prior to the presentation.

5.10.2 Updating of the Schedule

5.10.2.1 The Schedule documents will be updated monthly at a minimum to reflect progress through the "Data Date". All contract changes as they are agreed to shall be specifically incorporated into the appropriate Schedule update. The Data Date may be the last working day of the month or it may be the "closure" date of the requisition for payment, as the Contractor may choose and as approved by the Designated Representative. However, when one of the above Data Dates is selected, it will be used throughout the project. The update will be submitted within **seven (7) calendar days** following the Data Date.

5.10.2.1 The Contractor shall submit marked up copies of the approved critical path schedule and the bar chart indicating progress through the data date. If the Contractor has elected to submit a computer generated schedule, monthly update reports and schedule plots shall be submitted as directed by the Designated Representative.

5.10.3 Revision of the Schedule

5.10.3.1 Every effort shall be made by all parties to Work in accordance with the accepted Project Schedule. The Schedule will be revised only if the actual status of Work cannot be brought into conformance with the existing Schedule. If the Schedule is revised, the revised Schedule will be submitted as if any initial Schedule.

5.10.4 Minor Changes of the Schedule

5.10.4.1 The Schedule is not considered to be "revised" if the Contractor must make minor changes, such as:

(a.) Adding additional details to a sub-network to facilitate coordination of subcontract Work.
(b.) Additions/deletions/modifications of Schedule activities to reflect Work added or deleted by change order.

5.10.5 Extensions of Contract Time

5.10.5.1 All claims for extensions to contract time shall be supported by a detailed comprehensive analysis of the accepted Schedule. This analysis shall provide sufficient supporting evidence to justify a time extension. No time claims will be considered without the supporting analysis. If a time extension is granted, it shall be included in the next update of the Schedule.

5.10.6 During Construction

5.10.6.1 Construction milestone event dates will be incorporated into the detailed Construction Schedule as "target dates". These dates will be clearly noted and fixed on the Schedule graphics and corresponding computer file. It is the intent that the Work will be undertaken so as to achieve each target date and thereby achieve overall project completion as specified in the Contract.

5.10.6.2 The milestone event target dates will not be revised unless delays beyond the control of the Contractor occur.

5.10.6.3 If, when the Schedule is updated, the planned dates for achieving any milestone(s) falls more than ten (10) working days behind the target date(s), and if this has occurred through no fault of the Owner, the Architect/Engineer or their consultants, the Contractor may be directed by the Owner or the Designated Representative, to take any and all actions required to bring the actual construction back into accordance with the target dates.

5.10.6.4 When the Contractor falls behind its schedule and is not entitled to any time extension other than extensions already reflected in the current approved schedule, he shall submit its plan for bringing the Work back up to schedule and shall implement the plan. If other measures will not be sufficient to make up the lag, the Contractor's plan and implementation thereof shall include, but not be limited to increasing the number of shifts and days of Work, additional Work, additional equipment, increasing manpower and expediting deliveries, all at the Contractor's sole expense.

5.10.6.5 If the Contractor works overtime, more than forty (40) hours per week, Saturdays, Sundays or holidays; whether by choice or by necessity, the Contractor shall be responsible for the reimbursement of the Owner for additional costs

incurred for the Owner's, Designated Representative's and Architect/Engineer's overtime services.

5.10.6.6 In the event the Contractor fails or refuses to implement such measures as will bring its Work back up to conformity with the approved schedule, its right to proceed with any or all portions of the Contract requirements may be canceled or suspended; but permitting the Contractor to proceed shall in no way operate as a waiver of any rights of the Owner or deprive the Owner of its rights under any provisions of this contract.

5.10.6.7 The Contractor shall include milestone activities in the Schedule as applicable to the Work. Milestone events shall at a minimum include the following as applicable:

(a.) Demolition and Excavation complete
(b.) Start foundation concrete
(c.) Complete footings and piers
(d.) Complete all subgrade concrete construction
(e.) Each level's structural slab complete
(f.) Roof level structural slab complete
(g.) Penthouse Level structural slab complete
(h.) Begin structural steel
(i.) Complete structural steel
(j.) Complete decks/structure
(k.) Permanent power available
(l.) Temporary heating/cooling available
(m.) Begin roofing
(n.) Complete roofing
(o.) Begin exterior facades
(p.) Complete exterior facades
(q.) Begin exterior glazing
(r.) Complete exterior glazing
(s.) Building dry-in
(t.) Elevators operational
(u.) Begin mechanical/electrical/plumbing rough-in
(v.) Begin building controls
(w.) Complete building controls
(x.) System start-up
(y.) Begin partition rough-in
(z.) Complete partition rogh-in
(aa) Begin drywall
(bb) Begin finishes and millwork
(cc) Complete finishes and millwork
(dd) Begin site work and landscaping
(ee) Complete grading
(ff) Begin underground utilities
(gg) Complete underground utilities
(hh) Complete site paving
(ii) Complete landscaping
(jj) Substantial completion
(kk) Start installation of Owner furnished equipment
(ll) Project complete/beneficial occupancy

5.10.7 Owner Directed Schedule

5.10.7.1 On projects involving extensive coordination between the Contractor and the Owner's ongoing operations, the Owner may issue with the Contract Documents an Owner Directed Schedule which shall be used by the Contractor in preparing its plan of operations. The Contractor shall not deviate from the Owner Directed Schedule without the written prior approval of the Owner or Designated Representative. As indicated in Paragraph 5.10.6, the Contractor may be directed by the Owner or Designated Representative to take any and all actions required to perform the actual construction in accordance with the Owner Directed Schedule and its "target dates".

5.11 SUBMITTAL SCHEDULE

5.11.1 The Contractor shall prepare a schedule of required submittals not later than **fourteen (14) days** after the receipt of the Notice to Proceed. The schedule shall include a complete list of items requiring shop drawings, design mixes, material certification, product data, brochures, catalog cuts, etc., to be approved by the Architect/Engineer. The Contractor shall coordinate all submittals requiring approvals by code enforcement agencies and shall include these special approvals in the submittal schedule. The schedule is to be submitted on a form approved by the Designated Representative. The schedule shall be updated monthly or as required by the Designated Representative. All shop drawings and other submittals shall be accompanied by a transmittal letter and reference should be indicated to the item numbers of the above mentioned schedule. The Contractor is to indicate the following in its submittal schedule.

(a.) Description of item
(b.) Specification division, page numbers, article and paragraph
(c.) Type of submittal (shop drawings, sample, product data)

(d.) Date that submittal shall be delivered to the Designated Representative's office.
(e.) Date that Contractor must have approval.
(f.) Date that material, equipment must be on site in order to maintain the Contractor's progress schedule.

5.11.2 The Contractor's submittal schedule shall allow reasonable time (15 calendar days minimum) for review by the Designated Representative and the Architect/Engineer, and revision or correction, resubmittal and approval, sufficiently in advance of the time that the item is scheduled for incorporation into the Work.

5.11.3 The Designated Representative and the Architect/Engineer shall review the Contractor's submittal schedule for completeness, fulfillment of Specification requirements and compatibility with the anticipated construction schedule. The sequence and duration of Contractor, Architect/Engineer, Designated Representative activities on the submittal schedule may be adjusted by the Designated Representative.

5.12 DRAWINGS AND SPECIFICATIONS AT THE SITE

5.12.1 The Contractor shall maintain at the site for the Designated Representative and the Architect/Engineer, two (2) copies of all drawings, specifications, addenda, change orders, responses to requests for information, proposals and other modifications, in good order and marked currently to record all changes made during the construction, including any changes in locations, size and arrangement of the various components of the Work or any other variations from the drawings or shop drawings. The Contractor shall mark each drawing as the Work shown thereon is completed in the field, revising any or adding lines, dimensions, elevations, depths, notes or any other information required to accurately record conditions. These drawings, marked to record all changes during the construction and approved shop drawings, product data, samples, addenda, change orders, responses to requests for information, proposals and other records of modifications shall be delivered to the Designated Representative, for the Owner, upon completion of the Work.

5.12.1.1 In addition to maintaining and delivering to the Designated Representative those record drawings required by Subparagraph 5.12.1, the Contractor shall also prepare and submit to the Designated Representative, upon completion of the Work, record reproducible drawings if the technical specifications so require.

5.13 USE OF SITE

5.13.1 The Contractor shall confine operations at the site to areas approved by the Designated Representative, permitted by law, ordinances, permits and the Contract Documents and shall not unreasonably encumber the site with any materials or equipment.

5.13.2 The Contractor shall not disturb existing monuments and markers at the site. Should monuments or markers or both be disturbed at any time by the Contractor, he shall bear the cost of a licensed surveyor engaged by the Owner for the purpose of relocating such monuments or markers.

5.13.3 The Contractor shall lay out its Work and shall be responsible for the accuracy of all lines, elevations and measurements, grading, utilities and other Work executed by him under its Contract. He must exercise proper precaution to verify figures shown on drawing before laying out Work and will be held responsible for any error resulting from its failure to exercise such precaution.

5.13.4 All discrepancies shall be brought to the attention of the Designated Representative in writing for review and direction before proceeding with the Work. Should the Contractor proceed without direction, he shall be responsible to make whatever changes are necessary and pay call costs incurred by that Contractor, the Designated Representative, the Owner or other Contractors.

5.13.5 Any enclosure including safety barricades, perimeter rails, opening covers and devices required to protect the Work, workmen, materials or equipment shall be provided by the Contractor.

5.13.6 Weather protection shall be supplied by the Contractor and shall include all enclosure, supplemental heating and furnishing all other features (insulation, etc.), or meeting conditions required by the Designated Representative or by the specifications relative to the Contractor's Work, to protect the Work and any materials stored on site.

5.13.7 Protection of finished Work until acceptance shall be furnished by the Contractor.

5.14 CUTTING AND PATCHING WORK

5.14.1 The Contractor shall be responsible for all cutting or patching that may be required to complete the Work or to make its several parts fit together properly. He shall provide protection of existing Work as required.

5.14.2 The Contractor shall not damage or endanger any portion of the Work or the Work of any separate contractors by cutting, patching or otherwise altering any Work or by excavation. The Contractor shall not cut or otherwise alter the Work of any separate contractor except with the written consent of the Designated Representative and of such separate contractor. The Contractor shall not unreasonably withhold from any separate contractor its consent to cutting or otherwise altering the Work.

5.14.3 The Contractor shall not cut, weld to or otherwise alter any structural member without the written consent of the Architect/Engineer obtained through the Designated Representative.

5.15 DAILY AND FINAL CLEAN UP

5.15.1 The Contractor shall be responsible for daily and final clean up and continuous removal of all rubbish and debris from the building and site.

5.15.1.1 The Contractor at all times shall keep the premises free from accumulation of waste materials or rubbish caused by its operations. At the completion of the Work he shall remove all its waste materials and rubbish from and about the Project, as well as all its tools, construction equipment, machinery and surplus materials.

5.15.2 The job site shall be maintained in a neat and orderly condition and kept free from accumulations of waste materials and rubbish during the entire construction period. Remove all crates, cartons and other flammable waste materials or trash from the Work areas at the end of each working day to appropriate waste hauling receptacles.

5.15.3 Elevator shafts, electrical closets, pipe and duct shafts, chases, furred spaces and similar spaces which are generally unfinished, shall be cleaned and left free from rubbish, loose plaster, mortar drippings, extraneous construction materials, dirt and dust before Substantial Completion inspection.

5.15.4 The Contractor shall be responsible for the cleaning of all surfaces as necessary to make them free of spatters or other deposits of paint, plaster, mortar, concrete, adhesives, roofing, dirt, soil, oil, and all other materials foreign to the surface involved.

5.16 COMMUNICATIONS

5.16.1 The Contractor shall forward all communications to the Owner and Architect/Engineer through the Designated Representative.

5.16.1.1 The Contractor shall promptly return telephone calls or respond to any other form of communication initiated by the Designated Representative. Failure to promptly do so shall be considered lack of performance on the part of the Contractor.

5.16.1.2 All written correspondence to the Designated Representative shall be dated and signed by the Contractor or its authorized representative.

5.16.2 Weekly project progress review meetings will be conducted with Designated Representative, Architect/Engineer, their consultants as necessary, and Contractor in attendance. The Designated Representative may call for special meetings of the Contractor, Subcontractors and material suppliers as he deems necessary for the proper coordination of the Work. Such meetings shall be held at the job site on regular working days during regular working hours. Unless otherwise directed by the Designated Representative, attendance shall be mandatory for all parties notified to attend the meeting.

5.17 ROYALTIES AND PATENTS

5.17.1 The Contractor shall pay all royalties and license fees. He shall defend all suits or claims for infringement of any patent rights and shall save the Owner and Designated Representative harmless from loss on account thereof, except that the Owner shall be responsible for all such loss when a particular design, process or the product of a particular manufacturer or manufacturers is specified, but if the Contractor has reason to believe the design, process or product specified is an infringement of a patent, he shall be responsible for such loss unless he promptly gives such information to the Designated Representative.

5.18 INSURANCE

5.18.1 Indemnification

5.18.1.1 CONTRACTOR shall defend, indemnify and save harmless the COUNTY, its officers, agents and employees from any and all claims, demands, damages, costs, expenses (including attorney's fees), judgments or liabilities arising out of this Agreement or occasioned by the performance or attempted performance of the provisions hereof; including, but not limited to, any act or omission to act on the part of the CONTRACTOR or its agents or employees or other independent contractors directly responsible to him; except those claims, demands, damages, costs, expenses (including attorney's fees), judgments or liabilities resulting from the sole negligence or willful misconduct of the COUNTY.

5.18.1.2 CONTRACTOR shall notify the COUNTY immediately in the event of any accident or injury arising out of or in connection with this Agreement.

5.18.2 Insurance Requirements for Contractor

5.18.2.1 Without limiting the CONTRACTOR's indemnification of the COUNTY, CONTRACTOR shall procure the following required insurance coverage's at its sole cost and expense. All insurance coverage's are to be placed with insurers which (1) have a Best's rating of no less than A: VII, and (2) are admitted insurance companies in the State of California. All other insurers require the prior approval of the COUNTY. Such insurance coverage shall be maintained during the term of this Agreement. Failure to comply with the insurance requirements shall place

CONTRACTOR in default. Upon request by the COUNTY, CONTRACTOR shall provide a certified copy of any insurance policy to the COUNTY within ten (10) working days.

5.18.2.2 Workers' Compensation Insurance: Statutory Workers' Compensation and Employers Liability Insurance shall cover all CONTRACTOR's staff while performing any work incidental to the performance of this Agreement. The policy shall provide that no cancellation, or expiration or reduction of coverage shall be effective or occur until at least thirty (30) days after receipt of such notice by the COUNTY. In the event CONTRACTOR is self-insured, it shall furnish a copy of Certificate of Consent to Self-Insure issued by the Department of Industrial Relations for the State of California. This provision does not apply if CONTRACTOR has no employees as defined in Labor Code Section 3350 et seq. during the entire period of this Agreement and CONTRACTOR submits a written statement to the COUNTY stating that fact.

5.18.2.3 General and Automobile Liability Insurance: The general liability insurance shall include bodily injury, property damage and personal injury liability coverage, shall afford coverage for all premises, operations, products and completed operations of CONTRACTOR and shall include contractual liability coverage sufficiently broad so as to include the insurable liability assumed by the CONTRACTOR in the indemnity and hold harmless provisions [above] of the Indemnification Section of this Agreement between COUNTY and CONTRACTOR. The automobile liability insurance shall cover all owned, non-owned and hired motor vehicles that are operated on behalf of CONTRACTOR pursuant to CONTRACTOR's activities hereunder. CONTRACTORS shall require all subcontractors to be included under its policies or furnish separate certificates and endorsements to meet the standards of these provisions by each subcontractor. COUNTY, its officers, agents, and employees shall be Additional Insured status on any policy. A cross liability clause, or equivalent wording, stating that coverage will apply separately to each named or additional insured as if separate policies had been issued to each shall be included in the policies. A copy of the endorsement evidencing that the policy has been changed to reflect the Additional Insured status must be attached to the certificate of insurance. The limit of liability of said policy or policies for general and automobile liability insurance shall not be less than $1,000,000 per occurrence and $2,000,000 in the aggregate. Any deductible or Self-Insured Retention {SIR} over $10,000 requires approval by the COUNTY.

Said policy or policies shall include a severability of interest or cross liability clause or equivalent wording. Said policy or policies shall contain a provision of the following form: "Such insurance as is afforded by this policy shall be primary and non-contributory to the full limits stated in the declarations, and if the COUNTY has other valid and collectible insurance for a loss covered by this policy, that other insurance shall be excess only."

If the policy providing liability coverage is on a ‘claims-made’ form, the CONTRACTOR is required to maintain such coverage for a minimum of three years following completion of the performance or attempted performance of the provisions of this agreement. Said policy or policies shall provide that the COUNTY shall be given thirty (30) days written notice prior to cancellation or expiration of the policy or reduction in coverage.

5.18.2.4 CONTRACTOR shall submit to the office of the designated COUNTY representative certificate(s) of insurance documenting the required insurance as specified above prior to this Agreement becoming effective. COUNTY shall maintain current certificate(s) of insurance at all times in the office of the designated County representative as a condition precedent to any payment under this Agreement. Approval of insurance by COUNTY or acceptance of the certificate of insurance by COUNTY shall not relieve or decrease the extent to which the CONTRACTOR may be held responsible for payment of damages resulting from CONTRACTOR'S services of operation pursuant to the contract, nor shall it be deemed a waiver of COUNTY'S rights to insurance coverage hereunder. In the event the CONTRACTOR is not able to comply with the COUNTY’S insurance requirements, COUNTY may, at their sole discretion and at the CONTRACTOR’S expense, provide compliant coverage.

5.18.2.5 The above insurance requirements are subject to periodic review by the COUNTY. The COUNTY’s Risk Manager is authorized to change the above insurance requirements, with the concurrence of County Counsel, to include additional types of insurance coverage or higher coverage limits, provided that such change is reasonably based on changed risk of loss or in light of past claims against the COUNTY or inflation. This option may be exercised during any **amendment** of this Agreement **that results in an increase in the nature of COUNTY's risk** and such change of provisions will be in effect for the term of the **amended** Agreement. Such change pertaining to types of insurance coverage or higher coverage limits must be made by **written** amendment to this Agreement. CONTRACTOR agrees to execute any such amendment within thirty (30) days of acceptance of the amendment or modification.

5.19 CONTRACTOR QUALITY CONTROL SYSTEM

5.19.1 The Contractor shall provide and maintain an effective quality control program of Contractor inspection system, which will assure that all supplies and services required under the Contract conform to the Contract Documents whether constructed or processed by the Contractor or procured from subcontractors or vendors. The Contractor shall substantiate that all supplies and services conform to the Contract Documents and shall also perform or have performed all inspections and tests otherwise required by the Contract Documents unless the required inspection and test is specifically designated to be performed by the Owner or the Owner's designated representative. Mechanical and electrical personnel, either engineers or highly qualified technicians shall be provided during the testing, balancing, adjusting and regulating mechanical and electrical devices and systems. The Contractor's inspection system shall be documented, as specified herein, and shall be available for review by the Designated Representative prior to the start of construction and throughout the life of the Contract. The Contractor shall notify the Designated Representative in writing of any proposed change to its inspection system and change shall be subject to disapproval if they would, in the opinion of the Designated Representative, result in non-conformance

with the Contract requirements. The Contractor's inspection system shall include the minimum requirements stated below. The Contractor's full time job site superintendent may function as the Contractor's Contractor Quality Control representative.

5.19.1.1 Preparatory Inspection: The Contractor's Quality Control organization shall perform prior to the beginning any Work on any definable segment of Work; a review of contract requirements; a check to assure that all materials and equipment have been tested, submitted and approved; a check to assure that provisions have been made to provide required control testing; examination of the Work area to ascertain that all preliminary Work has been completed; and a physical examination of materials and equipment to assure that they conform to approved shop drawings or submittal data and that all material and equipment are on hand. As a part of this preparatory Work, the Contractor's Quality Control organization will review and certify all shop drawings, certificates and other submittal data prior to submission to the Designated Representative. Each submittal offered to the Designated Representative will bear the date and the signature of a member of the Contractor's Quality Control organization indicating that he has reviewed the submittal and certified it to be in compliance with the Contract Documents (or showing the required change). The Designated Representative shall be notified a minimum of seventy two (72) hours prior to the beginning of a Preparatory Inspection.

5.19.1.2 Initial Inspection: The Contractor's Quality Control organization shall perform, as soon as a representative segment of the particular item of Work has been accomplished, an examination of the quality of workmanship and a review of control testing for compliance with Contract Requirements, use of defective or damaged materials, omissions, and dimensions requirements.

5.19.1.3 Follow-Up Inspection: The Contractor's Quality Control organization shall perform daily, or as frequently as necessary, follow up inspections to assure continuing compliance with Contract Requirements, including control testing, until completion of the particular segment of the Work.

5.19.1.4 The Contractor shall maintain current records on an appropriate approved format of all inspections and tests performed. These records should provide factual evidence that the required inspections or tests have been performed, including type and number of inspections or tests involved; results of inspections or tests; nature of defects, causes for rejection, etc.; proposed remedial action and corrective actions taken. The Contractor shall not build upon or conceal any feature of the Work containing uncorrected defects, and payment on deficient items will be withheld until satisfactorily corrected or other actions taken as authorized. These records must cover both conforming and defective items and shall include a statement that all supplies and materials, incorporated in the Work, are in full compliance with the terms of the contract. Legible copies shall be furnished to the Designated Representative. The report will cover all Work placement subsequent to the previous report and will be verified by the prime Contractor's Quality Control representative. The Contractor shall include in all subcontracts, purchase orders or other agreements, either written or oral, with a commercial testing laboratory for quality control testing under the subject Contract, a requirement that copies of any test reports, data or other information relating to tests conducted by said laboratory under this Contract, be mailed simultaneously to the Designated Representative when said report, data or other information are mailed or delivered to the Contractor.

5.19.1.5 The Contractor shall establish controls necessary to assure scheduled completion dates established by the Contract are not impacted by the delinquent submittal data and operational tests. **twenty (20)** days in advance of the Substantial Completion and prior to scheduling a pre-final inspection of the Work, or any phase of Work, under the Contract, the Contractor's Quality Control organization shall submit to the Designated Representative a complete and factual report of all remaining submittals, inspections and tests required prior to acceptance of the Work. The report shall include the following:

(a.) A list of outstanding shop drawing submittals or re-submittals requiring approval by the Contractor.

(b.) A list of manuals, test reports, spare parts, keys, etc., to be furnished to the Designated Representative and scheduled submittal dates.

(c.) Schedule of required operations tests and instruction periods.

(d.) Scheduled delivery dates for materials or equipment impacting contract completion dates.

(e.) Plan of action by the Contractor for correcting all known contract deficiencies including delay in scheduled progress.

5.19.1.6 The Contractor shall maintain marked-up documents depicting Record Document conditions. These drawings will be maintained in a current condition at all times until completion of the Work and will be available for review by the Designated Representative at all times. All variations from the Contract Documents, for whatever reason, including those occasioned by the required coordination between trades, will be indicated. These variations will be shown in the same general detail utilized in the Contract Documents. Upon Substantial Completion, the marked-up documents shall be furnished to the Designated Representative for delivery to the Owner or the Owner's designated representative. The Contractor shall also furnish Record Documents as provided in the Technical Provisions of the specifications.

5.19.1.7 After the Contract is awarded and before construction operations are started, the Contractor shall meet with the Designated Representative and discuss the inspection system requirements. The meeting shall develop mutual understanding relative to details of the Contractor's Quality Control system including the form to be used for

recording the inspection, administration of the system and the interrelationship of the Contractor and the Designated Representative. The Contractor shall furnish to the Designated Representative within five (5) days after receipt of the Notice to Proceed, an inspection system plan which shall include the procedures, instructions and reports to be used. No progress payments will be processed under this Contract until the inspection plan is acceptable to the Owner and the Designated Representative. The Contractor's Quality Control plan documentation will include the following minimum elements:

(a.) The inspection organization.
(b.) Number and qualifications of inspection personnel to be used.
(c.) Authority and responsibilities of inspection personnel.
(d.) Schedule of use of inspection personnel by types and phase of Work.
(e.) Methods of inspection, including Subcontractor's work.
(f.) Test methods including as specified, name of qualified testing laboratory to be used, if applicable.
(g.) Method of documenting inspection and testing.
(h.) A copy of a letter of direction to the Contractor's Quality Control representative responsible for the quality control inspection, outlining its duties and responsibilities and signed by a responsible officer of the firm.

5.19.1.8 The Contractor's Quality Control inspection system shall provide for procedures which will assure that the latest applicable drawings, including shop drawings, specifications and instruction required by the contract, as well as authorized changes thereto, are used for fabrication, inspection and testing.

5.19.1.9 The Designated Representative and the Architect/Engineer reserves the right to inspect at source supplies or services not manufactured or performed within the Contractor's facility. The Designated Representative's and the Architect/Engineer's inspection shall not constitute acceptance, nor shall it in any way replace Contractor inspection or otherwise relieve the Contractor of its responsibility to furnish an acceptable end item. When inspection at Subcontractor's plant is performed by the Designated Representative, such inspection shall not be used by Contractor as evidence of effective inspection by such Subcontractor.

5.19.1.10 The Designated Representative may notify the Contractor or its Quality Control representative at the site of noncompliance with the foregoing provisions. This notice may be in writing by a form titled "Deficiency Correction Report" or "Notice of Noncompliance". The Contractor shall immediately, upon receipt of said notice, indicate the corrective action which will be taken and the date by which it will be complete, and submit this data for the Designated Representative's approval. If the Contractor refuses to comply promptly with these requirements, the Designated Representative may issue an order stopping all or part of the Work until satisfactory corrective action has been taken. No part of the time lost or cost of damages due to such stop orders shall be compensable and payment representing the noncompliance item and corrective action will be withheld until the Designated Representative has approved the corrective action.

5.19.1.11 Each of the Contractor's Quality Control Inspectors shall be responsible for inspecting the Work under its surveillance for compliance with OSHA Standards for the Construction Industry Section and approved safety program and shall immediately bring to the attention of the Contractor's supervisory personnel any unsafe Work conditions and instance of noncompliance noted.

5.19.2 Certificates of Compliance: The Designated Representative may require certificates of compliance with the specifications for materials or manufactured items produced outside of the job site. Such certificates will not relieve the Contractor from the requirements of providing material and manufactured items complying with the specifications even though they have been incorporated into the job.

5.19.3 Weighing Equipment: All scales used for proportioning materials shall be inspected for accuracy and certified within the past twelve (12) months by the State of California Bureau of Weights and Measures, by the County Director or Sealer of Weights and Measures, or by a Scale Mechanic registered with or licensed by the County.

5.19.3.1 The accuracy of the work of a scale service agency, except as stated herein, shall meet the standards of the California Business and Professions Code and the California Administrative Code pertaining to weighing devices. A certificate of compliance shall be presented prior to operation to the Designated Representative for approval and shall be renewed whenever required by the Designated Representative at no cost to the Owner.

5.19.3.2 All scales shall be so arranged that they may be read easily from the operator's platform or area. They shall indicate the true net weight without the application of any factor. The figures of the scales shall be clearly legible. Scales shall be accurate to within 1% when tested with the plant shut down. Weight equipment shall be so insulated against vibration or moving of other operating equipment in the plant area that the error in weighing with the entire plant running will not exceed 2% for any setting nor 1-1/2% for any batch.

5.20 COMPLETION INSPECTIONS

5.20.1 Contractor's Quality Control Completion Inspection: Based upon the Designated Representative's concurrence that the Work is nearing Substantial Completion, at least 15 days prior to pre-final inspection, the Contractor's Quality Control Inspection personnel shall conduct a detailed inspection. The Designated Representative shall be notified of the inspection date in order that he may participate, if s/he so elects. The Work shall be inspected for conformance to plans, specifications, quality, workmanship and completeness. The Contractor shall prepare an itemized list of Work not properly completed, inferior workmanship or not conforming to Contract Documents. The list shall also include outstanding administrative items such as Record Documents, operations and maintenance

manuals, spare parts, installed property list, etc. The list shall be included in the Quality Control documentation and submitted to the Designated Representative with an estimated date for correction of each deficiency within five (5) working days after conducting this inspection.

5.20.2 Pre-Final Inspection: The Contractor's Quality Control Inspection personnel, its superintendent, or other primary management person and the Designated Representative will be in attendance at this inspection. Additional Owner personnel, including but not limited to those from the Owner's General Services Department user groups, Board of Supervisors and the Architect/Engineer may be in attendance. The pre-final inspection will be formally scheduled by the Owner or the Designated Representative based upon notice from the Contractor. This notice will be given to the Owner or the Designated Representative at least **ten (10)** days prior to the pre-final inspection and must include the Contractor's assurance that all specific items previously identified to the Contractor as being unacceptable, along with the remaining Contract Work will be complete and acceptable by the date scheduled for the pre-final inspection. Failure of the Contractor to have all Contract Work acceptably complete for this inspection will be the cause of the Owner or the Designated Representative to be reimbursed by the Contractor for the additional inspection costs of the Owner or the Designated Representative. At this inspection, the Owner or the Designated Representative will develop a specific list of incomplete and unacceptable Work performed under the Contract and will subsequently furnish this list to the Contractor. Failure of the Owner or the Designated Representative to detect or list all incomplete and unacceptable Work during this inspection will not relieve the Contractor from acceptably performing all Work required by the Contract Documents. The Owner or the Designated Representative, at their option, may accept this inspection as the final acceptance inspection, if in its opinion the completion status of the inspected facilities and other Work performed under the Contract warrant this consideration.

5.20.3 Final Acceptance Inspection: The Contractor's Quality Control Inspection personnel, its superintendent or other primary management persons and the Owner or the Designated Representative will be in attendance at this inspection. Additional Owner personnel including, but not limited to, those from the Owner's General Services Department, user groups, Board of Supervisors and the Architect/Engineer may also be in attendance. The final acceptance inspection will be formally scheduled by the Owner based upon the Contractor's written assertion to the Owner that the Work is complete. This notice will be given to the Owner or the Designated Representative at least **five (5) days** prior to the final acceptance inspection and must include the Contractor's assurance that all specific items previously identified to the Contractor as being unacceptable, along with all remaining Work performed under the Contract, will be complete and acceptable by the date scheduled for the final acceptance inspection. Failure of the Contractor to have all Work acceptably complete for this inspection will be cause for the Owner and the Designated Representative to bill the Contractor for any additional inspection costs.

5.20.4 If, in the Designated Representative's judgment, the work has been completed in accordance with the plans and specifications and is ready for acceptance he will so certify to the Owner, which may accept the completed work. The Designated Representative will, in its certification to the Owner, give the date when the work was completed. This will be the date when the Contractor is relieved from responsibility to protect the work. This will also be the date to which liquidated damages will be computed.

5.21 WARRANTY OF CONSTRUCTION

5.21.1 Performance Bond: The Performance Bond shall remain in effect for a 12 month warranty period after the date of substantial completion, as determined by the County. Extended warranty periods shall be provided under manufacturer warranties, as required by project specifications.

5.21.2 In the event that the Contractor or its designated representative fails to commence and diligently pursue all Work required under Paragraph 5.5 within a reasonable time after receipt of written notification pursuant to the requirements thereof, the Owner or the Designated Representative shall have the right to demand that said Work be performed under the Performance Bond by making written notice on the surety. If the surety fails or refuses to perform the obligation it assumed under the Performance Bond, the Owner or the Designated Representative shall have the Work performed by others, and after completion of the Work, shall make demand for reimbursement of any or all expenses incurred by the Owner while performing the Work, including, but not limited to, administrative personnel.

5.21.3 Warranty repair work which arises to threaten the health or safety of personnel or the safety of property or equipment will be handled by the Contractor on an immediate basis as directed verbally by the Owner or the Designated Representative. Written verification will follow the Owner's or the Designated Representative's verbal instructions. Failure of the Contractor to respond as verbally directed will be cause for the Owner or the Designated Representative to have the warranty repair work performed by others and to proceed against the Contractor as outlined in Paragraph 5.21.2 above.

5.21.4 Pre-Warranty Conference: Prior to Substantial Completion and at a time designated by the Owner or the Designated Representative, the Contractor shall meet with the Owner or the Designated Representative to develop a mutual understanding with respect to the requirements of Paragraph 5.5 of this specification. The Owner or the Designated Representative shall establish communication procedures for the Contractor notification of warranty defects, priorities with respect to the type of defect and reasonable time required for the Contractor response and other details deemed necessary by the Owner or the Designated Representative for the execution of the construction warranty. In connection with these requirements, the Contractor will furnish the name, telephone number and address of a licensed and bonded company which is authorized to initiate and maintain warranty Work action on behalf of the Contractor. This single point of contact will be located within the local service area of the warranted construction and will be responsive to the Owner's inquiry on warranty Work action and status. This

requirement does not relieve the Contractor of any of its responsibilities in connection with Paragraph 5.5.

5.22 SUBCONTRACTS

5.22.1 Each bidder shall file with its bid the name, license number, and the location of the place of business of each subcontractor who will perform work or labor or render service to the Contractor in or about the construction of the work or improvement, or a subcontractor licensed by the State of California who, under subcontract to the Contractor, specially fabricates and installs a portion of the work or improvement according to detailed drawings contained in the plans and specifications, in an amount in excess of one-half of one percent of the Contractor's total bid. Each bidder shall state the portion of the work which will be done by each subcontractor under this act. The Contractor shall list only one subcontractor for each such portion as is defined by the Contractor in its bid.

5.22.2 In each instance, the nature and extent of the work to be sublet shall be described. The failure of the Contractor to specify a subcontractor, or the listing of more than one subcontractor for the same portion of the work, constitutes an agreement by the Contractor that he is fully qualified to perform that portion himself, and that he shall perform that portion himself.

5.22.3 The Contractor must have the written consent of the Owner to substitute a subcontractor other than that designated in the original bid, to permit any subcontract to be assigned or transferred, or to allow a subcontract to be performed by other than the original subcontractor. The Contractor shall submit an acknowledgement signed by the original subcontractor that there is no objection to its replacement by another subcontractor. Any substitution of subcontractors must comply with California Public Contract Code.

5.22.4 Subcontracting of work for which no subcontractor was designated in the original bid, and which is more than one-half of one percent of the work, will be allowed only in cases of public emergency or necessity, and then only after a finding reduced to writing as a public record of the Owner, setting forth the facts constituting the emergency or necessity.

5.22.5 Violation of any of the above provisions will be considered a violation of the Contract, and the Owner may cancel the Contract or assess the Contractor a penalty of not more than 10% of the subcontract involved.

5.22.6 All persons engaged in the work, including subcontractors and their employees, will be considered as employees of the Contractor. He will be held responsible for their work. The Owner will deal directly with, and make all payments to the Contractor.

5.22.7 When subcontracted work is not being prosecuted in a satisfactory manner, the Contractor will be notified to take corrective action. If the Owner so orders, and on receipt by the Contractor of written instructions from the Owner, the subcontractor shall be removed immediately from the work. He shall not again be employed on the work.

5.23 LAWS TO BE OBSERVED

5.23.1 The Contractor shall keep himself fully informed of State and National laws and County and municipal ordinances and regulations which in any manner affect those employed in the work or the materials used in the work or in any way affect the conduct of the work. He shall at all times observe and comply with all such laws, ordinances and regulations.

5.23.2 Santa Barbara County Ordinance 2946 Unlawful Discrimination in Employment Practices: Contractor agrees with the County of Santa Barbara that it will not discriminate against any employee or applicant for employment in violation of any applicable State or Federal laws, rules or regulations which may now or hereafter specifically prohibit such discrimination on such grounds as race, religion, sex, color, national origin, physical handicap when otherwise qualified, Vietnam era veteran/disabled or age. If it is determined by the Board of Supervisors upon recommendation of the Affirmative Action Officer and the County Counsel that during the life of this contract any such unlawful discriminations have occurred, the County Board of Supervisors may forthwith terminate this contract. Contractor further agrees that whether or not the term of this contract is still in existence at the time of final determination of such unlawful discrimination, that it will forthwith reimburse the County for any and all damages, costs and expenses incurred in connection with such unlawful discrimination, including but not limited to damages from loss of Federal or State grants, subventions or loans; costs of processing, investigating and reporting complaints of unlawful discrimination; additional costs or expenses incurred in completion of this agreement by another party if this agreement is terminated before completion; all costs of suit including reasonable attorney's fees incurred in collecting any such damages, costs and expenses; and interest at 7% on all such damages, costs and expenses from the date they are incurred to date of payment.

5.23.2.1 Employment practices shall include, but are not limited to employment, promotion, demotion, transfer, recruitment and advertising for recruitment, layoff or other termination, rates of pay, employee benefits and all other forms of compensation, selection for training and apprenticeship and probationary periods.

5.23.2.2 Contractor further agrees to permit access at all reasonable times and places to all of its records of employment advertising, application forms, tests and all other pertinent employment data and records, to the County of Santa Barbara, its officers, employees and agents for the purpose of investigation to ascertain if any unlawful discrimination as described herein has occurred or is being practiced.

5.23.2.3 Failure to fully comply with any of the foregoing provisions relating to unlawful discrimination in employment

practices shall be deemed to be a material breach of this contract.

ARTICLE 6: SUBCONTRACTORS

6.1 DEFINITION

6.1.1 A Subcontractor is a person or entity who has a direct contract with a Contractor to perform any of the Work at the site. The term Subcontractor is referred to throughout the Contract Documents as if singular in number and masculine in gender and means a Subcontractor or its authorized representative.

6.1.2 Nothing in the Contract Documents shall create any contractual relationship between the Owner, the Architect/Engineer or the Designated Representative and any Contractor, any Subcontractor, or any Sub-subcontractor or its authorized representative.

6.2 SUB-CONTRACTUAL RELATIONS

6.2.1 By an appropriate agreement, written where legally required for validity, the Contractor shall require each Subcontractor to the extent of the Work to be performed by the Subcontractor, to be bound to the Contractor, by the terms of the Contract Documents and to assume toward the Contractor all the obligations and responsibilities which the Contractor, by these documents, assumes toward the Owner, the Designated Representative or the Architect/Engineer. Said agreement shall preserve and protect the rights of the Owner, the Designated Representative and the Architect/Engineer under the Contract Documents with respect to the Work to be performed by the Subcontractor so that the subcontracting thereof will not prejudice such rights and shall allow to the Subcontractor, unless specifically provided otherwise in the Contractor-Subcontractor agreement, the benefit of all rights, remedies and redress against the Contractor that the Contractor, by these Documents has against the Owner or Designated Representative. Where appropriate, the Contractor shall require each Subcontractor to enter into similar agreements with its Sub-subcontractors. The Contractor shall make available to each proposed Subcontractor, prior to the execution of the Subcontract, copies of the Contract Documents to which the Subcontractor will be bound by this Paragraph 6.3 and shall identify to the Subcontractor any terms and conditions of the proposed Subcontract which may be at variance with the Contract Documents. Each Subcontractor shall similarly make copies of such Documents to its Subcontractors.

ARTICLE 7: SEPARATE CONTRACTS

7.1 OTHER CONTRACTORS

7.1.1 The Owner reserves the right to let other separate contracts in connection with the Work of the Project. The Contractor shall cooperate with other separate contractors and he shall afford the Designated Representative and other Contractors reasonable opportunity for the introduction and storage of their materials and equipment and execution of their Work and shall properly connect and coordinate its Work with others under the general direction of the Designated Representative. Temporary structures, equipment or materials shall be located where directed by the Designated Representative and if not so located, they shall be moved by the Contractor when directed at no additional cost.

7.2 CONTRACTOR TO INSPECT OTHER WORK

7.2.1 If any part of the Contractor's Work depends, for proper execution or results, upon the Work of the Designated Representative or any separate contractor, the Contractor shall, prior to proceeding with the Work, inspect and measure Work already in place and promptly report to the Designated Representative any discrepancies from the drawings and specifications or defects in such Work that render it unsuitable for such proper execution and results. The Contractor shall submit the report of discrepancies or defects in the form of a written request for information. Failure of the Contractor to so report shall constitute an acceptance of the other contractor's Work as fit and proper to receive its Work, except as to defect which may develop after the execution of its Work.

7.2.2 Copies of Drawings and specifications relating to these separate contracts will be available to the Contractor, upon request, for its information in carrying out the above provisions. The Contractor shall be held responsible for any damage or misfit resulting from its neglect to comply with the foregoing.

7.3 COORDINATION AND COOPERATION

7.3.1 The Contractor shall coordinate Work to be done hereunder with the Work of such other contractors in such manner as the Designated Representative may direct. The Work shall be scheduled and executed at such time and in such a way as to cause the least inconvenience to the Owner and with proper consideration for the rights of other contractors and public. The Contractor shall keep fully informed with the entire operation and install its Work promptly.

7.3.2 If the Designated Representative determines that the Contractor is failing to coordinate its Work with the Work of other contractors as directed, he may, upon written notice to the Contractor recommend the following actions by the Owner:

7.3.2.1 The Owner may withhold any payment otherwise due hereunder until the Designated Representative's directions are complied with by the Contractor.

7.3.2.2 The Owner, through the Designated Representative, may direct other contractors to perform portions of the contract and charge the cost of such Work to the contract amount.

7.3.2.3 The Owner may terminate any and all portions of the contract for the Contractor's failure to perform in accordance with the contract.

7.3.3 If the Contractor notifies the Designated Representative, in writing, that another contractor on this project is failing to coordinate its Work with the Work of this contract, as directed, the Designated Representative will promptly investigate the charge. If he finds it to be true, he will promptly issue such directions to the other contractor with respect thereto as the situation may require. The Designated Representative shall not, however, be liable for any damages suffered by this contractor by reason of the other contractor's failure to promptly comply with the directions so issued by the Designated Representative or by reason of another contractor's default in performance; it being understood that the Designated Representative does not guarantee the responsibility or continued efficiency of any contractor.

7.3.4 In the event of any labor dispute, affecting the Contractor or its employees, the Contractor shall utilize all possible means to resolve the dispute in order that the project not be delayed to any extent.

7.3.5 The Contractor shall cooperate with the Owner, the Architect/Engineer and the Designated Representative and other Contractors working on this project in order to avoid interference, inconvenience or damage. To aid in avoiding conflicts, the Contractor, without additional charge, shall make all reasonable modification in the Work as may be directed by the Designated Representative. In the event of the Contractor's operations causes any damage, interference, or inconvenience to Work being carried out under any other contract, the Contractor shall restore, replace, rectify, or otherwise make good any damage to the satisfaction of the Designated Representative or to the other contractors. Should the responsible Contractor fail to comply with this provision, the Work will be done by others at the expense of the responsible Contractor.

7.3.6 The Contractor shall ensure that all labor employed by him, its agents, or those he assigns for Work on the project shall be in harmony with and be compatible with all other labor being used by the Designated Representative or other Contractors. The Contractor shall observe hours and conditions of labor as directed by Designated Representative and in any event, in compliance with all applicable laws, ordinances and regulations. The Contractor shall coordinate its work with the work of other Contractors, the Owner and the Designated Representative and shall provide adequate information and planning of its work to allow for effective coordination by others with its operations. Whenever the Contractor has knowledge that any actual or potential labor dispute is delaying or threatens to delay the timely performance of the Work of this contract, the Contractor shall immediately give notice thereof to the Designated Representative. The Contractor shall then confirm the notice, in writing within 24 hours of the giving thereof, and shall include all relevant information with respect thereto. No claims will be accepted for costs incurred as a result of jurisdictional or labor practice disputes.

7.4 OWNER'S RIGHT TO CLEAN UP

7.4.1 If a dispute arises between the separate contractors as to their responsibility for cleaning up as required by Paragraph 5.15, the Owner may clean up and charge the cost thereof to the Contractor responsible therefore as the Owner shall determine to be just.

7.5 DAMAGES TO WORK

7.5.1 Should the Contractor wrongfully cause damage to the Work or property of the Owner or to other Work on the site, the Contractor shall promptly remedy such damage.

7.5.2 Should the Contractor wrongfully cause damage to the Work or property of any other Contractor, the Contractor shall, upon due notice, promptly attempt to settle with the other Contractor by agreement, or otherwise resolve the dispute. If such other Contractor sues the Owner or the Designated Representative or initiates any legal proceeding against the Owner or the Designated Representative on account of any damage alleged to have been caused by the Contractor, the Owner or Designated Representative shall notify the Contractor who shall defend such proceedings at the Contractor's expense and if any judgment or award against the Owner or Designated Representative arises from, the Contractor shall pay or satisfy it and shall reimburse the Owner or Designated Representative for all attorney's fees and court costs which the Owner or Designated Representative has incurred.

7.5.3 Should the Contractor sustain any damage through any act or omission of any other contractor having a contract for the performance of Work upon the site or of Work which may be necessary to be performed for the proper execution of the Work to be performed hereunder, the Contractor shall have no claim against the Owner, Architect/Engineer, Designated Representative or the Owner's consultants for such damage, but shall have a right to recover such damage from the other contractor as provided herein.

7.5.4 The Contractor shall indemnify and hold the Owner, Architect/Engineer and Designated Representative harmless from any and all claims or judgments for damages and from costs and expenses to which the Owner and Designated Representative may be subjected or which either may suffer or incur by reason of the Contractor's failure to comply with the Designated Representative's directions promptly.

ARTICLE 8: MISCELLANEOUS PROVISIONS

8.1 GOVERNING LAW

8.1.1 This contract shall be governed by the laws of the State of California.

8.2 SUCCESSORS AND ASSIGNS

8.2.1 The Owner and the Contractor each binds himself, its partners, successors, assignees and legal representatives to the other part hereto and to the partners, successors, assignees and legal representatives of such other parties in respect to all covenants, agreements and obligations contained in the Contract Documents. Neither party to the Contract shall assign the Contract nor sublet it as a whole without written consent of the other.

8.2.1.1 The Contractor shall not assign any monies due, or to become due, under this Contract without prior written consent of the Owner obtained through the Designated Representative.

8.3 WRITTEN NOTICE

8.3.1 Written notice shall be deemed to have been duly served if delivered in person to the individual or member of the firm or entity or to an officer of the corporation for whom it was intended, or if delivered at or sent by the registered or certified mail to the last business address known to him who gives the notice.

8.4 CLAIMS FOR DAMAGES

8.4.1 Should either party to the Contract suffer injury or damage to person or property because of any act or omission of the other party or of any of its employees, agents or others for whose acts he is legally liable, claims shall be made in writing to such other party within a reasonable time after the first observance of such injury or damage.

8.5 PERFORMANCE BOND AND LABOR MATERIAL PAYMENT BOND

8.5.1 The Contractor shall deliver to the Designated Representative, on forms approved by the Designated Representative and Owner, all executed and Standard Performance Bond and Standard Labor Material Payment Bond and a one (1) year Maintenance (Warranty) Bond, both with an approved surety acceptable to the Owner or Designated Representative and each payable in the amount at least equal to one hundred (100%) percent of the accepted bid as guarantee for the faithful performance of the Contractor and the payment of all persons who have, and fulfill, contracts which are directly with the successful bidder. The sureties of all bonds shall be of such security company or companies as are approved by the Designated Representative and the Owner. No Contract shall be deemed to be in effect until all bonds have been approved.

8.5.2 The insurance and bonding companies providing or underwriting such bonding shall be duly authorized and registered to do business in the State of California and shall be acceptable to the Owner and the Designated Representative.

8.5.3 The performance bond required by the Contract Documents shall remain in full force and effect during the warranty periods required by the Contract so as to give the Designated Representative and Owner recourse on the bond if the Contractor fails to remedy defects during the warranty period.

8.5.4 The Contractor's Payment and Performance Bond shall name the Owner as obligee.

8.6 RIGHTS AND REMEDIES

8.6.1 The duties and obligations imposed by the Contract Documents and the rights and remedies available there under shall be in addition to and not a limitation of any duties, obligations, rights and remedies otherwise imposed or available by law.

8.6.2 No action or failure to act by the Designated Representative, Architect/Engineer or Contractor shall constitute a waiver of any right or duty afforded any of them under the Contract Documents nor shall any such action or failure to act constitute an approval or acquiescence in any breach there under, except as may be specifically agreed in writing.

8.7 TESTS

8.7.1 If the Contract Documents, laws, ordinances, rules, regulations or orders of any public authority having jurisdiction require any portion of the Work to be inspected, tested or approved, the Contractor shall give the Designated Representative timely notice of its readiness so the Architect/Engineer and Designated Representative may observe such inspection, testing, or approval. The Owner shall bear all costs of such inspections, tests or approvals unless otherwise provided. The Contractor shall bear all costs of retesting any work failing to pass initial testing.

8.7.2 If the Architect/Engineer or Designated Representative determine that any Work requires special inspection, testing, or approval which Subparagraph 8.7.1 does not include, he will, through the Designated Representative, instruct the Contractor to prepare for such special inspection, testing or approval and the Contractor shall give notice as in Subparagraph 8.7.1 If such special inspection or testing reveals a failure of the Work to comply with the requirements of the Contract Documents, Contractor shall bear all costs thereof, including compensation for the

Architect/Engineer's and the Designated Representative's additional services made necessary by such failure. If the Work complies, the Owner shall bear such costs and an appropriate Change Order shall be issued.

8.7.3 Where operating tests are specified, the Contractor shall test its Work as it progresses, on its own account and shall make satisfactory preliminary tests in all cases before applying to the Designated Representative for official tests.

8.7.4 Official tests shall be made as directed by the Designated Representative, in the manner specified, for the different branches of the Work or portions thereof. The Contractor shall furnish all materials and apparatus, make connections and conduct the official test under the observation of the Owner's independent testing agency where appropriate. The official test will be conducted in the presence of a representative of the Designated Representative. Should defects appear, they shall be corrected by the Contractor and the official test repeated until the installation is acceptable to the Designated Representative.

8.7.5 Required certificates of inspection, testing or approval shall be secured by the Contractor and promptly delivered by him through the Designated Representative to the Architect/Engineer.

8.7.6 If the Architect/Engineer or Designated Representative is to observe the inspections, tests or approval required by the Contract Documents, he will do so promptly and, where practicable, at the source of supply.

8.7.7 The Contractor shall deliver test samples of any of the materials specified in any of the Sections of the Specifications to the Owner's testing agency. This may apply to materials proposed for use, materials already delivered to the job, or materials already incorporated into the construction.

8.7.8 Neither the observations of the Architect/Engineer or the Designated Representative in their Administration of the Construction Contract, nor inspections, tests or approvals by persons other than the Contractor shall relieve the Contractor from its obligation to perform the Work in accordance with the Contract Documents.

8.7.9 Any materials which fail to meet the requirements of these specifications shall not be used whether or not previously approved by the Architect/Engineer. If they have been delivered to the job, they shall be removed. If they have already been incorporated into the construction, the Designated Representative or Architect/Engineer may order them removed, or, at the discretion of the Owner through the Designated Representative, they may be permitted to remain in place, providing the Contractor agrees to a proper deduction from the contract sum.

8.7.10 The services of a testing and inspection engineer, selected by the Owner, Designated Representative and Architect/Engineer, shall be provided and paid for by the Owner for the tests required in the various sections, unless specifically stated otherwise or due to deficient Work.

8.7.11 No Work of any kind shall be covered or enclosed before it has been tested and approved.

8.8 ORDER OF PRECEDENCE

8.8.1 In the event of any conflict or discrepancy in the provisions of the Contract Documents, the documents shall be interpreted on the basis of the following order or priority:

(a.) Agreement between the Owner and the Contractor
(b.) Addenda, with later date having greater priority
(c.) Special Conditions
(d.) General Requirements and Other Conditions
(e.) Drawings and Specifications

8.8.2 In the case of an inconsistency between Drawings and Specifications or within either Document not clarified by addendum the better quality or greater quantity of Work shall be provided in accordance with the Architect/Engineer's and Designated Representative's interpretation.

ARTICLE 9: TIME

9.1 DEFINITIONS

9.1.1 Unless otherwise provided, the Contract Time is the period of time allotted in the Contract Documents for the Substantial Completion of the Work as defined in Subparagraph 9.1.3 including authorized adjustments thereto.

9.1.2 The date of commencement of the Work is the date established in a Notice to Proceed (NOP) from the Owner.

9.1.3 The Date of Substantial Completion of the Work or designated portion thereof is the date certified by the Architect/Engineer when construction is sufficiently complete in accordance with the Contract Documents, so that the Owner can occupy or utilize the Work or designated portion thereof for the use for which it is intended.

9.1.4 The term Day, as used in the Contract Documents, shall mean calendar day unless otherwise specifically designated.

9.2 PROGRESS AND COMPLETION

9.2.1 All time limits stated in the Contract Documents are of the essence of the Contract.

9.2.2 The Contractor shall begin the Work on the date of commencement as defined in Subparagraph 9.1.2. He shall carry the Work forward expeditiously with adequate forces and shall achieve Substantial Completion within the Contract Time. The actual date on which the Contractor starts work will not affect the required time for completion of the work.

9.2.3 The Contractor shall furnish sufficient forces, plant and equipment and shall Work such hours, including night shifts and lawful overtime operations as may be necessary to ensure the execution of the Work in accordance with the Construction Schedule. If, in the opinion of the Designated Representative, the Contractor falls behind the progress schedule, the Contractor shall take such steps as may be necessary to improve its progress and shall submit its plans demonstrating the manner in which the desired rate of progress may be regained. It shall be the responsibility of the Contractor to maintain its schedule so as not to delay the progress of the project. If the Contractor delays the progress of the project, he shall, in order to maintain the overall schedule, take all necessary actions, not limited to an increase in the number of shifts, days of Work and to the extent permitted by law, to institute or increase overtime operations, all without additional cost.

9.2.4 If the Designated Representative determines that the Contractor, without just cause, fails or refuses to employ an adequate working force, or to employ them for a maximum number of hours per day as permitted by law or by shifts of its working forces as would be sufficient, in the opinion of the Designated Representative to complete the Work in accordance with the approved project schedule or within the time to which such completion may be extended, then after formal notice to the Contractor, the Owner shall have the right to complete or to have the Work completed by such means and in such manner, by contract or otherwise, as permitted by law, as the Owner may deem advisable, utilizing for such purpose such of the Contractor's plant, materials, equipment, tools and supplies remaining on the site. Formal notice in this article shall be telegram, or registered letter to the last known business address of the Contractor.

9.2.5 The expense of such completion shall be charged against and deducted out of such money as would have been payable to the Contractor if he had completed the Work; the balance of such moneys, if any, subject to the other provisions of this contract, to be paid to the Contractor without interest after completion. Should the expense of such completion, so certified by the Designated Representative, exceed the total sum which would have been payable under this contract, if the same had been completed by the Contractor or its surety, the surety shall remit such balance due to the Owner upon its demand.

9.2.6 Whether or not the Contractor's right to proceed is terminated, he and its surety will be liable for any damage to the Owner, other Contractors and the Designated Representative from the Contractor's refusal to complete the Work in accordance with the approved progress schedule or within the time for which such completion may be extended. Formal notice in this article shall be by telegram, or registered letter to last known business address of the Contractor.

9.2.7 The permitting of the Contractor or the surety on the performance bond to proceed to complete all Work or any part of it after the date of Substantial Completion or after the date to which the time for Substantial Completion may have been extended, shall in no way operate as a waiver on the part of the Owner of any of its rights hereunder.

9.2.8 In order to expedite the completion of the Contractor's Work, the Designated Representative may direct the Contractor to Work on the basis of two (2) shifts instead of one (1) or to take such other measures as he deems necessary to expedite construction. If the need for such direction is not attributable to delays or other fault on the part of the Contractor, the Owner shall pay the Contractor any additional net cost. If, however, the Contractor is behind schedule due to its own delays or other fault on its part and the Designated Representative directs him to Work additional shifts, expedite deliveries or purchase additional materials or equipment in order to bring its Work up to schedule, all additional costs shall be borne by the Contractor.

9.2.9 With the Designated Representative's approval, the Contractor shall suspend any Work that may be subject to damage by climatic conditions. Under such conditions, the Contractor shall take measures to protect the Work and to minimize the impact on the progress of the Work.

9.3 DELAYS AND EXTENSIONS OF TIME

9.3.1 If the Contractor is delayed at any time in the progress of the Work by any act or neglect of the Owner, Designated Representative or the Architect/Engineer or by any employee of either, or by any separate contractor employed by the Owner, or by changes ordered in the Work, or by labor disputes, fire, unusual delay in transportation, adverse weather conditions not reasonably anticipated, unavoidable casualties or any causes beyond the Contractor's control, or by delay authorized by the Owner or Designated Representative pending litigation, or by any other cause which the Designated Representative determines may justify the delay, then the Contract Time shall be extended by Change Order for such reasonable time as the Director of General Services may determine.

9.3.2 Any claim for extension of time shall be made in writing to the Designated Representative not more than ten (10) days after commencement of the delay; otherwise, it shall be waived. Any claim for extension of time shall state the cause of the delay and the number of days of extension requested. If the cause of the delay is continuing, only one claim is necessary, but the Contractor shall report the termination of the cause for the delay within ten (10) days after such termination and shall simultaneously make final claim for said delay, otherwise any claim for extension of time based upon that cause shall be waived.

9.3.3 In the event of a delay attributable in part to the Contractor and in part to causes for which the Contractor is not responsible, then provided the Contractor has given proper and timely notice hereunder, the delay shall be equitably apportioned among the parties causing it and the Contractor shall remain liable for the portion not so excused.

9.3.4 If no agreement is made stating the dates upon which interpretations as set forth in Subparagraph 3.2.2 shall be furnished, then no claim for delay shall be allowed on account of failure to furnish such interpretations until fifteen days after written request is made for them and not then, unless such claim is reasonable.

9.3.5 If the Project is delayed as a result of the Contractor's refusal or failure to begin the Work on the date of commencement, as defined in Subparagraph 9.1.2, or its refusal or failure to carry the Work forward expeditiously with adequate forces, equipment, material or other resources, the Contractor shall be liable to the Owner for damages for every day Contractor's scheduled completion is exceeded, provided, however, that such refusal or failure is not the result of a justifiable delay as defined in Subparagraph 9.3.1.

9.3.6 Neither the Owner, Architect/Engineer, nor Designated Representative shall have liability to the Contractor nor to any other Contractor or subcontractor for delay, hindrance or interference in the performance of the Work, however caused, except for delay or hindrance resulting from active interference of the Owner or its representatives in such Contractor's execution of the Work.

9.3.7 In addition to damages, as defined in Subparagraph 9.3.5, the Contractor shall be liable to the Owner for any damages sustained as the result of the Contractor's refusal or failure to perform the Work, provided however that such refusal or failure is not the result of a justifiable delay as defined in Subparagraph 9.3.1

9.3.8 Contractor shall not request additional time to complete the project because of delays occurring on Sundays or holidays. Neither shall he request additional time for Saturday delays except and unless he can show proof of normally working on Saturdays in order to complete the Work on time.

9.3.9 Anticipated Normal Weather Days: The time estimated by the Contractor for completion of the entire Work ready for use shall include the number of calendar days, for anticipated delays due to normal weather conditions. No time extensions for delays due to weather will be allowed until and unless such delays exceed the time included for normal weather delays. In case of claims for extension of time because of abnormal inclement weather, such extension of time shall be granted only because such abnormal inclement weather prevented the execution of major items of Work on normal working days. A weather table reflecting the meteorological data from the Santa Barbara area is given following the General Conditions and will be used to determine any contract time extension due to abnormally inclement weather. For the purpose of this contract, "abnormal inclement weather" will be interpreted as the number of days in excess of the normal on which rainfall exceeds 0.01 inch or snow/ice pellets exceed 1.0 inch. Extension of time to complete the project will be based on actual working days, i.e., Saturdays, Sundays and holidays will be considered in granting extension of time.

9.3.10 Liquidated Damages: The Owner will suffer financial loss if the project is not substantially complete on the date set forth in the Contract Documents. The Contractor and its surety shall be liable for and pay to the Owner, hereinafter stipulated as fixed, agreed and liquidated damages for each consecutive calendar day of delay until the Work is substantially complete, the sum noted in the Notice to Bid. The Owner reserves the right to withhold the liquidated damages, incurred because of failure to complete the project on time, from the final payment to the Contractor. The Owner reserves the right to withhold liquidated damages from any progress payments occurring after the contract completion date.

9.3.11 If a suspension of work is ordered by the Designated Representative, due to the failure on the part of the Contractor to carry out orders given or to perform any provision of the contract, the days on which the suspension order is in effect shall be considered working days if such days are working days as defined.

ARTICLE 10: PAYMENTS AND COMPLETION

10.1 CONTRACT SUM

10.1.1 The Contract Sum is stated in the Agreement between the Owner and the Contractor including adjustments thereto and is the total amount payable to the Contractor for the performance of the Work under the Contract Documents.

10.1.2 Payment for work performed or materials furnished under an assessment proceedings contract will be made as provided in the particular proceedings or legislative act under which such contract was awarded.

10.1.3 Whenever any portion of the work is performed by the Owner at the Contractor's request, the cost thereof shall be charged against the Contractor, and may be deducted from any amount due or becoming due from the Owner.

10.2 SCHEDULE OF VALUES

10.2.1 Within **fifteen (15) days** after award of the contract and at least fifteen (15) days before the first Application for Payment, the Contractor shall submit to the Designated Representative a schedule of values allocated to the various portions of the Work prepared in such a form and supported by such data to substantiate its accuracy as the Designated Representative may require. This schedule, unless objected to by the Designated Representative, shall be used only as a basis for the Contractor's Application for Payment.

10.2.2 The schedule of values shall equal in total the Contract Sum and shall correctly represent a reasonable apportionment of the Contract Sum.

10.2.3 When a bid item is included in the proposal form and subject to the limitation and conditions in the contract documents, the Contractor shall itemize in the schedule of values the costs of mobilization work in advance of construction operations and not directly attributed to any specific bid item. When no such bid item is provided, payment for mobilization costs will be considered in the other items of work.

10.2.4 With said Schedule of Values contractor shall provide to Owner's Designated Representative copies of hourly wage rates for all workers in all trades associated with the job. If, during the course of construction, wage rates change, the contractor shall provide to Owner's Designated Representative copies of revised hourly wage rates the same day as said change is adopted or agreed-upon.

10.3 APPLICATION FOR PAYMENT

10.3.1 The Designated Representative will, after award of the contract, establish a closure date for the purpose of making monthly progress payments. The Contractor may request in writing that such monthly closure date be changed. The Designated Representative may approve such request when it is compatible with the Owner's payment procedures.

10.3.1.1 Each month, the Contractor will make an approximate measurement of the work performed to the closure date and as a basis for making monthly payments, estimate its value based on the contract unit prices or as provided for in the approved schedule of values.

10.3.1.2 At a fixed date each month as established by the Designated Representative during the progress of the Work, the Contractor shall render to the Designated Representative a notarized Application for Payment for a portion of the Contract Price, broken down into the categories itemized in the Contractor's Schedule of Values. The amounts invoiced shall be directly proportional to the percentage of completion of Work in each of the categories at the end of the closure date for the invoice period less any amounts previously invoiced. The Application for Payment shall be made on A.I.A. Document G702 with continuation sheets A.I.A. Document G703, or on other forms approved by the Designated Representative.

10.3.2 The Contractor shall certify monthly that he has made payment due to its Subcontractors and suppliers from the proceeds of prior payments and that he will make timely payments from the proceeds of the progress payment now due to its Subcontractor and suppliers in accordance with the contractual arrangements with them. The Contractor shall submit written certification that all amounts for equipment, materials, labor, union benefits and other services and all other items provided by the month covered by Contractor's invoice have been paid; and proof that Contractor has acquired title to the equipment and materials invoiced the previous month. Partial Waivers of Lien will be

required with the second and succeeding monthly invoices. The Designated Representative may request Record Documents, schedule updates, payrolls for all labor and other data supporting payment to Subcontractors and material suppliers before processing the requisition.

10.3.3 With respect to material purchased during the preceding month by the Contractor as Owner's special purchasing subagent, the Contractor shall provide the Designated Representative with a statement showing the costs of such materials and any state or local sales and use taxes paid by the Contractor in connection with the purchase or use thereof during the preceding month, which statement shall be supported by copies of invoices, receipts, etc., clearly and separately showing the costs of such materials and taxes. This statement shall be filed with the Designated Representative within one month after the purchase of such items.

10.3.4 Unless otherwise provided in the Contract Documents, payment will be made on account of materials or equipment not incorporated in the Work but delivered and suitably stored at the site. Payments made for materials or equipment stored on the site shall be conditioned upon submission by the Contractor of bills of sale or such other procedures satisfactory to the Designated Representative to establish the Owner's title to such materials or equipment or otherwise protect the Owner's interest. Materials invoiced in pay applications, if not stored on site, must be kept stored in a bonded warehouse approved by the Designated Representative.

10.3.5 The Contractor warrants that title to all Work, materials and equipment covered by an Application for Payment will pass to the Owner by incorporation in the construction and upon the receipt of final payment by the Contractor free and clear of all liens, claims, security interests or encumbrances, hereinafter referred to in this Article 10 as "liens" and that no Work, materials or equipment covered by an Application for Payment will have been acquired by the Contractor by any other person performing its Work at the site or furnishing materials and equipment for its Work, subject to an agreement under which an interest therein or an encumbrance thereon is retained by the seller or otherwise imposed by the Contractor or such other person. All Subcontractors and Sub-subcontractors agree that title will so pass upon their receipt of payment from the Contractor.

10.4 PROGRESS PAYMENTS

10.4.1 If the Contractor has made Application for Payment in accordance with the General Requirements, the Designated Representative will, with reasonable promptness, review and process such Application for Payment in accordance with the Contract. From each progress estimate, five (5%) percent will be deducted and retained by the Owner, and the remainder less the amount of all previous payments will be paid to the Contractor.

10.4.2 No approval of an application for a progress payment, nor any progress payment, nor any partial or entire use or occupancy of the project by the Owner, shall constitute an acceptance of any Work not in accordance with the Contract Documents. Nor shall the same relieve the Contractor or its surety from any obligation under the Contract or the Standard Performance Bond and the Standard Labor and Material Payment Bond.

10.4.3 Except in case of bona fide disputes, or where the Contractor has some other justifiable reason for delay, the Contractor shall pay for all transportation and utility services not later than the end of the calendar month following that in which services are rendered and for all materials, tools and other expendable equipment to the extent of ninety percent (90%) of the cost thereof not later than the end of the calendar month following that in which such materials, tools and equipment are delivered at the site of the Project. The Contractor shall pay to each of its Subcontractors, not later than the end of the calendar month in which each payment is made to the Contractor, the representative amount allowed the Contractor on account of the Work performed by its Subcontractors, to the extent of each Subcontractor's interest herein. The Contractor shall, by an appropriate agreement with each Subcontractor, also require each Subcontractor to make payments to its suppliers and sub-subcontractors in a similar manner.

10.4.4 Payment shall not relieve the Contractor from its obligations under the contract; nor shall such payment be construed to be acceptance of any of the work. Payment shall not be construed as the transfer of ownership of any equipment or materials to the Owner. Responsibility of ownership shall remain with the Contractor who shall be obligated to store, protect, repair, replace, rebuild or otherwise restore any fully or partially completed work or structure for which payment has been made; or replace any materials of equipment required to be provided under the contract which may be damaged, lost, stolen or otherwise degraded in any way prior to acceptance of the work under the contract, except as provided in Paragraph 10.7.2.

10.4.4.1 Guarantee periods shall not be affected by any payment but shall commence on the date equipment or material is placed into service at the direction of the Owner. In the event such items are not placed into service prior to partial or final acceptance of the project, the guarantee period will commence on the date of such acceptance.

10.4.4.2 If, within the time fixed by law, a properly executed notice to stop payment is filed with the Owner, due to the Contractor's failure to pay for labor or materials used in the work, all money due for such labor or materials will be withheld from payment to the Contractor in accordance with applicable laws.

10.4.5 Per the California Public Contract Code, upon the Contractor's request, the County will make payment of funds withheld to ensure performance of the Contract if the Contractor deposits in escrow with the Santa Barbara County Treasurer, or with a bank acceptable to the COUNTY/DISTRICT, securities eligible for investment under Government Code Section 16430 or bank or savings and loan certificates of deposit, upon the following conditions:

(a.) The Contractor shall bear the expense of the COUNTY/DISTRICT and the escrow agent, either the County

Treasurer or the bank, in connection with escrow deposit made.

(b.) Securities or certificates of deposit to be placed in escrow shall be of a value at least equivalent to the amount of retention to be paid to the Contractor pursuant to this section.

(c.) The Contractor shall enter into an escrow agreement satisfactory to the COUNTY/DISTRICT which agreement shall include provisions governing inter alia:

(1) the amount of securities to be deposited.
(2) the providing of power of attorney or other documents necessary for the transfer of the securities to be deposited.
(3) conversion to cash to provide funds to meet defaults by the Contractor including, but not limited to, termination of the Contractor's control over the work, stop notices filed pursuant to law, assessment of liquidated damages or other amounts to be kept or retained under the provisions of the contract.
(4) decrease in value of securities on deposit.
(5) the termination of the escrow upon completion of the Contract.

(d.) The Contractor shall obtain the written consent of the surety of such agreement.

10.5 PAYMENTS WITHHELD

10.5.1 The Designated Representative, Architect/Engineer or the Owner may decline approval of an Application for Payment if, in its opinion, the Application is not adequately supported. If the Contractor and the Designated Representative or Owner cannot agree on a revised amount, the Designated Representative shall process the application for the amount he deems appropriate. An amount equaling one hundred fifty (150%) percent of the value of the Work related to any Stop Notice shall be withheld from payments applied for by the Contractor until the Stop Notice is expunged. The Designated Representative may also decline to approve any Applications for Payment or, because of subsequently discovered evidence or subsequent inspections, he may nullify in whole or in part any approval previously made to such extent as may be necessary in its opinion because of:

(a.) Defective Work not remedied.
(b.) Third party claims filed or reasonable evidence indicating probably filing of such claims.
(c.) Failure of the Contractor to make payments properly to Subcontractor or for labor, materials or equipment.
(d.) Reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract Sum.
(e.) Damage to the Designated Representative, the Owner or another contractor working at the Project.
(f.) Reasonable evidence that the Work will not be completed within the Contract Time.
(g.) Persistent failure to carry out the Work in accordance with the Contract Documents.
(h.) The filing of a lien against the Project when lien is caused by the act or inaction of the Contractor or its subcontractor.
(i.) Refusal to follow the Project Safety Program issued as a Contract Document.
(j.) Failure to maintain records as specified.
(k.) Failure to maintain record drawings as specified.
(l.) Failure to secure required building inspections.

10.5.2 When the above grounds in Subparagraph 10.5.1 are removed, payment shall be made for the amounts withheld because of them, but in no case shall interest be paid on amounts withheld by the Owner to the Contractor.

10.6 FAILURE OF PAYMENT

10.6.1 If the Contractor is not paid within sixty (60) days after the Application for Payment is approved for payment by the Designated Representative and has become due and payable, then the Contractor may, upon thirty (30) additional days written notice to the Owner and the Designated Representative, stop the Work until payment of the amount owing has been received. The Contract Sum shall be increased by the amount of the Contractor's reasonable costs of shutdown, delay and start up, which shall be effected by the appropriate Change Order in accordance with Paragraph 13.3., but in no case shall interest be paid by the Owner to the Contractor.

10.7 SUBSTANTIAL COMPLETION

10.7.1 When the Contractor considers that the Work, or a designated portion thereof which is acceptable to the Owner, is substantially complete as defined in Subparagraph 9.1.3, the Contractor shall prepare for submission to the Designated Representative a list of items to be completed or corrected. The failure to include any items on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents. When the Designated Representative and Architect/Engineer, on the basis of inspection, determine that the Work or designated portion thereof is substantially complete, the Architect/Engineer will then prepare a Certificate of Substantial Completion which shall establish the Date of Substantial Completion, shall state the responsibilities of the Owner, the Designated Representative and the Contractor for security, maintenance, heat, utilities, damage to the Work, insurance and shall fix the time within which the Contractor shall complete the items listed therein. Warranties required by the Contract Documents shall commence on the Date of Substantial Completion of the Work or designated portion thereof unless otherwise provided in the Certificate of Substantial Completion. The Certificate of Substantial Completion shall be submitted to the Owner, the Designated Representative and the Contractor for their written acceptance of the responsibilities assigned to them in such Certificate. The Owner may retain a sum equal to an amount not to exceed one hundred twenty-five percent (125%) of the estimated cost of completing any unfinished items, separately listed and estimated at the time of substantial

completion. Thereafter, the Owner shall pay to the Contractor monthly, the amount retained for incomplete items as each of said items are completed.

10.7.2 The Owner shall have the right to take possession of and use for any purpose any partially completed portion of the Work. The Designated Representative will give notice to the Contractor of the Owner's intention to take said possession and use. Such taking possession or use shall not be deemed to be the Designated Representative's acknowledgement of completion and acceptance of said portion of Work.

10.7.2.1 The Owner's taking over and utilizing all or part of any completed facility or appurtenance will relieve the Contractor of responsibility for injury or damage to said completed portions of the improvement resulting from use by the public or from the action of the elements or from any other cause, except injury or damage resulting from the Contractor's operations or negligence. The Contractor will not be required to reclean such portions of the improvements before final acceptance, except for clean up made necessary by its operations. Nothing in this section shall be construed as relieving the Contractor from full responsibility for correcting defective work or materials.

10.7.2.2 In the event the Owner exercises its right to place into service and utilize all or part of any completed facility or appurtenance, the Owner shall assume the responsibility and liability for injury to persons or property arising out of or resulting from the utilization of the facility or appurtenance so placed into service, except for any such injury to persons or property caused by any willful or negligent act or omission of the Contractor, subcontractor, their officers, employees or agents.

10.8 FINAL COMPLETION AND FINAL PAYMENT

10.8.1 Following the Architect/Engineer's issuance of the Certificate of Substantial Completion of the Work or designated portion thereof and the Contractor's completion of the Work, the Contractor shall notify the Designated Representative in writing that the Work will be ready for final inspection and test on a definite date. Notice shall be given at least **five (5)** days in advance of said date. Designated Representative shall forward the notice to the Architect/Engineer who will attach its endorsement as to whether or not he concurs with the Contractor's statement that the Work will be ready for final inspection or test on the date given, but such endorsement shall not relieve the Contractor of its responsibility in the matter. If the Architect/Engineer concurs that the Work will be ready for final inspection or test on the date given, the Architect/Engineer and the Designated Representative will make such inspection. The Contractor is required to furnish access for the final inspection as provided in Subparagraph 3.2.1. If the Work is found acceptable under the Contract Documents and the Contract fully performed the Designated Representative, upon receipt of a correct final Application for Payment, shall recommend to the Owner that such payment be made.

10.8.2 Neither the final payment nor the remaining retained percentage shall become due until the Contractor submits to the Designated Representative all (1) inspection sign-offs, (2) final certificate of occupancy, (3) an affidavit that all payrolls, bills for materials and equipment and other indebtedness connected with the Work for which the Owner or its property might in any way be responsible, have been paid or otherwise, (4) consent of surety, if any, to final payment and executed "General Release and Lien Waiver and General Guarantee:, on forms to be provided by the Designated Representative, (5) if required by the Owner, other data establishing payment or satisfaction of all such obligations, such as receipts, releases and waivers of liens arising out of the contract, to the extent and in such form as may be designated by the Owner or Designated Representative. If any Subcontractor refuses to furnish a release or waiver required by the Owner or Designated Representative, the Contractor may furnish a bond satisfactory to the Owner and Designated Representative to indemnify them against any such lien. If any such lien remains unsatisfied after all payments are made, the Contractor shall refund to the Owner or Designated Representative all monies that the latter may be compelled to pay in discharging such lien, including all costs and reasonable attorney's fees. Contractor is required to submit all "Record Documents" and operating manuals as required by the Contract Documents prior to the processing of the final payment.

10.8.3 If, after Substantial Completion of the Work, final completion thereof is materially delayed through no fault of the Contractor or by the issuance of Change Orders affecting the final completion, and the Designated Representative so confirms, the Owner shall upon certification by the Designated Representative and without terminating the Contract, make payment of the balance due for that portion of the Work fully completed and accepted. If the remaining balance of Work not fully completed or corrected is less than the retention stipulated in the Contract Documents and if the bonds have been furnished as provided in Paragraph 8.5, the written consent of the surety to the payment of the balance due for that portion of the Work fully completed and accepted shall be submitted by the Contractor to the Designated Representative prior to such payment. Such payment shall be made under the terms and conditions governing final payment, except that it shall not constitute a waiver of claims.

10.8.4 Upon successful completion of the final inspection and Work required by the Contract, acceptance of the same by the Owner and the filing of all affidavits, consents of surety and other data required in Subparagraph 10.8.2 and the submission of all bonds, written warranties and guarantees and of all data documents required for project closeout by the Contract Documents, the Architect/Engineer shall file a written certification of completion with the Owner and with the Designated Representative as to the entire amount of Work performed and compensation earned, including extra Work and compensation therefore. At the expiration of thirty-five (35) days after the Owner's confirmation of such Certificate of Completion or as prescribed by law, the Owner shall pay the Contractor the amount stated therein, less all prior payments and advances, whatsoever, to or for the account of the Contractor except such amounts as are required to be withheld by properly executed and filed notices to stop payment or as may be authorized by the contract to be further retained. All prior estimates and payments including those relating to extra Work shall be subject to correction by this payment, which is throughout the Contract called "Final Payment."

10.8.5 The making of Final Payment shall constitute a waiver of all claims by the Owner or Designated Representative except those arising from:

(a.) Unsettled liens.
(b.) Faulty or defective Work appearing after Substantial Completion.
(c.) Failure of the Work to comply with the requirements of the Contract Documents
(d.) Terms of any special warranties required by the Contract Documents.

10.8.5.1 The acceptance by the Contractor of the Final Payment shall be and operate as a release to the Owner and to the Designated Representative of all claims and of all liability to the Contractor for all things done or furnished in connection with this Contract.

10.8.6 In accordance with Section 4551 of the Government Code, the Contractor and subcontractors shall conform to the following requirements. In entering into a public works contract or a subcontract to supply goods, services, or materials pursuant to a public works contract, the Contractor or subcontractor offers and agrees to assign to the awarding body all rights, title and interest in and to all causes of action it may have under Section 4 of the Clayton Act (15 U.S.C. Sec. 15) or under the Cartwright Act, Chapter 2 (commencing with Section 16700) of Part 2 of Division 7 of the Business and Professions Code, arising from purchases of goods, services, or materials pursuant to the public works contract of the subcontract. This assignment shall be made and become effective at the time the awarding body tenders final payment to the Contractor, without further acknowledgment by the parties.

10.8.7 In accordance with Section 4552 of the Government Code, the bidder shall conform to the following requirements. In submitting a bid to a public purchasing body, the bidder offers and agrees that if the bid is accepted, it will assign to the purchasing body all rights, title, and interest in and to all causes of action it may have under Section 4 of the Clayton Act, Chapter 2 (commencing with Section 16700) of Part 2 of Division 7 of the Business and Professions Code, arising from purchases of goods, materials, or services by the bidder for sale to the purchasing body pursuant to the bid. Such assignment shall be made and become effective at the time the purchasing body tenders final payment to the bidder.

10.9 MEASUREMENT OF QUANTITIES FOR UNIT PRICE WORK

10.9.1 General: Unless otherwise specified, quantities of work shall be determined from measurements or dimensions in horizontal planes. However, linear quantities of pipe, piling, fencing, and timber shall be considered as being the true length measured along the longitudinal axis. Unless otherwise provided in the Contract Documents, volumetric quantities shall be the product of the mean area of vertical or horizontal sections and the intervening horizontal or vertical dimension. The planimeter shall be considered an instrument of precision adapted to the measurement of all areas.

10.9.2 Methods of Measurement: Materials and items of work which are to be paid for on the basis of measurement shall be measured in accordance with the methods stipulated in the particular section involved.

10.9.3 Certified Weights: When payment is to be made on the basis of weight, the weighing shall be done on certified platform scales or, when approved by the Designated Representative, on a completely automated weighing and recording system. The Contractor shall furnish the Designated Representative with duplicate licensed weighmaster's certificates showing the actual net weights. The Designated Representative will accept the certificate as evidence of the weights delivered.

10.9.4 Units of Measurement: Measurements shall be in accordance with U. S. Standard Measures. A pound is an avoirdupois pound. A ton is 2,000 pounds avoirdupois. The unit of liquid measure is the U. S. gallon.

10.9.5 Lump Sum Items: Items for which quantities are indicated as "Lump Sum", "L.S.", "Job", or words of like import shall be paid for at the price named. Such payment shall be full compensation for the work named and all work appurtenant thereto required by the contract which is not specifically provided for by other pay items.

10.9.6 Actual Quantities: The quantities listed in the bid schedule will not govern final payment. Payment to the Contractor will be made only for the actual quantities of contract items constructed in accordance with the plans and specifications. Upon completion of the construction, if the actual quantities show either an increase or decrease from the quantities given in the bid schedule, the contract unit prices will prevail subject to the provisions of Article 13.

10.9.7 Waste: Payment will not be made for materials wasted or disposed of in a manner not called for under the Contract. This includes rejected materials not unloaded from vehicles, material rejected after it has been placed and material placed outside of the plan lines. No compensation will be allowed for disposing of rejected or excess material.

ARTICLE 11: PROTECTION OF PERSONS AND PROPERTY

11.1 SAFETY PRECAUTIONS AND PROGRAMS

11.1.1 The Contractor expressly undertakes, both directly and through its Subcontractor, to take every precaution at all times for the protection of persons, including employees and property. The Contractor shall be responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the Work.

11.1.2 The Contractor shall comply with the provisions of the "Construction Safety Act" and the "Occupational Safety and Health Act of 1970" and the Designated Representative's safety program, as well as all other applicable, Federal, State and local requirements. The Contractor shall submit its safety program to the Designated Representative prior to mobilizing the job and shall be responsible for the safety, efficiency and adequacy of its plant, appliances and methods and for any damage which might result from failure or improper construction, maintenance or operation. The Contractor shall provide a safety report to the Designated Representative on a weekly basis. During the conduct of the Work, the Contractor shall take immediate corrective action, as required upon notification of any deficiencies in safety provisions by the Designated Representative or identification of any deficiencies by Subcontractor personnel.

11.1.3 If the Contractor fails to maintain the safety precautions required by law or directed by the Designated Representative, the Designated Representative may take such steps as necessary and charge the Contractor therefore.

11.1.4 The failure of the Owner to take any such action shall not relieve the Contractor of its obligations in Subparagraph 11.1.1.

11.1.5 The Contractor shall immediately notify the Designated Representative of all accidents and submit a written report describing in detail the circumstances of all accidents within twenty-four (24) hours.

11.1.6 The Contractor alone shall be responsible for the safety, efficiency and adequacy of its plant, appliances and methods and for any damage which may result from their failure or their improper construction, maintenance or operation.

11.2 SAFETY OF PERSONS AND PROPERTY

11.2.1 The Contractor shall take all reasonable precautions for the safety of and shall provide all reasonable protection to prevent damage, injury or loss to:

(a.) All employees on the Project and all other persons who may be affected thereby;

(b.) All the Work and all materials and equipment to be incorporated therein, whether in storage on or off the site, under the care, custody or control of the Contractor or any of its Subcontractors or Sub-subcontractors; and

(c.) Other property at the site or adjacent thereto, including trees, shrubs, lawns walks, pavements, roadways, structures and utilities not designed for removal, relocation or replacement in the course of construction.

11.2.2 The Contractor shall give all notices and comply with all applicable laws, ordinances, rules, regulations and lawful orders of any public authority bearing on the safety of persons or property or their protection from damage, injury or loss.

11.2.3 The Contractor shall erect and maintain, as required by existing conditions and progress of the Work, all reasonable safeguards for safety and protection, including posting danger signs and other warnings against hazards promulgating safety regulations and notifying the Owners and users of adjacent utilities. He shall protect the Owner's property from injury or loss arising in connection with this Contract. He shall adequately protect adjacent property as provided by law and the Contract Documents. He shall provide and maintain all passageways, guard fences, light and other facilities for protection required by public authority, local conditions or any of the Contract Documents. If the Contractor fails to so comply, he shall, at the direction of the Designated Representative, remove all forces from the Project without cost or loss to the Owner or Designated Representative, until he is in compliance.

11.2.4 When the use or storage of explosives or other hazardous materials or equipment is necessary for the execution of the Work, the Contractor shall exercise the utmost care and shall carry on such activities under the supervision of properly qualified personnel.

11.2.5 The Contractor shall notify the Designated Representative of any flammable, combustible and toxic materials intended for use on the project and shall furnish the Designated Representative literature pertinent to the use and control of such materials.

11.2.6 Every employee will be dressed for the Work he performs. Minimum dress will consist of long pants, tee shirt and work shoes. Shorts, cut-offs, "tank-top" shirts or soft-soled shoes will not be permitted.

11.2.7 The Contractor shall promptly remedy all damage or loss (other than damage or loss insured under Paragraph 12.2) to any property, referred to under Articles 11.2.1.2 and 11.2.1.3, caused in whole or in part by the Contractor, its Subcontractors or anyone directly or indirectly employed by any of them, or by anyone for whose acts any of them may be liable and for which the Contractor is responsible under the Articles 11.2.1.2 and 11.2.1.3, except damage or loss attributable to the acts or omissions of the Owner or Architect/Engineer or anyone directly or indirectly employed by either of them or by anyone for whose acts either of them may be liable and not attributable to the fault or negligence of the Contractor. The foregoing obligations of the Contractor are in addition to its obligations under Paragraph 5.18. The Contractor shall be responsible to the Owner and the Designated Representative for the acts and omissions of all its employees and all Subcontractors, their agents and employees and all other persons performing any of the Work under a contract with the Contractor.

11.2.8 The Contractor and each Subcontractor shall designate a responsible member of its organization at the site to act as its Safety Representative whose duty shall be the prevention of accidents and who shall be responsible to maintain all Safety requirements of the Contractor and shall attend all Project Safety Meetings scheduled by the Contractor. This person shall be the Contractor's or Subcontractor's Superintendent unless otherwise designed by the Contractor in writing to the Designated Representative.

11.2.9 The Contractor shall not load or permit any part of the Work to be loaded so as to endanger safety.

11.2.10 When necessary for the proper protection of the Work, temporary heating of a type approved by the Designated Representative and Architect/Engineer shall be provided by the Contractor unless otherwise specified.

11.3 EMERGENCIES

11.3.1 In an emergency affecting the safety or life of individuals, of the Work, or of adjoining property, the Contractor without special instruction or authorization from the Owner or Designated Representative or Architect/Engineer shall act, at its discretion, to prevent such threatened loss or injury. Also, should he, to prevent threatened loss or injury, be instructed or authorized to act by the Owner or Designated Representative or Architect/Engineer, he shall so act, without appeal. Any additional compensation or extension of time claimed by the Contractor on account of any emergency Work shall be determined as provided by Article 13 - Changes in the Work.

11.3.2 Whenever immediate action is required to prevent impending injury, death, or property damage, and precautions which are the Contractor's responsibility have not been taken and are not reasonably expected to be taken, the Owner or Designated Representative may, after reasonable attempt to notify the Contractor, cause such precaution to be taken and shall charge the cost thereof against the Contractor, or may deduct such cost from any amount due or becoming due from the Owner. The Owner's or Designated Representative's action or inaction under such circumstances shall not be construed as relieving the Contractor or its surety from liability.

ARTICLE 12: UTILITIES

12.1 LOCATION

12.1.1 The Owner will search known substructure records and furnish the Contractor, when requested by the Contractor, with copies of documents which describe the location of utility substructures, or will indicate on the plans for the project those substructures, except for service connections, which may affect the work. Information regarding removal, relocation, abandonment, or installation of new utilities will be furnished to prospective bidders.

12.1.2 Where underground main distribution conduits such as water, gas, sewer, electric power, telephone or cable television are shown on the plans, the Contractor, for the purpose of preparing its bid, shall assume that every property parcel will be served by a service connection for each type of utility.

12.1.3 At least two (2) working days before entering on the work, the Contractor shall request the utility owners whose utilities will be affected by the Contractor's work to mark or otherwise indicate the approximate location of their subsurface facilities including, but not limited to, structures, main conduits and service connections. This requirement will not apply to sewer and storm drain installations where their location and depth are shown on the plans for the project.

12.1.4 It shall be the Contractor's responsibility to determine the location and depth of all utilities, including service connections, which have been marked by the respective utility owners and which he believes may affect or be affected by its operations. If no pay item is provided in the contract for this work, full compensation for such work shall be considered as included in the prices bid for other items of work.

12.2 PROTECTION

12.2.1 The Contractor shall not interrupt the service function or disturb the supporting base of any utility without authority from the utility owner or order from the Designated Representative.

12.2.2 Where protection is required to insure support of utilities located as shown on the plans or in accordance with Paragraph 12.1, the Contractor shall, unless otherwise provided, furnish and place the necessary protection at its expense.

12.2.3 Upon learning of the existence and location of any utility omitted from or shown incorrectly on the plans, or not properly marked, the Contractor shall immediately notify the Designated Representative in the form of a written request for information. When authorized by the Owner, support or protection of the utility will be paid for as provided in Article 13.

12.2.4 The Contractor shall immediately notify the Designated Representative and the utility owner if any utility is disturbed. The Contractor shall bear the costs of repair or replacement of any utility damaged.

12.2.5 When placing concrete around or contiguous to any non-metallic utility installation, the Contractor at its own expense, shall (1) furnish and install a two-inch cushion of expansion joint material or other similar resilient material; or (2) provide a sleeve or other opening which will result in a two-inch minimum clear annular space between the

concrete and the utility; or (3) provide other acceptable means to prevent embedment in or bonding to the concrete. Where concrete is used for backfill or for structures which would result in embedment, or partial embedment, of a metallic utility installation; or where the coating, bedding or other cathodic protection system is exposed or damaged by the Contractor's operations or as may be required by the work, the Contractor shall notify the Designated Representative and arrange to secure the advice of the affected utility owner regarding the procedures required to maintain or restore the integrity of the system.

12.3 EXCAVATIONS

12.3.1 For any displacement or excavation of the ground that may be required by any performance under this Contract, the Contractor shall obtain an inquiry identification number by calling Underground Service Alert (USA) 1 (800) 422-4133 or by such other means as may be required; shall conform to all requirements of Government Code Sections 4215 through 4217 regarding any such displacement or excavation, including the payment of any fees required; and shall facilitate performance by the Owner of any obligation required of the County under said sections.

12.3.2 There shall be no performance under this Contract by either party unless and until the provisions of such Sections are complied with and the Designated Representative is notified regarding the compliance.

12.4 REMOVAL

12.4.1 Unless otherwise specified, the Contractor shall remove all interfering portions of utilities shown on the plans or indicated in the bid documents as "abandoned" or "to be abandoned in place".

12.4.2 Before starting removal operations, the Contractor shall ascertain from the Designated Representative whether the utility abandonment is complete, and the costs involved in the removal and disposal shall be absorbed in the bid for the items of work necessitating such removals.

12.5 RELOCATION

12.5.1 When feasible, the utility owners responsible for utilities within the area affected by the work will complete their necessary installations, relocations, repairs or replacements before commencement of work by the Contractor. When the Contract Documents or plans indicate that a utility installation is to be relocated, altered or constructed by others, the Owner will conduct all negotiations with the utility owners and the work will be done at no cost to the Contractor.

12.5.2 Utilities which are relocated in order to avoid interference with the proposed permanent work shall be protected in their relocated position and the cost of such protection shall be absorbed in the various items of the contract.

12.5.3 After award of the contract, portions of utilities which are found to interfere with the work will be relocated, altered or reconstructed by the utility owners, or the Owner may order changes in the work to avoid interference. Such changes will be paid for in accordance with Article 13.

12.5.4 When the plans or specifications provide for the Contractor to alter, relocate, or reconstruct a utility, all costs for such work shall be included in the bid for the items of work necessitating such work. Temporary or permanent relocation or alteration of utilities requested by the Contractor for its own convenience shall be its responsibility, and he shall make all arrangements and bear all costs.

12.5.5 The utility owner will relocate service connections as necessary within the limits of the work or within temporary construction or slope easements unless otherwise specified. When directed by the Designated Representative, the Contractor shall arrange for the relocation of service connections as necessary between the meter and property line, or between a meter and the limits of temporary construction or slope easements. The relocation of such service connections when not detailed on the plans or in the specifications will be paid for in accordance with provisions of Article 13. Payment will include the restoration of all existing improvements which may be affected thereby. The Contractor may, for its own convenience or to expedite the work, agree with any utility owner to disconnect and reconnect interfering service connections. The Owner will not be involved in any such agreement.

12.6 DELAYS

12.6.1 The Contractor shall notify the Designated Representative of its construction schedule insofar as it affects the protection, removal or relocation of utilities. Said notification shall be in writing and shall be included as a part of the construction schedule required in Paragraph 5.10. He shall notify the Designated Representative in writing of any subsequent changes in its construction schedule which will affect the time available for protection, removal or relocation of utilities.

12.6.2 The Contractor will not be entitled to damages or additional payment for delays attributable to utility relocations or alterations if correctly located, noted and completed in accordance with Paragraph 12.1. The Contractor may be given an extension of time for unforeseen delays attributable to utility relocations or alterations not shown or incorrectly shown on the plans, or for unreasonably protracted interference by utilities in performing work correctly shown on the plans. If the Contractor sustains loss due to delays attributable to interferences, relocations or alterations not covered by Paragraph 12.1, which could not have been avoided by the judicious handling of forces, equipment or plant, there shall be paid to the Contractor such amount as the Owner may find to be fair and reasonable compensation for such part of the Contractor's actual loss as was unavoidable.

12.7 COOPERATION

12.7.1 When necessary, the Contractor shall so conduct its operations as to permit access to the work site and provide time for utility work to be accomplished during the progress of the contract work.

ARTICLE 13: CHANGES IN THE WORK

13.1 CHANGE ORDERS

13.1.1 A Change Order is a written order to the Contractor signed by the Owner issued after the execution of the Contract authorizing a change in the Work or an adjustment in the Contract Sum or the Contract Time. The Contract Sum and the Contract Time may be changed only by a Change Order. The County Director of General Services is authorized to execute Change Orders for the Owner in accordance with Article 2.3. A Change Order signed by the Contractor indicates its agreement therewith, including the adjustment in the Contract Sum or the Contract Time, and Contractor agrees that the change in the contract sum and contract time set forth in the Change Order shall constitute the complete compensation and time extension for the change in the work including, but not limited to, Contractor's field and home office overhead, profit, and supervision costs. The Contractor shall not proceed with any change in the Work unless directed in writing by the Designated Representative.

13.1.2 The Owner or Designated Representative, without invalidating the Contract, may order changes in the Work within the general scope of the Contract consisting of additions, deletions or other revisions, the Contract Time being adjusted accordingly. All such changes in the Work shall be authorized by a Change Order and shall be performed under the applicable conditions of the Contract Documents. Provisions of the Contract shall apply to all changes, modifications and additions with the same effect as if changes were embodied in the base Contract Documents.

13.1.3 A change in the Work may be initiated in one of three ways:

13.1.3.1 A "Request for Quotation" form from the Designated Representative to the Contractor describing the revision to the Work desired. Usually, it is accompanied by revised drawings, sketches or other data.

13.1.3.2 Formal notification from the Contractor documenting a "concealed condition" requesting investigation by the Designated Representative and Architect/Engineer which causes changes in the Contract Documents (and a subsequent Request for Quotation on the revised documents).

13.1.3.3 In response to a Contractor's "Request for Information", the Architect/Engineers' response may include instructions which the Contractor interprets as involving "extra work." In such cases, the Contractor must submit written notice to the Designated Representative requesting review and issuance of an appropriate Request for Quotation. Any other "instruction" given to the Contractor by the Owner, Designated Representative or Architect/Engineer shall require these procedures and as indicated in 13.4.1 below.

13.1.4 The cost or credit to the Owner resulting from changes in the Work, as outlined above, shall be made on the basis of one of the following methods:

(a.) By such applicable unit prices as set forth in the Contract Documents or subsequently agreed upon by both parties to the Contract.

(b.) By a lump sum mutually agreed upon by the Owner and the Contractor.

(c.) The Owner may direct the Contractor through the Designated Representative to proceed with Work on a time and material (T & M) basis, with a not to exceed cost and the Contractor shall keep and present, in such a form as the Designated Representative may direct, a correct account of all costs of the changes together with all vouchers. The costs shall include overhead and profit as subsequently set forth below. These costs then shall be finalized by a Change Order.

(d.) If the parties cannot agree upon a Lump Sum, Unit Pricing or T & M with a not to exceed cost, the Owner may, as recommended by the Designated Representative, issue a written directive Contract Amendment to proceed and the Contractor shall be compensated for the net cost of additional Work. The Contractor shall keep and present in such a form as the Designated Representative may direct a correct account of all costs of the changes together with all vouchers. The costs shall include overhead and profit as subsequently set forth below.

13.1.5 Lump sum prices and compensation for actual net cost plus overhead and profit shall be established as follows:

13.1.5.1 The net cost of Changes in the Work may include all items of labor or material, power tools and equipment actually used, prorate charges for foreman and payroll charges such as Public Liability and Workmen Compensation Insurance. No percentage for overhead, profit and commission shall be allowed on items of premium costs for overtime, social security, old age and unemployment insurance, fringe benefits, and payroll taxes. If deductions are ordered, the credit shall be the net cost. Items considered as overhead shall include insurance, other than that mentioned above, bond or bonds, superintendent, timekeeper, clerks, watchmen, use of small tools, incidental job burdens, transportation, and general offices expense. The percentages for overhead and profit shall be negotiated and may vary according to the nature, extent and complexity of the changed Work (other than those covered by unit prices set forth on the Contract Documents), but in no case shall exceed the following:

(a.) Allowable Mark-ups on Change Orders

Definitions:

Prime Contractor =	General Contractor
First Tier Subcontractor =	Contractor to the Prime Contractor
Second Tier Subcontractor =	Contractor to the First Tier Subcontractor

Case A: For work within the scope of the Change Order performed by forces of the Prime Contractor:
- Overhead: 10% to Prime Contractor only.
- Profit: 5% to Prime Contractor only.
- Commission: No commission to any party.

Case B: For work within the scope of the Change Order performed by forces of the First Tier Subcontractor(s):
- Overhead: 10% to First Tier Subcontractor(s) only.
- Profit: 5% to First Tier Subcontractor(s) only.
- Commission: 5% to Prime Contractor only.

Case C: For work within the scope of the Change Order performed by forces of the Second Tier Subcontractor(s):
- Overhead: 10% to the Second Tier Subcontractor(s) only.
- Profit: 5% to the Second Tier Subcontractor(s) only.
- Commission: 5% to the Prime Contractor.
  5% to the First Tier Subcontractor(s).
  No commission to Second Tier Subcontractor(s).

(b.) Not more than four (4) mark-ups (Case C), not to exceed the maximum percentages shown above, shall be allowed.

(c.) All Cost Proposals for work shall be submitted to the Designated Representative on the attached document: "County of Santa Barbara General Services/Capital Projects Division Cost Proposal".

13.1.5.2 On proposals covering both increases and decreases in the amount of the contract, overhead, profit and commission shall be allowed on the net increase only as determined above. When the net difference is a deletion, no percentage for overhead profit and commission shall be allowed.

13.1.5.3 Contractor's cost for preparation of change order proposals shall be deemed to be included in amount of change order proposal.

13.1.6 The Contractor shall respond to the Designated Representative's request for a proposal within seven calendar days. In this proposal, the Contractor shall furnish to the Designated Representative an itemized breakdown of the quantities and prices used in computing the value of changes that might be ordered. The Contractor shall submit with its proposal, its request for time extension (if any). If time for completion of the Contractor's Work is not affected by the change, the Contractor shall so state.

13.1.7 In figuring changes, instructions for measurements of quantities set forth in the specifications shall be followed.

13.1.8 After receipt of a proposal with a detailed breakdown, the Designated Representative shall act promptly thereon. However, when the necessity to proceed with a change does not allow sufficient time to properly check a proposal, the Owner through the Designated Representative may order the Contractor to proceed on the basis to be determined at the earliest practicable date. In this event, the value of the change, with the corresponding equitable adjustment to the contract, shall not be more than the increase or less than the decrease proposed.

13.1.9 The Designated Representative will inform the Contractor and the Contractor will inform the Designated Representative when either party recognizes that a proposed Request for Quotations (RFQ) may affect the progress of the Work schedule.

13.1.10 Designated Representative's Audit: Designated Representative's duly authorized auditors shall have access at all reasonable times, to all Contractor's and Subcontractors' personnel, books, records, correspondence, instructions, plans, drawings, receipts, vouchers and memoranda of every description pertaining to Change Orders for the purpose of auditing and verifying Contractor's net cost of Change Order or for any other reasonable purpose. Designated Representative's auditors shall have the right to reproduce any of the aforesaid documents. Contractor shall preserve and shall cause its Subcontractors to preserve all the aforesaid documents for a period of two (2) years after the completion and acceptance or termination of the Work.

13.1.11 If unit prices are stated in the Contract Documents or subsequently agreed upon and if the quantities originally contemplated are so changed in a proposed Change Order, that application of the agreed unit prices to the quantities of Work proposed will cause substantial inequity to the Owner, the Contractor or the Subcontractor, the applicable unit prices shall be equitably adjusted.

13.2 CONCEALED CONDITIONS

13.2.1 Should concealed conditions encountered in the performance of the Work below the surface of the ground or should concealed or unknown conditions in an existing structure be at variance with the conditions indicated by the Contract Documents, or should unknown physical conditions in an existing structure of an unusual nature, differing materially from those ordinarily encountered and generally recognized as inherent in Work of the character provided for in this Contract be encountered, the Contractor shall report the conditions to the Designated Representative before the conditions are disturbed. The Designated Representative shall thereupon notify the Architect/Engineer. Upon such notices, or upon its own observation of such conditions, the Architect/Engineer shall promptly make such changes in the Contract Documents as he finds necessary to conform to the different conditions. Any change in the cost of the Work or the time needed for completion resulting from concealed conditions shall be determined in accordance with Paragraph 13.1 provided a notice thereof is made within ten (10) days after the first observance of the conditions.

13.3 CLAIMS FOR ADDITIONAL COST

13.3.1 If the Contractor claims that any instructions given to him by the Owner or Designated Representative or by the Architect/Engineer, by drawings or otherwise, involve extra Work not covered by the Contract, he shall give the Designated Representative written notice thereof within ten (10) days after the receipt of such instructions and before proceeding to execute the Work, except in emergencies endangering life or property, in which case the Contractor shall proceed in accordance with Paragraph 11.3. Should it not be clear to the Contractor that a change will involve extra Work, written notice given within ten (10) days that the change may involve extra work will be considered sufficient notice. If it is later determined that the Work involved in such instruction shall be recognized as an extra, the amounts of additional compensation to be paid therefore, should be determined in accordance with Paragraph 13.1. Except as otherwise specifically provided, no claim for additional cost shall be allowed unless the notice specified by this Subparagraph is given by the Contractor or unless such Work is performed as provided in Subparagraph 13.1.4. Any change in the contract sum resulting from such claim shall be authorized by agreement amendment.

13.3.2 If the Contractor claims that additional cost is involved because of, but not limited to, (1) written interpretation issued pursuant to Subparagraph 3.2.2, (2) any order by the Owner or Designated Representative to stop the Work pursuant to Paragraph 4.3 where the Contractor was not at fault, or (3) any written order for a minor change in the Work issued pursuant to Paragraph 13.4, the Contractor shall make such claims as provided in Subparagraph 13.3.1.

13.3.2.1 Any claim for damages of any character, delays for which the Owner is liable under the Contract Documents, extra work or extra compensation of any other nature, shall be waived unless notice thereof is given to the Owner, in writing, within ten (10) days after the initial occurrence of the first event, which is relied upon to justify the claim or within such time as the event should have reasonably been discovered by the Contractor and in any event, before extra cost is incurred.

13.3.2.2 Any claim for a delay for which the Owner is liable will not be allowed where there is a concurrent delay that is the responsibility of the Contractor.

13.3.2.3 No claim for damages of any character due to delays caused by adverse weather, acts of God, strikes, fire or unavoidable casualties will be allowed. The Contractor shall bear the expenses related to additional time granted for "force majeure" events.

13.3.2.4 The written notice of potential claim shall set forth the reasons for which the Contractor believes additional compensation will or may be due, the nature of the costs involved, and, insofar as possible, the amount of the potential claim. The said notice as above required must have been given to the Designated Representative prior to the time that the Contractor shall have performed the work giving rise to the potential claim for additional compensation, if based on an act or failure to act by the Designated Representative, or in all other cases within ten (10) days after the happening of the event, thing or occurrence giving rise to the potential claim. It is the intention of this paragraph that differences between the parties arising under and by virtue of the contract be brought to the attention of the Designated Representative at the earliest possible time in order that such matters may be settled, if possible, or other appropriate action promptly taken. The Contractor hereby agrees that he shall have no right to additional compensation for any claim that may be based on any such act, failure to act, event, thing or occurrence for which no written notice of potential claim as herein required was filed.

13.4 MINOR CHANGES IN THE WORK

13.4.1 The Architect/Engineer will have the authority to order, through the Designated Representative, minor changes in the Work not involving an adjustment in the Contract Sum or an extension of the Contract Time and not inconsistent with the intent of the Contract Documents. Such changes will be effected by written order and such changes shall be binding on the Owner, the Designated Representative and the Contractor. The Contractor shall carry out such written orders promptly.

ARTICLE 14: UNCOVERING AND CORRECTION OF WORK

14.1 UNCOVERING OF WORK

14.1.1 If any portion of the Work should be covered contrary to the request of the Owner through the Designated Representative or Architect/Engineer, or to requirements specifically expressed in the Contract Documents, it shall, if required in writing by the Designated Representative, be uncovered for their observation and replaced, at the Contractor's expense.

14.1.2 If any other portion of the Work has been covered which neither the Designated Representative nor the Architect/Engineer has specifically requested to observe prior to being covered, the Architect/Engineer or Designated Representative, with written approval of the Owner, may request to see such work and it shall be uncovered by the Contractor. If such work is found in accordance with the Contract, the cost of uncovering and replacement shall, by an appropriate Change Order, be charged to the Owner, as the case may be. If such Work is found not in accordance with the Contract Documents, the Contractor shall pay such costs unless it is found that this condition was caused by a separate contractor employed as provided in Article 7 and in that event, the separate contractor shall be responsible for payment of such costs.

14.2 CORRECTION OF WORK

14.2.1 The Contractor shall promptly correct all Work rejected by the Architect/Engineer or the Designated Representative as defective or as failing to conform to the Contract Documents whether observed before or after Substantial Completion and whether or not fabricated, installed or completed. The Contractor shall bear all costs of correcting such rejected Work, including compensation for the Architect/Engineer's and Designated Representative's additional services made necessary thereby.

14.2.2 Notwithstanding acceptance of the Work by the Owner,if any of the Work is found to be defective or not in accordance with the Contract Documents, the Contractor shall correct it promptly after receipt of written notice from the Designated Representative to do so, unless the Owner has previously given the Contractor a written acceptance of such condition. This obligation shall survive the termination of the Contract. The Designated Representative shall give such notice promptly after discovery of the condition.

14.2.2.1 If, within one (1) year after the Date of Substantial Completion of the Work or the designated portion thereof, or within one (1) year after acceptance by the Owner of designated equipment or within such longer period of time as may be prescribed by law or by the terms of any applicable special warranty required by the Contract Documents, the Contractor shall correct it promptly after receipt of written notice from the Owner or Designated Representative to do so unless the Owner or the Designated Representative has previously given the Contractor written acceptance of such condition. This obligation shall survive the termination of the Contract. The Owner or Designated Representative shall give such notice promptly after discovery of the condition.

14.2.3 The Contractor shall remove from the site all portions of the Work which are defective or nonconforming and which have not been corrected under Subparagraph 5.5.1, 14.2.1 and 14.2.2 unless removal has been waived by the Owner.

14.2.4 If the Contractor fails to correct the defective or nonconforming Work as provided in Subparagraph 5.5.1, 14.2.1 and 14.2.2, the Owner may correct it in accordance with Subparagraph 4.3.2.

14.2.5 If the Contractor does not proceed with the correction of such defective or nonconforming Work within a reasonable time fixed by written notice from the Designated Representative, the Owner may remove it and may store the materials or equipment at the expense of the Contractor. If the Contractor does not pay the cost of such removal and storage within ten (10) days thereafter, the Owner may, upon ten (10) additional days written notice, sell such Work at auction or at private sale and shall account for the net proceeds thereof, after deducting all costs that should have been borne by the Contractor, including compensation for the Designated Representative's additional services made necessary thereby. If such proceeds of sale do not cover all costs, which the Contractor should have borne, the difference shall be charged to the Contractor and the appropriate Change Order shall be issued. If the payments then or thereafter due the Contractor are not sufficient to cover such amount, the Contractor shall pay the difference to the Owner.

14.2.6 The Contractor shall bear the cost of making good all Work of the Owner or other contractors destroyed or damaged by such removal or correction.

14.2.7 Nothing contained in this Paragraph 14.2 shall be construed to establish a period of limitation with respect to any other obligation which the Contractor might have under the Contract Documents, including Paragraph 5.5 hereof. The establishment of the time period of one (1) year after the Date of Substantial Completion or such longer period of time as may be prescribed by law or by the terms of any warranty required by the Contract Documents, relates only to the specific obligation of the Contractor to correct the Work and has no relationship to the time within which its obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish the Contractor's liability with respect to its obligations other than specifically to correct the Work.

14.3 ACCEPTANCE OF DEFECTIVE OR NONCONFORMING WORK

14.3.1 If the Owner prefers to accept defective or nonconforming Work, he may do so instead of requiring its removal and correction, in which case a Change Order will be issued to reflect reduction in the Contract Sum where appropriate and equitable. Such adjustment shall be affected whether or not Final Payment has been made.

ARTICLE 15: TERMINATION OF THE CONTRACT

15.1 TERMINATION BY THE CONTRACTOR

15.1.1 If the Work is stopped under an order of any court or other public authority having jurisdiction for a period of three (3) months, through no fault of the Contractor or a Subcontractor or their agents or employees or any other person performing any of the Work under a contract with the Contractor, or if the Designated Representative should arbitrarily fail to issue any certificate for payment within a reasonable time after it is due, or if the Owner should fail to pay within sixty (60) days, any sum certified by the Designated Representative to the Contractor, he may, upon thirty (30) additional days written notice by the Contractor, stop Work or terminate the Contract and recover from the Owner payment for all Work executed and for any proven loss sustained upon any materials, equipment, tools, construction equipment and machinery.

15.2 TERMINATION BY THE OWNER

15.2.1 If the Contractor is adjudged bankrupt or if he makes a general assignment for the benefit of its creditors or if a receiver is appointed on account of its insolvency, or if he persistently or repeatedly refuses or fails, except in cases for which extension of time is provided, to supply enough properly skilled workmen or proper materials, or if he fails to make prompt payment to Subcontractors or for materials or labor, or persistently disregards laws, ordinances, rules regulations, orders of any public authority having jurisdiction, or otherwise is guilty of a substantial violation of a provision of the Contract Documents, then the Owner may, without prejudice to any right or remedy and after giving the Contractor and its surety, ten (10) days written notice, terminate the employment of the Contractor and take possession of the site and of all materials, equipment, tools, construction equipment and machinery thereon owned by the Contractor and may finish the Work by whatever method he may deem expedient. In such case the Contractor shall not be entitled to receive any further payment until the Work is finished.

15.2.1.1 If the unpaid balance of the Contract Sum exceeds the costs of finishing the Work, including compensation for the Designated Representative's additional services made necessary thereby, such excess shall be paid to the Contractor. If such costs exceed the unpaid balance, the Contractor shall pay the difference to the Owner.

15.2.1.2 The expenses incurred by the Owner or Designated Representative and the damage incurred through the Contractor's default shall be certified by the Architect/Engineer.

15.2.2 The Owner may terminate the contract at its own discretion or when conditions encountered during the work make it impossible or impracticable to proceed, or when the Owner is prevented from proceeding with the contract by act of God, by law, or by official action of a public authority.

15.2.3 After receipt of a Notice of Termination, the Contractor shall submit to the Owner through the Designated Representative its written termination claim in the form and with the certification which the Owner or Designated Representative may require. Such claims shall be submitted promptly, but in no event more than thirty (30) days after the effective date of termination.

ARTICLE 16: PROJECT REQUIREMENTS

16.1 PROJECT REPORTS

16.1.1 Contractor Reports: Immediately after the contract is awarded, a meeting will be scheduled at the project site to review project procedures, designation of name and title of the authorized person or persons, representing the Contractor and responsible for the project management and field operation, designation of Emergency Contact, designation of representative for progress meetings, the requirements for daily, weekly and monthly reports and other submittals required to perform and administer the project. Without limiting the reports required, several reports are indicated below with their requirements:

16.1.2 Daily Force and Activity Reports: The Contractor shall prepare and submit to the Designated Representative, including similar data for each of its Subcontractors, a Daily Force and Activity Report. This report shall be on a form approved by the Designated Representative and shall indicate all Supervisors, Journeymen, Laborers or Helpers and, by crew, the activities, related to the Contractor's schedule, that are being performed. The Daily Force and Activity Report shall include information on material deliveries, tests, weather conditions and other significant events. Each Daily Force and Activity Report shall be delivered to the Designated Representative at the job site by 9:00 a.m. on the next succeeding business day.

16.1.3 Daily Change Documentation: The Contractor shall submit to the Designated Representative for review and verification, separate daily documentation of any "Change in the Work" being performed on any basis, other than agreed upon lump sum, as described in Article 13 of the General Conditions. This report shall be on a form approved by the Designated Representative. The Contractor shall certify the accuracy of this report.

16.1.4 Safety Reports: The Contractor shall submit to the Designated Representative copies of all accident reports and weekly minutes/reports of Safety Program "Tool Box" meeting and other safety information.

16.1.5 Material Status Reports: The Contractor shall prepare a Materials Status Report not later than fifteen (15) calendar days after the Notice to Proceed. The report shall include a complete list of suppliers, items to be purchased from them, the fabricator and manufacturer, the time required and the promised delivery dates for each item. This report shall be updated and submitted with the payment requisition monthly as an integral part thereof and more frequently as requested by the Designated Representative.

16.1.6 Purchase Orders: A copy of each purchase order as issued by the Contractor shall be furnished to the Designated Representative, except that prices may be omitted.

16.1.7 Job Cost Breakdown: The Contractor shall submit job cost breakdown reports for record and tax purposes to the Designated Representative. The first report shall be submitted within thirty (30) calendar days after date of each Notice to Proceed on any portion of the Work and shall be consistent in format with the schedule of values. Another report shall be submitted at the completion of the job and shall include all additions and deletions. Interim reports on various elements of the Work shall be submitted as required by the Owner for investment, tax credit, pollution control, financing and other purposes.

16.1.8 Monthly Progress Payment Applications: The Contractor shall submit Monthly Progress Payment Applications in the form and at the time as approved by the Designated Representative.

16.1.9 Monthly Reports: The Contractor shall submit to the Designated Representative copies of all monthly reports, such as MBE Participation, etc., required by governing bodies.

16.1.10 Monthly Certification: The Contractor shall submit to the Designated Representative periodic evidence and a monthly certification that "Record Documents", Test Reports and other Project Record Documents are being maintained for ultimate submittal to the Designated Representative and Owner at the completion of the Work.

16.1.11 Weekly Request for Information Status: The Contractor shall submit, each week on a day agreed to between the Contractor and the Designated Representative, a Request for Information Status Report indicating the Contractor's perception of the status of all submitted Requests for Information. The Request for Information Status Report will include a brief description of the request, date the request was submitted to the Designated Representative, date a response is needed from the Architect/Engineer, date a response is actually made by the Architect/Engineer, and any pertinent remarks. The Request for Information Status Report shall be in a format approved by the Designated Representative.

16.2 DRAWINGS, PRODUCT DATA AND SAMPLES

16.2.1 Shop Drawings: Shop drawings are drawings, diagrams, schedules and other data especially prepared for the Work by the Contractor, Subcontractor, Sub-subcontractor, manufacturer, supplier or distributor to illustrate some portion of the Work. Shop drawings shall be signed by a registered professional engineer where required by law.

16.2.2 Product Data: Product data are illustrations, standard schedules, performance charts, instructions, brochures, diagrams and other information furnished by the Contractor to illustrate a material, product, equipment or system for some portion of the Work.

16.2.3 Samples: Samples are physical examples which illustrate materials, equipment or workmanship and establish standards by which the Work will be judged.

16.2.4 Submittals: Submittals forwarded by the Contractor to the Designated Representative shall be in conformance with the requirements of the Contract Documents. The Contractor shall notify the Architect/Engineer and Designated Representative in writing of any deviations in the submittals from the requirements of the Contract Documents at the time of submission. Before submission of each Shop Drawing, Product Data or Sample, the Contractor shall have determined and verified all quantities, dimensions, specified design and performance criteria, installation requirements, materials, catalog numbers and similar data with respect thereto and review or coordinated each Shop Drawing, Product Data or Sample with other Shop Drawings, Product Data and Samples and with the requirements of the Work and the Contract Documents. The term "submittal" as used herein includes Shop Drawings, Product Data and/or Samples as required by the Contract Documents. All submittals shall be submitted thirty (30) days prior to commencement of work affected.

16.2.5 Notice of Variation: At the time of each submission, the Contractor shall give the Architect/Engineer specific written notice of each Contractor perceived variation that the submittal may have from the requirements of the Contract Documents and, in addition, the Contractor shall cause a specific notation to be made on each Shop Drawing, Product Data and/or Sample submitted to the Architect/Engineer for review and "approval" demonstrating each such perceived variation.

16.2.6 Architect/Engineer Submittal Review: The Architect/Engineer will review and "approve" with reasonable promptness the required submittals. The Architect/Engineer's review and approval of the Contractor's submittal does not constitute a complete check, but indicates only that design, general method of construction and detailing is satisfactory. The Architect/Engineer's review and approval does not permit any deviation from the Contract Requirements and does not relieve the Contractor of the responsibility for errors in dimensions, details, sizes of member, etc., or the coordinating of installation and construction with actual conditions of the Work. The Architect/Engineer's review and "approval" will be only for conformance with the design concept of the Project and

for compliance with the information given in the Contract Documents and shall not extend to means, methods, techniques, sequences or procedures of construction (except where a specific means, the methods, technique sequence or procedure of construction is indicated in or required by the Contract Documents) or to safety precautions or safety programs incident thereto. The individual review and "approval" of a component item as such will not indicate "approval" of the integrated final assembly into which the item is placed and in which the item must function. The Contractor shall make any corrections required by the Architect/Engineer, without any additional cost to the Owner. The Contractor shall return the required number of corrected copies of submittals to the Architect/Engineer who will promptly, as required, review the re-submittals for conformance with the design concept.

16.2.7 Resubmission Notice: The Contractor shall direct specific attention, in writing or on resubmitted Shop Drawings, Product Data or Samples, to all revisions other than those requested by the Architect/Engineer or Designated Representative on previous submittals.

16.2.8 Contractor Responsibility: Review and "approval" of submittals by the Architect/Engineer shall not relieve the Contractor from responsibility for any variation from the requirements of the Contract Documents unless the Contractor has in writing called the Architect/Engineer's attention to each such variation at the time of submission as required and the Architect/Engineer has given written approval of each such variation by a specific written notation thereof incorporated in or accompanying the submittal "approval"; nor will any "approval" by the Architect/Engineer relieve the Contractor from the responsibility for the Contractor's own errors or omissions in the submittal or from the Contractor's responsibility for compliance with all Contract Document provisions.

16.2.9 No Work Prior to Submittal Approval: The Contractor shall resubmit submittals as required until the Architect/Engineer's approval is obtained. No work requiring submittals shall be executed until the Architect/Engineer's approval is given. Where a submittal is required by the Specifications, any related work performed prior to the Architect/Engineer's review and "approval" of the pertinent submission will be at the sole risk, expense and responsibility of the Contractor.

16.2.10 Transmittal Requirements: After checking and verifying all field measurements and complying with applicable procedures specified in the Contract Documents, the Contractor shall transmit all submittals to the Architect/Engineer with one (1) copy to the Designated Representative and shall include:

(a.) Date and revision dates.
(b.) Project title and number.
(c.) The names of:
  (1.) Architect/Engineer
  (2.) Designated Representative
  (3.) Contractor
  (4.) Contract Number
  (5.) Subcontractor or Supplier
  (6.) Manufacturer
  (7.) Separate Detailer when pertinent

(d.) Number of Shop Drawings, Product Data and Sample submitted. (System to be established by Designated Representative.)
(e.) Identification of product or material.
(f.) Relation to adjacent structure or materials.
(g.) Field dimensions, clearly identified as such.
(h.) Specification section number and paragraph.
(i.) Applicable standards such as ASTM number or Federal Specification.
(j.) A blank space, minimum of 2 1/2 by 3 1/2 inches for the Architect/Engineer stamp.
(k.) Identification of deviations from Contract Documents.
(l.) Other pertinent data.

16.2.11 Approval Delays: The Contractor shall be responsible for any delays caused by the rejection of the submittal for inadequate or incorrect shop drawings, manufacturer’s data or other information.

16.2.12 Working Drawings: The Contractor is responsible for seeing that only "Approved" copies of shop drawings bearing the stamp of the Architect/Engineer are allowed on the job.

16.2.13 Approved Equals: The Contractor's attention is directed to Article 5.4 LABOR AND MATERIALS. Where two or more products are specified for an item of Work, either one thereof is acceptable and the choice is left to the Contractor. Where only one product is specified and where the term "or approved equal" or similar wording is used in connection with specified products, the Contractor may, if he so desires, offer for consideration a substitute product which he judges to be equal in every respect to the required product. When a specific process is specified as well as a guarantee of the results, the Contractor shall, if in its judgement the process may not produce the required result, submit for approval, an alternative process which he would guarantee. All such submittals shall be made, within forty (40) calendar days after award of the Contract, in writing to the Designated Representative, who in turn will forward them to the Architect/Engineer. Review of any substitute product will (1) be contingent upon submission of substantiating serviceability to specified product; (2) use of the item will not entail changes in details and construction of related Work; (3) item conforms to required design and artistic effect. The Contractor shall furnish with the first submittal, a sufficient number of drawings, specifications, samples, performance data and other information necessary to assist the Architect/Engineer in determining whether the proposed substitution is

acceptable. The burden of proof shall be upon the Contractor. No consideration will be given to incomplete submittals. Substitutions shall be approved in writing before they may be used.

16.2.14 Conflicting Instructions: When product manufacturer's instructions are in conflict with the Contract Documents, the Contractor shall notify the Designated Representative for clarification before proceeding. The Contractor shall keep a copy of the various product manufacturer's instructions applicable to the Work at the project site.

16.2.15 Submittal Log: Each week on a day agreed to between the Contractor and the Designated Representative, the Contractor shall submit an updated submittal log to the Designated Representative indicating the Contractor's perception of the status of all required submittals and reviews. Similar information to that outlined below shall be provided for any required re-submittals. The submittal log will include such information as:

(a.) The schedule date to receive information from a subcontractor or supplier.
(b.) The actual date information was received from a subcontractor or supplier.
(c.) The scheduled date to submit information to the Architect/Engineer.
(d.) The date information was submitted to Architect/Engineer.
(e.) Anticipated date of return of information from Architect/Engineer.
(f.) Actual date information was received from Architect/Engineer.
(g.) Status or actions required.

16.2.16 Sample Submission: The Contractor shall submit all required samples for review and "approval" by the Architect/Engineer, with such promptness as to cause no delay in the Work. All samples shall be checked by the Contractor and accompanied by a specific written indication that the Contractor has satisfied Contractor's responsibilities under the Contract Documents with respect to the Contractor's review of the submission. The samples shall be identified clearly as to equipment, material, supplies and include pertinent data such as demonstrating compliance with a certain Specification Section, catalog number, etc., and the use for which the material is intended. An approved sample of each material shall be provided to the Designated Representative prior to delivery of any materials for which submission of samples is required.

16.2.17 Sample Review: The Contractor shall submit four (4) samples of materials to the Architect/Engineer for approval as indicated in the Specifications. All samples shall be properly labeled to indicate type of material submitted, intended use, manufacturer's name, trade name, project name, Designated Representative's name, Contractor's, Subcontractor's and Supplier's names; and shall be transmitted as required by paragraph 16.2.10. Samples will be inspected and tested as required and if acceptable an approved notice will be sent to the Contractor along with one (1) approved sample. Rejected samples will be returned along with a statement of reasons for rejection. Accepted samples will be retained by the Architect/Engineer, one of which will be provided to the Designated Representative and shall become the property of the Owner.

16.2.18 Submittals Affecting the Contract Sum: The Architect/Engineers approval of submittals which deviate from the Contract Documents does not authorize changes to the Contract Sum. The Contractor shall notify the Architect/Engineer and the Designated Representative in writing at the time of transmittal of any changes to the Contract Sum affected by such approval of a submittal; otherwise, claim for extras will not be considered.

16.2.19 Ductwork Layout Drawings: As soon as practical and in no case starting later than thirty (30) days after the award of contract, the Mechanical Subcontractor shall prepare layout drawings of all duct work and piping at not less than 3/8" scale. The ductwork layout drawings shall show registers, grilles, diffusers and similar features as well as locations of all valves, dampers and other items requiring access for service and maintenance. The ductwork layout drawings shall also show beams, ceiling heights, walls, floor to floor dimensions, columns, doors and other major architectural and structural features as shown on the architectural and structural drawings.

16.2.20 Coordination with Subcontractors: The Contractor shall, within sixty (60) days after award, send a reproducible and two (2) prints of the ductwork layout drawings to the plumbing, materials handling, fire protection and electrical subcontractors who shall then make on the reproducible their own routings as well as other major items such as valves, access panels, switch panels, etc., as required to determine interrelationship and possible interferences with the mechanical ductwork and architectural or structural features. The marked-up reproducible shall then be returned to the Mechanical Subcontractor through the Contractor with copies to the Designated Representative no less than thirty (30) days after receipt by the other Subcontractors.

16.2.21 Composite Drawings: The Mechanical Subcontractor shall prepare preliminary composite drawings of such layout drawings, incorporating all the information and routings provided by the other Subcontractors. (At its option, a group of transparent overlays may be substituted, provided that they clearly show the relationship of all proposed installations.) The preliminary composite drawings, or the overlays, shall be reviewed during a series of meetings, called by the Contractor and attended by the Architect/Engineer and the Designated Representative, at which all Subcontractors and trades shall be represented, in order to review and resolve any real or apparent interferences or conflicts.

16.2.22 Agreement by Subcontractors: After all conflicts or interferences are resolved the Mechanical Subcontractor shall develop a final set of composite drawings showing the agreed upon routing, layout and juxtaposition of all ductwork, conveyers, piping, major conduit, valves, panels, lighting fixtures and all other major mechanical and electrical installations. In areas where no mechanical ductwork occurs, but where other mechanical and electrical installations are installed, each Subcontractor shall be responsible for its own Work and shall cooperate in preparing similar composite drawings, shall perform its own drafting Work and pay its own costs in connection therewith. In

preparation of all the final composite drawings, large scale details as well as cross and longitudinal sections shall be as required to fully delineate all conditions. Particular attention shall be given to the locations, size and clearance dimensions of equipment items, shafts and similar features. These final composite drawings shall then be signed-off by each of the Subcontractors, including the Mechanical Subcontractor, and the Contractor indicating their awareness of and agreement with the indicated routings and layouts and their interrelationship with the adjoining or contiguous Work. Thereafter, no unauthorized deviations will be permitted and if made without knowledge or agreement of the Architect/Engineer and Designated Representative, this unauthorized Work will be subject to removal and correction at no additional cost to Owner.

16.2.23 Minor Changes: In preparing the composite drawings, minor changes in duct, pipe or conduit routings that do not affect the intended function may be made as required to avoid space conflicts, when mutually agreed, but items may not be resized or exposed items relocated without the Architect/Engineers and Designated Representative's written approval No changes shall be made in any wall or chase locations, ceiling heights, door swings or locations, window or other openings or other features affecting the function or aesthetic effect of the building. If conflicts or interferences cannot be satisfactorily resolved, the Architect/Engineer and the Designated Representative shall be notified and their decision obtained.

16.2.24 Distribution of Composite Drawings: After the final composite drawings have been agreed upon and signed by all Subcontractors, the Contractor shall provide and distribute four (4) prints to each of the Subcontractors, to the Architect/Engineer and to the Designated Representative for reference and record purposes. The Contractor shall make similar distribution of all supplementary composite drawings, initiated by other Subcontractors as indicated herein before. All Subcontractors desiring additional prints of such drawings, beyond the basic distribution indicated above, shall arrange for and pay the cost of the same.

16.2.25 Record Composite Drawings: The record copies of the final composite drawings shall be retained by the Designated Representative and each Contractor as a working reference. All shop drawings, prior to their submittal to the Architect/Engineer, shall be compared with the composite drawings and developed accordingly by the Contractor and the responsible Subcontractor. Any revision to the composite drawings which may become necessary during the progress of the Work shall be noted by the Contractor and all Subcontractors and shall be neatly and accurately recorded on the record copies. The Contractor and each Subcontractor shall be responsible for the up-to-date maintenance of its record copies of the composite drawings and to keep two (2) copies available at the site. The composite drawings and any subsequent changes thereto, shall be utilized by the Contractor and each Subcontractor in the development of its "Record Document" drawings.

16.2.26 Timely Submissions: The composite drawings need not be submitted as a whole, but they shall be submitted in all cases in ample time to avoid construction delay. The coordination drawings may lack complete data in certain instances pending receipt of shop drawings, but sufficient space shall be allotted for the items affected. When final information is received, such data shall be promptly inserted on the composite drawings.

16.2.27 Improperly Coordinated Work: No extra compensation will be paid for relocating any duct, pipe, conduit, or other material that has been installed without proper coordination between the Contractor and all Subcontractors involved. If any improperly coordinated Work or Work installed that is not in accordance with the approved composite drawings, necessitates additional Work by the Contractor or other Subcontractors, the costs of all such additional Work shall be borne solely by the Contractor or the Subcontractor responsible for the nonconforming Work.

16.2.28 Incorporation of Changes: All changes in the scope of Work due to revisions formally issued and approved shall be shown on the composite drawings.

16.2.29 Quality Draftsmanship: All Work on shop drawings, ductwork layout drawings, coordination drawings, and composite drawings shall be performed by competent draftsmen and shall be clear and fully legible. The Architect/Engineer shall be the sole judge of the acceptability of the drawings.

16.2.30 Structural Cutting: The Contractor shall obtain specific positive written instructions from the Architect/Engineer through the Designated Representative before cutting beams or other structural members, arches or lintels, and the Contractor shall be guided by such instructions.

16.3 TEMPORARY SERVICES, SYSTEMS AND FACILITIES

16.3.1 Temporary Lighting, Power and Water: At its own expense, the Contractor shall furnish, install, maintain, and remove all temporary lighting, electric power, and potable water, including piping, wiring, lamps, and other equipment necessary for the execution and security of the Work; and shall be responsible for the cost of power and water usage. The Contractor shall not draw water from any fire hydrant, except to extinguish a fire, without first obtaining permission from the water agency concerned. The Contractor shall provide for distribution of drinking water to all work forces under this Contract.

16.3.2 Sanitation: The Contractor shall provide and maintain portable enclosed toilets for the use of all work forces under this Contract. These accommodations shall be maintained in a neat and sanitary condition. They shall also comply with all applicable laws, ordinances and regulations pertaining to the public health and sanitation of dwellings and camps. The Contractor shall not interrupt the flow of existing sanitary sewers. Should the Work involve the disruption of existing sewer facilities, the Contractor shall convey the sewage in closed containers and shall dispose of it in a sanitary sewer system as approved by local health authorities and the Designated Representative. Sewage shall not be permitted to flow in trenches or be covered by backfill.

16.3.3 Vermin Control: The Contractor shall maintain the job site free of rodents, insects, vermin and pests throughout all phases of construction, including suspensions of work, and until final acceptance of the Work. Necessary extermination work shall be arranged and paid for by the Contractor as part of the contract work and contract time and shall be performed by a licensed agency in accordance with requirements of governing authorities. The Contractor shall be liable for injury to persons or property and responsible for the elimination of offensive odors resulting from extermination operations.

16.3.4 Water Pollution Control: The Contractor shall exercise every reasonable precaution to protect channels, storm drains, and bodies of water from pollution and shall conduct and schedule its operations so as to minimize or avoid muddying and silting of said channels, drains, and waters. Water pollution control work shall consist of constructing those facilities which may be required to provide prevention, control, and abatement of water pollution.

16.3.5 Air Pollution Control: The Contractor shall not discharge smoke, dust, or any other air contaminants into the atmosphere in such quantity as will violate the regulations of any legally constituted authority.

16.3.6 Project Site Maintenance: Throughout all phases of construction, including suspensions of work, and until final acceptance of the Work, the Contractor shall keep the job site, including the interior of all structures, clean and free from rubbish and debris. The Contractor shall provide and maintain rubbish containers and periodic rubbish removal services as required by the pace of the Work and health regulations, and as acceptable to the Designated Representative.

16.3.6.1 The Contractor shall abate dust nuisance by cleaning, sweeping, and sprinkling with water, or other means as necessary. The use of water resulting in mud on public streets will not be permitted as a substitute for sweeping or other methods.

16.3.6.2 Materials and equipment shall be removed from the site as soon as they are no longer necessary; and upon completion of the Work and before final inspection the entire work site shall be cleared of equipment, unused materials, and rubbish so as to present a satisfactory clean and neat appearance. All cleanup costs shall be absorbed in the Contractor's bid.

16.3.6.3 The Contractor shall take care to avoid spillage on haul routes. Any such spillage shall be removed immediately and the area cleaned by the Contractor.

16.3.6.4 Burning or burying of rubbish and waste materials on the project site is prohibited. Disposal of volatile fluid wastes in storm and sanitary sewer systems is prohibited.

16.3.6.5 Waste materials shall not be dropped or thrown from heights. Cleaning operations shall be scheduled so that dust and other contaminants resulting from the cleaning process will not fall on wet or newly painted surfaces. Dusty debris shall be sprinkled lightly with water as required to control dust.

16.3.6.6 The Contractor shall vacuum clean the interior of buildings prior to the start of finish painting. The Contractor shall continue vacuum cleaning thereafter on an as needed basis until the building is ready for acceptance.

16.3.6.7 Failure of the Contractor to comply with the Designated Representative's cleanup orders may result in an order to suspend the Work until the condition is corrected. No additional compensation will be allowed as a result of such suspension.

16.3.7 Final Cleaning: At the completion of the Work, the Contractor at its sole expense shall remove all waste materials and rubbish from and about the project, as well as all tools, construction equipment, temporary facilities, machinery, and surplus materials.

16.3.7.1 At completion of construction and just prior to final inspection, the Contractor shall thoroughly clean the interior and exterior of the buildings, including hardware, floors, roofs, sills, ledges, glass, or other surfaces where debris, plaster, paint, spots, and dirt or dust may have collected. All glass shall be washed clean and polished. All grease, stains, labels, fingerprints, and other foreign materials shall be removed from interior and exterior surfaces. The Contractor shall repair, patch, and touch up marred surfaces to match adjacent finishes.

16.3.7.2 The Contractor shall use only experienced workmen or professional cleaners for final cleaning. Use only cleaning materials recommended by the manufacturer of the surface to be cleaned, and use cleaning materials only on surfaces recommended by the cleaning material manufacturer.

16.3.7.3 The Contractor shall broom clean all paved surfaces and rake clean other surfaces of grounds.

16.3.7.4 The Contractor shall replace air conditioning filters, if units were operated during construction. The Contractor shall clean all ducts, blowers, and coils if air conditioning units were operated at any time without filters during construction.

16.3.7.5 The Contractor shall maintain the building in a clean condition until it is accepted by the Owner.

16.3.8 Fire Protection: The Contractor at its sole expense shall provide temporary fire safety equipment for general use. The Contractor shall provide fire extinguishers for its trailers, for use as required when cutting and burning is

performed, and as required throughout the job site as instructed by the local fire marshal.

16.3.9 Communication Systems: The Contractor shall provide telephone services at its own expense. The Contractor at its sole expense shall maintain in service a facsimile telecopy machine whenever telephone service is available at the job site. The use of portable radios shall be in accordance with Federal Regulations and shall not interfere with other local radio operations.

16.3.10 Office Facilities: The Contractor at its sole expense shall provide, maintain and remove temporary field office facilities, including all furniture, equipment, copiers, heating, cooling, lighting, power, telephones, drinking water, plumbing and toilet fixtures as necessary for its performance of the Work; and shall make these spaces, telephones, and services available for the use of the Owner, the Designated Representative and the Architect/Engineer. A designated work area shall be provided for the use of the Owner, the Designated Representative and the Architect/Engineer.

16.3.11 Weather Protection: The Contractor at its sole expense shall be responsible for providing protection for its own Work against inclement weather, in order to maintain all Work, materials, apparatus, and equipment. All Work subject to damage by adverse weather conditions shall be covered or otherwise protected as required. Weather protection shall be adequate to permit the Contractor to Work on a continuous basis without shutdown due to temperature or weather conditions as far as possible.

16.3.12 Dewatering: The Contractor at its sole expense shall provide all temporary drainage and dewatering measures including all pumping, drainage, erosion control or other work required to protect the Work while in progress.

16.3.12.1 Inundation of partially completed work due to lack of control during non-working periods will not be permitted, and may be cause for requiring removal of work already completed with replacement at the Contractor's expense.

16.3.12.2 The Contractor shall be responsible for obtaining the use of any property, in addition to that provided for in the plans and specifications, which may be required for the diversion and protective works so as not to create a hazard to persons or property or to interfere with the water rights of others.

16.3.12.3 It shall be understood and agreed that the Contractor shall hold the Owner and the Designated Representative harmless from legal action taken by any third party with respect to construction and operation of the diversion and protective works.

16.3.12.4 All works installed by the Contractor in connection with dewatering, control, and diversion of water but not specified to become a permanent part of the project, shall be removed and the site restored, insofar as practical, to its original condition prior to completion of construction or when directed by the Designated Representative.

16.3.13 Material Handling: The Contractor at its sole expense shall be responsible for handling and transporting, including lifting, its material and equipment to the location of need in a timely manner.

16.3.14 Cranes, Hoists and Scaffolds: The Contractor at its sole expense shall furnish, erect, maintain and remove all cranes, temporary hoists and scaffolding as may be required by the Contractor for the performance of the Work.

16.3.15 Storage: The Contractor at its sole expense shall provide and remove whatever temporary storage facilities, sheds, buildings, enclosures, partitions, etc., he deems necessary for the protection of its materials, tools and equipment after receiving approval from the Designated Representative on specific details of the method proposed. Any damage caused to Work in place by these temporary measures will be repaired / replaced at the Contractor's expense.

16.3.16 Security Fences: The Contractor at its sole expense shall provide temporary site enclosures (fences), barriers, and pedestrian walkways as indicated by the Contract Documents or as required to control access to the job site.

16.3.17 Security Services: The Contractor at its sole expense shall be responsible for job site security during various phases of the Work, including non-working hours and at other times, and as may be required for the protection of the Owner and the Designated Representative's interests. All costs for same will be paid by the Contractor.

16.3.18 Openings, Sleeves and Supports: The Contractor at its sole expense shall provide all necessary openings, channels, chases, flues, sleeves, inserts, hangers, etc, if any, and such cutting, patching, finishing, etc., if any, required by the Contract Documents to complete the Work.

16.3.19 Protection and Restoration of Existing Improvements: The Contractor at its sole expense shall be responsible for the protection of public and private property adjacent to the Work and shall exercise due caution to avoid damage to such property. All costs to the Contractor for protecting, removing, and restoring existing improvements shall be paid by the Contractor.

16.3.19.1 The Contractor at its sole expense shall repair or replace all existing improvements which are damaged or removed as a result of its operations and which are not designated for removal (e.g. curbs, sidewalks, driveways, fences, walls, ceilings, floor coverings, signs, utility installations, pavements, structures, trees, shrubbery, grass etc.).

16.3.19.2 Repairs and replacements shall be at least equal to existing improvements and shall match them in finish and dimensions in such a manner that the repaired work will not be readily noticeable.

16.3.20 Excavation Protection: The Contractor at its sole expense shall provide and maintain fencing, shoring and bracing and dewatering of all excavation.

16.3.21 Temporary Safety Measures: The Contractor at its sole expense shall provide, maintain and remove when no longer required all temporary safety measures, including all construction supplies, barricades, pedestrian walkways and equipment as may be required by the Contract Documents for its Work.

16.3.22 Advertising: The names of the Contractor, Subcontractors, the Architect/Engineer, including their consultants, with their addresses and the designation of their particular specialties, may be displayed on removable signs. The size, format and location of such signs shall be subject to the Designated Representative's approval. Commercial advertising matter shall not be attached or painted on the surfaces of buildings, fences, canopies, or barricades. All signs shall be removed when directed by the Designated Representative but not later than final acceptance of the Work.

16.4 SAFETY

16.4.1 OSHA and California Codes and Regulations: The Contractor at its sole expense shall provide, erect, maintain, dismantle and remove any and all barricades, railings, covers, warning lights, safety netting, and similar safety devices required to complete its Work and protect the public in accordance with OSHA, California Administrative Code, Title 8 Industrial Relations, Chapter 4 Division of Industrial Safety, Section 4 Construction and Safety Orders, Article 8 Explosives, and all other applicable code requirements.

16.4.2 Traffic Control: The Contractor shall conduct its Work so as to interfere as little as possible with pedestrian and vehicular traffic and he shall, at its sole expense, provide and maintain proper warnings and detour signs at all pedestrian and vehicular closures, intersections and along detours, directing traffic around closed portions of roadways. He shall, at its own expense, wherever necessary or required, provide and maintain fences, temporary roadways, temporary crossing signs, watchmen, warning lights and take such other precautions as may be necessary to protect life and property and shall be responsible for all damages occasioned in any way by its act or neglect. All barricades and obstructions shall be illuminated at night and all lights shall be kept on from one-half hour before sunset until one-half hour after sunrise.

16.4.3 Fall Protection: When performing any cutting, removal, creating openings or holes, etc., the Contractor at its sole expense, by use of barricades, flagmen or other means, shall provide protective measures to assure that other workmen or the public are not exposed to potential injury by the operation being conducted.

16.4.4 Welding Protection: The Contractor at its sole expense shall provide, maintain and remove all shielding or similar precautions required to be taken adjacent to welding operations.

16.4.5 Personal Equipment: The Contractor at its sole expense shall provide and supervise the use of all proper safety and protective devices by its employees during any potentially dangerous phases of its Work.

16.4.6 Safety Orders: The Contractor shall have at the work site, copies or suitable extracts of: Construction Safety Orders, Electrical Safety Orders, and General Industrial Safety Orders issued by the State Division of Industrial Safety. The Contractor shall comply and shall require the compliance by all Subcontractors with provisions of these Safety Orders and all other applicable laws, ordinances, and regulations.

16.4.7 Trench Excavations: As required by Section 6705 of the California Labor Code and in addition thereto, whenever work under the Contract involves the excavation of any trench or trenches five (5) feet or more in depth, the Contractor shall submit for acceptance by the Owner, a detailed plan showing protection of the worker from the hazard of caving ground.

16.4.8 Use of Explosives: Explosives may be used only when authorized in writing by the Owner, or as otherwise stated in the Contract Documents. Explosives shall be handled, used, and stored in accordance with all applicable regulations. The Owner's approval of the use of explosives shall not relieve the Contractor from its liability for claims caused by its blasting operations.

16.4.9 Hazardous Materials: The Contractor shall immediately stop work if unforeseen suspected hazardous material conditions are encountered. The Contractor shall immediately report the unforeseen conditions in the written form of a request for information submitted to the Designated Representative. Work shall be resumed after the Owner has fully resolved the questions related to the unforeseen conditions and has remediated any hazardous materials determined to be present.

END OF GENERAL CONDITIONS

GENERAL SERVICES – CAPITAL PROJECTS DIVISION

ADDENDUM NOTICE

May 19, 2025

ADDENDUM NO. 1

COUNTY PROJECT NO. 22011

REHABILITATE TIE-DOWN APRON
900 AIRPORT ROAD, SANTA YNEZ, CA.

Prepared By: Jason Hargreaves Date: May 19, 2025

Reviewed By: Steven Manuel Date: May 19, 2025

To All Prospective Bidders:

Your attention is directed to the bid information on the attached page(s) that contain a summary of the modifications to the identified Bid Documents and the revised Plan and Specification sheets.

This Addendum does not alter the bid opening time and date for this project.

You must acknowledge this addendum on your Bid Form and attach it to your Bid.

This Addendum and all contents mentioned herein, are hereby made a part of the Contract Documents to the same extent as though they were originally included therein; all other conditions shall remain the same.

Bidders are hereby notified of the following:

GENERAL

1. Pre-Pid Job Walk Sign-In Sheet – The sign-in sheet is included as an attachment to this addendum.
2. The Pre-bid job walk is non-mandatory. Any reference to the job walk being mandatory should be disregarded.

CHANGES TO PLANS

3. Plan Sheet 1 – A signature has been added. The revised plan sheet is included is Included as an attachment to this Addendum.

CHANGES TO SPECIFICATIONS

4. Page 1 (Notice to Contractors) – Change the construction cost estimate from "$705,000.00" to now be "$550,000.00".
5. Page 1 (Notice to Contractors) – Change the title of the third paragraph from "Mandatory Job Walk" to now be "Non-Mandatory Job Walk".

CHANGES TO BID SCHEDULE

6. Page 13 (proposal) – Page 13 of the Specification booklet includes the Bid Schedule. Several modifications to the estimated quantities have changed. Page 13 has been revised and is included as an attachment to this Addendum: Summary of Bid Schedule Changes:
   Item 4; Remove Pavement Markings: Change of quantity from 1.0 SF to now be 8,000.0 SF.
   Item 5; Crack Seal: Change of quantity from 1.0 LF to now be 46,000.0 LF.
   Item 6; Emulsified Asphalt Seal Coat: Change of quantity from 1.0 SY to now be 72,500.0 SY.
   Item 7; Markings: 2-Coat with Reflective Media: Change of quantity from 1.0 SF to now be 14,600.0 SF.
   Item 8; Markings: 2-Coat w/o Reflective Media: Change of quantity from 1.0 SF to now be 5,100.0 SF.

ATTACHMENTS

- Pre-Bid Job Walk Sign-In Sheet
- Revised Plan Sheet 1
- Revised Page 13 of the Specification Book (Bid Schedule)

END OF ADDENDUM

SIGN-IN SHEET

Monday, May 19, 2025
900 Airport Road
Pre-Bid Conference/Job Walk
(Non-Mandatory)

No	Firm	Attendee	Phone	E-Mail
1	Tartaglia	Jason Hagreaves	805 556-5771	Jason@tartaglia-engineering.com
2	SBCO	Steven Manuel	805-266-4176	STMANUEL@COUNTYOFSB.ORG
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				


SANTA BARBARA COUNTY, CALIFORNIA

SANTA YNEZ VALLEY AIRPORT

CONSTRUCTION PLANS FOR

REHABILITATE TIE-DOWN APRON

COUNTY PROJECT: NO. 22011
FAA: AIP 3-06-0243-023-2023 (DESIGN)
FAA: AIP 3-06-0243-024-2025 (CONSTRUCTION)

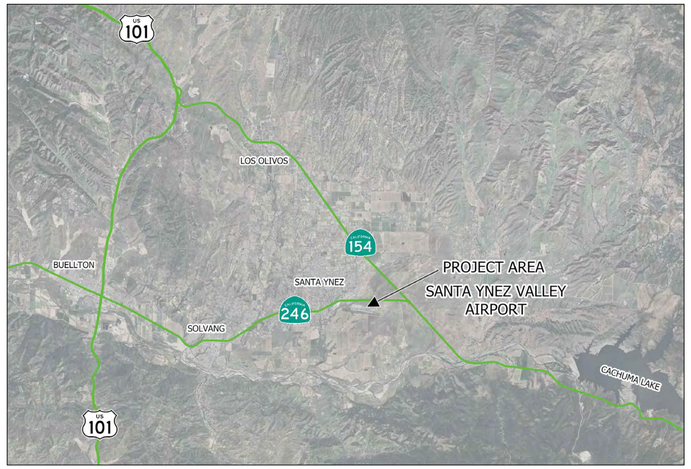

REGIONAL MAP
NO SCALE

APRIL, 2025

GENERAL PROJECT DESCRIPTION

1. REHABILITATE TIE-DOWN APRON AND HANGAR ROWS CONSISTING OF CRACK FILL & SEAL AND P-608 PAVEMENT SEAL COAT, FOLLOWED BY PAVEMENT MARKINGS.

GENERAL CONSTRUCTION ELEMENTS

1. AIRFIELD SAFETY AND SECURITY.
2. CRACK FILL & SEAL.
3. OBLITERATE EXISTING PAVEMENT MARKINGS.
4. REMOVE AND RE-INSTALL AIRCRAFT TIE-DOWN CABLES AND CHAINS.
5. APPLICATION OF P-608 PAVEMENT SEAL COAT.
6. APPLICATION OF OF NEW PAVEMENT MARKINGS.



LOCATION MAP
NO SCALE

SUBMITTED John A. Smith DATE 5-9-2025
JOHN A. SMITH RCE 46852
PROJECT ENGINEER

REGISTERED PROFESSIONAL ENGINEER
JOHN A. SMITH
No. 46852
EXP. 6-30-25
CIVIL
STATE OF CALIFORNIA

REV.	DESCRIPTION	DATE	APP.

UNDERGROUND SERVICE ALERT
811
DIAL 811
TWO WORKING DAYS BEFORE YOU DIG

TARTAGLIA ENGINEERING

1 OF 14
SHEET

22-55
DRAWING NO.

PLOT DATE: 4/11/2025

PROJECT BID SCHEDULE

ITEM NO.	SPEC SECTION	DESCRIPTION	UNIT	ESTIMATED QUANTITY	UNIT PRICE (Figures)	EXTENDED TOTAL (Figures)
1	C-105	Mobilization (8% Max)	LS	1.0	$	$
2	C-104T	Airport Safety and Security (5% Max)	LS	1.0	$	$
3	P-101	Uninstall & Re-Install Tie Down Cables and Chains	LS	1.0	$	$
4	P-101	Remove Pavement Markings	SF	8,000.0	$	$
5	P-101	Crack Seal	LF	46,000.0	$	$
6	P-608	Emulsified Asphalt Seal Coat	SY	72,500.0	$	$
7	P-620	Markings: 2-Coat with Reflective Media	SF	14,600.0	$	$
8	P-620	Markings: 2-Coat w/o Reflective Media	SF	5,100.0	$	$
TOTAL, BID SCHEDULE (Written in Figures):						$

Abbreviations to Bid Schedule(s):

LS = lump sum	TON = 2000 pounds	LF = lineal foot	EA = each unit
SF = square foot	CY = cubic yard	SY = square yard	T&M = time and materials
ACRE = 43,560 square feet		CF = cubic foot	GAL = 1 U.S. Gallon, liquid measure

Total Bid, Basis of Award:

Written in Words:_____

Written in Figures: $_____

In the event of discrepancy between words and figures, the words shall prevail.

In the event that the product of a unit price and an estimated quantity does not equal the extended amount quoted, the unit price shall govern and the correct product of the unit price and the estimated quantity shall be deemed to be the amount bid.

In order for a Bid to be responsive, Bidder must complete all blanks in the Bid Schedule. The failure to do so shall result in the Bid being rejected as non-responsive.

It is understood that Owner reserves the right to reject the proposal and that it shall remain open and not be withdrawn for a period of one hundred twenty (120) calendar days from the date prescribed for its opening.

Attached hereto and incorporated herein is the complete and entire list of subcontractors to be employed by the undersigned and in the performance of the Work.

GENERAL SERVICES – CAPITAL PROJECTS DIVISION

ADDENDUM NOTICE

May 28, 2025

ADDENDUM NO. 2

COUNTY PROJECT NO. 22011

REHABILITATE TIE-DOWN APRON
900 AIRPORT ROAD, SANTA YNEZ, CA.

Prepared By: Jason Hargreaves Date: May 28, 2025

Reviewed By: Diana Estorga Date: May 28, 2025

To All Prospective Bidders:

Your attention is directed to the bid information on the attached page(s) that contain a summary of the modifications to the identified Bid Documents and the revised Plan and Specification sheets.

The bid opening date has been revised to now be Monday, June 2nd, 2025, at 3:00 PM

You must acknowledge this addendum on your Bid Form and attach it to your Bid.

This Addendum and all contents mentioned herein, are hereby made a part of the Contract Documents to the same extent as though they were originally included therein; all other conditions shall remain the same.

Bidders are hereby notified of the following:

GENERAL

1. The latest federal wage rates are included as an attachment to this Addendum.

CHANGES TO SPECIFICATIONS

2. Page 117 (P-608) – Change the bolded sentence in the middle of the page that reads "The asphalt material….. shall contain no less than one percent (3%) polymer." to now be "The asphalt material….. shall contain no less than three and a half percent (3.5%) polymer."
3. Page 119 (P-608) – In the application rate table, change the rate of emulsion from "0.20-0.22" to now be "0.17-0.22."
4. At all locations in the specification booklet that reference the bid opening date, change the bid opening date to now by 3:00 pm Monday June 2, 2025.

CHANGES TO BID SCHEDULE

5. Page 13 (proposal) – The following changes were made to the bid schedule quantities:
   Item 7; Markings: 2-Coat with Reflective Media: Change of quantity from 14,600.0 SF to now be 5,100.0 SF.
   Item 8; Markings: 2-Coat w/o Reflective Media: Change of quantity from 5,100.0 SF to now be 14,600.0 SF.
   Contractors shall use the revised bid schedule with their bids.

ATTACHMENTS

- Revised Bid Schedule: Page 13 of the Specification Book
- Revised Pages: Cover Page, Page 1, 2, 12, 16, 21, 117, and 119 (8 pages)
- Federal Wage Rates (24 pages)

END OF ADDENDUM

PROJECT BID SCHEDULE

ITEM NO.	SPEC SECTION	DESCRIPTION	UNIT	ESTIMATED QUANTITY	UNIT PRICE (Figures)	EXTENDED TOTAL (Figures)
1	C-105	Mobilization (8% Max)	LS	1.0	$	$
2	C-104T	Airport Safety and Security (5% Max)	LS	1.0	$	$
3	P-101	Uninstall & Re-Install Tie Down Cables and Chains	LS	1.0	$	$
4	P-101	Remove Pavement Markings	SF	8,000.0	$	$
5	P-101	Crack Seal	LF	46,000.0	$	$
6	P-608	Emulsified Asphalt Seal Coat	SY	72,500.0	$	$
7	P-620	Markings: 2-Coat with Reflective Media	SF	5,100.0	$	$
8	P-620	Markings: 2-Coat w/o Reflective Media	SF	14,600.0	$	$
TOTAL, BID SCHEDULE (Written in Figures):						$

Abbreviations to Bid Schedule(s):

LS = lump sum	TON = 2000 pounds	LF = lineal foot	EA = each unit
SF = square foot	CY = cubic yard	SY = square yard	T&M = time and materials
ACRE = 43,560 square feet		CF = cubic foot	GAL = 1 U.S. Gallon, liquid measure

Total Bid, Basis of Award:

Written in Words:_____

Written in Figures: $_____

In the event of discrepancy between words and figures, the words shall prevail.

In the event that the product of a unit price and an estimated quantity does not equal the extended amount quoted, the unit price shall govern and the correct product of the unit price and the estimated quantity shall be deemed to be the amount bid.

In order for a Bid to be responsive, Bidder must complete all blanks in the Bid Schedule. The failure to do so shall result in the Bid being rejected as non-responsive.

It is understood that Owner reserves the right to reject the proposal and that it shall remain open and not be withdrawn for a period of one hundred twenty (120) calendar days from the date prescribed for its opening.

Attached hereto and incorporated herein is the complete and entire list of subcontractors to be employed by the undersigned and in the performance of the Work.

ADDENDUM 2

County of Santa Barbara

Rehabilitate Tie-Down Apron

Santa Ynez Airport

900 Airport Road, Santa Ynez, California

AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

JOB WALK:
Monday, May 19, 2025 at 11:00 A.M.
900 Airport Road, Santa Ynez, C.A.

BID OPENING DATE:
3:00 P.M., ~~Friday, May 30, 2025~~
Monday, June 2, 2025

BID OPENING LOCATION:
Bids to be Submitted Electronically

NOTICE TO BIDDERS

Notice is hereby given that the General Services Department, County of Santa Barbara will receive bids for:

COUNTY OF SANTA BARBARA,

Rehabilitate Tie-Down Apron

Santa Ynez Airport

900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

JOB WALK:
Monday, May 19, 2025 at 11:00 A.M.
900 Airport Road, Santa Ynez, C.A.

BID DUE DATE:
3:00 P.M., ~~Friday, May 30, 2025~~ Monday, June 2, 2025

CONSTRUCTION COST ESTIMATE: ~~$705,000.00~~ Dollars
$ 550,000.00

PROJECT LOCATION:
Santa Ynez Airport, 900 Airport Road, Santa Ynez, Santa Barbara County, California

NON-MANDATORY
~~MANDATORY~~ JOB WALK:
There will be a job walk on Monday, May 19, 2025 at 11:00 A.M. Meet outside the Airport Administration office, 900 Airport Road, Santa Ynez, California**.**

PROJECT DESCRIPTION:
The project focuses on rehabilitating the tie-down apron including crack repair and a surface treatment with the following work elements:

- Airfield safety and security.
- Clearing, grubbing, and removals.
- Temporary removal of tie down cables, chains, and fasteners.
- Pavement cleaning.
- Crack fill and seal.
- Application of an emulsified asphalt seal coat.
- Pavement markings.
- Reinstallation of aircraft tie down cables, chains, and fasteners

BIDDERS QUESTIONS:
All questions MUST be submitted electronically through the project Public Purchase Portal (www.publicpurchase.com) on or before 3:00 pm, five (5) business days prior to the day of the bid opening. Any changes or additional information needed for bidding will be provided in an Addendum posted on the Public Purchase site. Contractors shall be responsible for addendums

BID SUBMITTAL INSTRUCTIONS: Each bid shall be in accordance with the plans and specifications approved by the General Services Department. The bid MUST be submitted electronically through the Public Purchase website (www.publicpurchase.com) on or before **3:00 P.M., ~~Friday, May 30, 2025~~** Monday, June 2, 2025

SUBSTITUTION OF SECURITIES: Pursuant to Section 22300 of the Public Contract Code and the project specifications, the CONTRACTOR may substitute securities or request that the County make payment of retentions to an escrow agent for any money held by the COUNTY to ensure contract performance.

REGISTRATION: No contractor or subcontractor may be listed on a bid proposal for a public works project (submitted on or after March 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5 [with limited exceptions from this requirement for bid purposes only under Labor Code § 1771.1(a)]; no contractor or subcontractor may be awarded a contract for public work on a public works project (awarded on or after April 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5; and this project is subject to compliance monitoring and enforcement by the Department of Industrial Relations.

QUALIFYING CONTRACTOR OR SUBCONTRACTOR: Pursuant to the provisions of Section 4104 of the California Public Contracting Code a contractor or subcontractor shall not be qualified to bid on, be listed in a bid proposal or engage in the performance of any contract for public work, as defined in Section 4104, unless currently registered with the Department of Industrial Relations and qualified to perform public work pursuant to Section 1725.5 California Labor Code.

WITHDRAWAL OF BIDS:
The COUNTY reserves the right to reject any and or all bids or waive any informality in a bid. No bidder may withdraw his bid for a period of one hundred twenty (120) days after the date set for the opening thereof.

BID SELECTION:
The COUNTY reserves the right to select any one or any combination of bids, whichever is in the best interest of the COUNTY.

CONSTRUCTION TIME:
The successful CONTRACTOR (after receiving the Notice to Proceed) shall have **50 Working days** to complete all work called for under the Contract Documents.

LIQUIDATED DAMAGES:
The liquidated damages will be **$500.00 Dollars** per calendar day for project delays that are determined to be attributable to the CONTRACTOR.

BID BOND:
Each bid must be accompanied by a Certified Check, a Cashier's Check or a Bid Bond, as here and after provided in the amount of Ten Percent (10%) of the total of the bid, made payable to the County of Santa Barbara, as a guarantee that the bidder, if awarded the contract, will enter into a Contract for the performance thereof, satisfactory to said County's Board of Supervisors. Surety shall be listed in the Insurance Organizations Authorized By The Insurance Commissioner To Transact Business Of Insurance In The State Of California During 1994 (including changes effective January 1, 1995) published by the Department of Insurance, State of California, or successor publication. Personal and Corporate guarantees will not be acceptable.

PROPOSAL

Pursuant to and in compliance with your Notice to Bidders and the Contract Documents relating to the construction of:

County of Santa Barbara

Rehabilitate Tie-Down Apron

900 Airport Road, Santa Ynez, California
County Project No. 22011-AIP XX
Bid Date 3:00 pm, ~~**Friday, May 30, 2025**~~
Monday, June 2, 2025

including Addendum No(s). ___, ___, ___, ___, ___, ___, ___, the undersigned bidder, having become thoroughly familiar with the terms and conditions of the Contract Documents and with local conditions affecting the performance and the costs of the Work at the place where the Work is to be done, hereby proposes and agrees to fully perform the Work within the time stated in and in strict accordance with the Contract Documents (including the furnishing of any and all labor, materials, tools, expendable equipment and utility and transportation services necessary to fully perform the work and complete it in a workmanlike manner) for the total sum of:

Written if Figures: $_____

Written in Words: _____

Bid Schedule follows on the next page. Bidding Contractors to complete all blanks on the Bid Schedule:

Name of Bidder: _____

California Contractors License Number (Class): _____

DESIGNATION OF SUBCONTRACTORS

The bidder agrees if this proposal is accepted, that he will contract with the County of Santa Barbara to do all work and furnish all labor, materials, machinery, tools and apparatus necessary to completely perform said Contracts in the manner and time prescribed by said Contract.

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011
Bid Date 3:00 pm, ~~**Friday, May 30, 2025**~~
Monday, June 2, 2025

In compliance with the provisions of Section 4100-4107 of the Public Contract Code of the State of California, and any amendments, thereof, the undersigned bidder has set forth below the name and location of the place of business of each subcontractor who will perform work or labor or render service to the undersigned in or about the construction of the work to be performed. That portion of the work which will be done by each subcontractor for each subcontract in excess of one-half of one percent of the undersigned's total aggregate bid shall be listed..

SUBCONTRACTORS LIST		
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )

BIDDER'S BOND

KNOW ALL MEN BY THESE PRESENTS:

That we, _____ as Principal, and _____ as Surety (hereinafter referred to as Surety), are held firmly bound unto the County of Santa Barbara, State of California (hereinafter called "Owner") in the penal sum of Ten Percent (10%) of the total aggregate amount of the bid of the Principal above named, submitted by said Principal to Owner for the work described below, for the payment of which sum in lawful money of the United States, well and truly to be made, we bind ourselves, our heirs, executors, administrators, and successors, jointly and severally, firmly by these presents. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications. In no case shall the liability of the Surety hereunder exceed the sum of _____ DOLLARS ($_____). The condition of this obligation is such that a bid to Owner for certain construction specifically described as follows:

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
County Project No. 22011-AIG XX

for which bids are to be opened on **3:00 pm, ~~Friday, May 30, 2025~~,** Monday, June 2, 2025 has been submitted by Principal to Owner.

NOW, THEREFORE, if the aforesaid Principal shall not withdraw said bid within the period therein after the opening of the same, or, if no period be specified within one hundred twenty (120) days after said opening and shall within the period specified therefore, or, if no period be specified, within eight (8) days after the prescribed forms are presented to him for signature, enter into a written Contract with Owner, in the prescribed form, in accordance with the bid as accepted, and file the two Bonds with Owner, one to guarantee faithful performance and the other to guarantee payment for labor and materials, as required by law, then this obligation shall be null and void; otherwise, it shall remain in full force, virtue and affect.

Said Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration or addition to the terms of said Contract or to the work to be performed thereunder or the Specifications accompanying the same shall in any manner affects its obligations on this bond, and it does hereby waive notice of any change, extension, alteration, or addition.

It is hereby agreed that any progress payment made after the scheduled completion date will not constitute a waiver of any liquidated damages heretofore agreed upon.

In the event suit is brought upon said Bond by Owner and judgment is recovered, the Surety shall pay all costs incurred by Owner in such suit, including a reasonable attorney's fee to be fixed by the Court.

Death, Bankruptcy, Receivership, Going Out of Business for any reason, or incompetence of the

608-2.2 Asphalt Emulsion. The asphalt emulsion shall meet the properties in the following table:

Concentrated Asphalt Emulsion Properties

Properties	Specification	Limits
Viscosity, Saybolt Furol at 77°F (25°C)	ASTM D7496	20 – 100 seconds
Residue by Distillation or Evaporation	ASTM D6997 or ASTM D6934	57% minimum
Sieve Test	ASTM D6933	0.1% maximum
24-hour Stability	ASTM D6930	1% maximum
5-day Settlement Test	ASTM D6930	5.0% maximum
Particle Charge [1]	ASTM D7402	Positive 6.5 maximum pH

[1] pH may be used in lieu of the particle charge test which is sometimes inconclusive in slow setting, asphalt emulsions.

The asphalt material base residue shall contain not less than 20% gilsonite, or uintaite and shall not contain any tall oil pitch or coal tar material and shall contain no less than three and a half percent (3.5%) polymer.

Tests on Residue from Distillation or Evaporation

Properties	Specification	Limits
Viscosity at 275°F (135°C)	ASTM D4402	1750 cts maximum
Solubility in 1, 1, 1 trichloroethylene	ASTM D2042	97.5% minimum
Penetration	ASTM D5	50 dmm maximum
Asphaltenes	ASTM D2007	15% minimum
Saturates	ASTM D2007	15% maximum
Polar Compounds	ASTM D2007	25% minimum
Aromatics	ASTM D2007	15% minimum

The asphalt emulsion, when diluted in the volumetric proportion of two parts concentrated asphalt material to one part hot water shall have the following properties:

Two-to-One Dilution Emulsion Properties

Properties	Specification	Limits
In Ready-to-Apply Form, two parts concentrate to one part water, by volume		
Viscosity, Saybolt Furol at 77°F (25°C)	ASTM D7496	5 – 50 seconds
Residue by Distillation or Evaporation	ASTM D6997 or ASTM D6934	38% minimum
Pumping Stability		Pass

test shall indicate no apparent adverse effect with time relative to friction values and existing pavement surface.

Seal coat material submittal without required friction performance will not be approved. Friction tests performed on this project cannot be used as a substitute of this requirement.

COMPOSITION AND APPLICATION RATE

608-3.1 Application Rate. The approximate amounts of materials per square yard (square meter) for the asphalt surface treatment shall be as provided in the table for the treatment area(s) at the specified dilution rate(s) as noted on the plans. The actual application rates will vary within the range specified to suit field conditions and will be recommended by the manufacturer's representative and approved by the RPR from the test area/sections evaluation.

Application Rate

Dilution Rate	Quantity of Emulsion gal/yd^2	Quantity of Aggregate lb/yd^2
2:1	0.17-0.22	0.30-0.40

608-3.2 Control areas and control strips. Prior to full application, the control strip must be accepted by the RPR. A qualified manufacturer's representative shall be present in the field to assist the Contractor in applying control areas and/or control strips to determine the appropriate application rate of both emulsion and aggregate to be approved by the RPR.

a. For taxiway, taxilane and apron surfaces. Prior to full application, the Contractor shall place test areas at varying application rates as recommended by the Contractor's manufacturer's representative to determine appropriate application rate(s). The test areas will be located on representative section(s) of the pavement to receive the asphalt surface treatment designated by the RPR.

b. For runway and high-speed exit taxiway surfaces. N/A.

CONSTRUCTION METHODS

608-4.1 Worker safety. The Contractor shall obtain a Safety Data Sheet (SDS) for both the asphalt emulsion product and sand and require workmen to follow the manufacturer's recommended safety precautions.

608-4.2 Weather limitations. The asphalt emulsion shall be applied only when the existing pavement surface is dry and when the weather is not foggy, rainy, or when the wind velocity will prevent the uniform application of the material. No material shall be applied in strong winds that interfere with the uniform application of the material(s), or when dust or sand is blowing or when rain is anticipated within eight (8) hours of application completion. The atmospheric temperature and the pavement surface temperature shall both be at, or above 60°F (16°C) and rising. Seal coat shall not be applied when pavement temperatures are expected to exceed 130ºF within the subsequent 72 hours if traffic will be opened on pavement within those 72 hours. During application, account for wind drift. Cover existing buildings, structures, runway edge lights, taxiway edge lights, informational signs, retro-reflective marking and in-pavement duct markers as necessary to protect against overspray before applying the emulsion. Should emulsion get on any light or marker fixture, promptly clean the fixture. If cleaning is

"General Decision Number: CA20250014 03/28/2025

Superseded General Decision Number: CA20240014

State: California

Construction Types: Building, Heavy (Heavy and Dredging) and Highway

County: Santa Barbara County in California.

BUILDING, DREDGING (does not include hopper dredge work), HEAVY (does not include water well drilling), AND HIGHWAY CONSTRUCTION PROJECTS

Note: Contracts subject to the Davis-Bacon Act are generally required to pay at least the applicable minimum wage rate required under Executive Order 14026 or Executive Order 13658. Please note that these Executive Orders apply to covered contracts entered into by the federal government that are subject to the Davis-Bacon Act itself, but do not apply to contracts subject only to the Davis-Bacon Related Acts, including those set forth at 29 CFR 5.1(a)(1).

If the contract is entered into on or after January 30, 2022, or the contract is renewed or extended (e.g., an option is exercised) on or after January 30, 2022:	. Executive Order 14026 generally applies to the contract. . The contractor must pay all covered workers at least $17.75 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on the contract in 2025.
If the contract was awarded on or between January 1, 2015 and January 29, 2022, and the contract is not renewed or extended on or after January 30, 2022:	. Executive Order 13658 generally applies to the contract. . The contractor must pay all covered workers at least $13.30 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on that contract in 2025.

The applicable Executive Order minimum wage rate will be adjusted annually. If this contract is covered by one of the Executive Orders and a classification considered necessary for performance of work on the contract does not appear on this wage determination, the contractor must still submit a conformance request.

Additional information on contractor requirements and worker protections under the Executive Orders is available at http://www.dol.gov/whd/govcontracts.

Modification Number	Publication Date
0	01/03/2025
1	01/10/2025
2	01/24/2025
3	02/07/2025
4	02/21/2025
5	02/28/2025
6	03/28/2025

ASBE0005-002 09/01/2023

	Rates	Fringes
Asbestos Workers/Insulator (Includes the application of all insulating materials, protective coverings, coatings, and finishes to all types of mechanical systems)	$ 49.58	25.27
Fire Stop Technician (Application of Firestopping Materials for wall openings and penetrations in walls, floors, ceilings and curtain walls)	$ 36.97	20.36

ASBE0005-004 07/04/2022

	Rates	Fringes
Asbestos Removal worker/hazardous material handler (Includes preparation, wetting, stripping, removal, scrapping, vacuuming, bagging and disposing of all insulation materials from mechanical systems, whether they contain asbestos or not)	$ 23.52	13.37

BOIL0092-003 01/01/2024

	Rates	Fringes
BOILERMAKER	$ 51.98	42.11

BRCA0004-003 05/01/2024

	Rates	Fringes
Bricklayer; Marble Setter	$ 45.53	20.29

BRCA0018-008 06/01/2024

	Rates	Fringes
MARBLE FINISHER	$ 43.38	15.36
TILE FINISHER	$ 37.96	13.77

* BRCA0018-010 09/01/2024

	Rates	Fringes
TERRAZZO FINISHER	$ 42.11	14.67

TERRAZZO WORKER/SETTER.....$ 49.62 15.26

BRCA0018-011 06/01/2023

	Rates	Fringes
TILE LAYER	$ 48.29	19.18

CARP0213-001 01/01/2024

	Rates	Fringes
CARPENTER		
(1) Carpenter, Cabinet Installer, Insulation Installer, Hardwood Floor Worker and acoustical installer	$ 48.86	22.88
(2) Millwright	$ 49.36	22.88
(3) Piledrivermen/Derrick Bargeman, Bridge or Dock Carpenter, Heavy Framer, Rock Bargeman or Scowman, Rockslinger, Shingler (Commercial)	$ 48.99	22.88
(4) Pneumatic Nailer, Power Stapler	$ 51.85	16.28
(5) Sawfiler	$ 51.69	16.28
(6) Scaffold Builder	$ 40.77	22.38
(7) Table Power Saw Operator	$ 51.70	16.28

FOOTNOTE: Work of forming in the construction of open cut sewers or storm drains, on operations in which horizontal lagging is used in conjunction with steel H-Beams driven or placed in pre- drilled holes, for that portion of a lagged trench against which concrete is poured, namely, as a substitute for back forms (which work is performed by piledrivers): $0.13 per hour additional.

CARP0213-002 07/01/2021

	Rates	Fringes
Diver		
(1) Wet	$ 834.40	16.28
(2) Standby	$ 445.84	16.28
(3) Tender	$ 437.84	16.28
(4) Assistant Tender	$ 413.84	16.28

Amounts in ""Rates' column are per day

CARP0213-004 01/01/2024

	Rates	Fringes
Drywall		
DRYWALL INSTALLER/LATHER	$ 48.86	22.88
STOCKER/SCRAPPER	$ 20.80	9.97

CARP0721-001 07/01/2021

	Rates	Fringes

Modular Furniture Installer.....$ 21.85 7.15

ELEC0413-001 01/01/2025

	Rates	Fringes
Electricians:.....	$ 52.15	3%+23.23

CABLE SPLICERS: $2.00 additional per hour.

ALL WORK AT VANDENBERG AFB: $3.75 additional per hour.

FOOTNOTE: Work from trusses, swinging scaffolds, open ladders, scaffolds, bosun's chairs, stacks, or the maintenance of towers or open platforms where the worker is subject to a direct fall or where the worker has to work from a ladder or other support from a platform within 5 ft. of any direct fall a distance of 50 ft. from the ground floor or supporting structure: double the regular straight-time rate of pay. Safety nets, if used, will not invalidate this.

ELEC0413-003 12/31/2024

COMMUNICATIONS AND SYSTEMS WORK

	Rates	Fringes
Communications System Installer.....	$ 48.13	3%+16.05

SCOPE OF WORK:
Installation, testing, service and maintenance of systems utilizing the transmission and/or transference of voice, sound, vision and digital for commercial, educational, security and entertainment purposes for the following: TV monitoring and surveillance, background-foreground music, intercom and telephone interconnect, inventory control systems, microwave transmission, multi-media, multiplex, nurse call systems, radio page, school intercom and sound, burglar alarms, fire alarm (see last paragraph below) and low voltage master clock systems in commercial buildings. Communication Systems that transmit or receive information and/or control systems that are intrinsic to the above listed systems; inclusion or exclusion of terminations and testings of conductors determined by their function; excluding all other data systems or multiple systems which include control function or power supply; excluding installation of raceway systems, conduit systems, line voltage work, and energy management systems. Does not cover work performed at China Lake Naval Ordnance Test Station. Fire alarm work shall be performed at the current inside wireman total cost package.

ELEC1245-001 01/01/2025

	Rates	Fringes
LINE CONSTRUCTION		
(1) Lineman; Cable splicer..	$ 70.16	24.71
(2) Equipment specialist (operates crawler tractors, commercial motor		

vehicles, backhoes, trenchers, cranes (50 tons and below), overhead & underground distribution line equipment)	$ 53.30	22.26
(3) Groundman	$ 40.76	21.76
(4) Powderman	$ 51.87	18.79

HOLIDAYS: New Year's Day, M.L. King Day, Memorial Day, Independence Day, Labor Day, Veterans Day, Thanksgiving Day and day after Thanksgiving, Christmas Day

---

ELEV0018-001 01/01/2025

	Rates	Fringes
ELEVATOR MECHANIC	$ 69.43	38.435+a+b

FOOTNOTE:

a. PAID VACATION: Employer contributes 8% of regular hourly rate as vacation pay credit for employees with more than 5 years of service, and 6% for 6 months to 5 years of service.

b. PAID HOLIDAYS: New Year's Day, Memorial Day, Independence Day, Labor Day, Veterans' Day, Thanksgiving Day, Friday after Thanksgiving, and Christmas Day.

ENGI0012-004 08/01/2024

	Rates	Fringes
OPERATOR: Power Equipment (DREDGING)		
(1) Leverman	$ 64.10	38.75
(2) Dredge dozer	$ 58.13	38.75
(3) Deckmate	$ 58.02	38.75
(4) Winch operator (stern winch on dredge)	$ 57.47	38.75
(5) Fireman-Oiler, Deckhand, Bargeman, Leveehand	$ 56.93	38.75
(6) Barge Mate	$ 57.54	38.75

ENGI0012-024 07/01/2023

	Rates	Fringes
OPERATOR: Power Equipment (All Other Work)		
GROUP 1	$ 53.90	32.80
GROUP 2	$ 54.68	32.80
GROUP 3	$ 54.97	32.80
GROUP 4	$ 56.46	32.80
GROUP 6	$ 56.68	32.80
GROUP 8	$ 56.79	32.80
GROUP 10	$ 56.91	32.80
GROUP 12	$ 57.08	32.80
GROUP 13	$ 57.18	32.80
GROUP 14	$ 57.21	32.80
GROUP 15	$ 57.29	32.80
GROUP 16	$ 57.41	32.80
GROUP 17	$ 57.58	32.80
GROUP 18	$ 57.68	32.80

GROUP 19.....$ 57.79 32.80
GROUP 20.....$ 57.91 32.80
GROUP 21.....$ 58.08 32.80
GROUP 22.....$ 58.18 32.80
GROUP 23.....$ 58.29 32.80
GROUP 24.....$ 58.41 32.80
GROUP 25.....$ 58.58 32.80

OPERATOR: Power Equipment (Cranes, Piledriving & Hoisting)

GROUP 1.....$ 55.25 32.80
GROUP 2.....$ 56.03 32.80
GROUP 3.....$ 56.32 32.80
GROUP 4.....$ 56.46 32.80
GROUP 5.....$ 56.68 32.80
GROUP 6.....$ 56.79 32.80
GROUP 7.....$ 56.91 32.80
GROUP 8.....$ 57.08 32.80
GROUP 9.....$ 57.25 32.80
GROUP 10.....$ 58.25 32.80
GROUP 11.....$ 59.25 32.80
GROUP 12.....$ 60.25 32.80
GROUP 13.....$ 61.25 32.80

OPERATOR: Power Equipment (Tunnel Work)

GROUP 1.....$ 55.75 32.80
GROUP 2.....$ 56.53 32.80
GROUP 3.....$ 56.82 32.80
GROUP 4.....$ 56.96 32.80
GROUP 5.....$ 57.18 32.80
GROUP 6.....$ 57.29 32.80
GROUP 7.....$ 57.41 32.80

PREMIUM PAY:

$10.00 per hour shall be paid on all Power Equipment Operator work on the followng Military Bases: China Lake Naval Reserve, Vandenberg AFB, Point Arguello, Seely Naval Base, Fort Irwin, Nebo Annex Marine Base, Marine Corp Logistics Base Yermo, Edwards AFB, 29 Palms Marine Base and Camp Pendleton

Workers required to suit up and work in a hazardous material environment: $2.00 per hour additional. Combination mixer and compressor operator on gunite work shall be classified as a concrete mobile mixer operator.

SEE ZONE DEFINITIONS AFTER CLASSIFICATIONS

POWER EQUIPMENT OPERATORS CLASSIFICATIONS

GROUP 1: Bargeman; Brakeman; Compressor operator; Ditch Witch, with seat or similar type equipment; Elevator operator-inside; Engineer Oiler; Forklift operator (includes loed, lull or similar types under 5 tons; Generator operator; Generator, pump or compressor plant operator; Pump operator; Signalman; Switchman

GROUP 2: Asphalt-rubber plant operator (nurse tank operator);Coil Tubing Rig Operator, Concrete mixer operator-skip type; Conveyor operator; Fireman; Forklift operator (includes loed, lull or similar types over 5 tons; Hydrostatic pump operator; oiler crusher (asphalt or concrete plant); Petromat laydown machine; PJU side dum jack; Screening and conveyor machine operator (or similar types); Skiploader (wheel type up to 3/4 yd. without

attachment); Tar pot fireman; Temporary heating plant operator; Trenching machine oiler

GROUP 3: Asphalt-rubber blend operator; Bobcat or similar type (Skid steer); Equipment greaser (rack); Ford Ferguson (with dragtype attachments); Helicopter radioman (ground); Stationary pipe wrapping and cleaning machine operator

GROUP 4: Asphalt plant fireman; Backhoe operator (mini-max or similar type); Boring machine operator; Boxman or mixerman (asphalt or concrete); Chip spreading machine operator; Concrete cleaning decontamination machine operator; Concrete Pump Operator (small portable);Direct Push Operator (Geoprobe or similar types) Drilling machine operator, small auger types (Texoma super economatic or similar types - Hughes 100 or 200 or similar types - drilling depth of 30' maximum); Equipment greaser (grease truck); Guard rail post driver operator; Highline cableway signalman; Hydra-hammer-aero stomper; Micro Tunneling (above ground tunnel); Power concrete curing machine operator; Power concrete saw operator; Power-driven jumbo form setter operator; Power sweeper operator; Rock Wheel Saw/Trencher; Roller operator (compacting); Screed operator (asphalt or concrete); Trenching machine operator (up to 6 ft.); Vacuum or much truck

GROUP 6: Articulating material hauler; Asphalt plant engineer; Batch plant operator; Bit sharpener; Concrete joint machine operator (canal and similar type); Concrete planer operator; Dandy digger; Deck engine operator; Derrickman (oilfield type); Drilling machine operator, bucket or auger types (Calweld 100 bucket or similar types - Watson 1000 auger or similar types - Texoma 330, 500 or 600 auger or similar types - drilling depth of 45' maximum); Drilling machine operator; Hydrographic seeder machine operator (straw, pulp or seed), Jackson track maintainer, or similar type; Kalamazoo Switch tamper, or similar type; Machine tool operator; Maginnis internal full slab vibrator, Mechanical berm, curb or gutter(concrete or asphalt); Mechanical finisher operator (concrete, Clary-Johnson-Bidwell or similar); Micro tunnel system (below ground); Pavement breaker operator (truck mounted); Road oil mixing machine operator; Roller operator (asphalt or finish), rubber-tired earth moving equipment (single engine, up to and including 25 yds. struck); Self-propelled tar pipelining machine operator; Skiploader operator (crawler and wheel type, over 3/4 yd. and up to and including 1-1/2 yds.); Slip form pump operator (power driven hydraulic lifting device for concrete forms); Tractor operator-bulldozer, tamper-scraper (single engine, up to 100 h.p. flywheel and similar types, up to and including D-5 and similar types); Tugger hoist operator (1 drum); Ultra high pressure waterjet cutting tool system operator; Vacuum blasting machine operator

GROUP 8: Asphalt or concrete spreading operator (tamping or finishing); Asphalt paving machine operator (Barber Greene or similar type); Asphalt-rubber distribution operator; Backhoe operator (up to and including 3/4 yd.), small ford, Case or similar types; Cable Bundling Machine Operator (excluding handheld); Cable Trenching Machine Operator (Spider Plow or similar types) Cast-in-place pipe laying machine operator; Combination mixer and compressor operator (gunite work); Compactor operator (self-propelled);

Concrete mixer operator (paving); Crushing plant operator; Drill Doctor; Drilling machine operator, Bucket or auger types (Calweld 150 bucket or similar types - Watson 1500, 2000 2500 auger or similar types - Texoma 700, 800 auger or similar types - drilling depth of 60' maximum); Elevating grader operator; Grade checker; Gradall operator; Grouting machine operator; Heavy-duty repairman; Heavy equipment robotics operator; Kalamazoo balliste regulator or similar type; Kolman belt loader and similar type; Le Tourneau blob compactor or similar type; Loader operator (Athey, Euclid, Sierra and similar types); Mobark Chipper or similar; Ozzie padder or similar types; P.C. slot saw; Pneumatic concrete placing machine operator (Hackley-Presswell or similar type); Pumpcrete gun operator; RCM Cementing Unit Operator, Rail/Switch Grinder Operator (Harsco or similar types) Rock Drill or similar types; Rotary drill operator (excluding caisson type); Rubber-tired earth-moving equipment operator (single engine, caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds. up to and including 50 cu. yds. struck); Rubber-tired earth-moving equipment operator (multiple engine up to and including 25 yds. struck); Rubber-tired scraper operator (self-loading paddle wheel type-John Deere, 1040 and similar single unit); Self- propelled curb and gutter machine operator; Shuttle buggy; Skiploader operator (crawler and wheel type over 1-1/2 yds. up to and including 6-1/2 yds.); Soil remediation plant operator; Surface heaters and planer operator; Tractor compressor drill combination operator; Tractor operator (any type larger than D-5 - 100 flywheel h.p. and over, or similar-bulldozer, tamper, scraper and push tractor single engine); Tractor operator (boom attachments), Traveling pipe wrapping, cleaning and bendng machine operator; Trenching machine operator (over 6 ft. depth capacity, manufacturer's rating); trenching Machine with Road Miner attachment (over 6 ft depth capacity): Ultra high pressure waterjet cutting tool system mechanic; Water pull (compaction) operator

GROUP 10: Drilling machine operator, Bucket or auger types (Calweld 200 B bucket or similar types-Watson 3000 or 5000 auger or similar types-Texoma 900 auger or similar types-drilling depth of 105' maximum); Dual drum mixer, dynamic compactor LDC350 (or similar types); Monorail locomotive operator (diesel, gas or electric); Motor patrol-blade operator (single engine); Multiple engine tractor operator (Euclid and similar type-except Quad 9 cat.); Rubber-tired earth-moving equipment operator (single engine, over 50 yds. struck); Pneumatic pipe ramming tool and similar types; Prestressed wrapping machine operator; Rubber-tired earth-moving equipment operator (single engine, over 50 yds. struck); Rubber tired earth moving equipment operator (multiple engine, Euclid, caterpillar and similar over 25 yds. and up to 50 yds. struck), Tower crane repairman; Tractor loader operator (crawler and wheel type over 6-1/2 yds.); Woods mixer operator (and similar Pugmill equipment)

GROUP 12: Auto grader operator; Automatic slip form operator; Drilling machine operator, bucket or auger types (Calweld, auger 200 CA or similar types - Watson, auger 6000 or similar types - Hughes Super Duty, auger 200 or similar types - drilling depth of 175' maximum); Hoe ram or similar with compressor; Mass excavator operator less tha 750 cu. yards; Mechanical finishing machine operator; Mobile form

traveler operator; Motor patrol operator (multi-engine); Pipe mobile machine operator; Rubber-tired earth- moving equipment operator (multiple engine, Euclid, Caterpillar and similar type, over 50 cu. yds. struck); Rubber-tired self- loading scraper operator (paddle-wheel-auger type self-loading - two (2) or more units)

GROUP 13: Rubber-tired earth-moving equipment operator operating equipment with push-pull system (single engine, up to and including 25 yds. struck)

GROUP 14: Canal liner operator; Canal trimmer operator; Remote- control earth-moving equipment operator (operating a second piece of equipment: $1.00 per hour additional); Wheel excavator operator (over 750 cu. yds.)

GROUP 15: Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (single engine, Caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds. and up to and including 50 yds. struck); Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (multiple engine-up to and including 25 yds. struck)

GROUP 16: Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (single engine, over 50 yds. struck); Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (multiple engine, Euclid, Caterpillar and similar, over 25 yds. and up to 50 yds. struck)

GROUP 17: Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (multiple engine, Euclid, Caterpillar and similar, over 50 cu. yds. struck); Tandem tractor operator (operating crawler type tractors in tandem - Quad 9 and similar type)

GROUP 18: Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - single engine, up to and including 25 yds. struck)

GROUP 19: Rotex concrete belt operator (or similar types); Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - single engine, Caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds.and up to and including 50 cu. yds. struck); Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - multiple engine, up to and including 25 yds. struck)

GROUP 20: Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - single engine, over 50 yds. struck); Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps, and similar types in any combination, excluding compaction units - multiple engine, Euclid, Caterpillar and similar, over 25 yds. and up to 50 yds. struck)

GROUP 21: Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar

types in any combination, excluding compaction units - multiple engine, Euclid, Caterpillar and similar type, over 50 cu. yds. struck)

GROUP 22: Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (single engine, up to and including 25 yds. struck)

GROUP 23: Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (single engine, Caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds. and up to and including 50 yds. struck); Rubber-tired earth-moving equipment operator, operating with the tandem push-pull system (multiple engine, up to and including 25 yds. struck)

GROUP 24: Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (single engine, over 50 yds. struck); Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (multiple engine, Euclid, Caterpillar and similar, over 25 yds. and up to 50 yds. struck)

GROUP 25: Concrete pump operator-truck mounted; Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (multiple engine, Euclid, Caterpillar and similar type, over 50 cu. yds. struck); Spyder Excavator Operator, with all attachments

CRANES, PILEDRIVING AND HOISTING EQUIPMENT CLASSIFICATIONS

GROUP 1: Engineer oiler; Fork lift operator (includes loed, lull or similar types)

GROUP 2: Truck crane oiler

GROUP 3: A-frame or winch truck operator; Ross carrier operator (jobsite)

GROUP 4: Bridge-type unloader and turntable operator; Helicopter hoist operator

GROUP 5: Hydraulic boom truck; Stinger crane (Austin-Western or similar type); Tugger hoist operator (1 drum)

GROUP 6: Bridge crane operator; Cretor crane operator; Hoist operator (Chicago boom and similar type); Lift mobile operator; Lift slab machine operator (Vagtborg and similar types); Material hoist and/or manlift operator; Polar gantry crane operator; Self Climbing scaffold (or similar type); Shovel, backhoe, dragline, clamshell operator (over 3/4 yd. and up to 5 cu. yds. mrc); Tugger hoist operator

GROUP 7: Pedestal crane operator; Shovel, backhoe, dragline, clamshell operator (over 5 cu. yds. mrc); Tower crane repair; Tugger hoist operator (3 drum)

GROUP 8: Crane operator (up to and including 25 ton capacity); Crawler transporter operator; Derrick barge operator (up to and including 25 ton capacity); Hoist operator, stiff legs, Guy derrick or similar type (up to and including 25 ton capacity); Shovel, backhoe, dragline, clamshell operator (over 7 cu. yds., M.R.C.)

GROUP 9: Crane operator (over 25 tons and up to and including 50 tons mrc); Derrick barge operator (over 25 tons up to and including 50 tons mrc); Highline cableway operator; Hoist operator, stiff legs, Guy derrick or similar type (over 25 tons up to and including 50 tons mrc); K-crane operator; Polar crane operator; Self erecting tower crane operator maximum lifting capacity ten tons

GROUP 10: Crane operator (over 50 tons and up to and including 100 tons mrc); Derrick barge operator (over 50 tons up to and including 100 tons mrc); Hoist operator, stiff legs, Guy derrick or similar type (over 50 tons up to and including 100 tons mrc), Mobile tower crane operator (over 50 tons, up to and including 100 tons M.R.C.);

GROUP 11: Crane operator (over 100 tons and up to and including 200 tons mrc); Derrick barge operator (over 100 tons up to and including 200 tons mrc); Hoist operator, stiff legs, Guy derrick or similar type (over 100 tons up to and including 200 tons mrc); Mobile tower crane operator (over 100 tons up to and including 200 tons mrc) ; Tower crane operator and tower gantry

GROUP 12: Crane operator (over 200 tons up to and including 300 tons mrc); Derrick barge operator (over 200 tons up to and including 300 tons mrc); Hoist operator, stiff legs, Guy derrick or similar type (over 200 tons, up to and including 300 tons mrc); Mobile tower crane operator (over 200 tons, up to and including 300 tons mrc)

GROUP 13: Crane operator (over 300 tons); Derrick barge operator (over 300 tons); Helicopter pilot; Hoist operator, stiff legs, Guy derrick or similar type (over 300 tons); Mobile tower crane operator (over 300 tons)

TUNNEL CLASSIFICATIONS

GROUP 1: Skiploader (wheel type up to 3/4 yd. without attachment)

GROUP 2: Power-driven jumbo form setter operator

GROUP 3: Dinkey locomotive or motorperson (up to and including 10 tons)

GROUP 4: Bit sharpener; Equipment greaser (grease truck); Slip form pump operator (power-driven hydraulic lifting device for concrete forms); Tugger hoist operator (1 drum); Tunnel locomotive operator (over 10 and up to and including 30 tons)

GROUP 5: Backhoe operator (up to and including 3/4 yd.); Small Ford, Case or similar; Drill doctor; Grouting machine operator; Heading shield operator; Heavy-duty repairperson; Loader operator (Athey, Euclid, Sierra and similar types); Mucking machine operator (1/4 yd., rubber-tired, rail or track type); Pneumatic concrete placing machine operator (Hackley-Presswell or similar type); Pneumatic heading shield (tunnel); Pumpcrete gun operator; Tractor compressor drill combination operator; Tugger hoist operator (2 drum); Tunnel locomotive operator (over 30 tons)

GROUP 6: Heavy Duty Repairman

GROUP 7: Tunnel mole boring machine operator

ENGINEERS ZONES

$1.00 additional per hour for all of IMPERIAL County and the portions of KERN, RIVERSIDE & SAN BERNARDINO Counties as defined below:

That area within the following Boundary: Begin in San Bernardino County, approximately 3 miles NE of the intersection of I-15 and the California State line at that point which is the NW corner of Section 1, T17N,m R14E, San Bernardino Meridian. Continue W in a straight line to that point which is the SW corner of the northwest quarter of Section 6, T27S, R42E, Mt. Diablo Meridian. Continue North to the intersection with the Inyo County Boundary at that point which is the NE corner of the western half of the northern quarter of Section 6, T25S, R42E, MDM. Continue W along the Inyo and San Bernardino County boundary until the intersection with Kern County, as that point which is the SE corner of Section 34, T24S, R40E, MDM. Continue W along the Inyo and Kern County boundary until the intersection with Tulare County, at that point which is the SW corner of the SE quarter of Section 32, T24S, R37E, MDM. Continue W along the Kern and Tulare County boundary, until that point which is the NW corner of T25S, R32E, MDM. Continue S following R32E lines to the NW corner of T31S, R32E, MDM. Continue W to the NW corner of T31S, R31E, MDM. Continue S to the SW corner of T32S, R31E, MDM. Continue W to SW corner of SE quarter of Section 34, T32S, R30E, MDM. Continue S to SW corner of T11N, R17W, SBM. Continue E along south boundary of T11N, SBM to SW corner of T11N, R7W, SBM. Continue S to SW corner of T9N, R7W, SBM. Continue E along south boundary of T9N, SBM to SW corner of T9N, R1E, SBM. Continue S along west boundary of R1E, SMB to Riverside County line at the SW corner of T1S, R1E, SBM. Continue E along south boundary of T1s, SBM (Riverside County Line) to SW corner of T1S, R10E, SBM. Continue S along west boundary of R10E, SBM to Imperial County line at the SW corner of T8S, R10E, SBM. Continue W along Imperial and Riverside county line to NW corner of T9S, R9E, SBM. Continue S along the boundary between Imperial and San Diego Counties, along the west edge of R9E, SBM to the south boundary of Imperial County/California state line. Follow the California state line west to Arizona state line, then north to Nevada state line, then continuing NW back to start at the point which is the NW corner of Section 1, T17N, R14E, SBM

$1.00 additional per hour for portions of SAN LUIS OBISPO, KERN, SANTA BARBARA & VENTURA as defined below:

That area within the following Boundary: Begin approximately 5 miles north of the community of Cholame, on the Monterey County and San Luis Obispo County boundary at the NW corner of T25S, R16E, Mt. Diablo Meridian. Continue south along the west side of R16E to the SW corner of T30S, R16E, MDM. Continue E to SW corner of T30S, R17E, MDM. Continue S to SW corner of T31S, R17E, MDM. Continue E to SW corner of T31S, R18E, MDM. Continue S along West side of R18E, MDM as it crosses into San Bernardino Meridian numbering area and becomes R30W. Follow the west side of R30W, SBM to the SW corner of T9N, R30W, SBM. Continue E along the south edge of T9N, SBM to the Santa Barbara County and Ventura County boundary at that point whch is the SW corner of Section 34.T9N, R24W, SBM, continue S along the Ventura County line to that point which is the SW corner of the SE quarter of Section 32, T7N, R24W, SBM. Continue E

along the south edge of T7N, SBM to the SE corner to T7N, R21W, SBM. Continue N along East side of R21W, SBM to Ventura County and Kern County boundary at the NE corner of T8N, R21W. Continue W along the Ventura County and Kern County boundary to the SE corner of T9N, R21W. Continue North along the East edge of R21W, SBM to the NE corner of T12N, R21W, SBM. Continue West along the north edge of T12N, SBM to the SE corner of T32S, R21E, MDM. [T12N SBM is a think strip between T11N SBM and T32S MDM]. Continue North along the East side of R21E, MDM to the Kings County and Kern County border at the NE corner of T25S, R21E, MDM, continue West along the Kings County and Kern County Boundary until the intersection of San Luis Obispo County. Continue west along the Kings County and San Luis Obispo County boundary until the intersection with Monterey County. Continue West along the Monterey County and San Luis Obispo County boundary to the beginning point at the NW corner of T25S, R16E, MDM.

$2.00 additional per hour for INYO and MONO Counties and the Northern portion of SAN BERNARDINO County as defined below:

That area within the following Boundary: Begin at the intersection of the northern boundary of Mono County and the California state line at the point which is the center of Section 17, T10N, R22E, Mt. Diablo Meridian. Continue S then SE along the entire western boundary of Mono County, until it reaches Inyo County at the point which is the NE corner of the Western half of the NW quarter of Section 2, T8S, R29E, MDM. Continue SSE along the entire western boundary of Inyo County, until the intersection with Kern County at the point which is the SW corner of the SE 1/4 of Section 32, T24S, R37E, MDM. Continue E along the Inyo and Kern County boundary until the intersection with San Bernardino County at that point which is the SE corner of section 34, T24S, R40E, MDM. Continue E along the Inyo and San Bernardino County boundary until the point which is the NE corner of the Western half of the NW quarter of Section 6, T25S, R42E, MDM. Continue S to that point which is the SW corner of the NW quarter of Section 6, T27S, R42E, MDM. Continue E in a straight line to the California and Nevada state border at the point which is the NW corner of Section 1, T17N, R14E, San Bernardino Meridian. Then continue NW along the state line to the starting point, which is the center of Section 18, T10N, R22E, MDM.

REMAINING AREA NOT DEFINED ABOVE RECIEVES BASE RATE

IRON0433-006 01/01/2025

	Rates	Fringes
IRONWORKER		
Fence Erector	$ 45.78	26.51
Ornamental, Reinforcing and Structural	$ 50.70	35.15

PREMIUM PAY:

$9.00 additional per hour at the following locations:

China Lake Naval Test Station, Chocolate Mountains Naval Reserve-Niland,
Edwards AFB, Fort Irwin Military Station, Fort Irwin Training

Center-Goldstone, San Clemente Island, San Nicholas Island, Susanville Federal Prison, 29 Palms - Marine Corps, U.S. Marine Base - Barstow, U.S. Naval Air Facility - Sealey, Vandenberg AFB Army Defense Language Institute - Monterey, Fallon Air Base, Naval Post Graduate School - Monterey, Yermo Marine Corps Logistics Center
Port Hueneme, Port Mugu, U.S. Coast Guard Station - Two Rock

LABO0220-001 07/01/2022

	Rates	Fringes
LABORER (TUNNEL)		
GROUP 1	$ 45.68	23.30
GROUP 2	$ 46.00	23.30
GROUP 3	$ 46.46	23.30
GROUP 4	$ 47.15	23.30
LABORER		
GROUP 1	$ 36.39	21.04
GROUP 2	$ 36.94	21.04
GROUP 3	$ 37.49	21.04
GROUP 4	$ 39.04	21.04
GROUP 5	$ 39.39	21.04

LABORER CLASSIFICATIONS

GROUP 1: Cleaning and handling of panel forms; Concrete screeding for rough strike-off; Concrete, water curing; Demolition laborer, the cleaning of brick if performed by a worker performing any other phase of demolition work, and the cleaning of lumber; Fire watcher, limber, brush loader, piler and debris handler; Flag person; Gas, oil and/or water pipeline laborer; Laborer, asphalt-rubber material loader; Laborer, general or construction; Laborer, general clean-up; Laborer, landscaping; Laborer, jetting; Laborer, temporary water and air lines; Material hose operator (walls, slabs, floors and decks); Plugging, filling of shee bolt holes; Dry packing of concrete; Railroad maintenance, repair track person and road beds; Streetcar and railroad construction track laborers; Rigging and signaling; Scaler; Slip form raiser; Tar and mortar; Tool crib or tool house laborer; Traffic control by any method; Window cleaner; Wire mesh pulling - all concrete pouring operations

GROUP 2: Asphalt shoveler; Cement dumper (on 1 yd. or larger mixer and handling bulk cement); Cesspool digger and installer; Chucktender; Chute handler, pouring concrete, the handling of the chute from readymix trucks, such as walls, slabs, decks, floors, foundation, footings, curbs, gutters and sidewalks; Concrete curer, impervious membrane and form oiler; Cutting torch operator (demolition); Fine grader, highways and street paving, airport, runways and similar type heavy construction; Gas, oil and/or water pipeline wrapper - pot tender and form person; Guinea chaser; Headerboard person - asphalt; Laborer, packing rod steel and pans; Membrane vapor barrier installer; Power broom sweeper (small); Riprap stonepaver, placing stone or wet sacked concrete; Roto scraper and tiller; Sandblaster (pot tender); Septic tank digger and installer(lead); Tank scaler and cleaner; Tree climber, faller, chain saw operator, Pittsburgh chipper and similar type brush shredder; Underground laborer, including caisson bellower

GROUP 3: Buggymobile person; Concrete cutting torch; Concrete pile cutter; Driller, jackhammer, 2-1/2 ft. drill steel or longer; Dri-pak-it machine; Gas, oil and/or water pipeline wrapper, 6-in. pipe and over, by any method, inside and out; High scaler (including drilling of same); Hydro seeder and similar type; Impact wrench multi-plate; Kettle person, pot person and workers applying asphalt, lay-kold, creosote, lime caustic and similar type materials (""applying"" means applying, dipping, brushing or handling of such materials for pipe wrapping and waterproofing); Operator of pneumatic, gas, electric tools, vibrating machine, pavement breaker, air blasting, come-alongs, and similar mechanical tools not separately classified herein; Pipelayer's backup person, coating, grouting, making of joints, sealing, caulking, diapering and including rubber gasket joints, pointing and any and all other services; Rock slinger; Rotary scarifier or multiple head concrete chipping scarifier; Steel headerboard and guideline setter; Tamper, Barko, Wacker and similar type; Trenching machine, hand-propelled

GROUP 4: Asphalt raker, lute person, ironer, asphalt dump person, and asphalt spreader boxes (all types); Concrete core cutter (walls, floors or ceilings), grinder or sander; Concrete saw person, cutting walls or flat work, scoring old or new concrete; Cribber, shorer, lagging, sheeting and trench bracing, hand-guided lagging hammer; Head rock slinger; Laborer, asphalt- rubber distributor boot person; Laser beam in connection with laborers' work; Oversize concrete vibrator operator, 70 lbs. and over; Pipelayer performing all services in the laying and installation of pipe from the point of receiving pipe in the ditch until completion of operation, including any and all forms of tubular material, whether pipe, metallic or non-metallic, conduit and any other stationary type of tubular device used for the conveying of any substance or element, whether water, sewage, solid gas, air, or other product whatsoever and without regard to the nature of material from which the tubular material is fabricated; No-joint pipe and stripping of same; Prefabricated manhole installer; Sandblaster (nozzle person), water blasting, Porta Shot-Blast

GROUP 5: Blaster powder, all work of loading holes, placing and blasting of all powder and explosives of whatever type, regardless of method used for such loading and placing; Driller: All power drills, excluding jackhammer, whether core, diamond, wagon, track, multiple unit, and any and all other types of mechanical drills without regard to the form of motive power; Toxic waste removal

TUNNEL LABORER CLASSIFICATIONS

GROUP 1: Batch plant laborer; Changehouse person; Dump person; Dump person (outside); Swamper (brake person and switch person on tunnel work); Tunnel materials handling person; Nipper; Pot tender, using mastic or other materials (for example, but not by way of limitation, shotcrete, etc.);

GROUP 2: Bull gang mucker, track person; Chucktender, Cabletender; Concrete crew, including rodder and spreader; Loading and unloading agitator cars; Vibrator person, jack hammer, pneumatic tools (except driller)

GROUP 3: Blaster, driller, powder person; Chemical grout jet

person; Cherry picker person; Grout gun person; Grout mixer person; Grout pump person; Jackleg miner; Jumbo person; Kemper and other pneumatic concrete placer operator; Miner, tunnel (hand or machine); Nozzle person; Operating of troweling and/or grouting machines; Powder person (primer house); Primer person; Sandblaster; Shotcrete person; Steel form raiser and setter; Timber person, retimber person, wood or steel; Tunnel Concrete finisher

GROUP 4: Diamond driller; Sandblaster; Shaft and raise work

LABO0220-004 07/01/2024

	Rates	Fringes
Brick Tender	$ 41.53	22.54

LABO0300-005 07/01/2024

	Rates	Fringes
Asbestos Removal Laborer	$ 43.88	25.13

SCOPE OF WORK: Includes site mobilization, initial site cleanup, site preparation, removal of asbestos-containing material and toxic waste, encapsulation, enclosure and disposal of asbestos- containing materials and toxic waste by hand or with equipment or machinery; scaffolding, fabrication of temporary wooden barriers and assembly of decontamination stations.

LABO0345-001 07/01/2024

	Rates	Fringes
LABORER (GUNITE)		
GROUP 1	$ 53.48	22.77
GROUP 2	$ 52.53	22.77
GROUP 3	$ 48.99	22.77

FOOTNOTE: GUNITE PREMIUM PAY: Workers working from a Bosn'n's Chair or suspended from a rope or cable shall receive 40 cents per hour above the foregoing applicable classification rates. Workers doing gunite and/or shotcrete work in a tunnel shall receive 35 cents per hour above the foregoing applicable classification rates, paid on a portal-to-portal basis. Any work performed on, in or above any smoke stack, silo, storage elevator or similar type of structure, when such structure is in excess of 75'-0"" above base level and which work must be performed in whole or in part more than 75'-0"" above base level, that work performed above the 75'-0"" level shall be compensated for at 35 cents per hour above the applicable classification wage rate.

GUNITE LABORER CLASSIFICATIONS

GROUP 1: Rodmen, Nozzlemen

GROUP 2: Gunmen

GROUP 3: Reboundmen

LABO1184-001 07/01/2024

	Rates	Fringes
Laborers: (HORIZONTAL DIRECTIONAL DRILLING)		
(1) Drilling Crew Laborer	$ 45.34	20.06
(2) Vehicle Operator/Hauler	$ 45.51	20.06
(3) Horizontal Directional Drill Operator	$ 47.36	20.06
(4) Electronic Tracking Locator	$ 49.36	20.06
Laborers: (STRIPING/SLURRY SEAL)		
GROUP 1	$ 46.65	23.17
GROUP 2	$ 47.95	23.17
GROUP 3	$ 49.96	23.17
GROUP 4	$ 51.70	23.17

LABORERS - STRIPING CLASSIFICATIONS

GROUP 1: Protective coating, pavement sealing, including repair and filling of cracks by any method on any surface in parking lots, game courts and playgrounds; carstops; operation of all related machinery and equipment; equipment repair technician

GROUP 2: Traffic surface abrasive blaster; pot tender - removal of all traffic lines and markings by any method (sandblasting, waterblasting, grinding, etc.) and preparation of surface for coatings. Traffic control person: controlling and directing traffic through both conventional and moving lane closures; operation of all related machinery and equipment

GROUP 3: Traffic delineating device applicator: Layout and application of pavement markers, delineating signs, rumble and traffic bars, adhesives, guide markers, other traffic delineating devices including traffic control. This category includes all traffic related surface preparation (sandblasting, waterblasting, grinding) as part of the application process. Traffic protective delineating system installer: removes, relocates, installs, permanently affixed roadside and parking delineation barricades, fencing, cable anchor, guard rail, reference signs, monument markers; operation of all related machinery and equipment; power broom sweeper

GROUP 4: Striper: layout and application of traffic stripes and markings; hot thermo plastic; tape traffic stripes and markings, including traffic control; operation of all related machinery and equipment

---

LABO1414-003 08/07/2024

	Rates	Fringes
LABORER		
PLASTER CLEAN-UP LABORER	$ 43.57	25.17
PLASTER TENDER	$ 46.12	25.17

Work on a swing stage scaffold: $1.00 per hour additional.

Work at Military Bases - $3.00 additional per hour:
Coronado Naval Amphibious Base, Fort Irwin, Marine Corps Air Station-29 Palms, Imperial Beach Naval Air Station, Marine Corps Logistics Supply Base, Marine Corps Pickle Meadows, Mountain Warfare Training Center, Naval Air Facility-Seeley, North Island Naval Air Station, Vandenberg AFB.

PAIN0036-002 07/01/2023

	Rates	Fringes
Painters: (Including Lead Abatement)		
(1) Journeyman Painter	$ 36.44	18.58
(2) Repaint	$ 26.40	17.02
(3) Iron & Steel	$ 33.12	17.18
(4) High Iron & Steel	$ 35.12	17.18
(5) All Other Work	$ 36.44	18.58

REPAINT:
Repaint of any structure with the exception of work involving the aerospace industry, breweries, commercial recreational facilities, hotels which operate commercial establishments as part of hotel service, and sports facilities, tenant improvement work not included in conjunction with the construction of the building and all repainting of tenant improvement projects.

HIGH IRON & STEEL:
Aerial towers, towers, radio towers, smoke stacks, flag poles (any flag poles that can be finished from the ground with a ladder excluded), elevated water towers, steeples and domes in their entirety and any other extremely high and hazardous work, cooning steel, bos'n chair, or other similar devices, painting in other high hazardous work shall be classified as high iron & steel

---

PAIN0036-008 09/01/2024

	Rates	Fringes
DRYWALL FINISHER/TAPER	$ 49.33	26.82

---

* PAIN0036-015 01/01/2025

	Rates	Fringes
GLAZIER	$ 53.05	30.64

FOOTNOTE: Additional $1.25 per hour for work in a condor, from the third (3rd) floor and up Additional $1.25 per hour for work on the outside of the building from a swing stage or any suspended contrivance, from the ground up

---

PAIN1247-002 01/01/2025

	Rates	Fringes
SOFT FLOOR LAYER	$ 45.15	19.43

PLAS0200-006 08/03/2022

	Rates	Fringes
PLASTERER	$ 47.37	19.64

VANDENBURG AFB: $3.00 additional per hour.

PLAS0500-002 07/01/2023

	Rates	Fringes
CEMENT MASON/CONCRETE FINISHER	$ 44.00	27.11

PLUM0016-004 09/01/2024

	Rates	Fringes
PLUMBER/PIPEFITTER		
Vandenburg Air Force Base, Work ONLY on new additions and remodeling of bars, restaurants, stores and commercial buildings not to exceed 5,000 sq. ft. of floor space	$ 63.98	26.61
Work ONLY on strip malls, light commercial, tenant improvement and remodel work	$ 57.67	25.63
All other work except work on new additions and remodeling of bars, restaurant, stores and commercial buildings not to exceed 5,000 sq. ft. of floor space and work on strip malls, light commercial, tenant improvement and remodel work	$ 44.24	23.96
	$ 59.48	26.61

PLUM0345-001 09/01/2023

	Rates	Fringes
PLUMBER		
Landscape/Irrigation Fitter	$ 40.20	25.90
Sewer & Storm Drain Work	$ 44.29	23.28

ROOF0036-002 08/01/2024

	Rates	Fringes
ROOFER	$ 49.43	20.58

FOOTNOTE: Pitch premium: Work on which employees are exposed to pitch fumes or required to handle pitch, pitch base or pitch impregnated products, or any material containing coal tar pitch, the entire roofing crew shall receive $1.75 per hour ""pitch premium"" pay.

SFCA0669-014 01/01/2025

	Rates	Fringes
SPRINKLER FITTER	$ 46.42	28.42

SHEE0273-002 08/01/2019

	Rates	Fringes
SHEET METAL WORKER	$ 45.48	30.05

HOLIDAYS: New Year's Day, Martin Luther King Day, President's Day, Good Friday, Memorial Day, Indepdendence Day, Labor Day, Veterans Day,Thankisgiving Day & Friday after, Christmas Day

---

TEAM0011-002 07/01/2024

	Rates	Fringes
TRUCK DRIVER		
GROUP 1	$ 39.59	34.34
GROUP 2	$ 39.74	34.34
GROUP 3	$ 39.87	34.34
GROUP 4	$ 40.06	34.34
GROUP 5	$ 40.09	34.34
GROUP 6	$ 40.12	34.34
GROUP 7	$ 40.37	34.34
GROUP 8	$ 40.62	34.34
GROUP 9	$ 40.82	34.34
GROUP 10	$ 41.12	34.34
GROUP 11	$ 41.62	34.34
GROUP 12	$ 42.05	34.34

WORK ON ALL MILITARY BASES:
PREMIUM PAY: $3.00 per hour additional.
[29 palms Marine Base, Camp Roberts, China Lake, Edwards AFB, El Centro Naval Facility, Fort Irwin, Marine Corps Logistics Base at Nebo & Yermo, Mountain Warfare Training Center, Bridgeport, Point Arguello, Point Conception, Vandenberg AFB]

TRUCK DRIVERS CLASSIFICATIONS

GROUP 1: Truck driver

GROUP 2: Driver of vehicle or combination of vehicles - 2 axles; Traffic control pilot car excluding moving heavy equipment permit load; Truck mounted broom

GROUP 3: Driver of vehicle or combination of vehicles - 3 axles; Boot person; Cement mason distribution truck; Fuel truck driver; Water truck - 2 axle; Dump truck, less than 16 yds. water level; Erosion control driver

GROUP 4: Driver of transit mix truck, under 3 yds.; Dumpcrete truck, less than 6-1/2 yds. water level

GROUP 5: Water truck, 3 or more axles; Truck greaser and tire person ($0.50 additional for tire person); Pipeline and utility working truck driver, including winch truck and plastic fusion, limited to pipeline and utility work; Slurry truck driver

GROUP 6: Transit mix truck, 3 yds. or more; Dumpcrete truck, 6-1/2 yds. water level and over; Vehicle or combination of vehicles - 4 or more axles; Oil spreader truck; Dump truck, 16 yds. to 25 yds. water level

GROUP 7: A Frame, Swedish crane or similar; Forklift driver; Ross carrier driver

GROUP 8: Dump truck, 25 yds. to 49 yds. water level; Truck repair person; Water pull - single engine; Welder

GROUP 9: Truck repair person/welder; Low bed driver, 9 axles or over

GROUP 10: Dump truck - 50 yds. or more water level; Water pull - single engine with attachment

GROUP 11: Water pull - twin engine; Water pull - twin engine with attachments; Winch truck driver - $1.25 additional when operating winch or similar special attachments

GROUP 12: Boom Truck 17K and above

WELDERS - Receive rate prescribed for craft performing operation to which welding is incidental.

==========

Note: Executive Order (EO) 13706, Establishing Paid Sick Leave for Federal Contractors applies to all contracts subject to the Davis-Bacon Act for which the contract is awarded (and any solicitation was issued) on or after January 1, 2017. If this contract is covered by the EO, the contractor must provide employees with 1 hour of paid sick leave for every 30 hours they work, up to 56 hours of paid sick leave each year. Employees must be permitted to use paid sick leave for their own illness, injury or other health-related needs, including preventive care; to assist a family member (or person who is like family to the employee) who is ill, injured, or has other health-related needs, including preventive care; or for reasons resulting from, or to assist a family member (or person who is like family to the employee) who is a victim of, domestic violence, sexual assault, or stalking. Additional information on contractor requirements and worker protections under the EO is available at https://www.dol.gov/agencies/whd/government-contracts.

Unlisted classifications needed for work not included within the scope of the classifications listed may be added after award only as provided in the labor standards contract clauses (29CFR 5.5 (a) (1) (iii)).

The body of each wage determination lists the classifications and wage rates that have been found to be prevailing for the type(s) of construction and geographic area covered by the wage determination. The classifications are listed in alphabetical order under rate identifiers indicating whether the particular rate is a union rate (current union negotiated rate), a survey rate, a weighted union average rate, a state adopted rate, or a

supplemental classification rate.

Union Rate Identifiers

A four-letter identifier beginning with characters other than ""SU"", ""UAVG"", ?SA?, or ?SC? denotes that a union rate was prevailing for that classification in the survey. Example: PLUM0198-005 07/01/2024. PLUM is an identifier of the union whose collectively bargained rate prevailed in the survey for this classification, which in this example would be Plumbers. 0198 indicates the local union number or district council number where applicable, i.e., Plumbers Local 0198. The next number, 005 in the example, is an internal number used in processing the wage determination. The date, 07/01/2024 in the example, is the effective date of the most current negotiated rate.

Union prevailing wage rates are updated to reflect all changes over time that are reported to WHD in the rates in the collective bargaining agreement (CBA) governing the classification.

Union Average Rate Identifiers

The UAVG identifier indicates that no single rate prevailed for those classifications, but that 100% of the data reported for the classifications reflected union rates. EXAMPLE: UAVG-OH-0010 01/01/2024. UAVG indicates that the rate is a weighted union average rate. OH indicates the State of Ohio. The next number, 0010 in the example, is an internal number used in producing the wage determination. The date, 01/01/2024 in the example, indicates the date the wage determination was updated to reflect the most current union average rate.

A UAVG rate will be updated once a year, usually in January, to reflect a weighted average of the current rates in the collective bargaining agreements on which the rate is based.

Survey Rate Identifiers

The ""SU"" identifier indicates that either a single non-union rate prevailed (as defined in 29 CFR 1.2) for this classification in the survey or that the rate was derived by computing a weighted average rate based on all the rates reported in the survey for that classification. As a weighted average rate includes all rates reported in the survey, it may include both union and non-union rates. Example: SUFL2022-007 6/27/2024. SU indicates the rate is a single non-union prevailing rate or a weighted average of survey data for that classification. FL indicates the State of Florida. 2022 is the year of the survey on which these classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 6/27/2024 in the example, indicates the survey completion date for the classifications and rates under that identifier.

?SU? wage rates typically remain in effect until a new survey is conducted. However, the Wage and Hour Division (WHD) has the discretion to update such rates under 29 CFR 1.6(c)(1).

State Adopted Rate Identifiers

The ""SA"" identifier indicates that the classifications and prevailing wage rates set by a state (or local) government were adopted under 29 C.F.R 1.3(g)-(h). Example: SAME2023-007

01/03/2024. SA reflects that the rates are state adopted. ME refers to the State of Maine. 2023 is the year during which the state completed the survey on which the listed classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 01/03/2024 in the example, reflects the date on which the classifications and rates under the ?SA? identifier took effect under state law in the state from which the rates were adopted.

WAGE DETERMINATION APPEALS PROCESS

1) Has there been an initial decision in the matter? This can be:

a) a survey underlying a wage determination
b) an existing published wage determination
c) an initial WHD letter setting forth a position on a wage determination matter
d) an initial conformance (additional classification and rate) determination

On survey related matters, initial contact, including requests for summaries of surveys, should be directed to the WHD Branch of Wage Surveys. Requests can be submitted via email to davisbaconinfo@dol.gov or by mail to:

Branch of Wage Surveys
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

Regarding any other wage determination matter such as conformance decisions, requests for initial decisions should be directed to the WHD Branch of Construction Wage Determinations. Requests can be submitted via email to BCWD-Office@dol.gov or by mail to:

Branch of Construction Wage Determinations
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

2) If an initial decision has been issued, then any interested party (those affected by the action) that disagrees with the decision can request review and reconsideration from the Wage and Hour Administrator (See 29 CFR Part 1.8 and 29 CFR Part 7). Requests for review and reconsideration can be submitted via email to dba.reconsideration@dol.gov or by mail to:

Wage and Hour Administrator
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

The request should be accompanied by a full statement of the interested party's position and any information (wage payment data, project description, area practice material, etc.) that the requestor considers relevant to the issue.

3) If the decision of the Administrator is not favorable, an

interested party may appeal directly to the Administrative Review Board (formerly the Wage Appeals Board). Write to:

Administrative Review Board
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210.

==========

END OF GENERAL DECISION"


SANTA BARBARA COUNTY, CALIFORNIA

SANTA YNEZ VALLEY AIRPORT

CONSTRUCTION PLANS FOR

REHABILITATE TIE-DOWN APRON

COUNTY PROJECT: NO. 22011
FAA: AIP 3-06-0243-023-2023 (DESIGN)
FAA: AIP 3-06-0243-024-2025 (CONSTRUCTION)

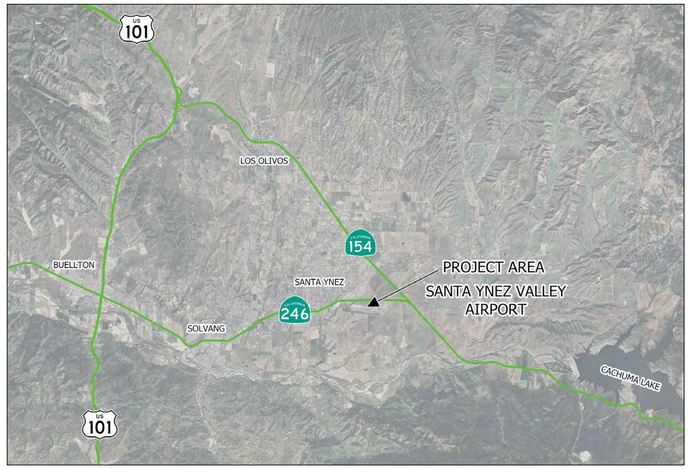

REGIONAL MAP
NO SCALE

APRIL, 2025

GENERAL PROJECT DESCRIPTION

1. REHABILITATE TIE-DOWN APRON AND HANGAR ROWS CONSISTING OF CRACK FILL & SEAL AND P-608 PAVEMENT SEAL COAT, FOLLOWED BY PAVEMENT MARKINGS.

GENERAL CONSTRUCTION ELEMENTS

1. AIRFIELD SAFETY AND SECURITY.
2. CRACK FILL & SEAL.
3. OBLITERATE EXISTING PAVEMENT MARKINGS.
4. REMOVE AND RE-INSTALL AIRCRAFT TIE-DOWN CABLES AND CHAINS.
5. APPLICATION OF P-608 PAVEMENT SEAL COAT.
6. APPLICATION OF OF NEW PAVEMENT MARKINGS.



LOCATION MAP
NO SCALE

SUBMITTED _____ DATE _____

JOHN A. SMITH RCE 46852
PROJECT ENGINEER

REGISTERED PROFESSIONAL ENGINEER
JOHN A. SMITH
No. 46852
EXP. 6-30-25
CIVIL
STATE OF CALIFORNIA

REV.	DESCRIPTION	DATE	APP.

UNDERGROUND SERVICE ALERT
811
DIAL 811
TWO WORKING DAYS BEFORE YOU DIG

TARTAGLIA ENGINEERING

1 OF 14
SHEET

22-55
DRAWING NO.

PLOT DATE: 4/11/2025

GENERAL NOTES:

1. UNLESS STATED ELSEWHERE, SANTA YNEZ AIRPORT WILL REMAIN OPEN AT ALL TIMES DURING CONSTRUCTION.
2. THE CONSTRUCTION WORK ON THIS PROJECT WILL OCCUR WITHIN OR ADJACENT TO THE ACTIVE AIRPORT OPERATIONS AREA (AOA) AND IS SUBJECT TO THE OPERATIONAL SAFETY REQUIREMENTS OF THE FEDERAL AVIATION ADMINISTRATION (FAA). DURING THE COURSE OF THE PROJECT, CONTRACTOR SHALL COMPLY WITH THE REQUIREMENTS IN FAA ADVISORY CIRCULAR 5370-2G "OPERATIONAL SAFETY ON AIRPORTS DURING CONSTRUCTION", INCLUDED IN THE CONTRACT BOOK.
3. THE ENGINEER HAS PREPARED A CONSTRUCTION SAFETY PHASING PLAN (CSPP) SPECIFICALLY FOR THIS PROJECT. THE CSPP IS INCLUDED IN THE CONTRACT BOOK. CONTRACTOR SHALL REVIEW THE CSPP AND PREPARE AND SUBMIT A SAFETY PLAN COMPLIANCE DOCUMENT (SPCD) TO THE ENGINEER FOR APPROVAL BEFORE COMMENCEMENT OF WORK.
4. THE AIRPORT SHALL BE SUPPLIED WITH THE NAMES AND NUMBERS OF AT LEAST TWO (2) PERSONS IN CHARGE OF, OR RESPONSIBLE FOR, THE WORK, WHO CAN BE REACHED FOR EMERGENCY WORK TWENTY-FOUR (24) HOURS A DAY, SEVEN (7) DAYS A WEEK.
5. THE RUNWAY OBJECT FREE AREA (ROFA) IS AN IMAGINARY SURFACE, 250 FEET WIDE, CENTERED ABOUT THE RUNWAY CENTERLINE. CONTRACTOR FORCES TO REMAIN CLEAR OF THE ROFA UNLESS THE RUNWAY IS CLOSED.
6. CONTRACTOR FOREMAN SHALL HAVE AN AIR-BAND RADIO ON HAND AT ALL TIMES, TUNED TO THE PROPER FREQUENCY. THE SANTA YNEZ AIRPORT AIR-BAND RADIO FREQUENCY IS 122.8.
7. ALL REQUIRED PERMITS SHALL BE OBTAINED BY THE CONTRACTOR AND APPROVED BY THE ENGINEER PRIOR TO CONSTRUCTION.
8. CONTRACTOR TO SHALL SECURE CONSTRUCTION WATER INCLUDING PAYING FOR ALL COSTS ASSOCIATED THERE-WITH.
9. CONTRACTOR SHALL REFER TO THE PROJECT LAYOUT PLAN FOR EQUIPMENT AND MATERIAL STORAGE AND STAGING AREAS, ACCESS TO THE AIRPORT, AND CONTRACTOR ROUTES INSIDE THE AIRPORT. THERE SHALL BE NO CONTRACTOR FORCES ON ACTIVE AIRFIELD PAVEMENT THAT IS OUTSIDE THE WORK AREA.
10. THE CONTRACTOR SHALL NOTIFY THE AIRPORT 72-HOURS IN ADVANCE FOR ALL TAXIWAY CLOSURES.
11. THE CONTRACTOR IS RESPONSIBLE TO PERFORM ALL SURVEY LAYOUT REQUIRED FOR THE CONSTRUCTION OF THE PROJECT. THE ENGINEER SHALL ESTABLISH NECESSARY HORIZONTAL AND VERTICAL CONTROL. CONTRACTOR IS RESPONSIBLE FOR PRESERVING INTEGRITY OF HORIZONTAL AND VERTICAL CONTROLS ESTABLISHED BY ENGINEER/RPR. IN CASE OF NEGLIGENCE ON THE PART OF THE CONTRACTOR OR THEIR EMPLOYEES, RESULTING IN THE DESTRUCTION OF ANY HORIZONTAL AND VERTICAL CONTROL, THE RESULTING COSTS WILL BE DEDUCTED FROM THE CONTRACTORS NEXT PAY REQUEST.
12. THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE PRESERVATION OF ALL EXISTING IMPROVEMENTS, PROPERTY AND FACILITIES. CONTRACTOR IS RESPONSIBLE FOR ALL COSTS ASSOCIATED WITH REPLACING EXISTING IMPROVEMENTS IF DAMAGED DURING CONSTRUCTION. DAMAGE SHALL BE REPORTED TO THE ENGINEER AND THE AIRPORT IMMEDIATELY.
13. CONTRACTOR SHALL PERFORM A USA CALL (811) AND POT HOLE ALL IDENTIFIED UNDERGROUND UTILITIES, PIPES, CONDUITS, ETC., TO HIS SATISFACTION. CONTRACTOR SHALL DOCUMENT ALL FOUND PIPE, CONDUITS, AND UNDERGROUND IMPROVEMENTS ON A SET OF PLANS, TO BE PROVIDED TO THE ENGINEER AT THE END OF THE PROJECT.
14. THE CONTRACTOR YARD IS IDENTIFIED ON THE PROJECT LAYOUT PLAN. THE CONTRACTOR IS RESPONSIBLE FOR ALL UTILITIES NEEDED FOR THE YARD.
15. CONTRACTOR SHALL IMPLEMENT A DUST CONTROL PROGRAM FOR THE DURATION OF THE PROJECT. THERE WILL BE NO SPECIFIC COMPENSATION FOR DUST CONTROL. THE CONTRACTOR'S RESPONSIBILITY FOR DUST CONTROL EXTENDS OVER EVENINGS, WEEKENDS, HOLIDAYS, AND ANY EXTENDED NON-WORK PERIODS.
16. CONTRACTOR IS REQUIRED TO PRESENT TO THE ENGINEER ANY DISCREPANCIES BETWEEN THE PLANS AND SPECIFICATIONS AND THE EXISTING FIELD CONDITIONS AS SOON AS THEY ARE DISCOVERED.
17. ALL ITEMS AND MATERIALS INTENDED TO BE REMOVED FROM THE SITE SHALL BE HAULED OFF IN A LEGAL-WEIGHT VEHICLE, TARPED, AND DISPOSED OF AT A LEGAL FACILITY.
18. ALL MATERIALS INTENDED TO BE SALVAGED TO THE AIRPORT SHALL REMAIN ON SITE AND DELIVERED TO A SPECIFIED AREA ON AIRPORT PROPERTY.
19. SOME OF THE WORK ON THIS PROJECT IS WITHIN THE TAXIWAY OBJECT FREE AREA (TOFA) OF AN ACTIVE TAXIWAY. WORK WITHIN THE TOFA SHALL BE ACCOMPLISHED UNDER RADIO CONTROL AND THE CONTRACTOR SHALL VACATE THE TOFA WHEN AIRCRAFT ARE PASSING BY.

AIRPORT ACCESS AND SECURITY:

1. THROUGHOUT THE DURATION OF THE PROJECT, AIRPORT PERIMETER SECURITY SHALL REMAIN EQUAL TO OR GREATER THAN WHAT CURRENTLY EXISTS.
2. CONTRACTOR TO PRACTICE AUTOMATIC GATE PROTOCOL:
   A. CONTRACTOR CLEAR GATE INDUCTION LOOPS SO GATE CAN CLOSE, WAIT, AND ENSURE GATE CLOSES WITH NO OTHER UNAUTHORIZED USER ENTERS THE AIRPORT.
   B. CONTRACTOR IS FULLY RESPONSIBLE FOR VEHICLES, EQUIPMENT, OR USER THAT ENTER A GATE BEHIND HIM.
   C. CONTRACTOR MUST BE PREPARED TO DENY ACCESS TO ANYONE UNAUTHORIZED FOR AIRPORT ACCESS.
   D. OTHERS WITH ACCESS AUTHORITY NOT AFFILIATED WITH THE PROJECT WILL WAIT UNTIL YOUR MOVEMENT IS COMPLETE. DO NOT ATTEMPT TO ACCOMMODATE.
3. ALL VEHICLES AND EQUIPMENT ENTERING THE AIRPORT SHALL BE LABELED WITH THE NAME OF THE FIRM ON AT LEAST TWO SIDES OF THE VEHICLE.
4. ALL VEHICLES AND EQUIPMENT SHALL BE EQUIPPED WITH AN ORANGE AND WHITE CHECKERED SAFETY FLAG (DAYTIME) OR FLASHING LIGHTS (DAYTIME OR NIGHT TIME), AT THE HIGHEST POINT OF THE VEHICLE.


ABBREVIATIONS:

<	ANGLE POINT
AC	ASPHALTIC CONCRETE
BLDR	BOULDER
BRD	BOARD
BSW	BACK OF SIDEWALK
C	CONCRETE
CB	CATCH BASIN
CLVRT	CULVERT
COMM	COMMUNICATIONS
DS	DOWNSPOUT
DWY	DRIVEWAY
E	EAST
EP	EDGE OF PAVEMENT
FC	FENCE
FL	FLOW LINE
FSW	FRONT OF SIDEWALK
G	GROUND
HDPE	HIGH DESNITY POLY ETHYLENE
HDR	HEADER
HDWL	HEADWALL
ICV	IRRIGATION CONTROL VALVE
INTX	INTERSECTION
INV	INVERT
JT	JOINT
LIP	LIP OF GUTTER
LITE	TAXIWAY OR RUNWAY LIGHTING
N	NORTH
NP	NO PARKING
POC	POINT ON CURVE
PVR	PAVER
RCP	REINFORCED CONCRETE PIPE
RET	RETAINING
S	SOUTH
SD	STORM DRAIN
STRIPE	PAINTED PAVEMENT MARKING
TC	TOP OF CURB
USA	UNDERGROUND SERVICE ALERT MARKING
VLT	VAULT
W	WEST
AOA	AIRPORT OPERATIONS AREA
BRL	BUILDING RESTRICTION LINE
RSA	RUNWAY SAFETY AREA
ROFA	RUNWAY OBJECT FREE AREA
TSA	TAXIWAY SAFETY AREA
TOFA	TAXIWAY OBJECT FREE AREA

*NOTE SOME ABBREVIATIONS MAY NOT HAVE BEEN REFERENCED IN THIS DRAWING SET.

SHEET LIST TABLE

NO.	TITLE	SUBTITLE
1	COVER	--
2	GENERAL INFORMATION	NOTES AND ABBREVIATIONS
3	PROJECT LAYOUT PLAN	PLAN VIEW AND PROJECT CONTROL
4	PHASING PLAN	PHASE 1 THROUGH 5
5	DEMOLITION PLAN	STA. 1+00 TO STA. 7+50
6	DEMOLITION PLAN	STA. 7+50 TO STA. 15+50
7	DEMOLITION PLAN	STA. 15+50 TO STA. 22+50
8	DEMOLITION PLAN	STA. 22+50 TO 27+50
9	IMPROVEMENT AND MARKING PLAN	STA. 1+00 TO STA. 7+50
10	IMPROVEMENT AND MARKING PLAN	STA. 7+50 TO STA. 15+50
11	IMPROVEMENT AND MARKING PLAN	STA. 15+50 TO STA. 22+50
12	IMPROVEMENT AND MARKING PLAN	STA. 22+50 TO 27+50
13	PAVEMENT MARKING LAYOUT	LINE - CURVE - POINT TABLES
14	DETAILS	CRACK REPAIR & PAVEMENT MARKINGS

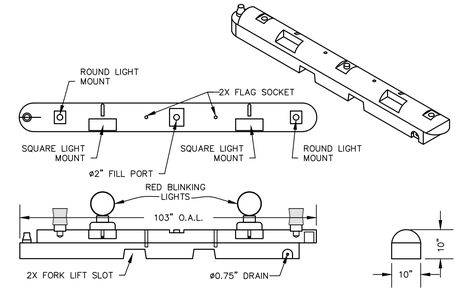

1. CONTRACTOR CAN ELECT EITHER 3 LED/SOLAR OR TWO BATTERY POWER LIGHTS PER DELINEATOR.
2. DELINEATORS TO BE PLACED EITHER INTERLOCKED OR SPACED WITH A 6' MAXIMUM GAP.
3. DELINEATORS TO BE WEIGHTED WITH SAND BAGS OR WATER.

LOW PROFILE LIGHTED DELINEATOR DETAIL

A/2

NO SCALE

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

GENERAL INFORMATION

NOTES AND ABBREVIATIONS

REV.	DESCRIPTION	DATE	APP.
1	-	-	-

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6-30-25 CIVIL STATE OF CALIFORNIA

DESIGN	JTH
DRAWN	JTH
CHECKED	JTH
DWG.NO.	22-55
DATE	8/10/2024
SHEET	2 OF 14

PLOT DATE: 8/11/2025

LEGEND:

- CONTROL POINT
- AREA OF IMPROVEMENTS
- CONTRACTOR PATH OF TRAVEL
- BRL — BUILDING RESTRICTION LINE (BRL)
- HYDRANT
- ROFA — RUNWAY OBJECT FREE AREA (ROFA)
- PL — AIRPORT PROPERTY LINE
- B — TAXIWAY DESIGNATION
- CONTRACTOR YARD
- G — G — AIRPORT ACCESS GATE
- RUNWAY PROTECTION ZONE (RPZ)
- TOFA — TAXIWAY OBJECT FREE AREA (TOFA)

GRAPHIC SCALE

100 0 50 100 200 400

(IN FEET)
1 inch = 100 ft.

BASIS OF BEARING:

THE BASIS OF BEARINGS FOR THIS SURVEY IS THE CALIFORNIA COORDINATE SYSTEM, ZONE 5, NAD83–2011, EPOCH 2010.0000, HOLDING IZA A 1989 FOR POSITION AND THE BEARING BETWEEN IZA A 1989 AND IZA B 1989 FOR LINE.


BENCHMARK:

NORTH AMERICAN VERTICAL DATUM OF 1988 (NAVD88), HOLDING IZA A 1989 WITH AN ELEVATION OF 678.00' NAVD88.

CONTROL POINTS:

NAD83–2011 Epoch 2010.000
NAVD88

Pt. No.	Northing	Easting	Elev	Description
10	2049859.91	5938222.12	672.87	MAG & SHINER
11	2050066.99	5937897.19	673.30	SCRIBED X IN TC
1001	2050214.76	5937224.85	674.74	Set No.5 Rebar & Plastic Cap "Control Point"
1005	2049690.94	5938540.72	672.17	Set X in Concrete
1006	2049824.12	5938562.54	673.50	Set X in Concrete
1007	2049909.66	5938074.97	672.13	Set X in Concrete
1008	2050037.16	5937838.95	673.19	Set X in Concrete
1009	2050080.52	5937568.27	673.09	Set X in Concrete
1010	2050014.00	5937039.79	667.89	Set X in Concrete
1011	2050311.03	5937095.24	667.31	Set X in Concrete
1012	2050291.14	5936959.65	668.07	Set X in Concrete
1013	2050056.23	5936920.62	667.73	Set X in Concrete
1014	2050076.83	5936789.90	667.62	Set X in Concrete
1015	2050049.63	5936657.84	667.13	Set X in Concrete
1016	2050398.21	5936715.45	667.51	Set X in Concrete
1017	2050366.67	5936838.13	668.03	Set X in Concrete
1018	2049904.03	5936837.75	663.60	Set X in Concrete
1019	2049845.74	5937258.53	668.36	Set No.5 Rebar & Plastic Cap "Control Point"
1020	2049765.31	5937679.42	668.62	Set X in Concrete
1021	2049715.72	5938035.26	670.79	Set No.5 Rebar & Plastic Cap "Control Point"
1022	2050416.92	5936534.85	663.60	SET X
1023	2050088.43	5936480.62	663.030,	SET X
1024	2049997.94	5936498.98,	660.429,	SET X
1025	2050442.66	5936341.87	662.174,	SET X
1026	2050185.99	5936299.31	661.786,	SET X
1027	2050028.35,	5936151.86	657.508,	SET X
1028	2050355.66,	5936115.53	663.825,	SET X
1029	2050434.58	5936048.65	664.877,	SET MAG+TIN
1030	2050072.48	5936009.71	658.638,	SET X
6009	2048953.09	5939112.41	678.00	3" NOS Disk IZA A 1989
6010	2049568.95	5935431.17	661.30	3" NOS Disk IZA B 1989

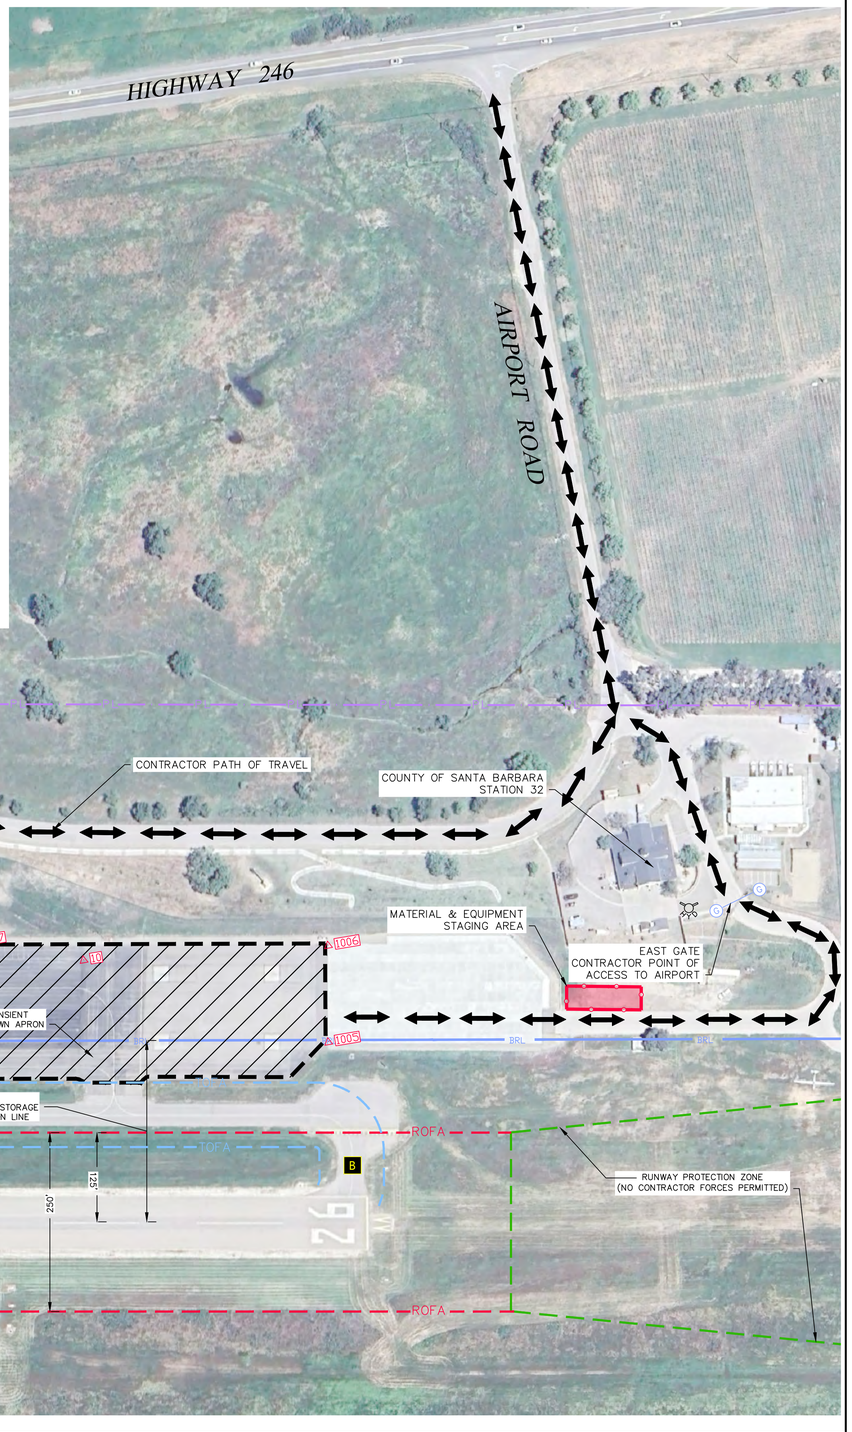

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

PROJECT LAYOUT PLAN

PLAN VIEW AND PROJECT CONTROL

REV.	DESCRIPTION	DATE	APP.
1	-	-	-

TARTAGLIA ENGINEERING


SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON


REGISTERED PROFESSIONAL ENGINEER
JOHN A. SMITH
No. 46852
EXP. 6-30-25
CIVIL
STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22-55
DATE 8/10/2024
SHEET 3 OF 14


PLOT DATE=11/2025

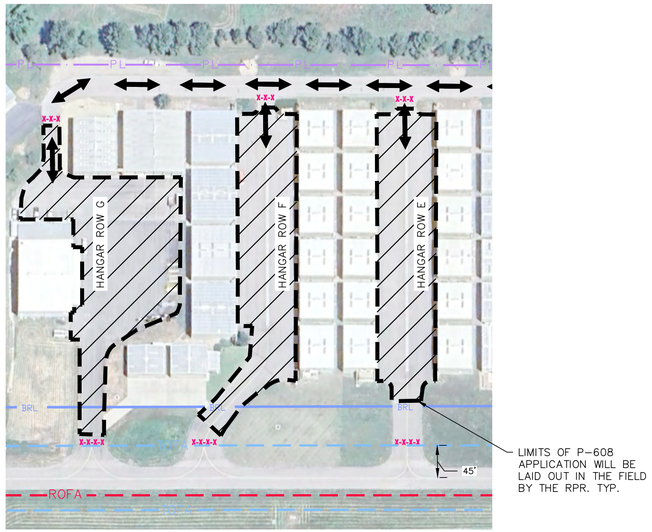


A/4 PHASE 1

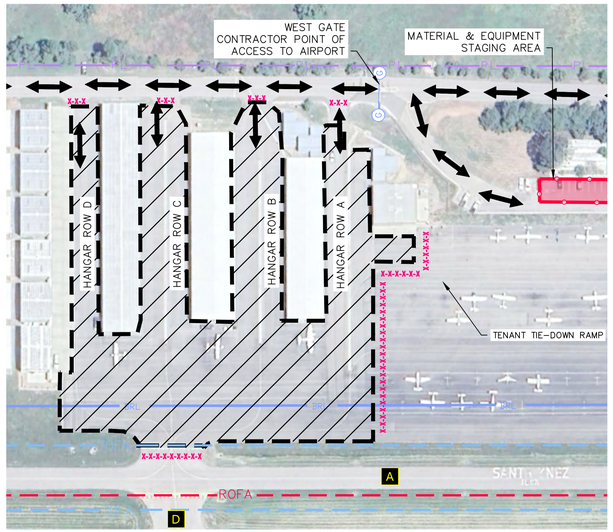

B/4 PHASE 2

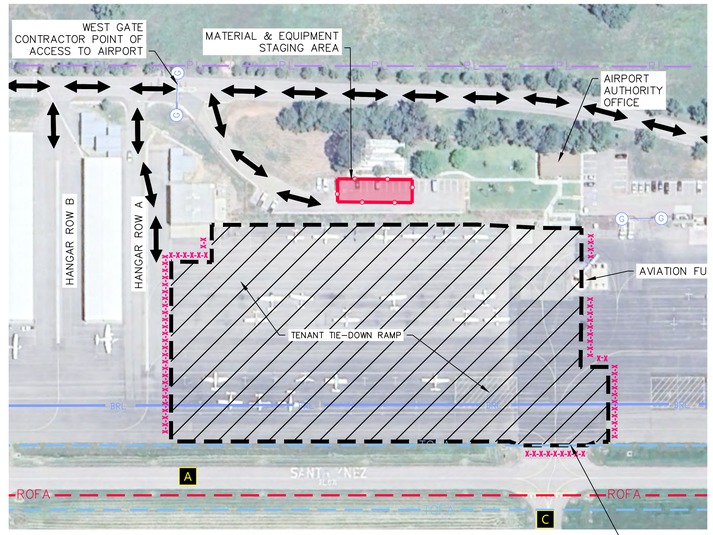

C/4 PHASE 3

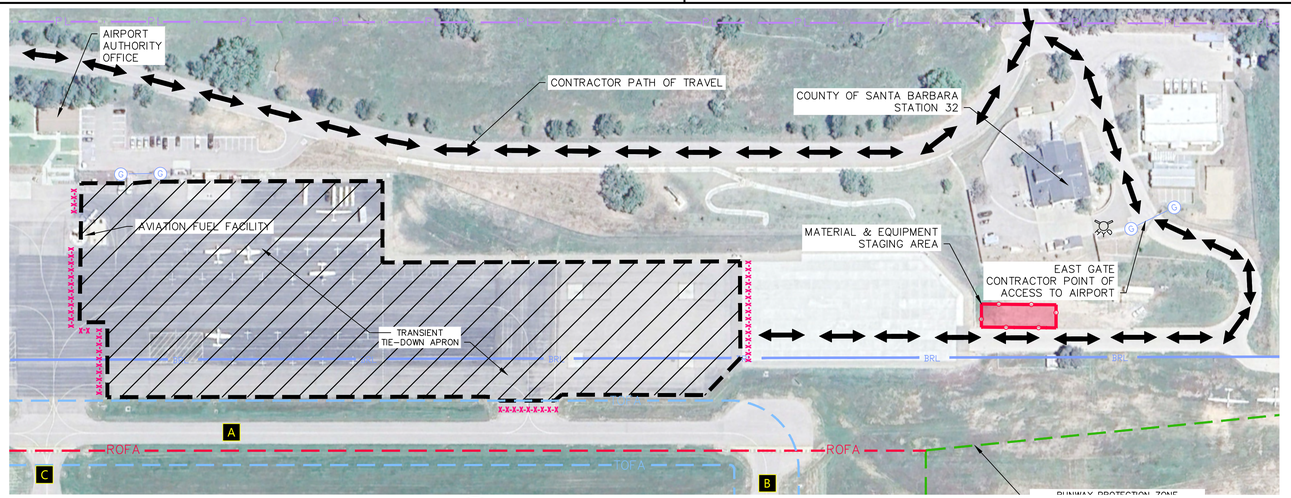

D/4 PHASE 4

LEGEND:

- LOW PROFILE DELINEATION (SEE DETAIL A, SHEET 2)
- AREA OF IMPROVEMENTS
- CONTRACTOR PATH OF TRAVEL
- BRL — BUILDING RESTRICTION LINE (BRL)
- HYDRANT
- ROFA — RUNWAY OBJECT FREE AREA (ROFA)
- PL — AIRPORT PROPERTY LINE
- B — TAXIWAY DESIGNATION
- CONTRACTOR YARD
- G — AIRPORT ACCESS GATE
- RUNWAY PROTECTION ZONE (RPZ)
- TOFA — TAXIWAY OBJECT FREE AREA (TOFA)

PHASING SUMMARY TABLE

PHASE	WORK AREAS	GENERAL WORK SUMMARY	DURATION
1	HANGAR ROWS E, F, & G	CRACK FILL & SEAL, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	7 WORKING DAYS
2	HANGAR ROWS A, B, C, & D	CRACK FILL & SEAL, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	8 WORKING DAYS
3	TENANT TIE-DOWN APRON	CRACK FILL & SEAL, REMOVAL & RE-INSTALLATION OF TIE-DOWN COMPONENTS, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	15 WORKING DAYS
TRANSITION		TRANSITION PERIOED TO ALLOW TENANTS TO RE-LOCATE AIRCRAFT BEFORE PHASE 4 BEGINS.	3 CALENDAR DAYS
4	TRANSIENT TIE-DOWN APRON	CRACK FILL & SEAL, REMOVAL & RE-INSTALLATION OF TIE-DOWN COMPONENTS, APPLICATION OF P-608 SURFACE TREATMENT, AND FIRST COAT OF PAVEMENT MARKINGS.	15 WORKING DAYS
5	ENTIRE PROJECT WORK AREA	SECOND COAT OF PAVEMENT MARKINGS	5 WORKING DAYS
TOTAL			50 WORKING DAYS

PHASING NOTES:

1. WORK SHALL BE ACCOMPLISHED IN A PHASED APPROACH. THE WORK OF ONE PHASE SHALL BE COMPLETE, THE WORK AREA CLEANED, AND ALL ACCEPTED BY THE INSPECTOR BEFORE PROCEEDING TO THE NEXT PHASE. THE ONLY EXCEPTION TO THIS IS THE APPLICATION OF THE SECOND COAT OF PERMANENT PAVEMENT MARKINGS.
2. ALL SECOND COAT OF PERMANENT PAVEMENT MARKINGS TO OCCUR IN ONE MOVE IN, 30 DAYS+ AFTER THE FIRST COAT OF MARKINGS APPLIED DURING PHASE 4. A CONTRACT TIME SUSPENSION WILL OCCUR BETWEEN PHASE 4 AND PHASE 5 TO ALLOW FOR THE 30 DAYS OF CURE BEFORE APPLICATION OF THE SECOND COAT OF MARKINGS.
3. CONTRACTOR TO PREPARE A WORK PLAN FOR PHASE 5; SECOND COAT OF PAVEMENT MARKINGS. ENGINEER SHALL APPROVE THE WORK PLAN BEFORE ANY WORK BEGINS IN THIS PHASE. WORK PLAN SHALL CONSIDER AIRCRAFT OPERATIONS: ALLOW AIRCRAFT TO ACCESS THE FUEL FARM, TWO OF THE THREE TAXIWAY CONNECTORS BETWEEN TAXIWAY ALPHA AND THE APRON SHALL BE OPEN AT ALL TIMES. IT IS ANTICIPATED THAT THE WORK AREAS WILL BE SPLIT UP INTO THREE OR FOUR AREAS. LOW PROFILE DELINEATION IS REQUIRED TO CLOSE DOWN THE WORK AREA UNTIL THE PAVEMENT MARKINGS ARE DRY, AND THE MARKINGS ARE ACCEPTED BY THE RPR, BEFORE PROCEEDING TO ANOTHER WORK AREA.
4. DEPENDING ON TIME OF CONSTRUCTION START DATE, THE ORDER OF PHASE 1, 2, 3 AND 4 WORK MAY SHIFT OR CHANGE.
5. A PHASE TRANSITION PERIOD OF 3 CALENDAR DAYS WILL OCCUR BETWEEN PHASES 3 & 4 TO ALLOW TENANTS TO RE-LOCATE AIRCRAFT TO FACILITATE WORK ON THE SUBSEQUENT PHASE. DURING THIS PERIOD, NO CONTRACT WORKING DAYS WILL BR COUNTED TOWARDS ANY SPECIFIC PHASE OR THE OVERALL CONTRACT DURATION.
6. LOW PROFILE BARRICADES SHALL BE PLACED AT LOCATIONS SHOWN ON THESE PHASING PLANS. BARRICADES FOR DELINEATION SHALL BE INSTALLED AT THE BEGINNING OF THE PHASE, REMAIN IN-PLACE FOR THE DURATION OF THE PHASE (24 HOURS, 7 DAYS A WEEK) AND REMOVED WHEN THE PHASE IS COMPLETE AND ACCEPTED BY THE INSPECTOR. REFER TO DETAIL A, SHEET 2 FOR LOW PROFILE BARRICADE DETAIL.

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

PHASING PLAN

PHASE 1 THROUGH 5

REV.	DESCRIPTION	DATE	APP.
1	-	-	-

TARTAGLIA ENGINEERING


SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER — JOHN A. SMITH — No. 46852 — EXP. 6-30-25 — CIVIL — STATE OF CALIFORNIA

DESIGN	JTH
DRAWN	JTH
CHECKED	JTH
DWG.NO.	22-55
DATE	8/10/2024
SHEET	4 OF 14

PLOT DATE=8/11/2025

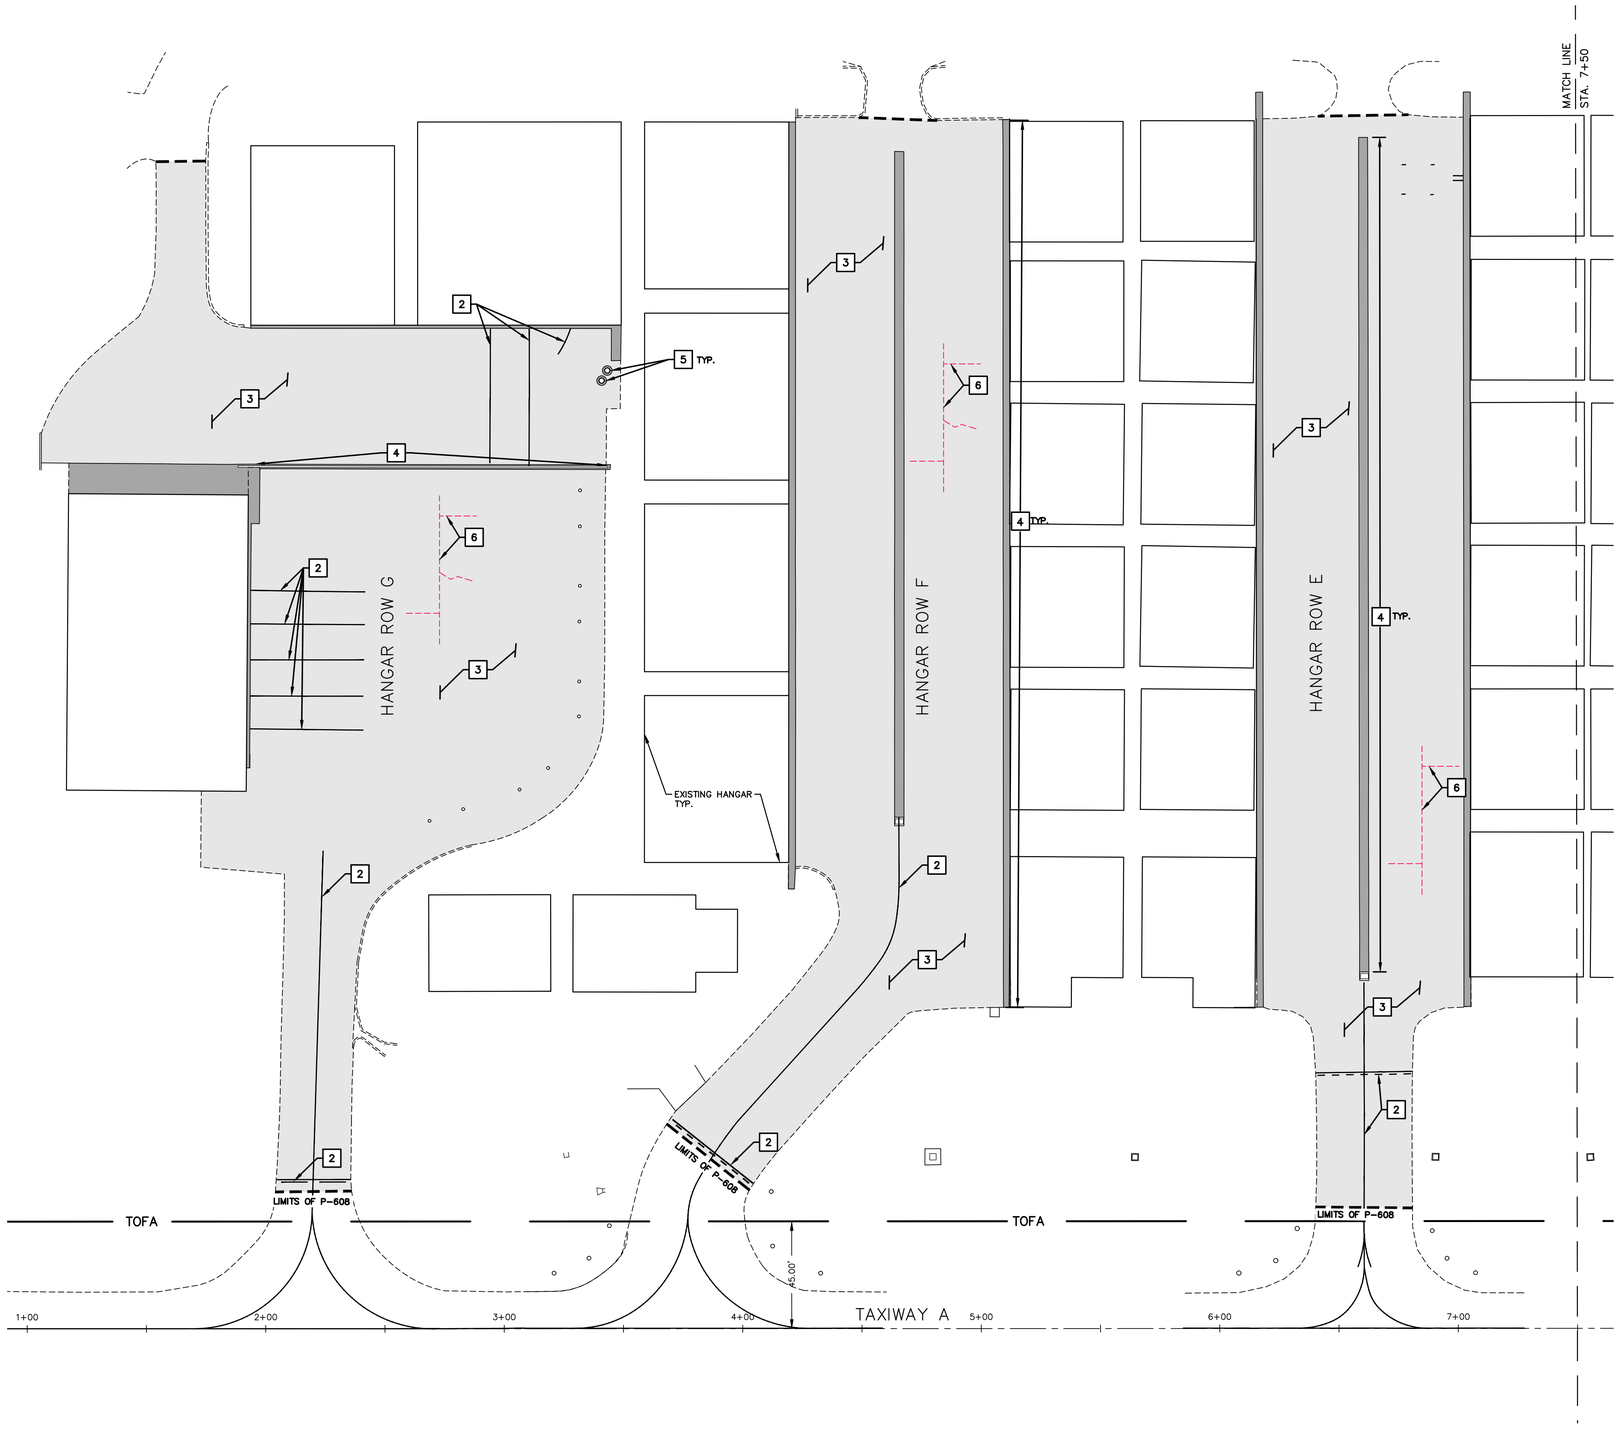

DEMOLITION & SURFACE PREPARATION NOTES (SHEETS 5-8):

1. REMOVE TIE-DOWN CABLES AND CHAINS BEFORE P-608 APPLICATION. CONTRACTOR TO STORE CABLES AND CHAINS UNTIL RE-INSTALLATION OCCURS AFTER P-608 SURFACE TREATMENT.
2. EXISTING PAVEMENT MARKING TO BE OBLITERATED WITHIN LIMITS OF WORK BEFORE P-608 APPLICATION.
3. PAVEMENT AREA TO BE CLEANED, AND SWEPT BEFORE P-608 APPLICATION.
4. MASK AND/OR SHIELD CONCRETE VALLEY GUTTER, CONCRETE HANGAR SPLASH PAD AND MISCELLANEOUS CONCRETE FLATWORK PRIOR TO AND DURING P-608 APPLICATION.
5. MASK CONCRETE TIE-DOWN ANCHOR OR UTILITY PRIOR TO P-608 APPLICATION.
6. PERFORM CRACK REPAIR ON TIE-DOWN APRON WITHIN THE LIMITS OF OF WORK. REFER TO DETAIL A, SHEET 14. RPR TO MARK OUT CRACKS TO BE REPAIRED. (SPECIFIC LOCATIONS NOT SHOWN).
7. EXISTING TAXIWAY CENTERLINE TO BE OBLITERATED UNDER RPR RADIO CONTROL. NOTE: THIS EFFORT IS WITH THE TAXIWAY ALPHA SAFETY AREA.

LEGEND (SHEETS 5-8):

- AREA OF P-608 SURFACE TREATMENT
- EXISTING CRACK (ASPHALT)
- EXISTING TIE-DOWN CHAIN
- EXISTING TIE-DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA

SCALE BAR
0 15 30 60
1 inch = 30 ft.

UNDERGROUND SERVICE ALERT
811
DIAL 811
TWO WORKING DAYS BEFORE YOU DIG

DEMOLITION PLAN

STA. 1+00 TO STA. 7+50

REV.	DESCRIPTION	DATE	APP.
1	-	-	-

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER
JOHN A. SMITH
No. 46852
EXP. 6-30-25
CIVIL
STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22-55
DATE 8/10/2024
SHEET 5 OF 14


PLOT DATE=8/11/2025

☐ DEMOLITION & SURFACE PREPARATION NOTES (SHEETS 5–8):

1. REMOVE TIE–DOWN CABLES AND CHAINS BEFORE P–608 APPLICATION. CONTRACTOR TO STORE CABLES AND CHAINS UNTIL RE–INSTALLATION OCCURS AFTER P–608 SURFACE TREATMENT.
2. EXISTING PAVEMENT MARKING TO BE OBLITERATED WITHIN LIMITS OF WORK BEFORE P–608 APPLICATION.
3. PAVEMENT AREA TO BE CLEANED, AND SWEPT BEFORE P–608 APPLICATION.
4. MASK AND/OR SHIELD CONCRETE VALLEY GUTTER, CONCRETE HANGAR SPLASH PAD AND MISCELLANEOUS CONCRETE FLATWORK PRIOR TO AND DURING P–608 APPLICATION.
5. MASK CONCRETE TIE–DOWN ANCHOR OR UTILITY PRIOR TO P–608 APPLICATION.
6. PERFORM CRACK REPAIR ON TIE–DOWN APRON WITHIN THE LIMITS OF OF WORK. REFER TO DETAIL A, SHEET 14. RPR TO MARK OUT CRACKS TO BE REPAIRED. (SPECIFIC LOCATIONS NOT SHOWN).
7. EXISTING TAXIWAY CENTERLINE TO BE OBLITERATED UNDER RPR RADIO CONTROL. NOTE: THIS EFFORT IS WITH THE TAXIWAY ALPHA SAFETY AREA.

LEGEND (SHEETS 5–8):

- AREA OF P–608 SURFACE TREATMENT
- EXISTING CRACK (ASPHALT)
- EXISTING TIE–DOWN CHAIN
- EXISTING TIE–DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA

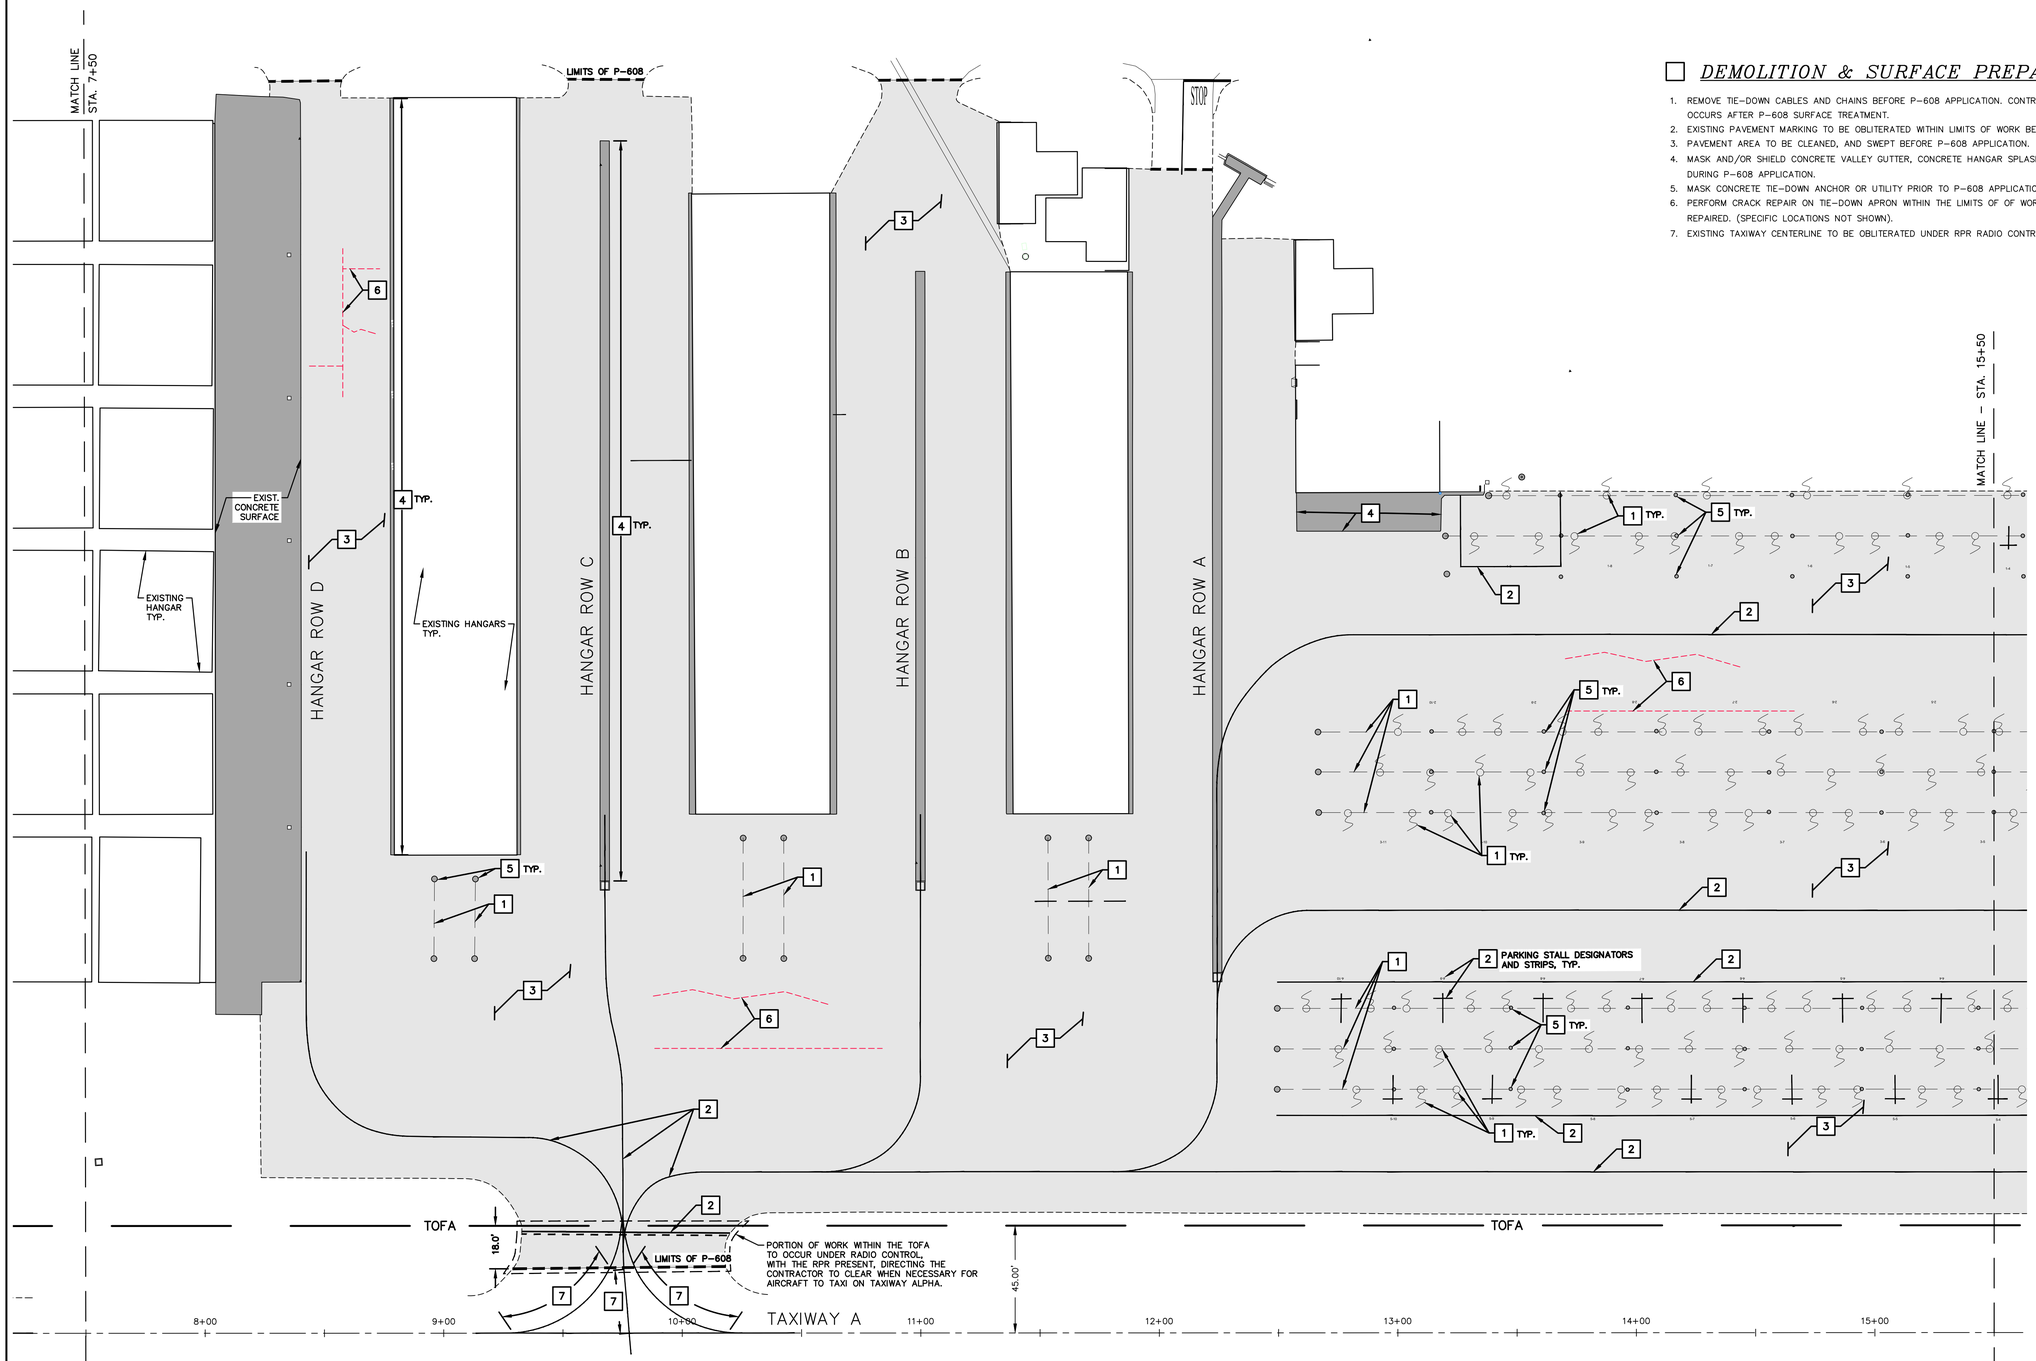

SCALE BAR

0 15 30 60

1 inch = 30 ft.

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

DEMOLITION PLAN

STA. 7+50 TO STA. 15+50

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6–30–25 CIVIL STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22–55
DATE 8/10/2024
SHEET 6 OF 14


PLOT DATE:8/11/2025

☐ DEMOLITION & SURFACE PREPARATION NOTES (SHEETS 5–8):

1. REMOVE TIE–DOWN CABLES AND CHAINS BEFORE P–608 APPLICATION. CONTRACTOR TO STORE CABLES AND CHAINS UNTIL RE–INSTALLATION OCCURS AFTER P–608 SURFACE TREATMENT.
2. EXISTING PAVEMENT MARKING TO BE OBLITERATED WITHIN LIMITS OF WORK BEFORE P–608 APPLICATION.
3. PAVEMENT AREA TO BE CLEANED, AND SWEPT BEFORE P–608 APPLICATION.
4. MASK AND/OR SHIELD CONCRETE VALLEY GUTTER, CONCRETE HANGAR SPLASH PAD AND MISCELLANEOUS CONCRETE FLATWORK PRIOR TO AND DURING P–608 APPLICATION.
5. MASK CONCRETE TIE–DOWN ANCHOR OR UTILITY PRIOR TO P–608 APPLICATION.
6. PERFORM CRACK REPAIR ON TIE–DOWN APRON WITHIN THE LIMITS OF OF WORK. REFER TO DETAIL A, SHEET 14. RPR TO MARK OUT CRACKS TO BE REPAIRED. (SPECIFIC LOCATIONS NOT SHOWN).
7. EXISTING TAXIWAY CENTERLINE TO BE OBLITERATED UNDER RPR RADIO CONTROL. NOTE: THIS EFFORT IS WITH THE TAXIWAY ALPHA SAFETY AREA.

LEGEND (SHEETS 5–8):

- AREA OF P–608 SURFACE TREATMENT
- EXISTING CRACK (ASPHALT)
- EXISTING TIE–DOWN CHAIN
- EXISTING TIE–DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA

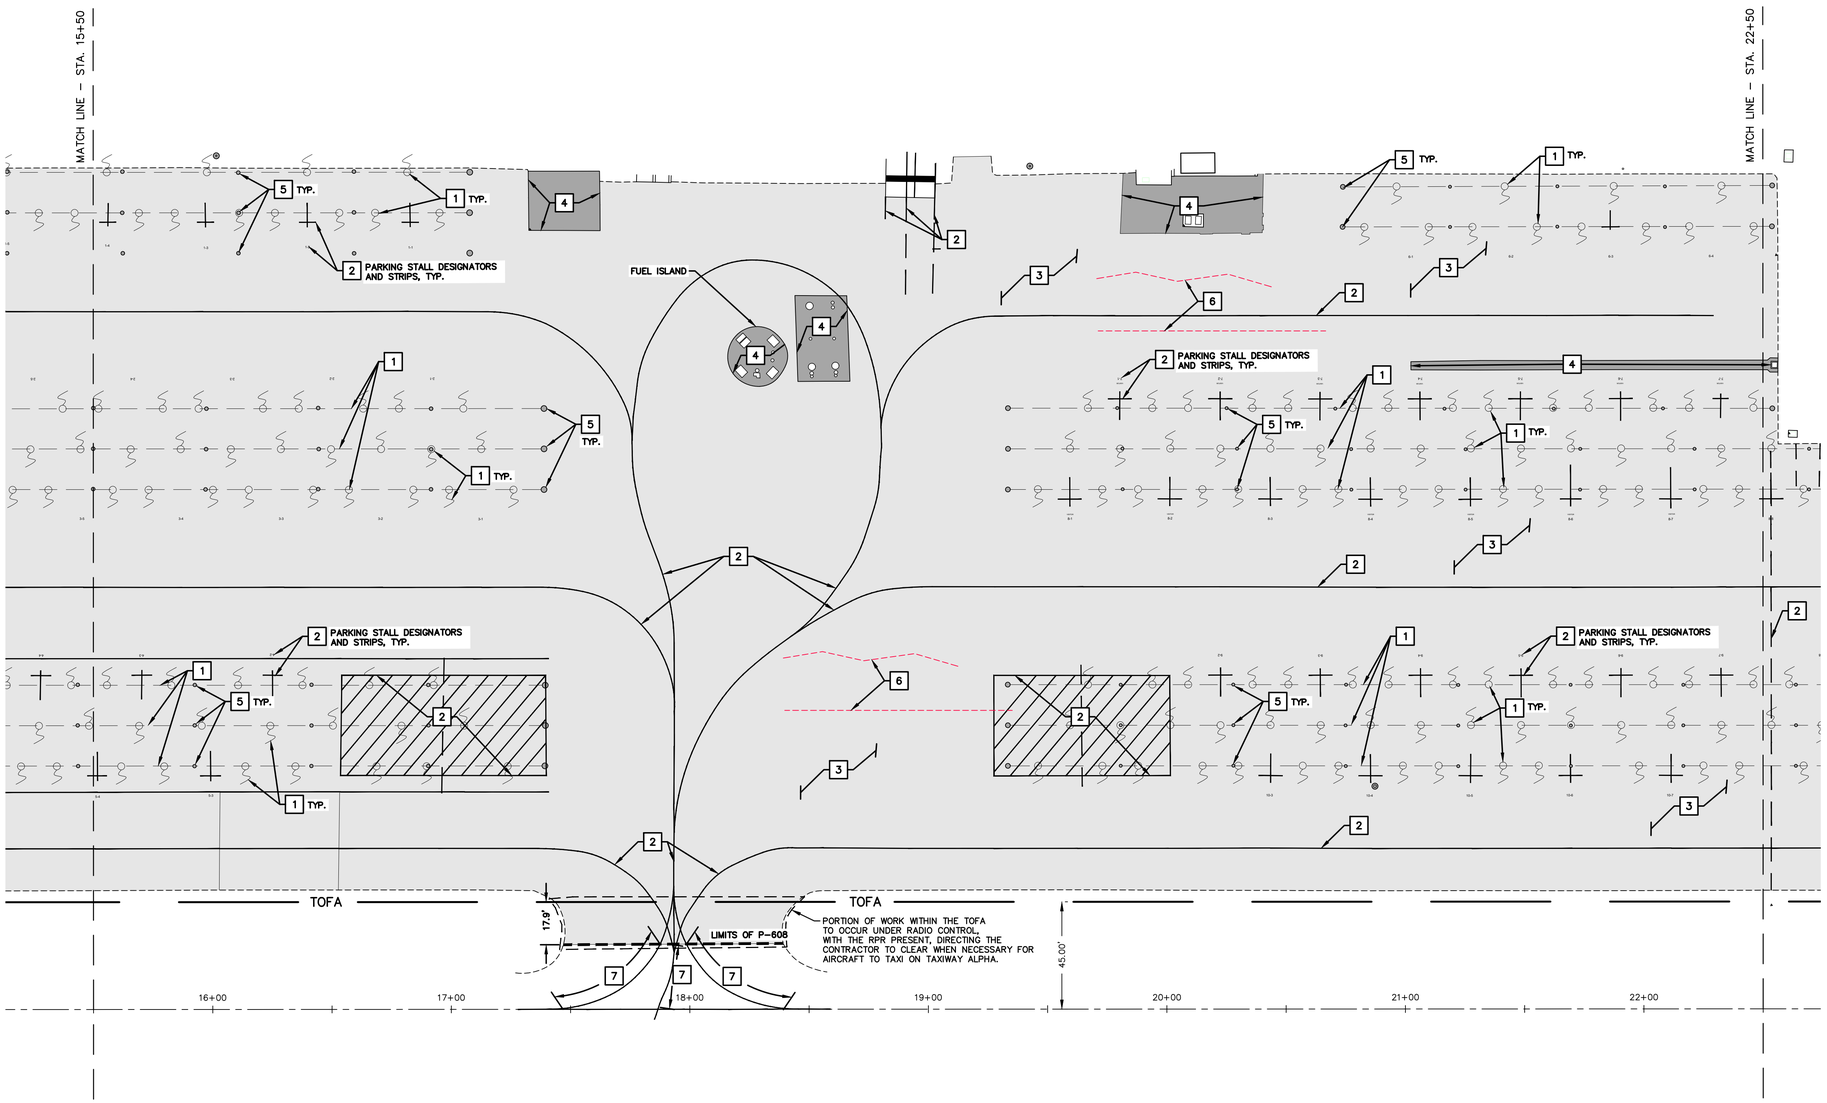

SCALE BAR

0 15 30 60

1 inch = 30 ft.

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

DEMOLITION PLAN

STA. 15+50 TO STA. 22+50

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6–30–25 CIVIL STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22–55
DATE 8/10/2024
SHEET 7 OF 14


PLOT DATE: 8/11/2025

☐ *DEMOLITION & SURFACE PREPARATION NOTES (SHEETS 5–8):*

1. REMOVE TIE–DOWN CABLES AND CHAINS BEFORE P–608 APPLICATION. CONTRACTOR TO STORE CABLES AND CHAINS UNTIL RE–INSTALLATION OCCURS AFTER P–608 SURFACE TREATMENT.
2. EXISTING PAVEMENT MARKING TO BE OBLITERATED WITHIN LIMITS OF WORK BEFORE P–608 APPLICATION.
3. PAVEMENT AREA TO BE CLEANED, AND SWEPT BEFORE P–608 APPLICATION.
4. MASK AND/OR SHIELD CONCRETE VALLEY GUTTER, CONCRETE HANGAR SPLASH PAD AND MISCELLANEOUS CONCRETE FLATWORK PRIOR TO AND DURING P–608 APPLICATION.
5. MASK CONCRETE TIE–DOWN ANCHOR OR UTILITY PRIOR TO P–608 APPLICATION.
6. PERFORM CRACK REPAIR ON TIE–DOWN APRON WITHIN THE LIMITS OF OF WORK. REFER TO DETAIL A, SHEET 14. RPR TO MARK OUT CRACKS TO BE REPAIRED. (SPECIFIC LOCATIONS NOT SHOWN).
7. EXISTING TAXIWAY CENTERLINE TO BE OBLITERATED UNDER RPR RADIO CONTROL. NOTE: THIS EFFORT IS WITH THE TAXIWAY ALPHA SAFETY AREA.

LEGEND (SHEETS 5–8):

- AREA OF P–608 SURFACE TREATMENT
- EXISTING CRACK (ASPHALT)
- EXISTING TIE–DOWN CHAIN
- EXISTING TIE–DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA

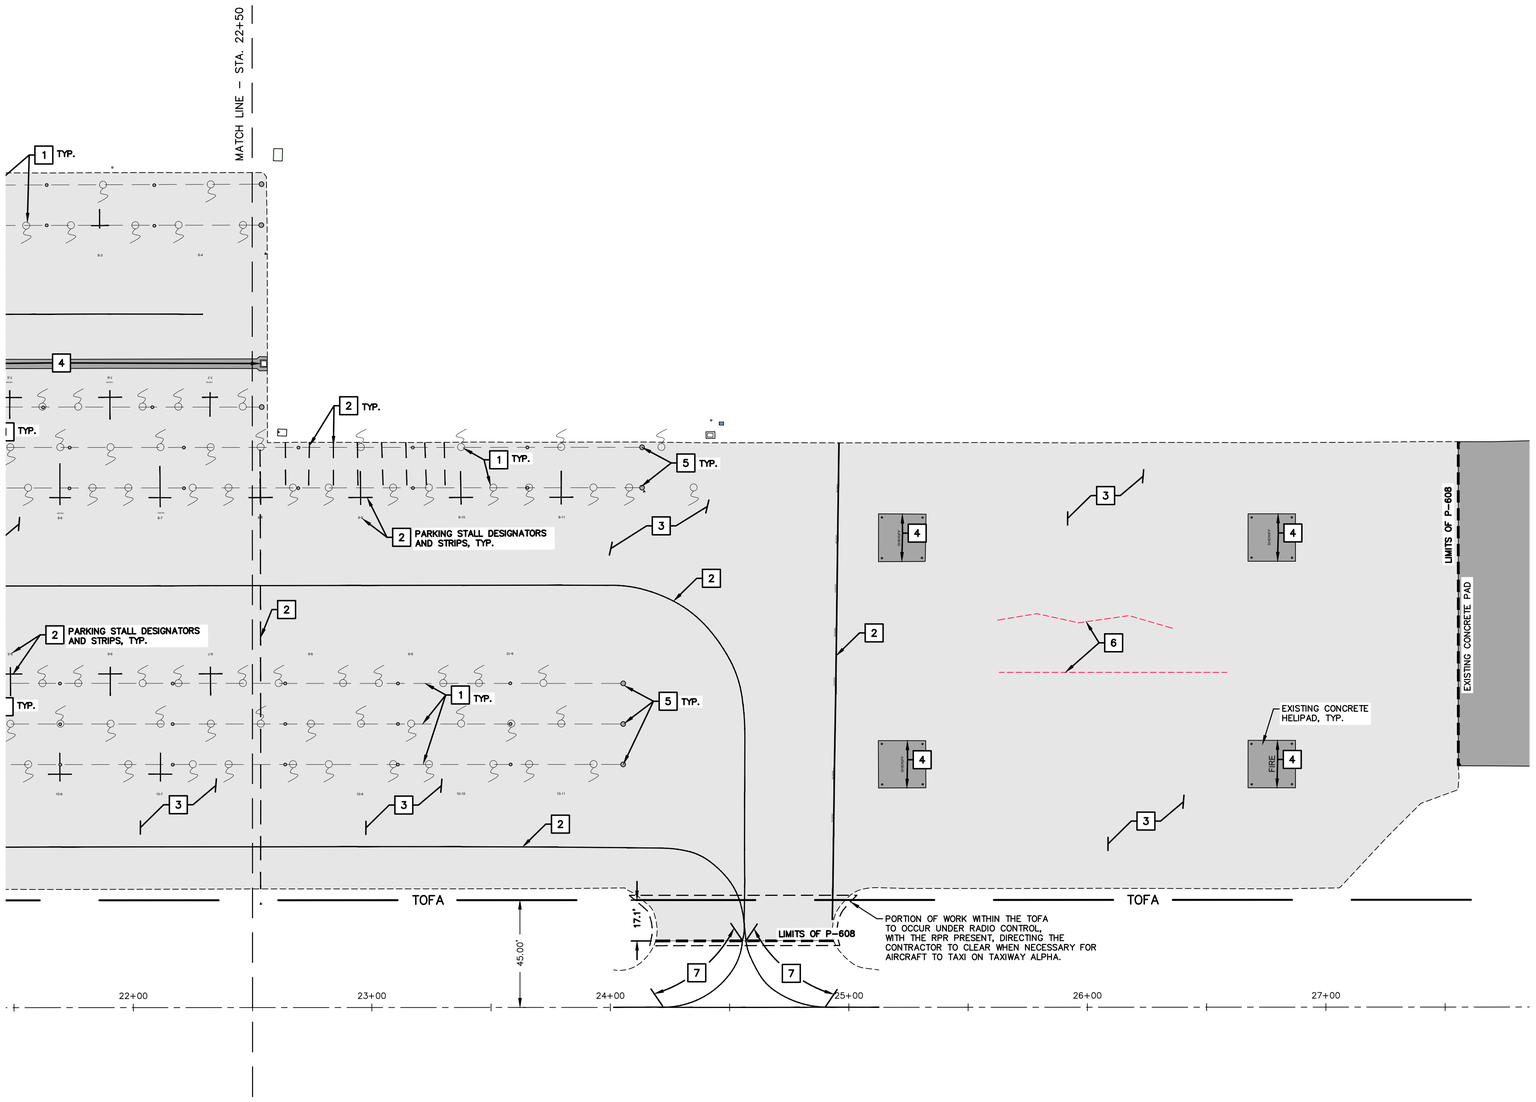

SCALE BAR

0 15 30 60

1 inch = 30 ft.

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

DEMOLITION PLAN

STA. 22+50 TO 27+50

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING


SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6-30-25 CIVIL STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22–55
DATE 8/10/2024
SHEET 8 OF 14

PLOT DATE 8-11-2024

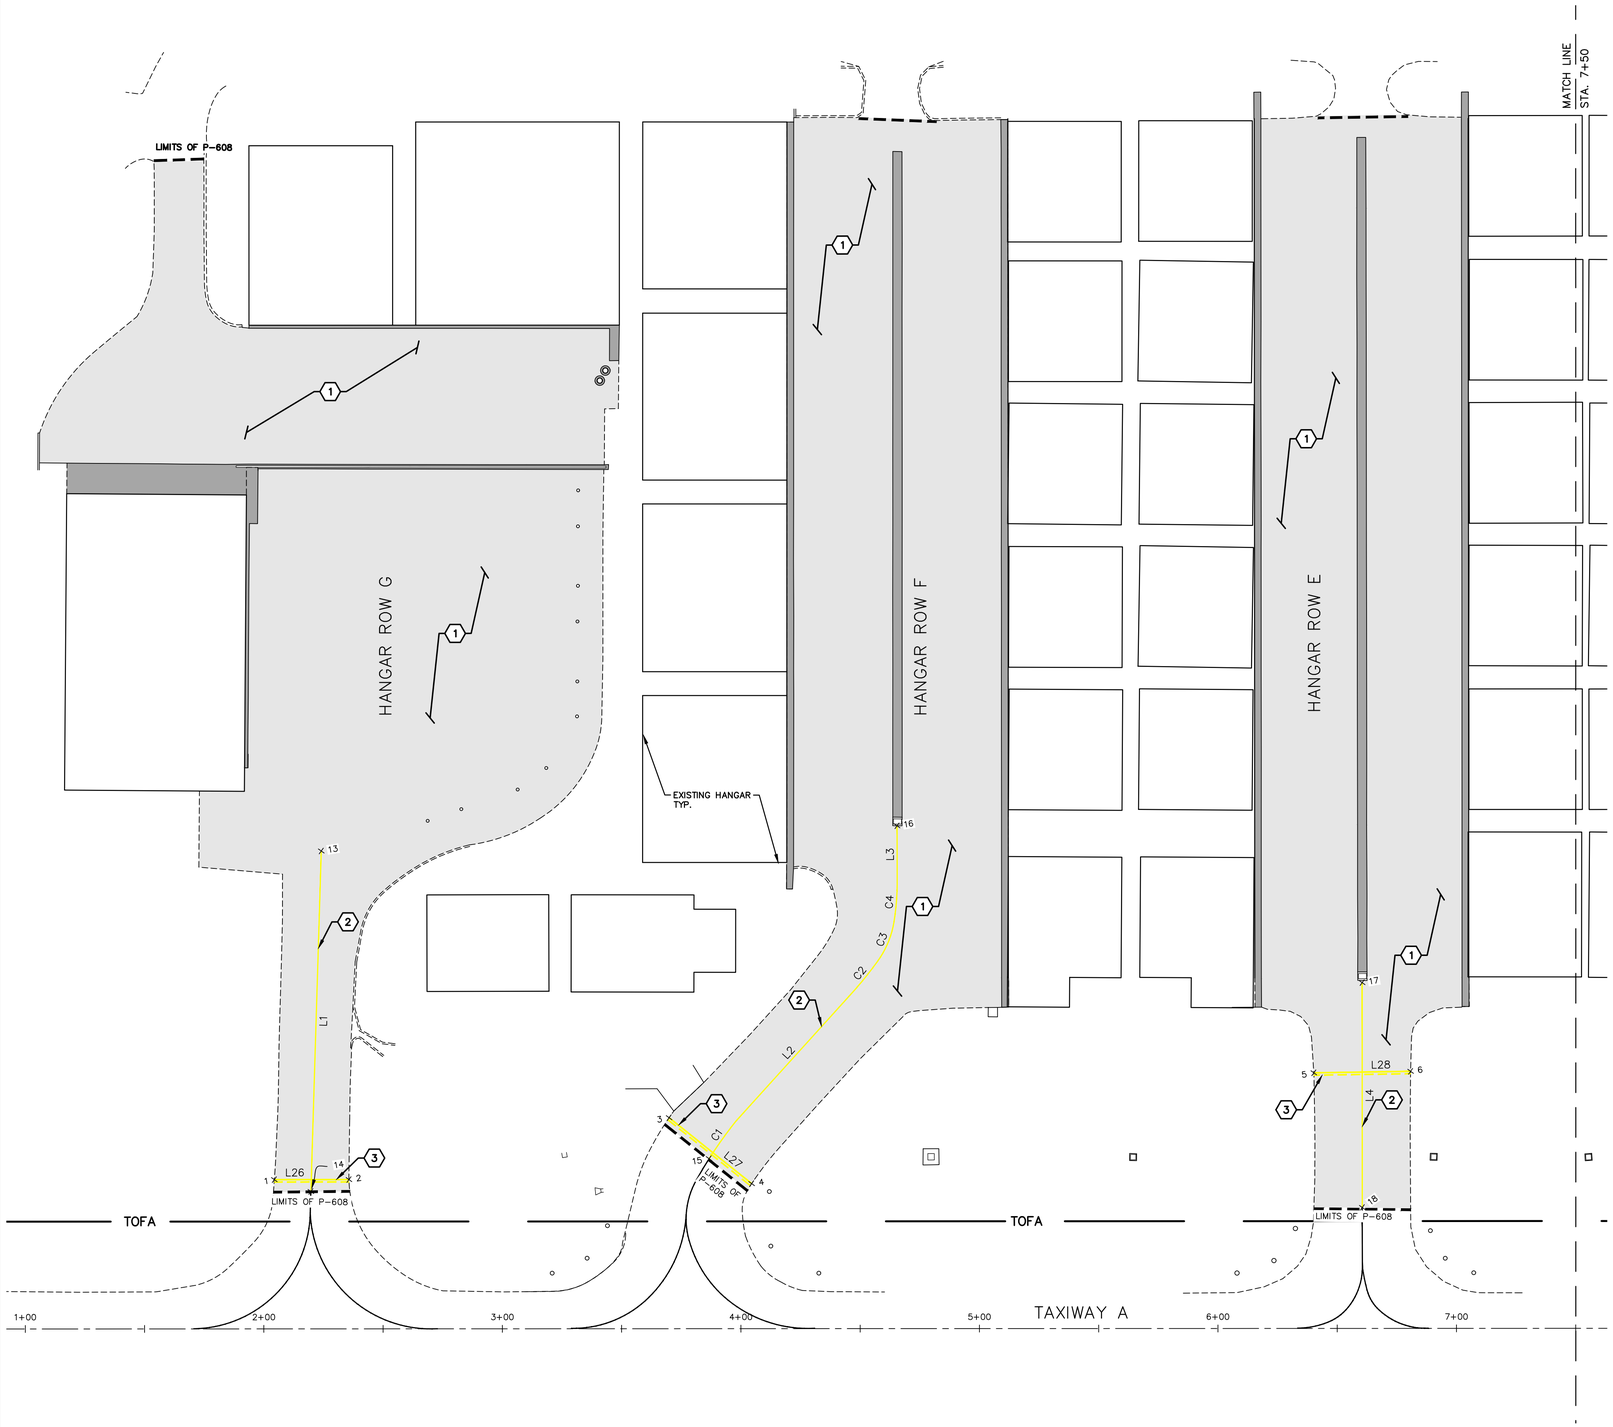

IMPROVEMENT AND MARKING NOTES (SHEETS 9–12):

1. APPLY P–608 SEAL COAT.
2. APPLY TAXIWAY CENTERLINE IN ACCORDANCE WITH DETAIL B, SHEET 14.
3. APPLY NON–MOVEMENT AREA MARKING IN ACCORDANCE IN ACCORDANCE WITH DETAIL F, SHEET 14. NOTE: THIS EFFORT IS WITHIN THE TAXIWAY ALPHA SAFETY AREA.
4. APPLY PARKING STALL MARKING (SMALL AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
5. APPLY PARKING STALL MARKING (LARGE AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
6. APPLY RESTRICTED AREA MARKING IN ACCORDANCE WITH DETAIL D, SHEET 14.
7. APPLY HELICOPTER PARKING AREA MARKING, IN ACCORDANCE WITH DETAIL E, SHEET 14.
8. AFTER APPLICATION OF P–608 SEAL COAT AND FIRST COAT OF PAVEMENT MARKINGS, RE–INSTALL TIE–DOWN CABLES AND CHAINS USING NEW HARDWARE. REFER TO DETAIL G, SHEET 14.

NOTE: SEE SHEET 13 FOR PAVEMENT MARKING LAYOUT – LINE, CURVE, & POINT TABLES.

LEGEND (SHEETS 9–12):

- AREA OF P–608 SURFACE TREATMENT
- PAVEMENT MARKING
- TIE–DOWN CHAIN
- TIE–DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA
- 1–1 PARKING STALL DESIGNATION

SCALE BAR
0 15 30 60
1 inch = 30 ft.

UNDERGROUND SERVICE ALERT
DIAL 811
TWO WORKING DAYS BEFORE YOU DIG

IMPROVEMENT AND MARKING PLAN

STA. 1+00 TO STA. 7+50

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6-30-25 CIVIL STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22–55
DATE 8/10/2024
SHEET 9 OF 14

PLOT DATE=8/11/2025

⬡ IMPROVEMENT AND MARKING NOTES (SHEETS 9–12):

1. APPLY P–608 SEAL COAT.
2. APPLY TAXIWAY CENTERLINE IN ACCORDANCE WITH DETAIL B, SHEET 14.
3. APPLY NON–MOVEMENT AREA MARKING IN ACCORDANCE IN ACCORDANCE WITH DETAIL F, SHEET 14. NOTE: THIS EFFORT IS WITHIN THE TAXIWAY ALPHA SAFETY AREA.
4. APPLY PARKING STALL MARKING (SMALL AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
5. APPLY PARKING STALL MARKING (LARGE AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
6. APPLY RESTRICTED AREA MARKING IN ACCORDANCE WITH DETAIL D, SHEET 14.
7. APPLY HELICOPTER PARKING AREA MARKING, IN ACCORDANCE WITH DETAIL E, SHEET 14.
8. AFTER APPLICATION OF P–608 SEAL COAT AND FIRST COAT OF PAVEMENT MARKINGS, RE–INSTALL TIE–DOWN CABLES AND CHAINS USING NEW HARDWARE. REFER TO DETAIL G, SHEET 14.

NOTE: SEE SHEET 13 FOR PAVEMENT MARKING LAYOUT – LINE, CURVE, & POINT TABLES.

LEGEND (SHEETS 9–12):

- AREA OF P–608 SURFACE TREATMENT
- PAVEMENT MARKING
- TIE–DOWN CHAIN
- TIE–DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA
- 1–1 — PARKING STALL DESIGNATION

MATCH LINE STA. 7+50

MATCH LINE – STA. 15+50

LIMITS OF P–608

EXISTING HANGAR TYP.

EXISTING HANGARS TYP.

HANGAR ROW D

HANGAR ROW C

HANGAR ROW B

HANGAR ROW A

TAXIWAY A

TOFA

LIMITS OF P–608

8+00 9+00 10+00 11+00 12+00 13+00 14+00 15+00

SCALE BAR

0 15 30 60

1 inch = 30 ft.

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

IMPROVEMENT AND MARKING PLAN

STA. 7+50 TO STA. 15+50

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6–30–25 CIVIL STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22–55
DATE 8/10/2024
SHEET 10 OF 14

PLOT DATE:4/1/2025


⬡ *IMPROVEMENT AND MARKING NOTES (SHEETS 9–12):*

1. APPLY P–608 SEAL COAT.
2. APPLY TAXIWAY CENTERLINE IN ACCORDANCE WITH DETAIL B, SHEET 14.
3. APPLY NON–MOVEMENT AREA MARKING IN ACCORDANCE IN ACCORDANCE WITH DETAIL F, SHEET 14. NOTE: THIS EFFORT IS WITHIN THE TAXIWAY ALPHA SAFETY AREA.
4. APPLY PARKING STALL MARKING (SMALL AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
5. APPLY PARKING STALL MARKING (LARGE AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
6. APPLY RESTRICTED AREA MARKING IN ACCORDANCE WITH DETAIL D, SHEET 14.
7. APPLY HELICOPTER PARKING AREA MARKING, IN ACCORDANCE WITH DETAIL E, SHEET 14.
8. AFTER APPLICATION OF P–608 SEAL COAT AND FIRST COAT OF PAVEMENT MARKINGS, RE–INSTALL TIE–DOWN CABLES AND CHAINS USING NEW HARDWARE. REFER TO DETAIL G, SHEET 14.

NOTE: SEE SHEET 13 FOR PAVEMENT MARKING LAYOUT – LINE, CURVE, & POINT TABLES.

LEGEND (SHEETS 9–12):

- AREA OF P–608 SURFACE TREATMENT
- PAVEMENT MARKING
- TIE–DOWN CHAIN
- TIE–DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA
- 1–1 — PARKING STALL DESIGNATION

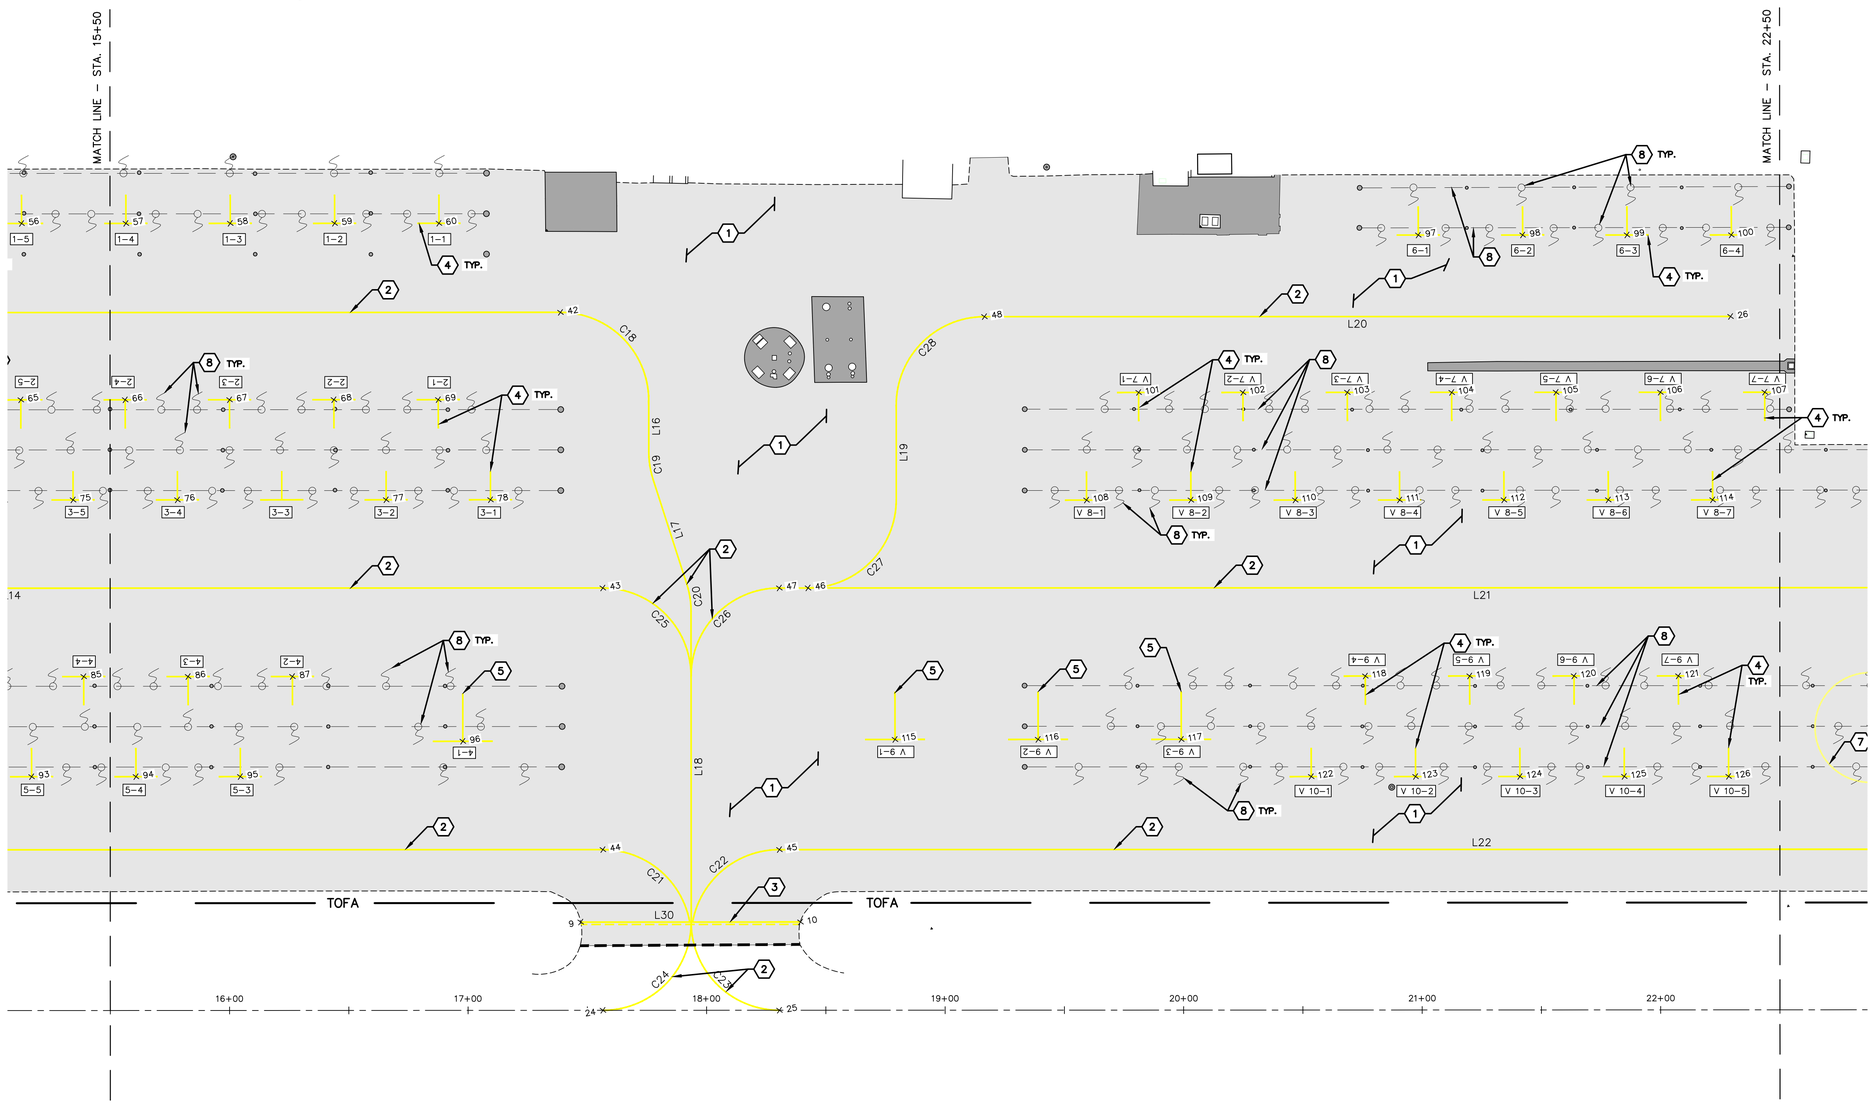

SCALE BAR

0 15 30 60

1 inch = 30 ft.

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

IMPROVEMENT AND MARKING PLAN

STA. 15+50 TO STA. 22+50

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER
JOHN A. SMITH
No. 46852
EXP. 6-30-25
CIVIL
STATE OF CALIFORNIA

DESIGN	JTH
DRAWN	JTH
CHECKED	JTH
DWG.NO.	22–55
DATE	8/10/2024
SHEET	11 OF 14

PLOT DATE: 8/11/2025


⬡ IMPROVEMENT AND MARKING NOTES (SHEETS 9–12):

1. APPLY P–608 SEAL COAT.
2. APPLY TAXIWAY CENTERLINE IN ACCORDANCE WITH DETAIL B, SHEET 14.
3. APPLY NON–MOVEMENT AREA MARKING IN ACCORDANCE IN ACCORDANCE WITH DETAIL F, SHEET 14. NOTE: THIS EFFORT IS WITHIN THE TAXIWAY ALPHA SAFETY AREA.
4. APPLY PARKING STALL MARKING (SMALL AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
5. APPLY PARKING STALL MARKING (LARGE AIRCRAFT) IN ACCORDANCE WITH DETAIL C, SHEET 14.
6. APPLY RESTRICTED AREA MARKING IN ACCORDANCE WITH DETAIL D, SHEET 14.
7. APPLY HELICOPTER PARKING AREA MARKING, IN ACCORDANCE WITH DETAIL E, SHEET 14.
8. AFTER APPLICATION OF P–608 SEAL COAT AND FIRST COAT OF PAVEMENT MARKINGS, RE–INSTALL TIE–DOWN CABLES AND CHAINS USING NEW HARDWARE. REFER TO DETAIL G, SHEET 14.

NOTE: SEE SHEET 13 FOR PAVEMENT MARKING LAYOUT – LINE, CURVE, & POINT TABLES.

LEGEND (SHEETS 9–12):

- AREA OF P–608 SURFACE TREATMENT
- PAVEMENT MARKING
- TIE–DOWN CHAIN
- TIE–DOWN ANCHOR
- TOFA — TAXIWAY OBJECT FREE AREA
- 1–1 PARKING STALL DESIGNATION

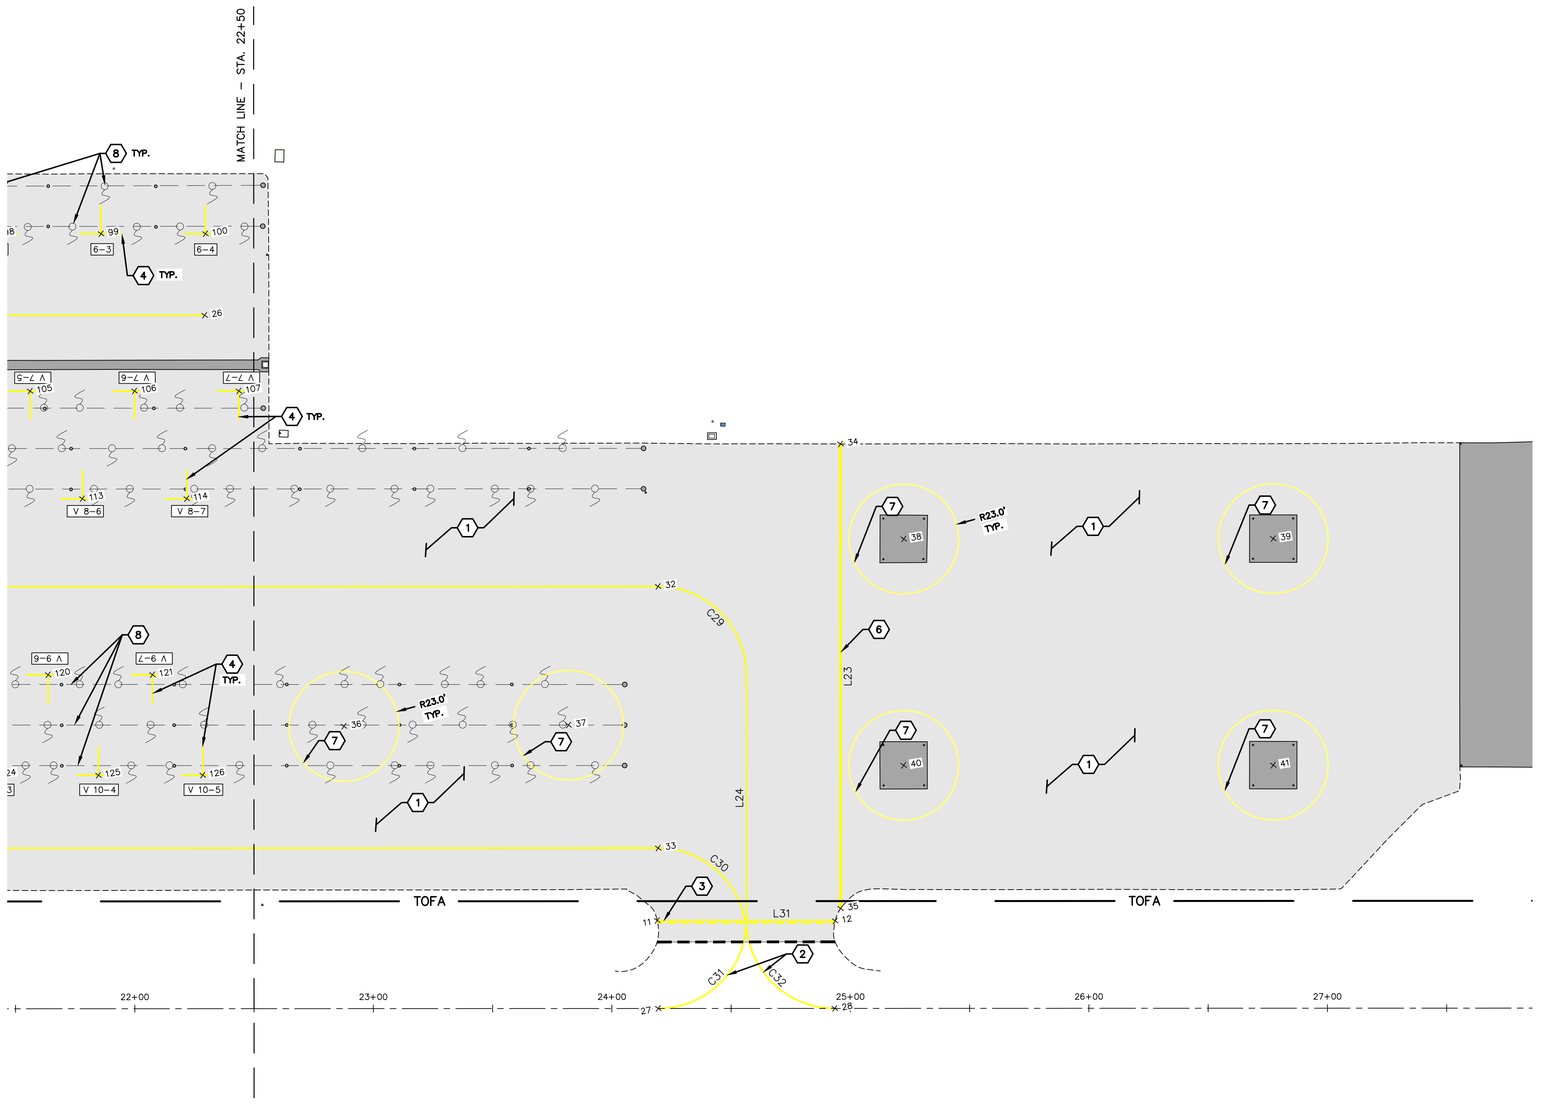

SCALE BAR

0 15 30 60

1 inch = 30 ft.

UNDERGROUND SERVICE ALERT

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

IMPROVEMENT AND MARKING PLAN

STA. 22+50 TO 27+50

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6–30–25 CIVIL STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22–55
DATE 8/10/2024
SHEET 12 OF 14

PLOT DATE: 8/13/2025

LINE TABLE

LINE #	LENGTH	DIRECTION
L1	142.85	S11° 11' 18"W
L2	72.02	N51° 37' 13"E
L3	23.89	N9° 18' 36"E
L4	94.28	S9° 24' 52"W
L5	82.59	N9° 24' 58"E
L6	58.48	N80° 34' 39"W
L7	64.60	S9° 24' 58"W
L8	47.93	S1° 31' 14"W
L9	58.06	S9° 24' 58"W
L10	98.10	N9° 24' 58"E
L11	46.33	N65° 17' 18"W
L12	151.25	N9° 24' 58"E
L13	629.40	N80° 34' 21"W
L14	495.35	N80° 34' 27"W
L15	477.66	S80° 34' 27"E
L16	21.58	S9° 24' 58"W
L17	46.35	S8° 22' 02"E
L18	130.36	S9° 24' 58"W
L19	39.73	S9° 24' 58"W
L20	312.80	N80° 34' 27"W
L21	588.92	N80° 34' 27"W
L22	588.92	S80° 34' 21"E
L23	194.81	S9° 24' 58"W
L24	103.11	N9° 24' 58"E
L25	51.03	N80° 34' 21"W
L26	31.29	S80° 38' 00"E
L27	44.30	S41° 55' 40"E
L28	40.58	S81° 26' 42"E
L29	88.02	S80° 34' 21"E
L30	92.14	S80° 34' 21"E
L31	74.64	S80° 34' 21"E

CURVE TABLE

CURVE #	LENGTH	RADIUS	DELTA	CHORD DIRECTION	CHORD LENGTH
C1	19.55	184.94	6.06	N44° 58' 15"E	19.54
C2	17.64	153.13	6.60	N48° 19' 15"E	17.63
C3	17.88	38.87	26.36	N31° 50' 35"E	17.73
C4	16.41	101.95	9.22	N14° 03' 08"E	16.40
C5	58.12	37.00	90.00	N35° 35' 02"W	52.33
C6	58.12	37.00	89.99	N35° 34' 50"W	52.32
C7	58.12	37.00	90.00	S54° 24' 58"W	52.33
C9	5.10	37.00	7.90	S5° 28' 06"W	5.09
C10	5.10	37.00	7.90	S5° 28' 06"W	5.09
C11	58.13	37.00	90.01	S54° 25' 18"W	52.33
C12	9.87	37.00	15.28	N72° 55' 50"W	9.84
C13	58.13	37.00	90.01	N54° 25' 18"E	52.33
C14	9.87	37.00	15.28	N72° 55' 50"W	9.84
C15	58.13	37.00	90.01	N54° 25' 18"E	52.33
C16	58.13	37.00	90.01	N54° 25' 16"E	52.33
C17	58.13	37.00	90.01	S54° 25' 16"W	52.33
C18	58.11	37.00	89.99	S35° 34' 44"E	52.32
C19	11.48	37.00	17.78	S0° 31' 28"W	11.44
C20	11.48	37.00	17.78	S0° 31' 28"W	11.44
C21	51.47	37.00	79.70	N40° 43' 29"W	47.42
C22	51.47	37.00	79.70	N59° 34' 46"E	47.42
C23	58.12	37.00	90.00	S35° 35' 02"E	52.33
C24	58.12	37.00	90.00	N54° 24' 58"E	52.33
C25	58.11	37.00	89.99	N35° 34' 44"W	52.32
C26	58.13	37.00	90.01	S54° 25' 16"W	52.33
C27	58.13	37.00	90.01	S54° 25' 16"W	52.33
C28	58.13	37.00	90.01	S54° 25' 16"W	52.33
C29	58.11	37.00	89.99	N35° 34' 44"W	52.32
C30	51.47	37.00	79.70	S40° 43' 29"E	47.42
C31	58.12	37.00	90.00	N54° 24' 58"E	52.33
C32	58.12	37.00	90.00	S35° 35' 02"E	52.33

POINT TABLE

Point #	Northing	Easting	Description
1	2050069.78	5936016.92	MV AREA
2	2050064.69	5936047.79	MV AREA
3	2050068.27	5936184.44	MV AREA
4	2050035.31	5936214.04	MV AREA
5	2050042.50	5936454.15	MV AREA
6	2050036.46	5936494.27	MV AREA
7	2049931.02	5936732.16	MV AREA
8	2049916.60	5936819.00	MV AREA
9	2049792.14	5937534.76	MV AREA
10	2049777.05	5937625.66	MV AREA
11	2049682.10	5938197.50	MV AREA
12	2049669.72	5938271.06	MV AREA
13	2050202.50	5936058.93	CL
14	2050062.36	5936031.21	CL
15	2050048.54	5936198.15	CL
16	2050173.34	5936298.78	CL
17	2050076.48	5936480.34	CL
18	2049983.47	5936464.92	CL
19	2050102.91	5936669.14	CL
20	2049888.04	5936730.28	CL
21	2049875.94	5936803.29	CL
22	2050097.55	5936795.15	CL
23	2050076.06	5936925.72	CL
24	2049754.11	5937537.88	CL
25	2049742.01	5937610.88	CL
26	2049963.58	5938051.94	CL
27	2049645.66	5938191.87	CL
28	2049633.55	5938264.87	CL
29	2050123.96	5937097.10	CL
30	2050009.94	5937078.19	CL
31	2049923.69	5936928.01	CL
32	2049820.25	5938220.83	CL
33	2049712.01	5938202.88	CL
34	2049866.65	5938306.05	RSTR AREA
35	2049674.47	5938274.18	RSTR AREA
36	2049783.99	5938081.29	HELI
37	2049769.05	5938174.24	HELI
38	2049822.98	5938325.70	HELI
39	2049797.73	5938478.54	HELI
40	2049729.36	5938310.07	HELI
41	2049704.03	5938462.95	HELI
42	2050045.74	5937568.31	CL
43	2049928.82	5937566.86	CL
44	2049820.59	5937548.91	CL
45	2049808.47	5937621.91	CL
46	2049914.72	5937651.74	CL
47	2049916.70	5937639.86	CL
48	2050014.81	5937743.36	CL
49	2049969.30	5936743.76	CL
50	2049957.19	5936816.77	CL
51	2049944.30	5937029.80	CL
52	2050148.21	5937178.89	PARKING
53	2050141.05	5937222.05	PARKING
54	2050133.90	5937265.22	PARKING
55	2050126.74	5937308.38	PARKING
56	2050119.58	5937351.54	PARKING
57	2050112.42	5937394.70	PARKING
58	2050105.26	5937437.86	PARKING
59	2050098.11	5937481.02	PARKING
60	2050090.95	5937524.18	PARKING

POINT TABLE

Point #	Northing	Easting	Description
61	2050082.45	5937123.32	PARKING
62	2050075.29	5937166.48	PARKING
63	2050068.13	5937209.64	PARKING
64	2050060.98	5937252.80	PARKING
65	2050046.66	5937339.12	PARKING
66	2050039.50	5937382.28	PARKING
67	2050032.35	5937425.44	PARKING
68	2050025.19	5937468.60	PARKING
69	2050018.03	5937511.76	PARKING
70	2050037.47	5937138.04	PARKING
71	2050030.31	5937181.20	PARKING
72	2050023.15	5937224.36	PARKING
73	2050015.99	5937267.52	PARKING
74	2050008.84	5937310.68	PARKING
75	2050001.68	5937353.84	PARKING
76	2049994.52	5937397.00	PARKING
77	2049980.21	5937483.32	PARKING
78	2049973.05	5937526.48	PARKING
79	2049970.81	5937087.13	PARKING
80	2049963.65	5937130.29	PARKING
81	2049956.49	5937173.45	PARKING
82	2049949.33	5937216.61	PARKING
83	2049942.18	5937259.77	PARKING
84	2049935.02	5937302.93	PARKING
85	2049927.86	5937346.09	PARKING
86	2049920.70	5937389.25	PARKING
87	2049913.55	5937432.41	PARKING
88	2049925.83	5937101.85	PARKING
89	2049918.67	5937145.01	PARKING
90	2049911.51	5937188.17	PARKING
91	2049904.35	5937231.33	PARKING
92	2049897.20	5937274.49	PARKING
93	2049890.04	5937317.65	PARKING
94	2049882.88	5937360.81	PARKING
95	2049875.72	5937403.97	PARKING
96	2049875.04	5937498.42	PARKING
97	2050018.74	5937928.39	PARKING
98	2050011.58	5937971.55	PARKING
99	2050004.42	5938014.71	PARKING
100	2049997.26	5938057.87	PARKING
101	2049972.86	5937801.92	PARKING
102	2049965.70	5937845.08	PARKING
103	2049958.54	5937888.24	PARKING
104	2049951.32	5937931.39	PARKING
105	2049944.23	5937974.56	PARKING
106	2049937.07	5938017.72	PARKING
107	2049929.91	5938060.88	PARKING
108	2049931.92	5937772.95	PARKING
109	2049924.76	5937816.11	PARKING
110	2049917.60	5937859.27	PARKING
111	2049910.44	5937902.43	PARKING
112	2049903.29	5937945.59	PARKING
113	2049896.13	5937988.76	PARKING
114	2049888.97	5938031.92	PARKING
115	2049846.07	5937677.29	PARKING
116	2049836.25	5937736.48	PARKING
117	2049826.44	5937795.67	PARKING
118	2049839.97	5937876.16	PARKING
119	2049832.81	5937919.32	PARKING
120	2049825.66	5937962.48	PARKING

POINT TABLE

Point #	Northing	Easting	Description
121	2049818.50	5938005.64	PARKING
122	2049802.10	5937846.87	PARKING
123	2049794.94	5937890.03	PARKING
124	2049787.79	5937933.19	PARKING
125	2049780.63	5937976.35	PARKING
126	2049773.47	5938019.51	PARKING
127	2050053.82	5937295.96	PARKING

UNDERGROUND SERVICE ALERT

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

PAVEMENT MARKING LAYOUT

LINE - CURVE - POINT TABLES

REV.	DESCRIPTION	DATE	APP.
1	-	-	-

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON


REGISTERED PROFESSIONAL ENGINEER JOHN A. SMITH No. 46852 EXP. 6-30-25 CIVIL STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22-55
DATE 8/10/2024
SHEET 13 OF 14

PLOT DATE=8/13/2025


CRACKS LESS THAN 1/4"– NO ROUTING OR CRACK FILL

CRACKS BETWEEN 1/4" AND 3/4"– ROUTE AND CRACKFILL




ROUTE SECTION


CRACKS GREATER THAN 3/4"



CLEAN SECTION




FILL SECTION



FILL SECTION

A/14 CRACK REPAIR DETAIL

NTS



B/14 TAXIWAY CENTERLINE MARKING

SCALE: 1" = 5'




1. OUTLINE SHALL BE 6", BOTH SIDES, BLACK WITHOUT REFLECTIVE MEDIA.
2. STRIPE SHALL BE 1.5' WIDE, YELLOW, WITH REFLECTIVE MEDIA.
3. TEXT SHALL BE 12" HIGH, CENTERED, WHITE, WITH REFLECTIVE MEDIA. MESSAGE SHALL REPEAT EVERY 50 FEET.

D/14 RESTRICTED AREA MARKING DETAIL

SCALE: 1" = 2'


PARKING STALL DIMENSIONS

SIZE	A	B
SMALL	18'–0"	12'–0"
LARGE	25'–0"	20'–0"

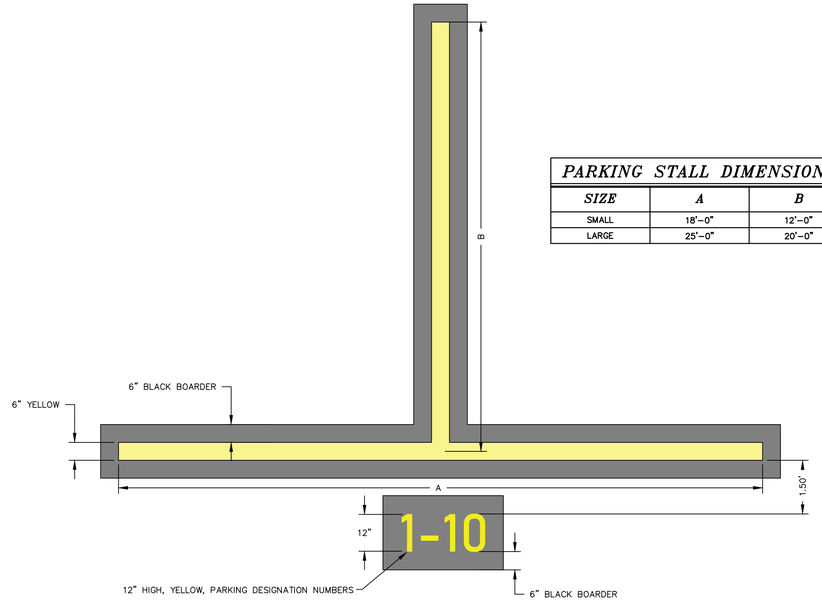


C/14 AIRCRAFT PARKING STALL MARKING DETAIL

SCALE: 1" = 2'




E/14 HELICOPTER PARKING AREA MARKING DETAIL

SCALE: 1" = 5'

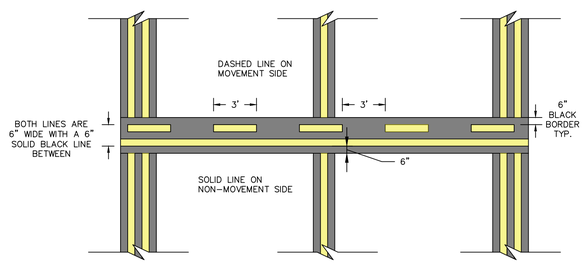

F/14 MOVEMENT AREA MARKING DETAIL

SCALE: 1" = 5'

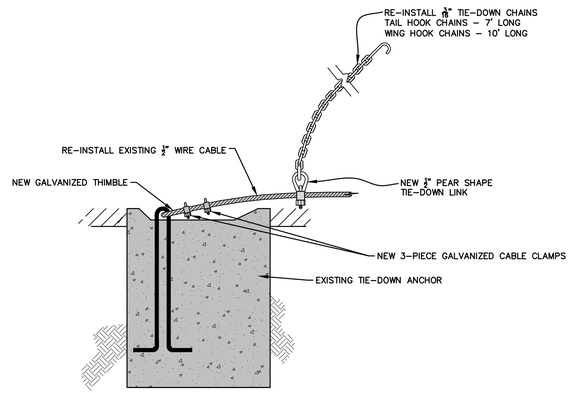

G/14 TIE–DOWN CABLE AND CHAIN RE–INSTALLATION DETAIL

UNDERGROUND SERVICE ALERT

811

DIAL 811

TWO WORKING DAYS BEFORE YOU DIG

DETAILS

CRACK REPAIR & PAVEMENT MARKINGS

REV.	DESCRIPTION	DATE	APP.
1	–	–	–

TARTAGLIA ENGINEERING

SANTA YNEZ AIRPORT

REHAB TIE-DOWN APRON

REGISTERED PROFESSIONAL ENGINEER — JOHN A. SMITH — No. 46852 — EXP. 6–30–25 — CIVIL — STATE OF CALIFORNIA

DESIGN JTH
DRAWN JTH
CHECKED JTH
DWG.NO. 22–55
DATE 8/10/2024
SHEET 14 OF 14

PLOT DATE:4/11/2025

GENERAL SERVICES – CAPITAL PROJECTS DIVISION

ADDENDUM NOTICE

May 19, 2025

ADDENDUM NO. 1

COUNTY PROJECT NO. 22011

REHABILITATE TIE-DOWN APRON
900 AIRPORT ROAD, SANTA YNEZ, CA.

Prepared By: Jason Hargreaves Date: May 19, 2025

Reviewed By: Steven Manuel Date: May 19, 2025

To All Prospective Bidders:

Your attention is directed to the bid information on the attached page(s) that contain a summary of the modifications to the identified Bid Documents and the revised Plan and Specification sheets.

This Addendum does not alter the bid opening time and date for this project.

You must acknowledge this addendum on your Bid Form and attach it to your Bid.

This Addendum and all contents mentioned herein, are hereby made a part of the Contract Documents to the same extent as though they were originally included therein; all other conditions shall remain the same.

Bidders are hereby notified of the following:

GENERAL

1. Pre-Pid Job Walk Sign-In Sheet – The sign-in sheet is included as an attachment to this addendum.
2. The Pre-bid job walk is non-mandatory. Any reference to the job walk being mandatory should be disregarded.

CHANGES TO PLANS

3. Plan Sheet 1 – A signature has been added. The revised plan sheet is included is Included as an attachment to this Addendum.

CHANGES TO SPECIFICATIONS

4. Page 1 (Notice to Contractors) – Change the construction cost estimate from "$705,000.00" to now be "$550,000.00".
5. Page 1 (Notice to Contractors) – Change the title of the third paragraph from "Mandatory Job Walk" to now be "Non-Mandatory Job Walk".

CHANGES TO BID SCHEDULE

6. Page 13 (proposal) – Page 13 of the Specification booklet includes the Bid Schedule. Several modifications to the estimated quantities have changed. Page 13 has been revised and is included as an attachment to this Addendum: Summary of Bid Schedule Changes:
   Item 4; Remove Pavement Markings: Change of quantity from 1.0 SF to now be 8,000.0 SF.
   Item 5; Crack Seal: Change of quantity from 1.0 LF to now be 46,000.0 LF.
   Item 6; Emulsified Asphalt Seal Coat: Change of quantity from 1.0 SY to now be 72,500.0 SY.
   Item 7; Markings: 2-Coat with Reflective Media: Change of quantity from 1.0 SF to now be 14,600.0 SF.
   Item 8; Markings: 2-Coat w/o Reflective Media: Change of quantity from 1.0 SF to now be 5,100.0 SF.

ATTACHMENTS

- Pre-Bid Job Walk Sign-In Sheet
- Revised Plan Sheet 1
- Revised Page 13 of the Specification Book (Bid Schedule)

END OF ADDENDUM

SIGN-IN SHEET

Monday, May 19, 2025
900 Airport Road
Pre-Bid Conference/Job Walk
(Non-Mandatory)

No	Firm	Attendee	Phone	E-Mail
1	Tartaglia	Jason Hagreaves	805 556-5771	Jason@tartaglia-engineering.com
2	SBCO	Steven Manuel	805-266-4176	STMANUEL@COUNTYOFSB.ORG
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				


SANTA BARBARA COUNTY, CALIFORNIA

SANTA YNEZ VALLEY AIRPORT

CONSTRUCTION PLANS FOR

REHABILITATE TIE-DOWN APRON

COUNTY PROJECT: NO. 22011
FAA: AIP 3-06-0243-023-2023 (DESIGN)
FAA: AIP 3-06-0243-024-2025 (CONSTRUCTION)

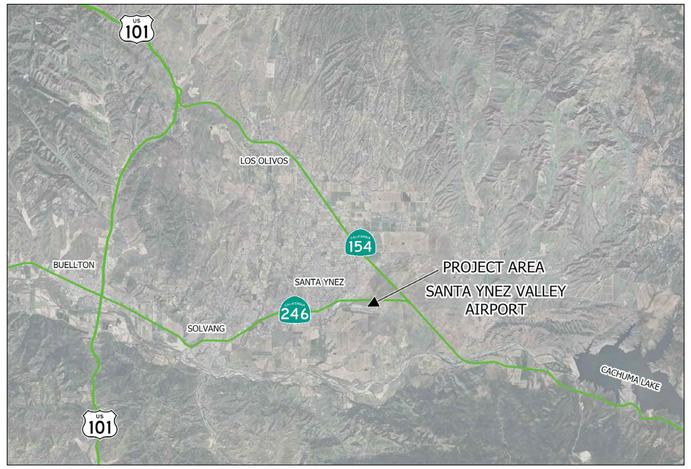

REGIONAL MAP
NO SCALE

APRIL, 2025

GENERAL PROJECT DESCRIPTION

1. REHABILITATE TIE-DOWN APRON AND HANGAR ROWS CONSISTING OF CRACK FILL & SEAL AND P-608 PAVEMENT SEAL COAT, FOLLOWED BY PAVEMENT MARKINGS.

GENERAL CONSTRUCTION ELEMENTS

1. AIRFIELD SAFETY AND SECURITY.
2. CRACK FILL & SEAL.
3. OBLITERATE EXISTING PAVEMENT MARKINGS.
4. REMOVE AND RE-INSTALL AIRCRAFT TIE-DOWN CABLES AND CHAINS.
5. APPLICATION OF P-608 PAVEMENT SEAL COAT.
6. APPLICATION OF OF NEW PAVEMENT MARKINGS.



LOCATION MAP
NO SCALE

SUBMITTED John A. Smith DATE 5-9-2025
JOHN A. SMITH RCE 46852
PROJECT ENGINEER

REGISTERED PROFESSIONAL ENGINEER
JOHN A. SMITH
No. 46852
EXP. 6-30-25
CIVIL
STATE OF CALIFORNIA

REV.	DESCRIPTION	DATE	APP.

UNDERGROUND SERVICE ALERT
811
DIAL 811
TWO WORKING DAYS BEFORE YOU DIG

TARTAGLIA ENGINEERING

1 OF 14
SHEET

22-55
DRAWING NO.

PLOT DATE: 4/11/2025

PROJECT BID SCHEDULE

ITEM NO.	SPEC SECTION	DESCRIPTION	UNIT	ESTIMATED QUANTITY	UNIT PRICE (Figures)	EXTENDED TOTAL (Figures)
1	C-105	Mobilization (8% Max)	LS	1.0	$	$
2	C-104T	Airport Safety and Security (5% Max)	LS	1.0	$	$
3	P-101	Uninstall & Re-Install Tie Down Cables and Chains	LS	1.0	$	$
4	P-101	Remove Pavement Markings	SF	8,000.0	$	$
5	P-101	Crack Seal	LF	46,000.0	$	$
6	P-608	Emulsified Asphalt Seal Coat	SY	72,500.0	$	$
7	P-620	Markings: 2-Coat with Reflective Media	SF	14,600.0	$	$
8	P-620	Markings: 2-Coat w/o Reflective Media	SF	5,100.0	$	$
TOTAL, BID SCHEDULE (Written in Figures):						$

Abbreviations to Bid Schedule(s):

LS = lump sum	TON = 2000 pounds	LF = lineal foot	EA = each unit
SF = square foot	CY = cubic yard	SY = square yard	T&M = time and materials
ACRE = 43,560 square feet		CF = cubic foot	GAL = 1 U.S. Gallon, liquid measure

Total Bid, Basis of Award:

Written in Words:_____

Written in Figures: $_____

In the event of discrepancy between words and figures, the words shall prevail.

In the event that the product of a unit price and an estimated quantity does not equal the extended amount quoted, the unit price shall govern and the correct product of the unit price and the estimated quantity shall be deemed to be the amount bid.

In order for a Bid to be responsive, Bidder must complete all blanks in the Bid Schedule. The failure to do so shall result in the Bid being rejected as non-responsive.

It is understood that Owner reserves the right to reject the proposal and that it shall remain open and not be withdrawn for a period of one hundred twenty (120) calendar days from the date prescribed for its opening.

Attached hereto and incorporated herein is the complete and entire list of subcontractors to be employed by the undersigned and in the performance of the Work.

GENERAL SERVICES – CAPITAL PROJECTS DIVISION

ADDENDUM NOTICE

May 28, 2025

ADDENDUM NO. 2

COUNTY PROJECT NO. 22011

REHABILITATE TIE-DOWN APRON
900 AIRPORT ROAD, SANTA YNEZ, CA.

Prepared By: Jason Hargreaves Date: May 28, 2025

Reviewed By: Diana Estorga Date: May 28, 2025

To All Prospective Bidders:

Your attention is directed to the bid information on the attached page(s) that contain a summary of the modifications to the identified Bid Documents and the revised Plan and Specification sheets.

The bid opening date has been revised to now be Monday, June 2nd, 2025, at 3:00 PM

You must acknowledge this addendum on your Bid Form and attach it to your Bid.

This Addendum and all contents mentioned herein, are hereby made a part of the Contract Documents to the same extent as though they were originally included therein; all other conditions shall remain the same.

Bidders are hereby notified of the following:

GENERAL

1. The latest federal wage rates are included as an attachment to this Addendum.

CHANGES TO SPECIFICATIONS

2. Page 117 (P-608) – Change the bolded sentence in the middle of the page that reads "The asphalt material….. shall contain no less than one percent (3%) polymer." to now be "The asphalt material….. shall contain no less than three and a half percent (3.5%) polymer."
3. Page 119 (P-608) – In the application rate table, change the rate of emulsion from "0.20-0.22" to now be "0.17-0.22."
4. At all locations in the specification booklet that reference the bid opening date, change the bid opening date to now by 3:00 pm Monday June 2, 2025.

CHANGES TO BID SCHEDULE

5. Page 13 (proposal) – The following changes were made to the bid schedule quantities:
   Item 7; Markings: 2-Coat with Reflective Media: Change of quantity from 14,600.0 SF to now be 5,100.0 SF.
   Item 8; Markings: 2-Coat w/o Reflective Media: Change of quantity from 5,100.0 SF to now be 14,600.0 SF.
   Contractors shall use the revised bid schedule with their bids.

ATTACHMENTS

- Revised Bid Schedule: Page 13 of the Specification Book
- Revised Pages: Cover Page, Page 1, 2, 12, 16, 21, 117, and 119 (8 pages)
- Federal Wage Rates (24 pages)

END OF ADDENDUM

PROJECT BID SCHEDULE

ITEM NO.	SPEC SECTION	DESCRIPTION	UNIT	ESTIMATED QUANTITY	UNIT PRICE (Figures)	EXTENDED TOTAL (Figures)
1	C-105	Mobilization (8% Max)	LS	1.0	$	$
2	C-104T	Airport Safety and Security (5% Max)	LS	1.0	$	$
3	P-101	Uninstall & Re-Install Tie Down Cables and Chains	LS	1.0	$	$
4	P-101	Remove Pavement Markings	SF	8,000.0	$	$
5	P-101	Crack Seal	LF	46,000.0	$	$
6	P-608	Emulsified Asphalt Seal Coat	SY	72,500.0	$	$
7	P-620	Markings: 2-Coat with Reflective Media	SF	5,100.0	$	$
8	P-620	Markings: 2-Coat w/o Reflective Media	SF	14,600.0	$	$
TOTAL, BID SCHEDULE (Written in Figures):						$

Abbreviations to Bid Schedule(s):

LS = lump sum	TON = 2000 pounds	LF = lineal foot	EA = each unit
SF = square foot	CY = cubic yard	SY = square yard	T&M = time and materials
ACRE = 43,560 square feet		CF = cubic foot	GAL = 1 U.S. Gallon, liquid measure

Total Bid, Basis of Award:

Written in Words:_____

Written in Figures: $_____

In the event of discrepancy between words and figures, the words shall prevail.

In the event that the product of a unit price and an estimated quantity does not equal the extended amount quoted, the unit price shall govern and the correct product of the unit price and the estimated quantity shall be deemed to be the amount bid.

In order for a Bid to be responsive, Bidder must complete all blanks in the Bid Schedule. The failure to do so shall result in the Bid being rejected as non-responsive.

It is understood that Owner reserves the right to reject the proposal and that it shall remain open and not be withdrawn for a period of one hundred twenty (120) calendar days from the date prescribed for its opening.

Attached hereto and incorporated herein is the complete and entire list of subcontractors to be employed by the undersigned and in the performance of the Work.

ADDENDUM 2

County of Santa Barbara

Rehabilitate Tie-Down Apron

Santa Ynez Airport

900 Airport Road, Santa Ynez, California

AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

JOB WALK:
Monday, May 19, 2025 at 11:00 A.M.
900 Airport Road, Santa Ynez, C.A.

BID OPENING DATE:
3:00 P.M., ~~Friday, May 30, 2025~~
Monday, June 2, 2025

BID OPENING LOCATION:
Bids to be Submitted Electronically

NOTICE TO BIDDERS

Notice is hereby given that the General Services Department, County of Santa Barbara will receive bids for:

COUNTY OF SANTA BARBARA,

Rehabilitate Tie-Down Apron

Santa Ynez Airport

900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

JOB WALK:
Monday, May 19, 2025 at 11:00 A.M.
900 Airport Road, Santa Ynez, C.A.

BID DUE DATE:
3:00 P.M., ~~Friday, May 30, 2025~~ Monday, June 2, 2025

CONSTRUCTION COST ESTIMATE: ~~$705,000.00~~ Dollars
$ 550,000.00

PROJECT LOCATION:
Santa Ynez Airport, 900 Airport Road, Santa Ynez, Santa Barbara County, California

NON-MANDATORY
~~MANDATORY~~ JOB WALK:
There will be a job walk on Monday, May 19, 2025 at 11:00 A.M. Meet outside the Airport Administration office, 900 Airport Road, Santa Ynez, California**.**

PROJECT DESCRIPTION:
The project focuses on rehabilitating the tie-down apron including crack repair and a surface treatment with the following work elements:

- Airfield safety and security.
- Clearing, grubbing, and removals.
- Temporary removal of tie down cables, chains, and fasteners.
- Pavement cleaning.
- Crack fill and seal.
- Application of an emulsified asphalt seal coat.
- Pavement markings.
- Reinstallation of aircraft tie down cables, chains, and fasteners

BIDDERS QUESTIONS:
All questions MUST be submitted electronically through the project Public Purchase Portal (www.publicpurchase.com) on or before 3:00 pm, five (5) business days prior to the day of the bid opening. Any changes or additional information needed for bidding will be provided in an Addendum posted on the Public Purchase site. Contractors shall be responsible for addendums

BID SUBMITTAL INSTRUCTIONS: Each bid shall be in accordance with the plans and specifications approved by the General Services Department. The bid MUST be submitted electronically through the Public Purchase website (www.publicpurchase.com) on or before **3:00 P.M., ~~Friday, May 30, 2025~~** Monday, June 2, 2025

SUBSTITUTION OF SECURITIES: Pursuant to Section 22300 of the Public Contract Code and the project specifications, the CONTRACTOR may substitute securities or request that the County make payment of retentions to an escrow agent for any money held by the COUNTY to ensure contract performance.

REGISTRATION: No contractor or subcontractor may be listed on a bid proposal for a public works project (submitted on or after March 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5 [with limited exceptions from this requirement for bid purposes only under Labor Code § 1771.1(a)]; no contractor or subcontractor may be awarded a contract for public work on a public works project (awarded on or after April 1, 2015) unless registered with the Department of Industrial Relations pursuant to Labor Code § 1725.5; and this project is subject to compliance monitoring and enforcement by the Department of Industrial Relations.

QUALIFYING CONTRACTOR OR SUBCONTRACTOR: Pursuant to the provisions of Section 4104 of the California Public Contracting Code a contractor or subcontractor shall not be qualified to bid on, be listed in a bid proposal or engage in the performance of any contract for public work, as defined in Section 4104, unless currently registered with the Department of Industrial Relations and qualified to perform public work pursuant to Section 1725.5 California Labor Code.

WITHDRAWAL OF BIDS:
The COUNTY reserves the right to reject any and or all bids or waive any informality in a bid. No bidder may withdraw his bid for a period of one hundred twenty (120) days after the date set for the opening thereof.

BID SELECTION:
The COUNTY reserves the right to select any one or any combination of bids, whichever is in the best interest of the COUNTY.

CONSTRUCTION TIME:
The successful CONTRACTOR (after receiving the Notice to Proceed) shall have **50 Working days** to complete all work called for under the Contract Documents.

LIQUIDATED DAMAGES:
The liquidated damages will be **$500.00 Dollars** per calendar day for project delays that are determined to be attributable to the CONTRACTOR.

BID BOND:
Each bid must be accompanied by a Certified Check, a Cashier's Check or a Bid Bond, as here and after provided in the amount of Ten Percent (10%) of the total of the bid, made payable to the County of Santa Barbara, as a guarantee that the bidder, if awarded the contract, will enter into a Contract for the performance thereof, satisfactory to said County's Board of Supervisors. Surety shall be listed in the Insurance Organizations Authorized By The Insurance Commissioner To Transact Business Of Insurance In The State Of California During 1994 (including changes effective January 1, 1995) published by the Department of Insurance, State of California, or successor publication. Personal and Corporate guarantees will not be acceptable.

PROPOSAL

Pursuant to and in compliance with your Notice to Bidders and the Contract Documents relating to the construction of:

County of Santa Barbara

Rehabilitate Tie-Down Apron

900 Airport Road, Santa Ynez, California
County Project No. 22011-AIP XX
Bid Date 3:00 pm, ~~**Friday, May 30, 2025**~~
Monday, June 2, 2025

including Addendum No(s). ___, ___, ___, ___, ___, ___, ___, the undersigned bidder, having become thoroughly familiar with the terms and conditions of the Contract Documents and with local conditions affecting the performance and the costs of the Work at the place where the Work is to be done, hereby proposes and agrees to fully perform the Work within the time stated in and in strict accordance with the Contract Documents (including the furnishing of any and all labor, materials, tools, expendable equipment and utility and transportation services necessary to fully perform the work and complete it in a workmanlike manner) for the total sum of:

Written if Figures: $_____

Written in Words: _____

Bid Schedule follows on the next page. Bidding Contractors to complete all blanks on the Bid Schedule:

Name of Bidder: _____

California Contractors License Number (Class): _____

DESIGNATION OF SUBCONTRACTORS

The bidder agrees if this proposal is accepted, that he will contract with the County of Santa Barbara to do all work and furnish all labor, materials, machinery, tools and apparatus necessary to completely perform said Contracts in the manner and time prescribed by said Contract.

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011
Bid Date 3:00 pm, ~~**Friday, May 30, 2025**~~
Monday, June 2, 2025

In compliance with the provisions of Section 4100-4107 of the Public Contract Code of the State of California, and any amendments, thereof, the undersigned bidder has set forth below the name and location of the place of business of each subcontractor who will perform work or labor or render service to the undersigned in or about the construction of the work to be performed. That portion of the work which will be done by each subcontractor for each subcontract in excess of one-half of one percent of the undersigned's total aggregate bid shall be listed..

SUBCONTRACTORS LIST		
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )

BIDDER'S BOND

KNOW ALL MEN BY THESE PRESENTS:

That we, _____ as Principal, and _____ as Surety (hereinafter referred to as Surety), are held firmly bound unto the County of Santa Barbara, State of California (hereinafter called "Owner") in the penal sum of Ten Percent (10%) of the total aggregate amount of the bid of the Principal above named, submitted by said Principal to Owner for the work described below, for the payment of which sum in lawful money of the United States, well and truly to be made, we bind ourselves, our heirs, executors, administrators, and successors, jointly and severally, firmly by these presents. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications. In no case shall the liability of the Surety hereunder exceed the sum of _____ DOLLARS ($_____). The condition of this obligation is such that a bid to Owner for certain construction specifically described as follows:

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
County Project No. 22011-AIG XX

for which bids are to be opened on **3:00 pm, ~~Friday, May 30, 2025~~,** Monday, June 2, 2025 has been submitted by Principal to Owner.

NOW, THEREFORE, if the aforesaid Principal shall not withdraw said bid within the period therein after the opening of the same, or, if no period be specified within one hundred twenty (120) days after said opening and shall within the period specified therefore, or, if no period be specified, within eight (8) days after the prescribed forms are presented to him for signature, enter into a written Contract with Owner, in the prescribed form, in accordance with the bid as accepted, and file the two Bonds with Owner, one to guarantee faithful performance and the other to guarantee payment for labor and materials, as required by law, then this obligation shall be null and void; otherwise, it shall remain in full force, virtue and affect.

Said Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration or addition to the terms of said Contract or to the work to be performed thereunder or the Specifications accompanying the same shall in any manner affects its obligations on this bond, and it does hereby waive notice of any change, extension, alteration, or addition.

It is hereby agreed that any progress payment made after the scheduled completion date will not constitute a waiver of any liquidated damages heretofore agreed upon.

In the event suit is brought upon said Bond by Owner and judgment is recovered, the Surety shall pay all costs incurred by Owner in such suit, including a reasonable attorney's fee to be fixed by the Court.

Death, Bankruptcy, Receivership, Going Out of Business for any reason, or incompetence of the

608-2.2 Asphalt Emulsion. The asphalt emulsion shall meet the properties in the following table:

Concentrated Asphalt Emulsion Properties

Properties	Specification	Limits
Viscosity, Saybolt Furol at 77°F (25°C)	ASTM D7496	20 – 100 seconds
Residue by Distillation or Evaporation	ASTM D6997 or ASTM D6934	57% minimum
Sieve Test	ASTM D6933	0.1% maximum
24-hour Stability	ASTM D6930	1% maximum
5-day Settlement Test	ASTM D6930	5.0% maximum
Particle Charge [1]	ASTM D7402	Positive 6.5 maximum pH

[1] pH may be used in lieu of the particle charge test which is sometimes inconclusive in slow setting, asphalt emulsions.

The asphalt material base residue shall contain not less than 20% gilsonite, or uintaite and shall not contain any tall oil pitch or coal tar material and shall contain no less than three and a half percent (3.5%) polymer.

Tests on Residue from Distillation or Evaporation

Properties	Specification	Limits
Viscosity at 275°F (135°C)	ASTM D4402	1750 cts maximum
Solubility in 1, 1, 1 trichloroethylene	ASTM D2042	97.5% minimum
Penetration	ASTM D5	50 dmm maximum
Asphaltenes	ASTM D2007	15% minimum
Saturates	ASTM D2007	15% maximum
Polar Compounds	ASTM D2007	25% minimum
Aromatics	ASTM D2007	15% minimum

The asphalt emulsion, when diluted in the volumetric proportion of two parts concentrated asphalt material to one part hot water shall have the following properties:

Two-to-One Dilution Emulsion Properties

Properties	Specification	Limits
In Ready-to-Apply Form, two parts concentrate to one part water, by volume		
Viscosity, Saybolt Furol at 77°F (25°C)	ASTM D7496	5 – 50 seconds
Residue by Distillation or Evaporation	ASTM D6997 or ASTM D6934	38% minimum
Pumping Stability		Pass

test shall indicate no apparent adverse effect with time relative to friction values and existing pavement surface.

Seal coat material submittal without required friction performance will not be approved. Friction tests performed on this project cannot be used as a substitute of this requirement.

COMPOSITION AND APPLICATION RATE

608-3.1 Application Rate. The approximate amounts of materials per square yard (square meter) for the asphalt surface treatment shall be as provided in the table for the treatment area(s) at the specified dilution rate(s) as noted on the plans. The actual application rates will vary within the range specified to suit field conditions and will be recommended by the manufacturer's representative and approved by the RPR from the test area/sections evaluation.

Application Rate

Dilution Rate	Quantity of Emulsion gal/yd^2	Quantity of Aggregate lb/yd^2
2:1	0.17-0.22	0.30-0.40

608-3.2 Control areas and control strips. Prior to full application, the control strip must be accepted by the RPR. A qualified manufacturer's representative shall be present in the field to assist the Contractor in applying control areas and/or control strips to determine the appropriate application rate of both emulsion and aggregate to be approved by the RPR.

a. For taxiway, taxilane and apron surfaces. Prior to full application, the Contractor shall place test areas at varying application rates as recommended by the Contractor's manufacturer's representative to determine appropriate application rate(s). The test areas will be located on representative section(s) of the pavement to receive the asphalt surface treatment designated by the RPR.

b. For runway and high-speed exit taxiway surfaces. N/A.

CONSTRUCTION METHODS

608-4.1 Worker safety. The Contractor shall obtain a Safety Data Sheet (SDS) for both the asphalt emulsion product and sand and require workmen to follow the manufacturer's recommended safety precautions.

608-4.2 Weather limitations. The asphalt emulsion shall be applied only when the existing pavement surface is dry and when the weather is not foggy, rainy, or when the wind velocity will prevent the uniform application of the material. No material shall be applied in strong winds that interfere with the uniform application of the material(s), or when dust or sand is blowing or when rain is anticipated within eight (8) hours of application completion. The atmospheric temperature and the pavement surface temperature shall both be at, or above 60°F (16°C) and rising. Seal coat shall not be applied when pavement temperatures are expected to exceed 130ºF within the subsequent 72 hours if traffic will be opened on pavement within those 72 hours. During application, account for wind drift. Cover existing buildings, structures, runway edge lights, taxiway edge lights, informational signs, retro-reflective marking and in-pavement duct markers as necessary to protect against overspray before applying the emulsion. Should emulsion get on any light or marker fixture, promptly clean the fixture. If cleaning is

"General Decision Number: CA20250014 03/28/2025

Superseded General Decision Number: CA20240014

State: California

Construction Types: Building, Heavy (Heavy and Dredging) and Highway

County: Santa Barbara County in California.

BUILDING, DREDGING (does not include hopper dredge work), HEAVY (does not include water well drilling), AND HIGHWAY CONSTRUCTION PROJECTS

Note: Contracts subject to the Davis-Bacon Act are generally required to pay at least the applicable minimum wage rate required under Executive Order 14026 or Executive Order 13658. Please note that these Executive Orders apply to covered contracts entered into by the federal government that are subject to the Davis-Bacon Act itself, but do not apply to contracts subject only to the Davis-Bacon Related Acts, including those set forth at 29 CFR 5.1(a)(1).

If the contract is entered into on or after January 30, 2022, or the contract is renewed or extended (e.g., an option is exercised) on or after January 30, 2022:	. Executive Order 14026 generally applies to the contract. . The contractor must pay all covered workers at least $17.75 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on the contract in 2025.
If the contract was awarded on or between January 1, 2015 and January 29, 2022, and the contract is not renewed or extended on or after January 30, 2022:	. Executive Order 13658 generally applies to the contract. . The contractor must pay all covered workers at least $13.30 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on that contract in 2025.

The applicable Executive Order minimum wage rate will be adjusted annually. If this contract is covered by one of the Executive Orders and a classification considered necessary for performance of work on the contract does not appear on this wage determination, the contractor must still submit a conformance request.

Additional information on contractor requirements and worker protections under the Executive Orders is available at http://www.dol.gov/whd/govcontracts.

Modification Number	Publication Date
0	01/03/2025
1	01/10/2025
2	01/24/2025
3	02/07/2025
4	02/21/2025
5	02/28/2025
6	03/28/2025

ASBE0005-002 09/01/2023

	Rates	Fringes
Asbestos Workers/Insulator (Includes the application of all insulating materials, protective coverings, coatings, and finishes to all types of mechanical systems)	$ 49.58	25.27
Fire Stop Technician (Application of Firestopping Materials for wall openings and penetrations in walls, floors, ceilings and curtain walls)	$ 36.97	20.36

ASBE0005-004 07/04/2022

	Rates	Fringes
Asbestos Removal worker/hazardous material handler (Includes preparation, wetting, stripping, removal, scrapping, vacuuming, bagging and disposing of all insulation materials from mechanical systems, whether they contain asbestos or not)	$ 23.52	13.37

BOIL0092-003 01/01/2024

	Rates	Fringes
BOILERMAKER	$ 51.98	42.11

BRCA0004-003 05/01/2024

	Rates	Fringes
Bricklayer; Marble Setter	$ 45.53	20.29

BRCA0018-008 06/01/2024

	Rates	Fringes
MARBLE FINISHER	$ 43.38	15.36
TILE FINISHER	$ 37.96	13.77

* BRCA0018-010 09/01/2024

	Rates	Fringes
TERRAZZO FINISHER	$ 42.11	14.67

TERRAZZO WORKER/SETTER.....$ 49.62 15.26

BRCA0018-011 06/01/2023

	Rates	Fringes
TILE LAYER	$ 48.29	19.18

CARP0213-001 01/01/2024

	Rates	Fringes
CARPENTER		
(1) Carpenter, Cabinet Installer, Insulation Installer, Hardwood Floor Worker and acoustical installer	$ 48.86	22.88
(2) Millwright	$ 49.36	22.88
(3) Piledrivermen/Derrick Bargeman, Bridge or Dock Carpenter, Heavy Framer, Rock Bargeman or Scowman, Rockslinger, Shingler (Commercial)	$ 48.99	22.88
(4) Pneumatic Nailer, Power Stapler	$ 51.85	16.28
(5) Sawfiler	$ 51.69	16.28
(6) Scaffold Builder	$ 40.77	22.38
(7) Table Power Saw Operator	$ 51.70	16.28

FOOTNOTE: Work of forming in the construction of open cut sewers or storm drains, on operations in which horizontal lagging is used in conjunction with steel H-Beams driven or placed in pre- drilled holes, for that portion of a lagged trench against which concrete is poured, namely, as a substitute for back forms (which work is performed by piledrivers): $0.13 per hour additional.

CARP0213-002 07/01/2021

	Rates	Fringes
Diver		
(1) Wet	$ 834.40	16.28
(2) Standby	$ 445.84	16.28
(3) Tender	$ 437.84	16.28
(4) Assistant Tender	$ 413.84	16.28

Amounts in ""Rates' column are per day

CARP0213-004 01/01/2024

	Rates	Fringes
Drywall		
DRYWALL INSTALLER/LATHER	$ 48.86	22.88
STOCKER/SCRAPPER	$ 20.80	9.97

CARP0721-001 07/01/2021

	Rates	Fringes

Modular Furniture Installer.....$ 21.85 7.15

ELEC0413-001 01/01/2025

	Rates	Fringes
Electricians:.....	$ 52.15	3%+23.23

CABLE SPLICERS: $2.00 additional per hour.

ALL WORK AT VANDENBERG AFB: $3.75 additional per hour.

FOOTNOTE: Work from trusses, swinging scaffolds, open ladders, scaffolds, bosun's chairs, stacks, or the maintenance of towers or open platforms where the worker is subject to a direct fall or where the worker has to work from a ladder or other support from a platform within 5 ft. of any direct fall a distance of 50 ft. from the ground floor or supporting structure: double the regular straight-time rate of pay. Safety nets, if used, will not invalidate this.

ELEC0413-003 12/31/2024

COMMUNICATIONS AND SYSTEMS WORK

	Rates	Fringes
Communications System Installer.....	$ 48.13	3%+16.05

SCOPE OF WORK:
Installation, testing, service and maintenance of systems utilizing the transmission and/or transference of voice, sound, vision and digital for commercial, educational, security and entertainment purposes for the following: TV monitoring and surveillance, background-foreground music, intercom and telephone interconnect, inventory control systems, microwave transmission, multi-media, multiplex, nurse call systems, radio page, school intercom and sound, burglar alarms, fire alarm (see last paragraph below) and low voltage master clock systems in commercial buildings. Communication Systems that transmit or receive information and/or control systems that are intrinsic to the above listed systems; inclusion or exclusion of terminations and testings of conductors determined by their function; excluding all other data systems or multiple systems which include control function or power supply; excluding installation of raceway systems, conduit systems, line voltage work, and energy management systems. Does not cover work performed at China Lake Naval Ordnance Test Station. Fire alarm work shall be performed at the current inside wireman total cost package.

ELEC1245-001 01/01/2025

	Rates	Fringes
LINE CONSTRUCTION		
(1) Lineman; Cable splicer..	$ 70.16	24.71
(2) Equipment specialist (operates crawler tractors, commercial motor		

vehicles, backhoes, trenchers, cranes (50 tons and below), overhead & underground distribution line equipment)	$ 53.30	22.26
(3) Groundman	$ 40.76	21.76
(4) Powderman	$ 51.87	18.79

HOLIDAYS: New Year's Day, M.L. King Day, Memorial Day, Independence Day, Labor Day, Veterans Day, Thanksgiving Day and day after Thanksgiving, Christmas Day

---

ELEV0018-001 01/01/2025

	Rates	Fringes
ELEVATOR MECHANIC	$ 69.43	38.435+a+b

FOOTNOTE:

a. PAID VACATION: Employer contributes 8% of regular hourly rate as vacation pay credit for employees with more than 5 years of service, and 6% for 6 months to 5 years of service.

b. PAID HOLIDAYS: New Year's Day, Memorial Day, Independence Day, Labor Day, Veterans' Day, Thanksgiving Day, Friday after Thanksgiving, and Christmas Day.

ENGI0012-004 08/01/2024

	Rates	Fringes
OPERATOR: Power Equipment (DREDGING)		
(1) Leverman	$ 64.10	38.75
(2) Dredge dozer	$ 58.13	38.75
(3) Deckmate	$ 58.02	38.75
(4) Winch operator (stern winch on dredge)	$ 57.47	38.75
(5) Fireman-Oiler, Deckhand, Bargeman, Leveehand	$ 56.93	38.75
(6) Barge Mate	$ 57.54	38.75

ENGI0012-024 07/01/2023

	Rates	Fringes
OPERATOR: Power Equipment (All Other Work)		
GROUP 1	$ 53.90	32.80
GROUP 2	$ 54.68	32.80
GROUP 3	$ 54.97	32.80
GROUP 4	$ 56.46	32.80
GROUP 6	$ 56.68	32.80
GROUP 8	$ 56.79	32.80
GROUP 10	$ 56.91	32.80
GROUP 12	$ 57.08	32.80
GROUP 13	$ 57.18	32.80
GROUP 14	$ 57.21	32.80
GROUP 15	$ 57.29	32.80
GROUP 16	$ 57.41	32.80
GROUP 17	$ 57.58	32.80
GROUP 18	$ 57.68	32.80

GROUP 19.....$ 57.79 32.80
GROUP 20.....$ 57.91 32.80
GROUP 21.....$ 58.08 32.80
GROUP 22.....$ 58.18 32.80
GROUP 23.....$ 58.29 32.80
GROUP 24.....$ 58.41 32.80
GROUP 25.....$ 58.58 32.80

OPERATOR: Power Equipment (Cranes, Piledriving & Hoisting)

GROUP 1.....$ 55.25 32.80
GROUP 2.....$ 56.03 32.80
GROUP 3.....$ 56.32 32.80
GROUP 4.....$ 56.46 32.80
GROUP 5.....$ 56.68 32.80
GROUP 6.....$ 56.79 32.80
GROUP 7.....$ 56.91 32.80
GROUP 8.....$ 57.08 32.80
GROUP 9.....$ 57.25 32.80
GROUP 10.....$ 58.25 32.80
GROUP 11.....$ 59.25 32.80
GROUP 12.....$ 60.25 32.80
GROUP 13.....$ 61.25 32.80

OPERATOR: Power Equipment (Tunnel Work)

GROUP 1.....$ 55.75 32.80
GROUP 2.....$ 56.53 32.80
GROUP 3.....$ 56.82 32.80
GROUP 4.....$ 56.96 32.80
GROUP 5.....$ 57.18 32.80
GROUP 6.....$ 57.29 32.80
GROUP 7.....$ 57.41 32.80

PREMIUM PAY:

$10.00 per hour shall be paid on all Power Equipment Operator work on the followng Military Bases: China Lake Naval Reserve, Vandenberg AFB, Point Arguello, Seely Naval Base, Fort Irwin, Nebo Annex Marine Base, Marine Corp Logistics Base Yermo, Edwards AFB, 29 Palms Marine Base and Camp Pendleton

Workers required to suit up and work in a hazardous material environment: $2.00 per hour additional. Combination mixer and compressor operator on gunite work shall be classified as a concrete mobile mixer operator.

SEE ZONE DEFINITIONS AFTER CLASSIFICATIONS

POWER EQUIPMENT OPERATORS CLASSIFICATIONS

GROUP 1: Bargeman; Brakeman; Compressor operator; Ditch Witch, with seat or similar type equipment; Elevator operator-inside; Engineer Oiler; Forklift operator (includes loed, lull or similar types under 5 tons; Generator operator; Generator, pump or compressor plant operator; Pump operator; Signalman; Switchman

GROUP 2: Asphalt-rubber plant operator (nurse tank operator);Coil Tubing Rig Operator, Concrete mixer operator-skip type; Conveyor operator; Fireman; Forklift operator (includes loed, lull or similar types over 5 tons; Hydrostatic pump operator; oiler crusher (asphalt or concrete plant); Petromat laydown machine; PJU side dum jack; Screening and conveyor machine operator (or similar types); Skiploader (wheel type up to 3/4 yd. without

attachment); Tar pot fireman; Temporary heating plant operator; Trenching machine oiler

GROUP 3: Asphalt-rubber blend operator; Bobcat or similar type (Skid steer); Equipment greaser (rack); Ford Ferguson (with dragtype attachments); Helicopter radioman (ground); Stationary pipe wrapping and cleaning machine operator

GROUP 4: Asphalt plant fireman; Backhoe operator (mini-max or similar type); Boring machine operator; Boxman or mixerman (asphalt or concrete); Chip spreading machine operator; Concrete cleaning decontamination machine operator; Concrete Pump Operator (small portable);Direct Push Operator (Geoprobe or similar types) Drilling machine operator, small auger types (Texoma super economatic or similar types - Hughes 100 or 200 or similar types - drilling depth of 30' maximum); Equipment greaser (grease truck); Guard rail post driver operator; Highline cableway signalman; Hydra-hammer-aero stomper; Micro Tunneling (above ground tunnel); Power concrete curing machine operator; Power concrete saw operator; Power-driven jumbo form setter operator; Power sweeper operator; Rock Wheel Saw/Trencher; Roller operator (compacting); Screed operator (asphalt or concrete); Trenching machine operator (up to 6 ft.); Vacuum or much truck

GROUP 6: Articulating material hauler; Asphalt plant engineer; Batch plant operator; Bit sharpener; Concrete joint machine operator (canal and similar type); Concrete planer operator; Dandy digger; Deck engine operator; Derrickman (oilfield type); Drilling machine operator, bucket or auger types (Calweld 100 bucket or similar types - Watson 1000 auger or similar types - Texoma 330, 500 or 600 auger or similar types - drilling depth of 45' maximum); Drilling machine operator; Hydrographic seeder machine operator (straw, pulp or seed), Jackson track maintainer, or similar type; Kalamazoo Switch tamper, or similar type; Machine tool operator; Maginnis internal full slab vibrator, Mechanical berm, curb or gutter(concrete or asphalt); Mechanical finisher operator (concrete, Clary-Johnson-Bidwell or similar); Micro tunnel system (below ground); Pavement breaker operator (truck mounted); Road oil mixing machine operator; Roller operator (asphalt or finish), rubber-tired earth moving equipment (single engine, up to and including 25 yds. struck); Self-propelled tar pipelining machine operator; Skiploader operator (crawler and wheel type, over 3/4 yd. and up to and including 1-1/2 yds.); Slip form pump operator (power driven hydraulic lifting device for concrete forms); Tractor operator-bulldozer, tamper-scraper (single engine, up to 100 h.p. flywheel and similar types, up to and including D-5 and similar types); Tugger hoist operator (1 drum); Ultra high pressure waterjet cutting tool system operator; Vacuum blasting machine operator

GROUP 8: Asphalt or concrete spreading operator (tamping or finishing); Asphalt paving machine operator (Barber Greene or similar type); Asphalt-rubber distribution operator; Backhoe operator (up to and including 3/4 yd.), small ford, Case or similar types; Cable Bundling Machine Operator (excluding handheld); Cable Trenching Machine Operator (Spider Plow or similar types) Cast-in-place pipe laying machine operator; Combination mixer and compressor operator (gunite work); Compactor operator (self-propelled);

Concrete mixer operator (paving); Crushing plant operator; Drill Doctor; Drilling machine operator, Bucket or auger types (Calweld 150 bucket or similar types - Watson 1500, 2000 2500 auger or similar types - Texoma 700, 800 auger or similar types - drilling depth of 60' maximum); Elevating grader operator; Grade checker; Gradall operator; Grouting machine operator; Heavy-duty repairman; Heavy equipment robotics operator; Kalamazoo balliste regulator or similar type; Kolman belt loader and similar type; Le Tourneau blob compactor or similar type; Loader operator (Athey, Euclid, Sierra and similar types); Mobark Chipper or similar; Ozzie padder or similar types; P.C. slot saw; Pneumatic concrete placing machine operator (Hackley-Presswell or similar type); Pumpcrete gun operator; RCM Cementing Unit Operator, Rail/Switch Grinder Operator (Harsco or similar types) Rock Drill or similar types; Rotary drill operator (excluding caisson type); Rubber-tired earth-moving equipment operator (single engine, caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds. up to and including 50 cu. yds. struck); Rubber-tired earth-moving equipment operator (multiple engine up to and including 25 yds. struck); Rubber-tired scraper operator (self-loading paddle wheel type-John Deere, 1040 and similar single unit); Self- propelled curb and gutter machine operator; Shuttle buggy; Skiploader operator (crawler and wheel type over 1-1/2 yds. up to and including 6-1/2 yds.); Soil remediation plant operator; Surface heaters and planer operator; Tractor compressor drill combination operator; Tractor operator (any type larger than D-5 - 100 flywheel h.p. and over, or similar-bulldozer, tamper, scraper and push tractor single engine); Tractor operator (boom attachments), Traveling pipe wrapping, cleaning and bendng machine operator; Trenching machine operator (over 6 ft. depth capacity, manufacturer's rating); trenching Machine with Road Miner attachment (over 6 ft depth capacity): Ultra high pressure waterjet cutting tool system mechanic; Water pull (compaction) operator

GROUP 10: Drilling machine operator, Bucket or auger types (Calweld 200 B bucket or similar types-Watson 3000 or 5000 auger or similar types-Texoma 900 auger or similar types-drilling depth of 105' maximum); Dual drum mixer, dynamic compactor LDC350 (or similar types); Monorail locomotive operator (diesel, gas or electric); Motor patrol-blade operator (single engine); Multiple engine tractor operator (Euclid and similar type-except Quad 9 cat.); Rubber-tired earth-moving equipment operator (single engine, over 50 yds. struck); Pneumatic pipe ramming tool and similar types; Prestressed wrapping machine operator; Rubber-tired earth-moving equipment operator (single engine, over 50 yds. struck); Rubber tired earth moving equipment operator (multiple engine, Euclid, caterpillar and similar over 25 yds. and up to 50 yds. struck), Tower crane repairman; Tractor loader operator (crawler and wheel type over 6-1/2 yds.); Woods mixer operator (and similar Pugmill equipment)

GROUP 12: Auto grader operator; Automatic slip form operator; Drilling machine operator, bucket or auger types (Calweld, auger 200 CA or similar types - Watson, auger 6000 or similar types - Hughes Super Duty, auger 200 or similar types - drilling depth of 175' maximum); Hoe ram or similar with compressor; Mass excavator operator less tha 750 cu. yards; Mechanical finishing machine operator; Mobile form

traveler operator; Motor patrol operator (multi-engine); Pipe mobile machine operator; Rubber-tired earth- moving equipment operator (multiple engine, Euclid, Caterpillar and similar type, over 50 cu. yds. struck); Rubber-tired self- loading scraper operator (paddle-wheel-auger type self-loading - two (2) or more units)

GROUP 13: Rubber-tired earth-moving equipment operator operating equipment with push-pull system (single engine, up to and including 25 yds. struck)

GROUP 14: Canal liner operator; Canal trimmer operator; Remote- control earth-moving equipment operator (operating a second piece of equipment: $1.00 per hour additional); Wheel excavator operator (over 750 cu. yds.)

GROUP 15: Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (single engine, Caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds. and up to and including 50 yds. struck); Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (multiple engine-up to and including 25 yds. struck)

GROUP 16: Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (single engine, over 50 yds. struck); Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (multiple engine, Euclid, Caterpillar and similar, over 25 yds. and up to 50 yds. struck)

GROUP 17: Rubber-tired earth-moving equipment operator, operating equipment with push-pull system (multiple engine, Euclid, Caterpillar and similar, over 50 cu. yds. struck); Tandem tractor operator (operating crawler type tractors in tandem - Quad 9 and similar type)

GROUP 18: Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - single engine, up to and including 25 yds. struck)

GROUP 19: Rotex concrete belt operator (or similar types); Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - single engine, Caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds.and up to and including 50 cu. yds. struck); Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - multiple engine, up to and including 25 yds. struck)

GROUP 20: Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar types in any combination, excluding compaction units - single engine, over 50 yds. struck); Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps, and similar types in any combination, excluding compaction units - multiple engine, Euclid, Caterpillar and similar, over 25 yds. and up to 50 yds. struck)

GROUP 21: Rubber-tired earth-moving equipment operator, operating in tandem (scrapers, belly dumps and similar

types in any combination, excluding compaction units - multiple engine, Euclid, Caterpillar and similar type, over 50 cu. yds. struck)

GROUP 22: Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (single engine, up to and including 25 yds. struck)

GROUP 23: Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (single engine, Caterpillar, Euclid, Athey Wagon and similar types with any and all attachments over 25 yds. and up to and including 50 yds. struck); Rubber-tired earth-moving equipment operator, operating with the tandem push-pull system (multiple engine, up to and including 25 yds. struck)

GROUP 24: Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (single engine, over 50 yds. struck); Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (multiple engine, Euclid, Caterpillar and similar, over 25 yds. and up to 50 yds. struck)

GROUP 25: Concrete pump operator-truck mounted; Rubber-tired earth-moving equipment operator, operating equipment with the tandem push-pull system (multiple engine, Euclid, Caterpillar and similar type, over 50 cu. yds. struck); Spyder Excavator Operator, with all attachments

CRANES, PILEDRIVING AND HOISTING EQUIPMENT CLASSIFICATIONS

GROUP 1: Engineer oiler; Fork lift operator (includes loed, lull or similar types)

GROUP 2: Truck crane oiler

GROUP 3: A-frame or winch truck operator; Ross carrier operator (jobsite)

GROUP 4: Bridge-type unloader and turntable operator; Helicopter hoist operator

GROUP 5: Hydraulic boom truck; Stinger crane (Austin-Western or similar type); Tugger hoist operator (1 drum)

GROUP 6: Bridge crane operator; Cretor crane operator; Hoist operator (Chicago boom and similar type); Lift mobile operator; Lift slab machine operator (Vagtborg and similar types); Material hoist and/or manlift operator; Polar gantry crane operator; Self Climbing scaffold (or similar type); Shovel, backhoe, dragline, clamshell operator (over 3/4 yd. and up to 5 cu. yds. mrc); Tugger hoist operator

GROUP 7: Pedestal crane operator; Shovel, backhoe, dragline, clamshell operator (over 5 cu. yds. mrc); Tower crane repair; Tugger hoist operator (3 drum)

GROUP 8: Crane operator (up to and including 25 ton capacity); Crawler transporter operator; Derrick barge operator (up to and including 25 ton capacity); Hoist operator, stiff legs, Guy derrick or similar type (up to and including 25 ton capacity); Shovel, backhoe, dragline, clamshell operator (over 7 cu. yds., M.R.C.)

GROUP 9: Crane operator (over 25 tons and up to and including 50 tons mrc); Derrick barge operator (over 25 tons up to and including 50 tons mrc); Highline cableway operator; Hoist operator, stiff legs, Guy derrick or similar type (over 25 tons up to and including 50 tons mrc); K-crane operator; Polar crane operator; Self erecting tower crane operator maximum lifting capacity ten tons

GROUP 10: Crane operator (over 50 tons and up to and including 100 tons mrc); Derrick barge operator (over 50 tons up to and including 100 tons mrc); Hoist operator, stiff legs, Guy derrick or similar type (over 50 tons up to and including 100 tons mrc), Mobile tower crane operator (over 50 tons, up to and including 100 tons M.R.C.);

GROUP 11: Crane operator (over 100 tons and up to and including 200 tons mrc); Derrick barge operator (over 100 tons up to and including 200 tons mrc); Hoist operator, stiff legs, Guy derrick or similar type (over 100 tons up to and including 200 tons mrc); Mobile tower crane operator (over 100 tons up to and including 200 tons mrc) ; Tower crane operator and tower gantry

GROUP 12: Crane operator (over 200 tons up to and including 300 tons mrc); Derrick barge operator (over 200 tons up to and including 300 tons mrc); Hoist operator, stiff legs, Guy derrick or similar type (over 200 tons, up to and including 300 tons mrc); Mobile tower crane operator (over 200 tons, up to and including 300 tons mrc)

GROUP 13: Crane operator (over 300 tons); Derrick barge operator (over 300 tons); Helicopter pilot; Hoist operator, stiff legs, Guy derrick or similar type (over 300 tons); Mobile tower crane operator (over 300 tons)

TUNNEL CLASSIFICATIONS

GROUP 1: Skiploader (wheel type up to 3/4 yd. without attachment)

GROUP 2: Power-driven jumbo form setter operator

GROUP 3: Dinkey locomotive or motorperson (up to and including 10 tons)

GROUP 4: Bit sharpener; Equipment greaser (grease truck); Slip form pump operator (power-driven hydraulic lifting device for concrete forms); Tugger hoist operator (1 drum); Tunnel locomotive operator (over 10 and up to and including 30 tons)

GROUP 5: Backhoe operator (up to and including 3/4 yd.); Small Ford, Case or similar; Drill doctor; Grouting machine operator; Heading shield operator; Heavy-duty repairperson; Loader operator (Athey, Euclid, Sierra and similar types); Mucking machine operator (1/4 yd., rubber-tired, rail or track type); Pneumatic concrete placing machine operator (Hackley-Presswell or similar type); Pneumatic heading shield (tunnel); Pumpcrete gun operator; Tractor compressor drill combination operator; Tugger hoist operator (2 drum); Tunnel locomotive operator (over 30 tons)

GROUP 6: Heavy Duty Repairman

GROUP 7: Tunnel mole boring machine operator

ENGINEERS ZONES

$1.00 additional per hour for all of IMPERIAL County and the portions of KERN, RIVERSIDE & SAN BERNARDINO Counties as defined below:

That area within the following Boundary: Begin in San Bernardino County, approximately 3 miles NE of the intersection of I-15 and the California State line at that point which is the NW corner of Section 1, T17N,m R14E, San Bernardino Meridian. Continue W in a straight line to that point which is the SW corner of the northwest quarter of Section 6, T27S, R42E, Mt. Diablo Meridian. Continue North to the intersection with the Inyo County Boundary at that point which is the NE corner of the western half of the northern quarter of Section 6, T25S, R42E, MDM. Continue W along the Inyo and San Bernardino County boundary until the intersection with Kern County, as that point which is the SE corner of Section 34, T24S, R40E, MDM. Continue W along the Inyo and Kern County boundary until the intersection with Tulare County, at that point which is the SW corner of the SE quarter of Section 32, T24S, R37E, MDM. Continue W along the Kern and Tulare County boundary, until that point which is the NW corner of T25S, R32E, MDM. Continue S following R32E lines to the NW corner of T31S, R32E, MDM. Continue W to the NW corner of T31S, R31E, MDM. Continue S to the SW corner of T32S, R31E, MDM. Continue W to SW corner of SE quarter of Section 34, T32S, R30E, MDM. Continue S to SW corner of T11N, R17W, SBM. Continue E along south boundary of T11N, SBM to SW corner of T11N, R7W, SBM. Continue S to SW corner of T9N, R7W, SBM. Continue E along south boundary of T9N, SBM to SW corner of T9N, R1E, SBM. Continue S along west boundary of R1E, SMB to Riverside County line at the SW corner of T1S, R1E, SBM. Continue E along south boundary of T1s, SBM (Riverside County Line) to SW corner of T1S, R10E, SBM. Continue S along west boundary of R10E, SBM to Imperial County line at the SW corner of T8S, R10E, SBM. Continue W along Imperial and Riverside county line to NW corner of T9S, R9E, SBM. Continue S along the boundary between Imperial and San Diego Counties, along the west edge of R9E, SBM to the south boundary of Imperial County/California state line. Follow the California state line west to Arizona state line, then north to Nevada state line, then continuing NW back to start at the point which is the NW corner of Section 1, T17N, R14E, SBM

$1.00 additional per hour for portions of SAN LUIS OBISPO, KERN, SANTA BARBARA & VENTURA as defined below:

That area within the following Boundary: Begin approximately 5 miles north of the community of Cholame, on the Monterey County and San Luis Obispo County boundary at the NW corner of T25S, R16E, Mt. Diablo Meridian. Continue south along the west side of R16E to the SW corner of T30S, R16E, MDM. Continue E to SW corner of T30S, R17E, MDM. Continue S to SW corner of T31S, R17E, MDM. Continue E to SW corner of T31S, R18E, MDM. Continue S along West side of R18E, MDM as it crosses into San Bernardino Meridian numbering area and becomes R30W. Follow the west side of R30W, SBM to the SW corner of T9N, R30W, SBM. Continue E along the south edge of T9N, SBM to the Santa Barbara County and Ventura County boundary at that point whch is the SW corner of Section 34.T9N, R24W, SBM, continue S along the Ventura County line to that point which is the SW corner of the SE quarter of Section 32, T7N, R24W, SBM. Continue E

along the south edge of T7N, SBM to the SE corner to T7N, R21W, SBM. Continue N along East side of R21W, SBM to Ventura County and Kern County boundary at the NE corner of T8N, R21W. Continue W along the Ventura County and Kern County boundary to the SE corner of T9N, R21W. Continue North along the East edge of R21W, SBM to the NE corner of T12N, R21W, SBM. Continue West along the north edge of T12N, SBM to the SE corner of T32S, R21E, MDM. [T12N SBM is a think strip between T11N SBM and T32S MDM]. Continue North along the East side of R21E, MDM to the Kings County and Kern County border at the NE corner of T25S, R21E, MDM, continue West along the Kings County and Kern County Boundary until the intersection of San Luis Obispo County. Continue west along the Kings County and San Luis Obispo County boundary until the intersection with Monterey County. Continue West along the Monterey County and San Luis Obispo County boundary to the beginning point at the NW corner of T25S, R16E, MDM.

$2.00 additional per hour for INYO and MONO Counties and the Northern portion of SAN BERNARDINO County as defined below:

That area within the following Boundary: Begin at the intersection of the northern boundary of Mono County and the California state line at the point which is the center of Section 17, T10N, R22E, Mt. Diablo Meridian. Continue S then SE along the entire western boundary of Mono County, until it reaches Inyo County at the point which is the NE corner of the Western half of the NW quarter of Section 2, T8S, R29E, MDM. Continue SSE along the entire western boundary of Inyo County, until the intersection with Kern County at the point which is the SW corner of the SE 1/4 of Section 32, T24S, R37E, MDM. Continue E along the Inyo and Kern County boundary until the intersection with San Bernardino County at that point which is the SE corner of section 34, T24S, R40E, MDM. Continue E along the Inyo and San Bernardino County boundary until the point which is the NE corner of the Western half of the NW quarter of Section 6, T25S, R42E, MDM. Continue S to that point which is the SW corner of the NW quarter of Section 6, T27S, R42E, MDM. Continue E in a straight line to the California and Nevada state border at the point which is the NW corner of Section 1, T17N, R14E, San Bernardino Meridian. Then continue NW along the state line to the starting point, which is the center of Section 18, T10N, R22E, MDM.

REMAINING AREA NOT DEFINED ABOVE RECIEVES BASE RATE

IRON0433-006 01/01/2025

	Rates	Fringes
IRONWORKER		
Fence Erector	$ 45.78	26.51
Ornamental, Reinforcing and Structural	$ 50.70	35.15

PREMIUM PAY:

$9.00 additional per hour at the following locations:

China Lake Naval Test Station, Chocolate Mountains Naval Reserve-Niland,
Edwards AFB, Fort Irwin Military Station, Fort Irwin Training

Center-Goldstone, San Clemente Island, San Nicholas Island, Susanville Federal Prison, 29 Palms - Marine Corps, U.S. Marine Base - Barstow, U.S. Naval Air Facility - Sealey, Vandenberg AFB Army Defense Language Institute - Monterey, Fallon Air Base, Naval Post Graduate School - Monterey, Yermo Marine Corps Logistics Center
Port Hueneme, Port Mugu, U.S. Coast Guard Station - Two Rock

LABO0220-001 07/01/2022

	Rates	Fringes
LABORER (TUNNEL)		
GROUP 1	$ 45.68	23.30
GROUP 2	$ 46.00	23.30
GROUP 3	$ 46.46	23.30
GROUP 4	$ 47.15	23.30
LABORER		
GROUP 1	$ 36.39	21.04
GROUP 2	$ 36.94	21.04
GROUP 3	$ 37.49	21.04
GROUP 4	$ 39.04	21.04
GROUP 5	$ 39.39	21.04

LABORER CLASSIFICATIONS

GROUP 1: Cleaning and handling of panel forms; Concrete screeding for rough strike-off; Concrete, water curing; Demolition laborer, the cleaning of brick if performed by a worker performing any other phase of demolition work, and the cleaning of lumber; Fire watcher, limber, brush loader, piler and debris handler; Flag person; Gas, oil and/or water pipeline laborer; Laborer, asphalt-rubber material loader; Laborer, general or construction; Laborer, general clean-up; Laborer, landscaping; Laborer, jetting; Laborer, temporary water and air lines; Material hose operator (walls, slabs, floors and decks); Plugging, filling of shee bolt holes; Dry packing of concrete; Railroad maintenance, repair track person and road beds; Streetcar and railroad construction track laborers; Rigging and signaling; Scaler; Slip form raiser; Tar and mortar; Tool crib or tool house laborer; Traffic control by any method; Window cleaner; Wire mesh pulling - all concrete pouring operations

GROUP 2: Asphalt shoveler; Cement dumper (on 1 yd. or larger mixer and handling bulk cement); Cesspool digger and installer; Chucktender; Chute handler, pouring concrete, the handling of the chute from readymix trucks, such as walls, slabs, decks, floors, foundation, footings, curbs, gutters and sidewalks; Concrete curer, impervious membrane and form oiler; Cutting torch operator (demolition); Fine grader, highways and street paving, airport, runways and similar type heavy construction; Gas, oil and/or water pipeline wrapper - pot tender and form person; Guinea chaser; Headerboard person - asphalt; Laborer, packing rod steel and pans; Membrane vapor barrier installer; Power broom sweeper (small); Riprap stonepaver, placing stone or wet sacked concrete; Roto scraper and tiller; Sandblaster (pot tender); Septic tank digger and installer(lead); Tank scaler and cleaner; Tree climber, faller, chain saw operator, Pittsburgh chipper and similar type brush shredder; Underground laborer, including caisson bellower

GROUP 3: Buggymobile person; Concrete cutting torch; Concrete pile cutter; Driller, jackhammer, 2-1/2 ft. drill steel or longer; Dri-pak-it machine; Gas, oil and/or water pipeline wrapper, 6-in. pipe and over, by any method, inside and out; High scaler (including drilling of same); Hydro seeder and similar type; Impact wrench multi-plate; Kettle person, pot person and workers applying asphalt, lay-kold, creosote, lime caustic and similar type materials (""applying"" means applying, dipping, brushing or handling of such materials for pipe wrapping and waterproofing); Operator of pneumatic, gas, electric tools, vibrating machine, pavement breaker, air blasting, come-alongs, and similar mechanical tools not separately classified herein; Pipelayer's backup person, coating, grouting, making of joints, sealing, caulking, diapering and including rubber gasket joints, pointing and any and all other services; Rock slinger; Rotary scarifier or multiple head concrete chipping scarifier; Steel headerboard and guideline setter; Tamper, Barko, Wacker and similar type; Trenching machine, hand-propelled

GROUP 4: Asphalt raker, lute person, ironer, asphalt dump person, and asphalt spreader boxes (all types); Concrete core cutter (walls, floors or ceilings), grinder or sander; Concrete saw person, cutting walls or flat work, scoring old or new concrete; Cribber, shorer, lagging, sheeting and trench bracing, hand-guided lagging hammer; Head rock slinger; Laborer, asphalt- rubber distributor boot person; Laser beam in connection with laborers' work; Oversize concrete vibrator operator, 70 lbs. and over; Pipelayer performing all services in the laying and installation of pipe from the point of receiving pipe in the ditch until completion of operation, including any and all forms of tubular material, whether pipe, metallic or non-metallic, conduit and any other stationary type of tubular device used for the conveying of any substance or element, whether water, sewage, solid gas, air, or other product whatsoever and without regard to the nature of material from which the tubular material is fabricated; No-joint pipe and stripping of same; Prefabricated manhole installer; Sandblaster (nozzle person), water blasting, Porta Shot-Blast

GROUP 5: Blaster powder, all work of loading holes, placing and blasting of all powder and explosives of whatever type, regardless of method used for such loading and placing; Driller: All power drills, excluding jackhammer, whether core, diamond, wagon, track, multiple unit, and any and all other types of mechanical drills without regard to the form of motive power; Toxic waste removal

TUNNEL LABORER CLASSIFICATIONS

GROUP 1: Batch plant laborer; Changehouse person; Dump person; Dump person (outside); Swamper (brake person and switch person on tunnel work); Tunnel materials handling person; Nipper; Pot tender, using mastic or other materials (for example, but not by way of limitation, shotcrete, etc.);

GROUP 2: Bull gang mucker, track person; Chucktender, Cabletender; Concrete crew, including rodder and spreader; Loading and unloading agitator cars; Vibrator person, jack hammer, pneumatic tools (except driller)

GROUP 3: Blaster, driller, powder person; Chemical grout jet

person; Cherry picker person; Grout gun person; Grout mixer person; Grout pump person; Jackleg miner; Jumbo person; Kemper and other pneumatic concrete placer operator; Miner, tunnel (hand or machine); Nozzle person; Operating of troweling and/or grouting machines; Powder person (primer house); Primer person; Sandblaster; Shotcrete person; Steel form raiser and setter; Timber person, retimber person, wood or steel; Tunnel Concrete finisher

GROUP 4: Diamond driller; Sandblaster; Shaft and raise work

LABO0220-004 07/01/2024

	Rates	Fringes
Brick Tender	$ 41.53	22.54

LABO0300-005 07/01/2024

	Rates	Fringes
Asbestos Removal Laborer	$ 43.88	25.13

SCOPE OF WORK: Includes site mobilization, initial site cleanup, site preparation, removal of asbestos-containing material and toxic waste, encapsulation, enclosure and disposal of asbestos- containing materials and toxic waste by hand or with equipment or machinery; scaffolding, fabrication of temporary wooden barriers and assembly of decontamination stations.

LABO0345-001 07/01/2024

	Rates	Fringes
LABORER (GUNITE)		
GROUP 1	$ 53.48	22.77
GROUP 2	$ 52.53	22.77
GROUP 3	$ 48.99	22.77

FOOTNOTE: GUNITE PREMIUM PAY: Workers working from a Bosn'n's Chair or suspended from a rope or cable shall receive 40 cents per hour above the foregoing applicable classification rates. Workers doing gunite and/or shotcrete work in a tunnel shall receive 35 cents per hour above the foregoing applicable classification rates, paid on a portal-to-portal basis. Any work performed on, in or above any smoke stack, silo, storage elevator or similar type of structure, when such structure is in excess of 75'-0"" above base level and which work must be performed in whole or in part more than 75'-0"" above base level, that work performed above the 75'-0"" level shall be compensated for at 35 cents per hour above the applicable classification wage rate.

GUNITE LABORER CLASSIFICATIONS

GROUP 1: Rodmen, Nozzlemen

GROUP 2: Gunmen

GROUP 3: Reboundmen

LABO1184-001 07/01/2024

	Rates	Fringes
Laborers: (HORIZONTAL DIRECTIONAL DRILLING)		
(1) Drilling Crew Laborer	$ 45.34	20.06
(2) Vehicle Operator/Hauler	$ 45.51	20.06
(3) Horizontal Directional Drill Operator	$ 47.36	20.06
(4) Electronic Tracking Locator	$ 49.36	20.06
Laborers: (STRIPING/SLURRY SEAL)		
GROUP 1	$ 46.65	23.17
GROUP 2	$ 47.95	23.17
GROUP 3	$ 49.96	23.17
GROUP 4	$ 51.70	23.17

LABORERS - STRIPING CLASSIFICATIONS

GROUP 1: Protective coating, pavement sealing, including repair and filling of cracks by any method on any surface in parking lots, game courts and playgrounds; carstops; operation of all related machinery and equipment; equipment repair technician

GROUP 2: Traffic surface abrasive blaster; pot tender - removal of all traffic lines and markings by any method (sandblasting, waterblasting, grinding, etc.) and preparation of surface for coatings. Traffic control person: controlling and directing traffic through both conventional and moving lane closures; operation of all related machinery and equipment

GROUP 3: Traffic delineating device applicator: Layout and application of pavement markers, delineating signs, rumble and traffic bars, adhesives, guide markers, other traffic delineating devices including traffic control. This category includes all traffic related surface preparation (sandblasting, waterblasting, grinding) as part of the application process. Traffic protective delineating system installer: removes, relocates, installs, permanently affixed roadside and parking delineation barricades, fencing, cable anchor, guard rail, reference signs, monument markers; operation of all related machinery and equipment; power broom sweeper

GROUP 4: Striper: layout and application of traffic stripes and markings; hot thermo plastic; tape traffic stripes and markings, including traffic control; operation of all related machinery and equipment

---

LABO1414-003 08/07/2024

	Rates	Fringes
LABORER		
PLASTER CLEAN-UP LABORER	$ 43.57	25.17
PLASTER TENDER	$ 46.12	25.17

Work on a swing stage scaffold: $1.00 per hour additional.

Work at Military Bases - $3.00 additional per hour:
Coronado Naval Amphibious Base, Fort Irwin, Marine Corps Air Station-29 Palms, Imperial Beach Naval Air Station, Marine Corps Logistics Supply Base, Marine Corps Pickle Meadows, Mountain Warfare Training Center, Naval Air Facility-Seeley, North Island Naval Air Station, Vandenberg AFB.

PAIN0036-002 07/01/2023

	Rates	Fringes
Painters: (Including Lead Abatement)		
(1) Journeyman Painter	$ 36.44	18.58
(2) Repaint	$ 26.40	17.02
(3) Iron & Steel	$ 33.12	17.18
(4) High Iron & Steel	$ 35.12	17.18
(5) All Other Work	$ 36.44	18.58

REPAINT:
Repaint of any structure with the exception of work involving the aerospace industry, breweries, commercial recreational facilities, hotels which operate commercial establishments as part of hotel service, and sports facilities, tenant improvement work not included in conjunction with the construction of the building and all repainting of tenant improvement projects.

HIGH IRON & STEEL:
Aerial towers, towers, radio towers, smoke stacks, flag poles (any flag poles that can be finished from the ground with a ladder excluded), elevated water towers, steeples and domes in their entirety and any other extremely high and hazardous work, cooning steel, bos'n chair, or other similar devices, painting in other high hazardous work shall be classified as high iron & steel

---

PAIN0036-008 09/01/2024

	Rates	Fringes
DRYWALL FINISHER/TAPER	$ 49.33	26.82

---

* PAIN0036-015 01/01/2025

	Rates	Fringes
GLAZIER	$ 53.05	30.64

FOOTNOTE: Additional $1.25 per hour for work in a condor, from the third (3rd) floor and up Additional $1.25 per hour for work on the outside of the building from a swing stage or any suspended contrivance, from the ground up

---

PAIN1247-002 01/01/2025

	Rates	Fringes
SOFT FLOOR LAYER	$ 45.15	19.43

PLAS0200-006 08/03/2022

	Rates	Fringes
PLASTERER	$ 47.37	19.64

VANDENBURG AFB: $3.00 additional per hour.

PLAS0500-002 07/01/2023

	Rates	Fringes
CEMENT MASON/CONCRETE FINISHER	$ 44.00	27.11

PLUM0016-004 09/01/2024

	Rates	Fringes
PLUMBER/PIPEFITTER		
Vandenburg Air Force Base, Work ONLY on new additions and remodeling of bars, restaurants, stores and commercial buildings not to exceed 5,000 sq. ft. of floor space	$ 63.98	26.61
Work ONLY on strip malls, light commercial, tenant improvement and remodel work	$ 57.67	25.63
All other work except work on new additions and remodeling of bars, restaurant, stores and commercial buildings not to exceed 5,000 sq. ft. of floor space and work on strip malls, light commercial, tenant improvement and remodel work	$ 44.24	23.96
	$ 59.48	26.61

PLUM0345-001 09/01/2023

	Rates	Fringes
PLUMBER		
Landscape/Irrigation Fitter	$ 40.20	25.90
Sewer & Storm Drain Work	$ 44.29	23.28

ROOF0036-002 08/01/2024

	Rates	Fringes
ROOFER	$ 49.43	20.58

FOOTNOTE: Pitch premium: Work on which employees are exposed to pitch fumes or required to handle pitch, pitch base or pitch impregnated products, or any material containing coal tar pitch, the entire roofing crew shall receive $1.75 per hour ""pitch premium"" pay.

SFCA0669-014 01/01/2025

	Rates	Fringes
SPRINKLER FITTER	$ 46.42	28.42

SHEE0273-002 08/01/2019

	Rates	Fringes
SHEET METAL WORKER	$ 45.48	30.05

HOLIDAYS: New Year's Day, Martin Luther King Day, President's Day, Good Friday, Memorial Day, Indepdendence Day, Labor Day, Veterans Day,Thankisgiving Day & Friday after, Christmas Day

---

TEAM0011-002 07/01/2024

	Rates	Fringes
TRUCK DRIVER		
GROUP 1	$ 39.59	34.34
GROUP 2	$ 39.74	34.34
GROUP 3	$ 39.87	34.34
GROUP 4	$ 40.06	34.34
GROUP 5	$ 40.09	34.34
GROUP 6	$ 40.12	34.34
GROUP 7	$ 40.37	34.34
GROUP 8	$ 40.62	34.34
GROUP 9	$ 40.82	34.34
GROUP 10	$ 41.12	34.34
GROUP 11	$ 41.62	34.34
GROUP 12	$ 42.05	34.34

WORK ON ALL MILITARY BASES:
PREMIUM PAY: $3.00 per hour additional.
[29 palms Marine Base, Camp Roberts, China Lake, Edwards AFB, El Centro Naval Facility, Fort Irwin, Marine Corps Logistics Base at Nebo & Yermo, Mountain Warfare Training Center, Bridgeport, Point Arguello, Point Conception, Vandenberg AFB]

TRUCK DRIVERS CLASSIFICATIONS

GROUP 1: Truck driver

GROUP 2: Driver of vehicle or combination of vehicles - 2 axles; Traffic control pilot car excluding moving heavy equipment permit load; Truck mounted broom

GROUP 3: Driver of vehicle or combination of vehicles - 3 axles; Boot person; Cement mason distribution truck; Fuel truck driver; Water truck - 2 axle; Dump truck, less than 16 yds. water level; Erosion control driver

GROUP 4: Driver of transit mix truck, under 3 yds.; Dumpcrete truck, less than 6-1/2 yds. water level

GROUP 5: Water truck, 3 or more axles; Truck greaser and tire person ($0.50 additional for tire person); Pipeline and utility working truck driver, including winch truck and plastic fusion, limited to pipeline and utility work; Slurry truck driver

GROUP 6: Transit mix truck, 3 yds. or more; Dumpcrete truck, 6-1/2 yds. water level and over; Vehicle or combination of vehicles - 4 or more axles; Oil spreader truck; Dump truck, 16 yds. to 25 yds. water level

GROUP 7: A Frame, Swedish crane or similar; Forklift driver; Ross carrier driver

GROUP 8: Dump truck, 25 yds. to 49 yds. water level; Truck repair person; Water pull - single engine; Welder

GROUP 9: Truck repair person/welder; Low bed driver, 9 axles or over

GROUP 10: Dump truck - 50 yds. or more water level; Water pull - single engine with attachment

GROUP 11: Water pull - twin engine; Water pull - twin engine with attachments; Winch truck driver - $1.25 additional when operating winch or similar special attachments

GROUP 12: Boom Truck 17K and above

WELDERS - Receive rate prescribed for craft performing operation to which welding is incidental.

==========

Note: Executive Order (EO) 13706, Establishing Paid Sick Leave for Federal Contractors applies to all contracts subject to the Davis-Bacon Act for which the contract is awarded (and any solicitation was issued) on or after January 1, 2017. If this contract is covered by the EO, the contractor must provide employees with 1 hour of paid sick leave for every 30 hours they work, up to 56 hours of paid sick leave each year. Employees must be permitted to use paid sick leave for their own illness, injury or other health-related needs, including preventive care; to assist a family member (or person who is like family to the employee) who is ill, injured, or has other health-related needs, including preventive care; or for reasons resulting from, or to assist a family member (or person who is like family to the employee) who is a victim of, domestic violence, sexual assault, or stalking. Additional information on contractor requirements and worker protections under the EO is available at https://www.dol.gov/agencies/whd/government-contracts.

Unlisted classifications needed for work not included within the scope of the classifications listed may be added after award only as provided in the labor standards contract clauses (29CFR 5.5 (a) (1) (iii)).

The body of each wage determination lists the classifications and wage rates that have been found to be prevailing for the type(s) of construction and geographic area covered by the wage determination. The classifications are listed in alphabetical order under rate identifiers indicating whether the particular rate is a union rate (current union negotiated rate), a survey rate, a weighted union average rate, a state adopted rate, or a

supplemental classification rate.

Union Rate Identifiers

A four-letter identifier beginning with characters other than ""SU"", ""UAVG"", ?SA?, or ?SC? denotes that a union rate was prevailing for that classification in the survey. Example: PLUM0198-005 07/01/2024. PLUM is an identifier of the union whose collectively bargained rate prevailed in the survey for this classification, which in this example would be Plumbers. 0198 indicates the local union number or district council number where applicable, i.e., Plumbers Local 0198. The next number, 005 in the example, is an internal number used in processing the wage determination. The date, 07/01/2024 in the example, is the effective date of the most current negotiated rate.

Union prevailing wage rates are updated to reflect all changes over time that are reported to WHD in the rates in the collective bargaining agreement (CBA) governing the classification.

Union Average Rate Identifiers

The UAVG identifier indicates that no single rate prevailed for those classifications, but that 100% of the data reported for the classifications reflected union rates. EXAMPLE: UAVG-OH-0010 01/01/2024. UAVG indicates that the rate is a weighted union average rate. OH indicates the State of Ohio. The next number, 0010 in the example, is an internal number used in producing the wage determination. The date, 01/01/2024 in the example, indicates the date the wage determination was updated to reflect the most current union average rate.

A UAVG rate will be updated once a year, usually in January, to reflect a weighted average of the current rates in the collective bargaining agreements on which the rate is based.

Survey Rate Identifiers

The ""SU"" identifier indicates that either a single non-union rate prevailed (as defined in 29 CFR 1.2) for this classification in the survey or that the rate was derived by computing a weighted average rate based on all the rates reported in the survey for that classification. As a weighted average rate includes all rates reported in the survey, it may include both union and non-union rates. Example: SUFL2022-007 6/27/2024. SU indicates the rate is a single non-union prevailing rate or a weighted average of survey data for that classification. FL indicates the State of Florida. 2022 is the year of the survey on which these classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 6/27/2024 in the example, indicates the survey completion date for the classifications and rates under that identifier.

?SU? wage rates typically remain in effect until a new survey is conducted. However, the Wage and Hour Division (WHD) has the discretion to update such rates under 29 CFR 1.6(c)(1).

State Adopted Rate Identifiers

The ""SA"" identifier indicates that the classifications and prevailing wage rates set by a state (or local) government were adopted under 29 C.F.R 1.3(g)-(h). Example: SAME2023-007

01/03/2024. SA reflects that the rates are state adopted. ME refers to the State of Maine. 2023 is the year during which the state completed the survey on which the listed classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 01/03/2024 in the example, reflects the date on which the classifications and rates under the ?SA? identifier took effect under state law in the state from which the rates were adopted.

WAGE DETERMINATION APPEALS PROCESS

1) Has there been an initial decision in the matter? This can be:

a) a survey underlying a wage determination
b) an existing published wage determination
c) an initial WHD letter setting forth a position on a wage determination matter
d) an initial conformance (additional classification and rate) determination

On survey related matters, initial contact, including requests for summaries of surveys, should be directed to the WHD Branch of Wage Surveys. Requests can be submitted via email to davisbaconinfo@dol.gov or by mail to:

Branch of Wage Surveys
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

Regarding any other wage determination matter such as conformance decisions, requests for initial decisions should be directed to the WHD Branch of Construction Wage Determinations. Requests can be submitted via email to BCWD-Office@dol.gov or by mail to:

Branch of Construction Wage Determinations
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

2) If an initial decision has been issued, then any interested party (those affected by the action) that disagrees with the decision can request review and reconsideration from the Wage and Hour Administrator (See 29 CFR Part 1.8 and 29 CFR Part 7). Requests for review and reconsideration can be submitted via email to dba.reconsideration@dol.gov or by mail to:

Wage and Hour Administrator
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

The request should be accompanied by a full statement of the interested party's position and any information (wage payment data, project description, area practice material, etc.) that the requestor considers relevant to the issue.

3) If the decision of the Administrator is not favorable, an

interested party may appeal directly to the Administrative Review Board (formerly the Wage Appeals Board). Write to:

Administrative Review Board
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210.

==========

END OF GENERAL DECISION"

EXHIBIT B

PROPOSAL

PROPOSAL

Pursuant to and in compliance with your Notice to Bidders and the Contract Documents relating to the construction of:

County of Santa Barbara

Rehabilitate Tie-Down Apron

900 Airport Road, Santa Ynez, California
County Project No. 22011-AIP XX
Bid Date 3:00 pm, **Friday, May 30, 2025**

including Addendum No(s). 1, 2, ___, ___, ___, ___, ___, the undersigned bidder, having become thoroughly familiar with the terms and conditions of the Contract Documents and with local conditions affecting the performance and the costs of the Work at the place where the Work is to be done, hereby proposes and agrees to fully perform the Work within the time stated in and in strict accordance with the Contract Documents (including the furnishing of any and all labor, materials, tools, expendable equipment and utility and transportation services necessary to fully perform the work and complete it in a workmanlike manner) for the total sum of:

Written if Figures: $ 388,350

Written in Words: Three hundred eighty eight thousand three hundred fifty dollars

Bid Schedule follows on the next page. Bidding Contractors to complete all blanks on the Bid Schedule:

Name of Bidder: American Road Maintenance

California Contractors License Number (Class): 982100 C32

PROJECT BID SCHEDULE

ITEM NO.	SPEC SECTION	DESCRIPTION	UNIT	ESTIMATED QUANTITY	UNIT PRICE (Figures)	EXTENDED TOTAL (Figures)
1	C-105	Mobilization (8% Max)	LS	1.0	$ 25,000	$ 25,000
2	C-104T	Airport Safety and Security (5% Max)	LS	1.0	$ 10,000	$ 10,000
3	P-101	Uninstall & Re-Install Tie Down Cables and Chains	LS	1.0	$ 20,000	$ 20,000
4	P-101	Remove Pavement Markings	SF	8,000.0	$ 3	$ 24,000
5	P-101	Crack Seal	LF	46,000.0	$ 1.50	$ 69,000
6	P-608	Emulsified Asphalt Seal Coat	SY	72,500.0	$ 2.50	$ 181,250
7	P-620	Markings: 2-Coat with Reflective Media	SF	5,100.0	$ 3	$ 15,300
8	P-620	Markings: 2-Coat w/o Reflective Media	SF	14,600.0	$ 3	$ 43,800
					TOTAL, BID SCHEDULE (Written in Figures):	$ 388,350

Abbreviations to Bid Schedule(s):

LS = lump sum	TON = 2000 pounds	LF = lineal foot	EA = each unit
SF = square foot	CY = cubic yard	SY = square yard	T&M = time and materials
ACRE = 43,560 square feet		CF = cubic foot	GAL = 1 U.S. Gallon, liquid measure

Total Bid, Basis of Award:

Written in Words: Three hundred eighty eight thousand three hundred fifty dollars

Written in Figures: $ 388,350

In the event of discrepancy between words and figures, the words shall prevail.

In the event that the product of a unit price and an estimated quantity does not equal the extended amount quoted, the unit price shall govern and the correct product of the unit price and the estimated quantity shall be deemed to be the amount bid.

In order for a Bid to be responsive, Bidder must complete all blanks in the Bid Schedule. The failure to do so shall result in the Bid being rejected as non-responsive.

It is understood that Owner reserves the right to reject the proposal and that it shall remain open and not be withdrawn for a period of one hundred twenty (120) calendar days from the date prescribed for its opening.

Attached hereto and incorporated herein is the complete and entire list of subcontractors to be employed by the undersigned and in the performance of the Work.

It is understood and agreed that if written notice of the acceptance of this proposal is mailed or delivered personally to the undersigned bidder within **one hundred twenty (120) calendar days** after the opening of the proposal, or at any time thereafter before it is withdrawn, the undersigned bidder will execute and deliver the Contract Documents to Owner in accordance with the proposal as accepted, and will also furnish and deliver to Owner any Payment Bond required under the provisions of California Civil Code Section 3247 through 3252 and Performance Bond as required under the provisions of the California Government Code and/or California Public Contract Code all within fourteen (14) calendar days after personal delivery or deposit in the mails, as the case may be, of the notifications of award. The work under the contract shall be commenced by the undersigned bidder on the date stated in COUNTY'S written Notice to Proceed and shall be completed within **50 Working** days thereafter.

Notice of acceptance or request for additional information may be addressed to the undersigned bidder at the business address set forth below.

The bid, contract or other submittal of the CONTRACTOR identified below in connection with the foregoing project is not made in the interest of or on behalf or any undisclosed person, partnership, company, association, organization, or corporation; and that the bid is genuine, and not collusive or sham; that the undersigned bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid and has not directly or indirectly colluded, conspired, connived or agreed with any bidder or anyone else to put in a sham bid, or to refrain from bidding; that the undersigned bidder has not directly or indirectly sought by agreement, communication or conference with anyone to fix his bid price or the bid price of any other bidder or to fix any overhead, profit or cost element of such bid price or of that of any other bidder or to secure any advantage against the COUNTY of Santa Barbara of anyone interested in the proposed contract; or all statements contained in this proposal are true; and that the undersigned bidder has not directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay any fee to any corporation, partnership, company association, organization, Bid Depository or to any member or agent thereof to effectuate a collusive or sham bid. I declare under the penalty of perjury under the laws of the State of California that the foregoing is true and correct.

In accordance with the provisions of Sections 1860 and 1861 of the California Labor Code, every CONTRACTOR will be required to secure the payment of compensation of his or her employees. Each CONTRACTOR to whom a public works contract is awarded shall sign the following certification prior to performing the work of the contract: "I am aware of the provisions of Section 3700 of the Labor Code which requires every employer to be insured against liability for worker's compensation or to undertake self-insurance in accordance with the provisions of that code, and I will comply with such provisions before commencing the performance of the work of this contract."

SIGNATURE PAGE

CONTRACTOR

American Road Maintenance	36-2615355
(Company)	(IRS No)
4554 E Eco Industrial Pl	4554 E Eco Industrial Pl Tucson, AZ 85756
(Street Address)	(Mailing Address)
Tucson	480-309-7102
(City)	(Phone Number)
1000041545	C32
(DIR Registration No)	(License Classification(s))
Kyle Paulson	
By (Name)	
	Officer
(Signature)	(Title)

DESIGNATION OF SUBCONTRACTORS

The bidder agrees if this proposal is accepted, that he will contract with the County of Santa Barbara to do all work and furnish all labor, materials, machinery, tools and apparatus necessary to completely perform said Contracts in the manner and time prescribed by said Contract.

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011
Bid Date 3:00 pm, **Friday, May 30, 2025**


In compliance with the provisions of Section 4100-4107 of the Public Contract Code of the State of California, and any amendments, thereof, the undersigned bidder has set forth below the name and location of the place of business of each subcontractor who will perform work or labor or render service to the undersigned in or about the construction of the work to be performed. That portion of the work which will be done by each subcontractor for each subcontract in excess of one-half of one percent of the undersigned's total aggregate bid shall be listed..

SUBCONTRACTORS LIST		
SUBCONTRACTOR: Global Road Sealing LOCATION/ADDRESS: 10641 Sycamore AVE		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage) 5, p-101 crack sealing
LICENSE NO. **CLASS:** 757584 A,C-10,C-32	**EXPIRATION DATE:** 6 / 30 / 27	PHONE: (714) 893-0845
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )

SUBCONTRACTORS LIST		
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )
SUBCONTRACTOR: LOCATION/ADDRESS:		ITEM OF WORK: (bid item number - if partial amount of bid item, list amount or percentage)
LICENSE NO. **CLASS:**	**EXPIRATION DATE:** / /	PHONE: ( )

NOTE: This form may be reproduced and attached behind this page to list more Subcontractors.


Bidding Contractor: American Road Maintenance

Bidder's Signature 

Kyle Paulson / Officer

CERTIFICATE OF COMPLIANCE

This is to certify that all requirements for insurance of subcontractors as specified for this project will be met.



6/2/25

Signature of Principal — Dated

Kyle Paulson / Officer

Printed Name, Title of Principal

American Road Maintenance

Company

4554 E Eco Industrial Pl

Address

Tucson, AZ 85756

City, State & Zip

BIDDER'S STATEMENTS

REGARDING INSURANCE COVERAGE:
Bidder hereby certifies that he has reviewed the insurance coverage requirements specified in the Contract Specifications. Should he be awarded the contract for the work, Bidder further certifies that he can meet all the Contract Specification requirements for insurance including insurance coverage of his subcontractors.

REGARDING TITLE 13 OF THE CA CODE OF REGULATIONS, BIDDER'S FLEET:
Bidder must provide to the County, prior to executing the Contract, a true and correct copy of each valid Certificate of Reported Compliance, as described in section 2449(n) of Title 13 of the California Code of Regulations, for Bidder's fleet, and for each fleet of each subcontractor listed in Bidder's Bid, of vehicles subject to 13 CCR section 2449 that may be used in performance of the Contract.

REGARDING PUBLIC CONTRACT CODE SECTION 10232:
In accordance with Public Contract Code Section 10232, the Contractor hereby states, under penalty of perjury, that no more than one final unappealable finding of contempt of court by a Federal Court has been issued against the Contractor within the immediately preceding two year period because of the Contractor's failure to comply with an order of a Federal Court which orders the Contractor to comply with an order of the National Labor Relations Board.

REGARDING PUBLIC CONTRACT CODE SECTION 10162:
In accordance with Public Contract Code Section 10162, the Bidder shall complete, under penalty of perjury, the following questionnaire:

Has the bidder, any officer of the bidder, or any employee of the bidder who has proprietary interest in the bidder, ever been disqualified, removed, or otherwise prevented from bidding on, or completing, a federal, state, or local government project because of a violation of law or safety regulation?

Yes ____ No ✓

(If the answer is yes, explain the circumstances on a separate sheet of paper and attach to proposal)

6/2/25
Date

Signature of Principal

Kyle Paulson / Officer
Printed Name, Title of Principal

American Road Maintenance
Company

4554 E Eco Industrial Pl
Address

Tucson, AZ 85756
City, State & Zip

ANTI-FRAUD CERTIFICATION

County of Santa Barbara

Rehabilitate Tie-Down Apron

900 Airport Road, Santa Ynez, California

AIG Project No. 3-06-0243-XXX-2025 (Construction)
County Project No. 22011

In accordance with Public Contract Code Section 10285.1 (Chapter 376, Stats. 1985), the bidder hereby declares under penalty of perjury that the bidder **has ___, has not** ✓, been convicted within the preceding three years of any offenses referred to in that section, including any charge of fraud, bribery, collusion, conspiracy, or any other act in violation of any state or federal antitrust law in connection with the bidding upon award of, or performance of, any public works contract, as defined in Public Contract Code Section 1101, with any public entity, as defined in Public Contract Code Section 1100, including the Regents of the University of California or Trustees of the California State University.

The term "bidder" is understood to include any partner, member, officer, director, responsible managing officer, or responsible managing employee thereof, as referred to in Section 10285.1.

NOTE: The bidder must place a check mark after "has" or "has not" in one of the blank spaces provided.

6/2/25
Date

Signature of Principal

Kyle Paulson / Officer
Printed Name, Title of Principal

American Road Maintenance
Company

4554 E Eco Industrial Pl
Address

Tucson, AZ 85756
City, State & Zip

BIDDER'S BOND

KNOW ALL MEN BY THESE PRESENTS:

That we, American Road Maintenance, Inc. as Principal, and Travelers Casualty and Surety Company of America as Surety (hereinafter referred to as Surety), are held firmly bound unto the County of Santa Barbara, State of California (hereinafter called "Owner") in the penal sum of Ten Percent (10%) of the total aggregate amount of the bid of the Principal above named, submitted by said Principal to Owner for the work described below, for the payment of which sum in lawful money of the United States, well and truly to be made, we bind ourselves, our heirs, executors, administrators, and successors, jointly and severally, firmly by these presents. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications. In no case shall the liability of the Surety hereunder exceed the sum of Ten Percent (10%) of Total Amount Bid DOLLARS ($ 10% TAB). The condition of this obligation is such that a bid to Owner for certain construction specifically described as follows:

County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, California
County Project No. 22011-AIG XX

for which bids are to be opened on **3:00 pm, Friday, May 30, 2025,** has been submitted by Principal to Owner.

NOW, THEREFORE, if the aforesaid Principal shall not withdraw said bid within the period therein after the opening of the same, or, if no period be specified within one hundred twenty (120) days after said opening and shall within the period specified therefore, or, if no period be specified, within eight (8) days after the prescribed forms are presented to him for signature, enter into a written Contract with Owner, in the prescribed form, in accordance with the bid as accepted, and file the two Bonds with Owner, one to guarantee faithful performance and the other to guarantee payment for labor and materials, as required by law, then this obligation shall be null and void; otherwise, it shall remain in full force, virtue and affect.

Said Surety, for value received, hereby stipulates and agrees that no change, extension of time, alteration or addition to the terms of said Contract or to the work to be performed thereunder or the Specifications accompanying the same shall in any manner affects its obligations on this bond, and it does hereby waive notice of any change, extension, alteration, or addition.

It is hereby agreed that any progress payment made after the scheduled completion date will not constitute a waiver of any liquidated damages heretofore agreed upon.

In the event suit is brought upon said Bond by Owner and judgment is recovered, the Surety shall pay all costs incurred by Owner in such suit, including a reasonable attorney's fee to be fixed by the Court.

Death, Bankruptcy, Receivership, Going Out of Business for any reason, or incompetence of the

Principal shall not relieve the Surety of its obligations hereunder.

American Road Maintenance, Inc.
Name of Principal

6/2/25
Date

(Seal)
Signature of Principal Kyle Paulson / Officer

Travelers Casualty and Surety Company of America
Name of Surety

One Tower Square
Address

Hartford, CT 06183
City, State & Zip

May 22, 2025
Date

(Seal)
Signature of Surety's Attorney-In-Fact
Sean J. McCauley, Jr.

Surety's Agent for Service of Process (located within the State of California):

McCauley Bond Agency ATTN: Sean McCauley, Jr.
Name of Agent

2 Ritz Carlton Drive, Suite 204
Address

Dana Point, CA 92629
City, State & Zip

Office No. 214-989-7047
Telephone Number

NOTE: Signatures of those executing for Surety MUST be properly acknowledged. This form may be reproduced for transmittal to the Surety for execution and attached to the front of the original Bid Bond Form.

NOTARY ACKNOWLEDGEMENT

State of Texas

County of Dallas

On this the 22nd day of MAY, 20 25, before me, Ashlyn Simchik (name of notary), personally appeared SEAN J. McCAULEY, JR., known to me (or satisfactorily proven) to be the person(s) whose name(s) is (is or are) subscribed to the within instrument and acknowledged that he (he/she/they) executed the same for the purposes therein contained.

In witness whereof, I hereunto set my hand.

Date: MAY 22, 2025

Ashlyn Simchik

Notary Public

ASHLYN SIMCHIK
NOTARY PUBLIC
STATE OF TEXAS
MY COMM. EXP. 06/05/27
NOTARY ID 13433618-2

Print Name: Ashlyn Simchik

Notary ID: 13433618-2

My Commission Expires:

June 5, 2027

TRAVELERS

Travelers Casualty and Surety Company of America
Travelers Casualty and Surety Company
St. Paul Fire and Marine Insurance Company

POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS: That Travelers Casualty and Surety Company of America, Travelers Casualty and Surety Company, and St. Paul Fire and Marine Insurance Company are corporations duly organized under the laws of the State of Connecticut (herein collectively called the "Companies"), and that the Companies do hereby make, constitute and appoint SEAN J MCCAULEY JR of DALLAS , **Texas** , their true and lawful Attorney(s)-in-Fact to sign, execute, seal and acknowledge any and all bonds, recognizances, conditional undertakings and other writings obligatory in the nature thereof on behalf of the Companies in their business of guaranteeing the fidelity of persons, guaranteeing the performance of contracts and executing or guaranteeing bonds and undertakings required or permitted in any actions or proceedings allowed by law.

IN WITNESS WHEREOF, the Companies have caused this instrument to be signed, and their corporate seals to be hereto affixed, this **21st** day of **April**, 2021.

State of Connecticut

City of Hartford ss.

By: _____
Robert L. Raney, Senior Vice President

On this the 21st day of April, **2021**, before me personally appeared **Robert L. Raney**, who acknowledged himself to be the Senior Vice President of each of the Companies, and that he, as such, being authorized so to do, executed the foregoing instrument for the purposes therein contained by signing on behalf of said Companies by himself as a duly authorized officer.

IN WITNESS WHEREOF, I hereunto set my hand and official seal.

My Commission expires the **30th** day of **June**, **2026**

_____
Anna P. Nowik, Notary Public

This Power of Attorney is granted under and by the authority of the following resolutions adopted by the Boards of Directors of each of the Companies, which resolutions are now in full force and effect, reading as follows:

RESOLVED, that the Chairman, the President, any Vice Chairman, any Executive Vice President, any Senior Vice President, any Vice President, any Second Vice President, the Treasurer, any Assistant Treasurer, the Corporate Secretary or any Assistant Secretary may appoint Attorneys-in-Fact and Agents to act for and on behalf of the Company and may give such appointee such authority as his or her certificate of authority may prescribe to sign with the Company's name and seal with the Company's seal bonds, recognizances, contracts of indemnity, and other writings obligatory in the nature of a bond, recognizance, or conditional undertaking, and any of said officers or the Board of Directors at any time may remove any such appointee and revoke the power given him or her; and it is

FURTHER RESOLVED, that the Chairman, the President, any Vice Chairman, any Executive Vice President, any Senior Vice President or any Vice President may delegate all or any part of the foregoing authority to one or more officers or employees of this Company, provided that each such delegation is in writing and a copy thereof is filed in the office of the Secretary; and it is

FURTHER RESOLVED, that any bond, recognizance, contract of indemnity, or writing obligatory in the nature of a bond, recognizance, or conditional undertaking shall be valid and binding upon the Company when (a) signed by the President, any Vice Chairman, any Executive Vice President, any Senior Vice President or any Vice President, any Second Vice President, the Treasurer, any Assistant Treasurer, the Corporate Secretary or any Assistant Secretary and duly attested and sealed with the Company's seal by a Secretary or Assistant Secretary; or (b) duly executed (under seal, if required) by one or more Attorneys-in-Fact and Agents pursuant to the power prescribed in his or her certificate or their certificates of authority or by one or more Company officers pursuant to a written delegation of authority; and it is

FURTHER RESOLVED, that the signature of each of the following officers: President, any Executive Vice President, any Senior Vice President, any Vice President, any Assistant Vice President, any Secretary, any Assistant Secretary, and the seal of the Company may be affixed by facsimile to any Power of Attorney or to any certificate relating thereto appointing Resident Vice Presidents, Resident Assistant Secretaries or Attorneys-in-Fact for purposes only of executing and attesting bonds and undertakings and other writings obligatory in the nature thereof, and any such Power of Attorney or certificate bearing such facsimile signature or facsimile seal shall be valid and binding upon the Company and any such power so executed and certified by such facsimile signature and facsimile seal shall be valid and binding on the Company in the future with respect to any bond or understanding to which it is attached.

I, **Kevin E. Hughes**, the undersigned, Assistant Secretary of each of the Companies, do hereby certify that the above and foregoing is a true and correct copy of the Power of Attorney executed by said Companies, which remains in full force and effect.

Dated this **22nd** day of **May** , **2025** .

_____
Kevin E. Hughes, Assistant Secretary

To verify the authenticity of this Power of Attorney, please call us at 1-800-421-3880.
Please refer to the above-named Attorney(s)-in-Fact and the details of the bond to which this Power of Attorney is attached.

No. 6516

STATE OF CALIFORNIA

DEPARTMENT OF INSURANCE

SAN FRANCISCO

Amended

Certificate of Authority

THIS IS TO CERTIFY *that, pursuant to the Insurance Code of the State of California,*

Travelers Casualty and Surety Company of America

of Hartford, Connecticut, organized under the laws of Connecticut, subject to its Articles of Incorporation or other fundamental organizational documents, is hereby authorized to transact within this State, subject to all provisions of this Certificate, the following classes of insurance:

Fire, Marine, Surety, Disability, Plate Glass, Liability, Workers' Compensation, Common Carrier Liability, Boiler and Machinery, Burglary, Credit, Sprinkler, Team and Vehicle, Automobile, Aircraft and Miscellaneous

as such classes are now or may hereafter be defined in the Insurance Laws of the State of California.

THIS CERTIFICATE *is expressly conditioned upon the holder hereof now and hereafter being in full compliance with all, and not in violation of any, of the applicable laws and lawful requirements made under authority of the laws of the State of California as long as such laws or requirements are in effect and applicable, and as such laws and requirements now are, or may hereafter be changed or amended.*

IN WITNESS WHEREOF, *effective as of the 1st day of July, 1997, I have hereunto set my hand and caused my official seal to be affixed this 16th day of June, 1997.*

Fee: $ 92.00
Rec. No.
Filed: 5/28/97

Chuck Quackenbush
Insurance Commissioner

By

Victoria S. Sidbury
Deputy

Certification

I, the undersigned Insurance Commissioner of the State of California, do hereby certify that I have compared the above copy of Certificate of Authority with the duplicate of original now on file in my office, and that the same is a full, true, and correct transcript thereof, and of the whole of said duplicate, and said Certificate of Authority is now in full force and effect.

IN WITNESS WHEREOF, *I have set my hand and caused my official seal to be affixed this 29th day of September, 2020.*

Ricardo Lara
Insurance Commissioner

By

Magnolia Gutierrez

NONCOLLUSION AFFIDAVIT

In accordance with Public Contract Code § 7106. Kyle Paulson
(Bidder's full name)

being first duly sworn, deposes and says that he or she is Officer
(Bidder's title)

of American Road Maintenance
(Company's name)

the party making the foregoing Bid, that the Bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the Bid is genuine and not collusive or sham; that the Bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham Bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any Bidder or anyone else to put in a sham Bid, or that anyone shall refrain from bidding; that the Bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the Bid price of the Bidder or any other Bidder, or to fix any overhead, profit, or cost element of the Bid price, or of that of any other Bidder, or to secure any advantage against the public body awarding the contract of anyone interested in the proposed Contract; that all statements contained in the Bid are true; and further, that the Bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, to any corporation, partnership, company, association, organization, bid depository, or to any member or agent thereof to effectuate a collusive or sham Bid and has not paid, and will not pay, any person or entity for such purpose.

Any person executing this declaration on behalf of a bidder that is a corporation, partnership, joint venture, limited liability company, limited liability partnership, or any other entity, hereby represents that he or she has full power to execute, and does execute, this declaration on behalf of the bidder.

I declare under penalty of perjury under the laws of the State of California that the foregoing is true and correct.

SIGNATURE BLOCK **(**Signature Block **must be completed in** ink**& changes must be** initialed**.)**
Bidder's Signature: _____ **Date:** 6/2/25
Bidder's Name & Title (Print): Kyle Paulson / Officer
At CITY: Tucson STATE: AZ

NONLOBBYING CERTIFICATION FOR FEDERAL-AID CONTRACTS

The prospective participant certifies, by signing and submitting this bid or proposal, to the best of his or her knowledge and belief, that:

(l) No Federal appropriated funds have been paid or will be paid, by or on behalf of the undersigned, to any person for influencing or attempting to influence an officer or employee of any Federal agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with the awarding of any Federal contract, the making of any Federal grant, the making of any Federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment, or modification of any Federal contract, grant, loan, or cooperative agreement.

(2) If any funds other than Federal appropriated funds have been paid or will be paid to any person for influencing or attempting to influence an officer or employee of any Federal agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with this Federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form-LLL, "Disclosure of Lobbying Activities," in conformance with its instructions.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by Section 1352, Title 31, U.S. Code. Any person who fails to file the required certification shall be subject to a civil penalty of not less than $10,000 and not more than $100,000 for each such failure.

The prospective participant also agrees by submitting his or her bid or proposal that he or she shall require that the language of this certification be included in all lower tier subcontracts, which exceed $100,000 and that all such subrecipients shall certify and disclose accordingly.

DISCLOSURE OF LOBBYING ACTIVITIES FORM

COMPLETE THIS FORM TO DISCLOSE LOBBYING ACTIVITIES PURSUANT TO 31 U.S.C. 1352

Standard Form LLL Rev. 09-12-97

1. Type of Federal Action:

☐ a. contract
b. grant
c. cooperative agreement
d. loan
e. loan guarantee
f. loan insurance

2. Status of Federal Action:

☐ a. bid/offer/application
b. initial award
c. post-award

3. Report Type:

☐ a. initial
b. material change

For Material Change Only:
Year _____ quarter _____
date of last report _____

4. Name and Address of Reporting Entity

☐ Prime ☐ Subawardee
Tier _____ , if known

Congressional District, if known

5. If Reporting Entity in No. 4 is Subawardee, Enter Name and Address of Prime:

Congressional District, if known

6. Federal Department/Agency:

7. Federal Program Name/Description:

CFDA Number, if applicable _____

8. Federal Action Number, if known:

9. Award Amount, if known:

10. a. Name and Address of Lobby Entity
(If individual, last name, first name, MI)

b. Individuals Performing Services (including address if different from No. 10a)
(last name, first name, MI)

(attach Continuation Sheet(s) if necessary)

11. Amount of Payment (check all that apply)

$ _____ ☐ actual ☐ Planned

12. Form of Payment (check all that apply):

☐ a. cash
☐ b. in-kind; specify: nature _____
value _____

13. Type of Payment (check all that apply)

☐ a. retainer
☐ b. one-time fee
☐ c. commission
☐ d. contingent fee
☐ e deferred
☐ f. other, specify _____

14. Brief Description of Services Performed or to be performed and Date(s) of Service, including officer(s), employee(s), or member(s) contacted, for Payment Indicated in Item 11:

(attach Continuation Sheet(s) if necessary)

15. Continuation Sheet(s) attached: **Yes** ☐ **No** ☐

No lobbying activities

16. Information requested through this form is authorized by Title 31 U.S.C. Section 1352. This disclosure of lobbying reliance was placed by the tier above when his transaction was made or entered into. This disclosure is required pursuant to 31 U.S.C. 1352. This information will be reported to Congress semiannually and will be available for public inspection. Any person who fails to file the required disclosure shall be subject to a civil penalty of not less than $10,000 and not more than $100,000 for each such failure.

Signature: _____
Print Name: Kyle Paulson
Title: Officer
Telephone No.: 480-309-7102 Date: 6/2/25

Federal Use Only:

Authorized for Local Reproduction
Standard Form – LLL

INSTRUCTIONS FOR COMPLETION OF SF-LLL, DISCLOSURE OF LOBBYING ACTIVITIES

This disclosure form shall be completed by the reporting entity, whether subawardee or prime Federal recipient, at the initiation or receipt of covered Federal action or a material change to previous filing pursuant to title 31 U.S.C. section 1352. The filing of a form is required for such payment or agreement to make payment to lobbying entity for influencing or attempting to influence an officer or employee of any agency, a Member of Congress an officer or employee of Congress or an employee of a Member of Congress in connection with a covered Federal action. Attach a continuation sheet for additional information if the space on the form is inadequate. Complete all items that apply for both the initial filing and material change report. Refer to the implementing guidance published by the Office of Management and Budget for additional information.

1. Identify the type of covered Federal action for which lobbying activity is and/or has been secured to influence, the outcome of a covered Federal action.
2. Identify the status of the covered Federal action.
3. Identify the appropriate classification of this report. If this is a follow-up report caused by a material change to the information previously reported, enter the year and quarter in which the change occurred. Enter the date of the last, previously submitted report by this reporting entity for this covered Federal action.
4. Enter the full name, address, city, state and zip code of the reporting entity. Include Congressional District if known. Check the appropriate classification of the reporting entity that designates if it is or expects to be a prime or subaward recipient. Identify the tier of the subawardee, e.g., the first subawardee of the prime is the first tier. Subawards include but are not limited to subcontracts, subgrants and contract awards under grants.
5. If the organization filing the report in Item 4 checks "Subawardee" then enter the full name, address, city, state and zip code of the prime Federal recipient. Include Congressional District, if known.
6. Enter the name of the Federal agency making the award or loan commitment. Include at least one organization level below agency name, if known. For example, Department of Transportation, United States Coast Guard.
7. Enter the Federal program name or description for the covered Federal action (item 1). If known, enter the full Catalog of Federal Domestic Assistance (CFDA) number for grants, cooperative agreements, loans and loan commitments.
8. Enter the most appropriate Federal identifying number available for the Federal action identification in item 1 (e.g., Request for Proposal (RFP) number, Invitation for Bid (IFB) number, grant announcement number, the contract grant. or loan award number, the application/proposal control number assigned by the Federal agency). Include prefixes, e.g., "RFP-DE-90-001."
9. For a covered Federal action where there has been an award or loan commitment by the Federal agency, enter the Federal amount of the award/loan commitments for the prime entity identified in item 4 or 5.
10. (a) Enter the full name, address, city, state and zip code of the lobbying entity engaged by the reporting entity identified in item 4 to influenced the covered Federal action.
    (b) Enter the full names of the individual(s) performing services and include full address if different from 10 (a). Enter Last Name, First Name and Middle Initial (Ml).
11. Enter the amount of compensation paid or reasonably expected to be paid by the reporting entity (item 4) to the lobbying entity (item 10). Indicate whether the payment has been made (actual) or will be made (planned). Check all boxes that apply. If this is a material change report, enter the cumulative amount of payment made or planned to be made.
12. Check the appropriate box(es). Check all boxes that apply. If payment is made through an in-kind

contribution, specify the nature and value of the in-kind payment.

13. Check the appropriate box(es). Check all boxes that apply. If other, specify nature.
14. Provide a specific and detailed description of the services that the lobbyist has performed or will be expected to perform and the date(s) of any services rendered. Include all preparatory and related activity not just time spent in actual contact with Federal officials. Identify the Federal officer(s) or employee(s) contacted or the officer(s) employee(s) or Member(s) of Congress that were contacted.
15. Check whether or not a continuation sheet(s) is attached.
16. The certifying official shall sign and date the form, print his/her name title and telephone number.

Public reporting burden for this collection of information is estimated to average 30 minutes per response, including time for reviewing instruction, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information.

LOCAL AGENCY BIDDER – DBE – INFORMATION

This information may be submitted with your bid proposal. If it is not, and you are the apparent low bidder or the second or third low bidder, it must be submitted and received as specified in Section 2-1.02B of the Special Provisions. Failure to submit the required DBE information will be grounds for finding the proposal nonresponsive.

CO.-RTE.-K.P.: COUNTY PROJECT NO. 22011
CONTRACT NO.: AIG Project No. 3-06-0243-XXX-2025
BID AMOUNT: $ 388,250
BID OPENING DATE: 6/2/25
BIDDER'S NAME: American Road Maintenance
DBE GOAL FROM CONTRACT: 38,835
DBE PRIME CONTRACTOR CERTIFICATION [1]: Not a DBE

CONTRACT ITEM NO.	ITEM OF WORK AND DESCRIPTION OR SERVICES TO BE SUBCONTRACTED OR MATERIALS TO BE PROVIDED [2]	DBE CERT. NO.	NAME OF DBEs (Must be certified on the date bids are opened - include DBE address and phone number)	DOLLAR AMOUNT DBE [3]
5	P-101 Crack seal	031176	Global Road Sealing	38,835

IMPORTANT: Identify all DBE firms being claimed for credit, regardless of tier. Copies of the DBE quotes are required. Names of the First Tier DBE Subcontractors and their respective item(s) of work listed above shall be consistent, where applicable, with the names and items of work in the "List of Subcontractors" submitted with your bid pursuant to the Subcontractors Listing Law and Section 2-1.01, "General," of the Special Provisions.

1. DBE prime contractors shall enter their DBE certification number. DBE prime contractors shall indicate all work to be performed by DBEs including work performed by its own forces.

2. If 100% of item is not to be performed or furnished by DBE, describe exact portion of item to be performed or furnished by DBE.

3. See Section 2-1.02, "Disadvantaged Business Enterprise," to determine the credit allowed for DBE firms.

Total Claimed Participation

$ 38,835

10 %

Signature of Bidder

6/2/25 — Date

480-309-7102 — (Area Code) Tel. No.

Kyle Paulson — Person to Contact (Please Type or Print)

CT Bidder - DBE Information (Rev 09-28-99)

DBE INFORMATION-GOOD FAITH EFFORTS

N/A meeting goal

Federal-aid Project No. AIG Project No. 3-06-0243-XXX-2025 (Construction) Bid Opening Date 6/2/25

The County of Santa Barbara established a Disadvantaged Business Enterprise (DBE) goal of **10.0%** for this project. The information provided herein shows that adequate good faith efforts were made.

A. The names and dates of each publication in which a request for DBE participation for this project was placed by the bidder (please attach copies of advertisements or proofs of publication):

Publications	Dates of Advertisement

B. The names and dates of written notices sent to certified DBEs soliciting bids for this project and the dates and methods used for following up initial solicitations to determine with certainty whether the DBEs were interested (please attach copies of solicitations, telephone records, fax confirmations, etc.):

Names of DBEs Solicited	Date of Inital Solicitation	Follow Up Methods and Dates

C. The items of work which the bidder made available to DBE firms, including, where appropriate, any breaking down of the contract work items (including those items normally performed by the bidder with its own forces) into economically feasible units to facilitate DBE participation. It is the bidder's responsibility to demonstrate that sufficient work to facilitate DBE participation was made available to DBE firms.

Items of Work	Breakdown of Items

D. The names, addresses and phone numbers of rejected DBE firms, the reasons for the bidder's rejection of the DBEs, and the firms selected for that work (please attach copies of quotes from the firms involved):

Names, addresses and phone numbers of rejected DBEs and the reasons for the bidder's rejection of the DBEs:

_____
_____
_____
_____

Names, addresses and phone numbers of firms selected for the work above:

_____
_____
_____
_____

E. Efforts made to assist interested DBEs in obtaining bonding, lines of credit or insurance, and any technical assistance or information related to the plans, specifications and requirements for the work which was provided to DBEs:

_____
_____
_____
_____

F. Efforts made to assist interested DBEs in obtaining necessary equipment, supplies, materials, or related assistance or services, excluding supplies and equipment the DBE subcontractor purchases or leases from the prime contractor or its affiliate.

_____
_____
_____
_____

G. The names of agencies, organizations or groups contacted to provide assistance in contacting, recruiting and using DBE firms (please attach copies of requests to agencies and any responses received, i.e., lists, Internet page download, etc.).

Name of Agency/Organization	Method/Date of Contact	Results

H. Any additional data to support a demonstration of good faith efforts (use additional sheets if necessary):(Refer to the Caltrans *Local Assistance Procedures Manual* for instructions)

BUY AMERICAN PREFERENCE

As a matter of bid responsiveness, the bidder or offeror must complete, sign, date, and submit this certification statement with their proposal. The bidder or offeror must indicate how they intend to comply with 49 USC § 50101 by selecting one on the following certification statements. These statements are mutually exclusive. Bidder must select one or the other (not both) by inserting a checkmark (✓) or the letter "X".

☑ Bidder or offeror hereby certifies that it will comply with 49 USC § 50101 by:

a) Only installing steel and manufactured products produced in the United States, or;
b) Installing manufactured products for which the FAA has issued a waiver as indicated by inclusion on the current FAA Nationwide Buy American Waivers Issued listing, or;
c) Installing products listed as an Excepted Article, Material or Supply in Federal Acquisition Regulation Subpart 25.108.

By selecting this certification statement, the bidder or offeror agrees:

1. To provide to the Owner evidence that documents the source and origin of the steel and manufactured product.
2. To faithfully comply with providing US domestic product
3. To furnish US domestic product for any waiver request that the FAA rejects
4. To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

☐ The bidder or offeror hereby certifies it cannot comply with the 100% Buy American Preferences of 49 USC § 50101(a) but may qualify for either a Type 3 or Type 4 waiver under 49 USC § 50101(b). By selecting this certification statement, the apparent bidder or offeror with the apparent low bid agrees:

1. To the submit to the Owner within 15 calendar days of the bid opening, a formal waiver request and required documentation that support the type of waiver being requested.
2. That failure to submit the required documentation within the specified timeframe is cause for a non-responsive determination may result in rejection of the proposal.
3. To faithfully comply with providing US domestic products at or above the approved US domestic content percentage as approved by the FAA.
4. To refrain from seeking a waiver request after establishment of the contract, unless extenuating circumstances emerge that the FAA determines justified.

Required Documentation

Type 3 Waiver - The cost of the item components and subcomponents produced in the United States is more that 60% of the cost of all components and subcomponents of the "item". The required documentation for a type 3 waiver is:

a) Listing of all product components and subcomponents that are not comprised of 100% US domestic content (Excludes products listed on the FAA Nationwide Buy American Waivers Issued listing and products excluded by Federal Acquisition Regulation Subpart 25.108; products of unknown origin must be considered as non-domestic products in their entirety)
b) Cost of non-domestic components and subcomponents, excluding labor costs associated


with final assembly at place of manufacture.

c) Percentage of non-domestic component and subcomponent cost as compared to total "item" component and subcomponent costs, excluding labor costs associated with final assembly at place of manufacture.

Type 4 Waiver – Total cost of project using US domestic source product exceeds the total project cost using non-domestic product by 25%. The required documentation for a type 4 of waiver is:

a) Detailed cost information for total project using US domestic product
b) Detailed cost information for total project using non-domestic product

False Statements: Per 49 USC § 47126, this certification concerns a matter within the jurisdiction of the Federal Aviation Administration and the making of a false, fictitious or fraudulent certification may render the maker subject to prosecution under Title 18, United States Code.

6/2/25	
Date	Signature
American Road Maintenance	Officer
Company Name	Title

REQUIRED CONTRACT PROVISIONS FOR AIRPORT IMPROVEMENT PROGRAM AND FOR OBLIGATED SPONSORS

1. ACCESS TO RECORDS AND REPORTS. (Reference: 2 CFR § 200.334; 2 CFR § 200.337; FAA Order 5100.38)
2. AFFIRMATIVE ACTION REQUIREMENT. (Reference: 41 CFR part 60-4; Executive Order 11246)
3. BREACH OF CONTRACT TERMS. (Reference 2 CFR § 200 Appendix II(A))
4. BUY AMERICAN PREFERENCE. (Reference: 49 USC § 50101)
5. CIVIL RIGHTS – GENERAL. (Reference: 49 USC § 47123)
6. CIVIL RIGHTS – TITLE VI ASSURANCES. (Reference: 49 USC § 47123)
7. CLEAN AIR AND WATER POLLUTION CONTROL. (Reference: 2 CFR § 200, Appendix II(G))
8. CONTRACT WORKHOURS AND SAFETY STANDARDS ACT REQUIREMENTS. (Reference: 2 CFR § 200, Appendix II(E))
9. COPELAND "ANTI-KICKBACK" ACT (Reference: 2 CFR § 200, Appendix II(D); 29 CFR parts 3 & 5)
10. DAVIS BACON REQUIREMENTS. (Reference: 2 CFR § 200, Appendix II(D); 29 CFR Part 5)
11. DEBARMENT AND SUSPENSION (NON-PROCUREMENT). (Reference: 2 CFR part 180 (Subpart C), 2 CFR part 1200, DOT Order 4200.5 DOT Suspension & Debarment Procedures & Ineligibility)
12. DISADVANTAGED BUSINESS ENTERPRISE. (Reference: 49 CFR part 26)
13. DISTRACTED DRIVING. (Reference: Executive Order 13513, DOT Order 3902.10)
14. PROHIBITION ON CERTAIN TELECOMMUNICATIONS AND VIDEO SURVEILLANCE SERVICES OR EQUIPMENT (Reference 2 CFR § 200, Appendix II(K), 2 CFR § 200.216)
15. DRUG FREE WORKPLACE (Reference: 49 CFR Part 29)
16. EQUAL EMPLOYMENT OPPORTUNITY (E.E.O.). (Reference: 2 CFR 200, Appendix II(C); 41 CFR § 60-1.4; 41 CFR § 60-4.3; Executive Order 11246)
17. FEDERAL FAIR LABOR STANDARDS ACT (FEDERAL MINIMUM WAGE). (Reference: 29 USC § 201, et seq.)
18. LOBBYING AND INFLUENCING FEDERAL EMPLOYEES. (Reference: 31 U.S.C. § 1352 – Byrd Anti-Lobbying Amendment; 2 CFR part 200, Appendix II(J); 49 CFR part 20, Appendix A)
19. PROHIBITION OF SEGREGATED FACILITIES. (Reference: 41 CFR § 60-1.8)
20. OCCUPATIONAL SAFETY AND HEALTH ACT OF 1970. (Reference 20 CFR part 1910)
21. PROCUREMENT OF RECOVERED MATERIALS. (Reference: 2 CFR § 200.322, 40 CFR part 247)
22. RIGHT TO INVENTIONS. (Reference 2 CFR § 200, Appendix II(F); 37 CFR §401)
23. SEISMIC SAFETY (Reference: National Earthquake Hazards Reduction Program)
24. TAX DELINQUENCY AND FELONY CONVICTIONS (Reference: Section 8113 of the Consolidated Appropriations Act, 2022)
25. TERMINATION OF CONTRACT. (Reference: 2 CFR § 200 Appendix II(A))
26. TRADE RESTRICTION CERTIFICATION. (Reference: 49 USC § 50104; 49 CFR part 30)
27. VETERAN'S PREFERENCE. (Reference: 49 USC § 47112(c))
28. DOMESTIC PREFERENCES FOR PROCUREMENTS (Reference 2 CFR § 200.322, 2 CFR Part 200, Appendix II(L)

The contractor (including all subcontractors) shall insert the federal contract provisions and clauses located in the appendix in each contract and subcontract. The contractor (or subcontractor) shall incorporate applicable requirements of the contract provisions by reference for work done under any purchase orders, rental agreements and other agreements for supplies or services. The prime contractor will be responsible for compliance with these contract provisions by any subcontractor, lower-tier subcontractor or service provider. No modifications to the provisions are allowed. Minor additions covering state or sponsor requirements may be included in a separate supplemental specification, provided they do not conflict with federal laws and regulations and do not change the intent of the required contract provision. By signing this signature page ensures that the contractor agrees with all terms of the required federal contract provisions.

Signature of Bidder

6/2/25

Date



List of Airfield Jobs Completed in the Last Three Years

Airport	Job Total
Alamo Landing Field	$21,661.20
Andrew Othole Memorial Airport	$199,205.00
ASI	$20,078.10
Aspen CO-Proline	$44,138.70
Aspen/Pitkin County Airport	$1,940,052.74
Atmore Airport	$89,250.00
Atoka Municipal Airport	$190,955.40
Atwood Rawlins County Airport	$157,242.30
Aztec Municipal Airport	$133,761.44
Banning Municipal Airport	$324,666.05
Beatty Airport	$127,545.00
Belen Airport	$204,082.80
Bell Helicopter Practice Airfield	$188,721.50
Benson Airport	$182,162.03
Bert Mooney Airport	$772,981.86
Big Sky Field Airport	$85,910.31
Bluegrass Airport	$41,878.00
Boundary County Airport	$196,780.00
Brownwood Airport	$252,710
Bullhead City Airport	$59,362.30
Burbank Airport	$58,641.50
Camdenton Airport	$178,659.80
Camp Pendleton	$241,405.50
Carson City Airport	$284,983.40
Caruthersville Memorial Airport	$280,199.70
Casper/Natrona County Intnl Airport	$928,301.53
Centenniel Airport	$176,250.00
Central Colorado Regional Airport	$271,587.90
Chandler Municipal Airport	$97,710.00
Chattanooga Airport	$30,000.00
Clayton Airport	$47,762.50
Cleburne Regional Airport	$166,333.50
Cochise Aviation College	$131,173.20
Harriet Alexander Field-Salida	$165,771.00
Kit Carson County Airport-Burlington	$203,362.70
Converse County Airport	$41,626.72
Dawson Community Airport Glendive MT	$403,747.98
Delta Regional Airport	$162,970.00
Deming Municipal Airport	$171,040.60
Driggs-Reed Memorial Airport	$244,223.45
Durango Airport	$202,611.40
Espanola Municipal Airport	$294,375.00
Fall River Mills Airport	$128,715.00
Farmington Airport	$210,599.15
Fort Morgan	$122,342.50
French Valley Airport	$120,730.00
Fresno Yosemite Itnl Airport	$184,800.00

Airport	Job Total
FT Dodge	$661,386.60
Ft Worth	$565,340.00
Gallup Municipal Airport	$220,236.25
Gibson County Airport	$124,996.25
Granby-Grand County Airport	$24,536.05
Grand Junction Regional Airport	$144,225.00
Buchanan Airport	$70,400.00
Grant County Airport	$138,100.00
Great Falls International Airport	$1,222,598.13
Greenlee County Airport	$146,625.00
Hanford	$313,853.70
Hatch Municipall Airport	$212,920.75
Havre City Airport	$316,405.48
Hawthorne Industrial Airport (NV)	$372,740.20
Hawthorne Municipal Airport	$374,458.11
Hobby Airport	$68,902.75
Holyoke Airport	$192,713.50
Hulett Municipal Airport	$246,109.75
Jacqueline Cochran Regional Airport	$1,028,663.42
Johnson County Airport	$114,128.62
las Cruces Airport	$383,002.50
Las Vegas NM Airport	$147,900.00
LAWA	$157,270.00
Lemhi County Airport	$99,485.00
Long Beach Airport	$84,226.00
Lusk Airport	$77,803.43
Main Street Materials	$43,792.00
Meeker Coulter Field Airport	$239,270.34
Midway Island Atoll	$3,479,507.51
Millard Airport	$136,064.75
Mission Field	$174,285.35
Mobile Regional Airport	$68,190.06
Mondell Field Airport	$72,539.97
Monte Vista	$238,838.57
Moriarty Municipal Airport	$179,176.20
NE Wyoming Airport	$95,461.82
NW Arkansas Memorial Airport	$99,895.10
Oakdale Municipal Airport	$115,282.50
Oceanside Municipal Airport	$57,850.00
Owyhee Airport	$214,853.02
Palo Alto Airport	$27,625.00
Perry Stokes-Trinidad	$142,335.00
Plains Airport	$138,911.39
Poplar Airport	$138,754.64
Portales Municipal Airport	$104,525.00
Prescott Airport	$135,502.50
Pueblo Airport	$387,217.35

Airport	Job Total
Questa Municipal Airport	$148,285.50
Rangely Airport	$283,140.08
Raton Municipal Airport	$326,836.00
Red Bluff Municipal Airport	$301,885.00
Reedley Municipal Airport	$44,782.00
Rolle Airport	$84,737.00
Rominger Airport	$147,037.50
Ronan Airport	$170,970.82
Roswell International Airprot	$254,150.99
Route 25	$44,265.50
Salinas Airport	$393,708.00
San Angelo Airport	$702,404.90
San Carlos Apache Airport	$9,160.00
Santa Fe Airport	$282,470.00
Santa Rosa Route 66 Airport	$126,999.50
Scotts Bluff Airport	$832,179.30
Shawnee Regional Airport	$498,097.95
Shelby Airport	$201,423.52
Sheridan County Airport	$426,351.50
Sherwood Airport	$125,674.36
Sidney-Richland Regional Airport	$533,956.64
Sioux Falls Regional Airport	$113,525.00
Slayton Airport	$119,937.50
Socorro Municipal Airport	$207,270.00
Stockton Metro Airport	$87,162.00
Taos Regional Airport	$296,553.54
Taylor Airport	$273,504.05
Telluride Regional Airport	$394,580.25
Texas A&M	$1,004,939.95
Tucson Drag Strip	$8,750.00
Tucson International Airport	$48,858.25
Tucumcari Municipal Airport	$349,482.25
Ukiah Municipal Airport	$110,775.00
Van Nuys Airport	$183,480.65
Vaughn Municipal Airport	$84,660.00
Victoria Regional Airport	$99,312.00
Wells Municipal Airport	$148,200.50
Western Emulsions.	$500.00
Wheatland County Airport	$85,787.06
White Sulpher Springs Airport	$133,218.80
Wickenburg Airport	$166,411.93
Willits Municipal Airport	$78,900.00
Yampa regional Airport	$153,218.40
Yellowstone Airport	$274,320.88
TOTAL	$34,691,127.39

AMERICAN ROAD MAINTENANCE

"We go the extra mile"

KEY PERSONNEL EXPERIENCE

Joe Coghill – Owner

- 20 plus years of experience in asphalt maintenance specializing in airfield pavements
- Proficient in the processes of seal coating, crack sealing, joint sealing, paint and rubber removal, pavement markings and layout, and friction testing to meet all FAA requirements
- Supervises contracts, the bid process and scheduling of crews

Kyle Paulson – Officer

- 10 plus years of experience in asphalt maintenance specializing in airfield pavements
- Proficient in the processes of seal coating, crack sealing, joint sealing, paint and rubber removal, pavement markings and layout, and friction testing to meet all FAA requirements
- Estimator and contract administrator

Dan Mueller – Project Manager

- 8 plus years of experience in asphalt maintenance specializing in airfield pavements
- Proficient in the processes of seal coating, crack sealing, joint sealing, paint and rubber removal, pavement markings and layout, and friction testing to meet all FAA requirements
- Certified friction tester
- Supervises all projects and the coordination of personnel

Walt Bills – Foreman

- 25 plus years of experience in construction as a CDL driver and equipment operator
- Proficient in the processes of seal coating, crack sealing, joint sealing, paint and rubber removal, pavement markings and layout, and friction testing to meet all FAA requirements
- Works on site as a crew leader and liaison for the engineers and management

Derek Hyatt – Asphalt Distributor Driver

- 10 plus years of experience in construction as a CDL driver and equipment operator
- Proficient in the processes of seal coating, crack sealing, joint sealing, paint and rubber removal, pavement markings and layout, and friction testing to meet all FAA requirements
- Specializes in the application of the P-608 and P-608R process on airfields

Mario Alfaro – Airfield Marking Foreman

- 25 plus years in pavement markings
- Specializes in the layout and placement of pavement marking on airfields
- Assures all striping of the project meets the requirements and specifications of the owner and engineer

AMERICAN ROAD MAINTENANCE

"We go the extra mile"

List of Available Equipment

6	Ram 2500 Utility Trucks
3	Ram 3500 Flatbed Utility Trucks
3	Bearcat Asphalt Distributors with Sand Applicators
1	Etneyre Asphalt Distributor with Sand Applicator
3	Friction Testers
2	Water blasting paint removal trucks
6	Graco ride on striping machines
2	Truck mounted tac pot kettles
4	Crack seal routers
2	Crafco crack seal kettles
1	Vacuum sweeper
4	Billy Goat blowers
2	Transport tankers
2	Forklifts
2	Air compressors
2	Scarifiers

AMERICAN ROAD MAINTENANCE

"We go the extra mile"

BIDDING POWER OF ATTORNEY

Know all men by these presents: American Road Maintenance, Inc doing business as a Corporation under the laws of the State of Illinois have a principal place of business at 4554 E Eco Industrial Pl, AZ 85756, hereby constitutes and appoints Kyle Paulson to act for and on its behalf as a true and lawful agent and attorney of the grantor and in the name, place and stead of said grantor, from this date, in the United States either in writing, electronically, or by other authorized means, to:

Endorse or sign documents required in connection with the bidding and or securing bids for said grantor;

Perform any act on condition, which may be required in connection with such bids;

Sign or swear to any document and to perform any act that may be necessary in connection with the preparation and submittal of such bids;

Giving to said agent the attorney full power and authority to do whatever is necessary to be done as fully as said grantor could do if present and acting, hereby confirming all that the said agent and attorney shall lawfully do by virtue of these presents'

This power of attorney to remain full force and effect until revocation in writing is duly given to and received by grantee.

Appointment as Officer/Estimator: Grantor authorizes the above grantee to act as lawful agent and sign or endorse documents pertaining to the bidding for work for the Grantor.

IN WITNESS WHEROF, the said American Road Maintenance, Inc caused these presents to be sealed and signed:

J Coghill 2-11-18

Joe Coghill, President of American Road Maintenance, Inc Date

Witness: _____

ASPHALT SYSTEMS INC.
ADVANCED PRESERVATION MATERIALS

Re: P-608 Emulsified Asphalt Seal Coat

To Whom It May Concern,

Per the requirements stated in P-608.5.2 Contractor Qualifications, American Road Maintenance exceeds the specified qualifications.

Respectfully Submitted,

John

John Hunter
Asphalt Systems Inc.



KALTER
FINANCIAL GROUP

AMERICAN ROAD MAINTENANCE, INC.

Reviewed Financial Statements
For the Year Ended December 31, 2024

Available upon request

Always *bringing* Value



Prior Project References:

Brandon Robinson P.E

Kimley-Horn

1001 W. Southern Ave Suite 131

Mesa AZ 85210

Brandon Direct line: 602.906.1185

Email: brandon.robinson@kimley-horn.com

Tim Archibeque P.E

Armstrong Consultants

2201 Buena Vista Dr Southeast

Albuquerque, NM 87106

Tim Direct line: 505.702.0027

Email: tarchibeque@armstrongconsultants.com

Christopher Flournoy E.I.T.

JUB Engineers – Aviation Services Group

Chris direct line: 208.376.7330

Email: cflournoy@jub.com

EXHIBIT C

Indemnification and Insurance Requirements
(For Construction Contracts)

INDEMNIFICATION

CONTRACTOR agrees to indemnify, defend (with counsel reasonably approved by COUNTY) and hold harmless COUNTY and its officers, officials, employees, agents and volunteers from and against any and all claims, actions, losses, damages, judgments and/or liabilities arising out of this Agreement from any cause whatsoever, including the acts, errors or omissions of any person or entity and for any costs or expenses (including but not limited to attorneys' fees) incurred by COUNTY on account of any claim except where such indemnification is caused by the active negligence, sole negligence, or willful misconduct of the COUNTY.

NOTIFICATION OF ACCIDENTS AND SURVIVAL OF INDEMNIFICATION PROVISIONS

CONTRACTOR shall notify COUNTY immediately in the event of any accident or injury arising out of or in connection with this Agreement. The indemnification provisions in this Agreement shall survive any expiration or termination of this Agreement.

INSURANCE

CONTRACTOR shall procure and maintain for the duration of this Agreement insurance against claims for injuries to persons or damages to property which may arise from or in connection with the performance of the work hereunder and the results of that work by the CONTRACTOR, its agents, representatives, employees or subcontractors.

A. Minimum Scope and Limit of Insurance
Coverage shall be at least as broad as:

1. **Commercial General Liability (CGL):** Insurance Services Office (ISO) Form CG 00 01 covering CGL on an "occurrence" basis, including products-completed operations, personal & advertising injury, with limits no less than $2,000,000 per occurrence and $4,000,000 in the aggregate.
2. **Automobile Liability**: Insurance Services Office Form CA 0001 covering Code 1 (any auto), with limits no less than $2,000,000 per accident for bodily injury and property damage.
3. **Workers' Compensation**: Insurance as required by the State of California, with Statutory Limits, and Employer's Liability Insurance with limit of no less than $1,000,000 per accident for bodily injury or disease.
4. **Contractor's Pollution Legal Liability and/or Asbestos Legal Liability:** (if project involves environmental hazards) with limits no less than $1,000,000 per occurrence or claim, and $2,000,000 policy aggregate.

If the CONTRACTOR maintains higher limits than the minimums shown above, the COUNTY requires and shall be entitled to coverage for the higher limits maintained by the CONTRACTOR. Any available insurance proceeds in excess of the specified minimum limits of insurance and coverage shall be available to the COUNTY.

B. Other Insurance Provisions
The insurance policies are to contain, or be endorsed to contain, the following provisions:

1. **Additional Insured** – COUNTY, its officers, officials, employees, agents and volunteers are to be covered as additional insureds on the CGL policy with respect to liability arising out of work or operations performed by or on behalf of the CONTRACTOR including materials, parts, or equipment furnished in connection with such work or operations. General liability coverage can be provided in the form of an endorsement to the CONTRACTOR'S insurance at least as broad as ISO Form CG 20 10 11 85 or **both** CG 20 10, CG 20 26, CG 20 33, or CG 20 38; **and** CG 20 37 forms if later revisions used).
2. **Primary Coverage** – For any claims related to this Agreement, the CONTRACTOR'S insurance coverage shall be primary insurance coverage at least as broad as ISO CG 20 01 04 13 as respects the COUNTY, its officers, officials, employees, agents and volunteers. Any insurance or self-insurance maintained by the COUNTY, its officers, officials, employees, agents or volunteers shall be excess of the CONTRACTOR'S insurance and shall not contribute with it.
3. **Notice of Cancellation** – Each insurance policy required above shall provide that coverage shall not be canceled, except with notice to the COUNTY.
4. **Waiver of Subrogation Rights** – **CONTRACTOR hereby agrees to waive rights of subrogation which any insurer of CONTRACTOR may acquire** from CONTRACTOR by virtue of the payment of any loss. CONTRACTOR agrees to obtain any endorsement that may be necessary to effect this waiver of subrogation. **The Workers' Compensation policy shall be endorsed with a waiver of subrogation** in favor of the COUNTY for all work performed by the CONTRACTOR, its employees, agents and subcontractors. This provision applies regardless of whether or not the COUNTY has received a waiver of subrogation endorsement from the insurer.
5. **Deductibles and Self-Insured Retention** – Any deductibles or self-insured retentions must be declared to and approved by the COUNTY. At the option of the COUNTY, either: the CONTRACTOR shall cause the insurer shall reduce or eliminate such deductibles or self-insured retentions as respects the COUNTY, its officers, officials, employees, agents and volunteers; or the CONTRACTOR shall provide a financial guarantee satisfactory to the COUNTY guaranteeing payment of losses and related investigations, claim administration, and defense expenses.
6. **Acceptability of Insurers** – Unless otherwise approved by Risk Management, insurance shall be written by insurers authorized to do business in the State of California and with a minimum A.M. Best's Insurance Guide rating of "A- VII".
7. **Verification of Coverage** – CONTRACTOR shall furnish the COUNTY with proof of insurance, original certificates and amendatory endorsements as required by this Agreement. The proof of insurance, certificates and endorsements are to be received and approved by the COUNTY before work commences. However, failure to obtain the required documents prior to the work beginning shall not waive the CONTRACTOR'S obligation to provide them. The CONTRACTOR shall furnish evidence of renewal of coverage throughout the term of the Agreement. The COUNTY reserves the right to require complete, certified copies of all required

insurance policies, including endorsements required by these specifications, at any time.

8. **Failure to Procure Coverage** – In the event that any policy of insurance required under this Agreement does not comply with the requirements, is not procured, or is canceled and not replaced, COUNTY has the right but not the obligation or duty to terminate the Agreement. Maintenance of required insurance coverage is a material element of the Agreement and failure to maintain or renew such coverage or to provide evidence of renewal may be treated by COUNTY as a material breach of contract.
9. **Subcontractors** – CONTRACTOR shall require and verify that all subcontractors maintain insurance meeting all the requirements stated herein, and CONTRACTOR shall ensure that COUNTY is an additional insured on insurance required from subcontractors. For CGL coverage subcontractors shall provide coverage with a format least as broad as CG 20 38 04 13.
10. **Claims Made Policies** – If any of the required policies provide coverage on a claims-made basis:
    i. The Retroactive Date must be shown and must be before the date of the contract or the beginning of contract work.
    ii. Insurance must be maintained and evidence of insurance must be provided for at least five (5) years after completion of contract work.
    iii. If coverage is canceled or non-renewed, and not replaced with another claims-made policy form with a Retroactive Date prior to the contract effective date, the CONTRACTOR must purchase “extended reporting” coverage for a minimum of five (5) years after completion of contract work.
11. **Special Risks or Circumstances** – COUNTY reserves the right to modify these requirements, including limits, based on the nature of the risk, prior experience, insurer, coverage, or other circumstances.

Any change requiring additional types of insurance coverage or higher coverage limits must be made by amendment to this Agreement. CONTRACTOR agrees to execute any such amendment within thirty (30) days of receipt.

Any failure, actual or alleged, on the part of COUNTY to monitor or enforce compliance with any of the insurance and indemnification requirements will not be deemed as a waiver of any rights on the part of COUNTY.

PAYMENT BOND

KNOW ALL MEN BY THESE PRESENTS:

That the County of Santa Barbara of the State of California (hereinafter referred to as the County) and American Road Maintenance, Inc. (hereinafter referred to as Principal) have by written agreement dated _____, entered into a contract identified as:

Project Title: County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, CA 93460
County Project No. 22011-AIG XX
(Hereinafter referred to as the Contract) and

That, pursuant to law and to said Contract, and before entering upon the performance of said Contract, the principal is required to file with the County a good and sufficient bond to secure the payment of labor and materials claims.

NOW, THEREFORE, said Principal and Travelers Casualty and Surety Company of America

as corporate surety (hereinafter referred to as Surety), are held firmly bound unto the County in the amount of $ $388,350.00* , for the payment of which Principal and Surety bind themselves, their heirs, executors, administrators, successors and assigns both jointly and severally. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications. *Three Hundred Eighty-eight Thousand Three Hundred Fifty & 00/100

THE CONDITION OF THIS OBLIGATION IS SUCH that if said principal, his or its subcontractors, heirs, executors, administrators, successors, or assigns, shall fail to pay any of the persons named or referred to in Section 9100 of the California Civil Code, or amounts due under Unemployment Insurance Code with respect to work or labor performed by any such claimant, or for any amounts required to be deducted, withheld and paid over to the Employment Development Department from the wages of employees of the Contractor and his subcontractors pursuant to Section 13020 of the Unemployment Insurance Code with respect to such work and labor as required by the California Civil Code, or this bond, then said Surety will pay for the same, in an amount not to exceed the amount hereinafter set forth.

This bond shall insure to the benefit of any and all persons, entities, companies and corporations named or referred to in Section 9100 of the California Civil Code, so as to give a right of action to them or their assign in any suit brought upon this bond.

And the said Surety, for value received, hereby agrees that no change, extension of time, alteration or addition to the terms of the Contract, or to the work to be performed thereunder, or the Specifications accompanying the same, shall in anywise affect its obligations on this bond, and it does hereby waive notice of any such change, extension of time, alteration or addition to the terms of the Contract or to the Specifications.

In the event suit is brought upon this Bond by County and judgment is recovered, Surety shall pay all costs incurred by the County in such suit, including a reasonable attorney's fee to be fixed by the court.

Death, illness, disability or disqualification of the Principal shall not relieve Surety of its obligations hereunder.

American Road Maintenance, Inc.
(Principal)

(By) Kyle Paulson / Officer

6/13/25
(Dated)

Travelers Casualty and Surety Company of America
(Surety)

(Signature of Attorney-In-Fact) Sean J McCauley Jr.

One Tower Square
(Address)

Hartford, CT 06183
(City, State & Zip)

Surety's Agent for Service of Process (located within the State of California):

McCauley Bond Agency - ATTN Sean McCauley, Jr.
Name of Agent

2 Ritz Carlton Drive, Suite 204
Address

Dana Point, CA 92629
City, State & Zip

(949) 355-5856
Telephone Number

NOTE: Signature of those executing for Surety must be properly acknowledged.

NOTARY ACKNOWLEDGEMENT

State of Texas

County of Dallas

On this the 11th day of JUNE, 20 25, before me, Ashlyn Simchik (name of notary), personally appeared SEAN J. McCAULEY, JR. known to me (or satisfactorily proven) to be the person(s) whose name(s) is (is or are) subscribed to the within instrument and acknowledged that ~~he~~ (he/she/they) executed the same for the purposes therein contained.

In witness whereof, I hereunto set my hand.

Date: JUNE 11, 2025

Ashlyn Simchik


Notary Public

Print Name: Ashlyn Simchik

Notary ID: 13433618-2

My Commission Expires:

June 5, 2027



PERFORMANCE BOND

KNOW ALL MEN BY THESE PRESENTS:

That the County of Santa Barbara of the State of California (hereinafter referred to as the County) and American Road Maintenance, Inc. (hereinafter referred to as Principal) have by written agreement dated _____, entered into a contract identified as:

Project Title: County of Santa Barbara
Rehabilitate Tie-Down Apron
900 Airport Road, Santa Ynez, CA 93460
County Project No. 22011-AIG XX
(Hereinafter referred to as the Contract) and

That, pursuant to law and to said Contract, and before entering upon the performance of said Contract, the Principal is required under the terms and conditions of said Contract to furnish a bond for the faithful performance of Contract.

NOW, THEREFORE, said Principal and Travelers Casualty and Surety Company of America as corporate surety (hereinafter referred to as Surety), are held firmly bound unto the County in the amount of $388,350.00*, for the payment of which Principal and Surety bind themselves, their heirs, executors, administrators, successors and assigns both jointly and severally. Surety shall be and hereby warrants that it is listed in the Insurance Organizations Authorized by the Insurance Commissioner to Transact Business of Insurance in the State of California, published by the Department of Insurance, State of California or successor publications. *Three Hundred Eighty-eight Thousand Three Hundred Fifty & 00/100

THE CONDITION OF THIS OBLIGATION IS SUCH that if the Principal, his heirs, executors, administrators, successors, or assigns, shall perform all of the covenants, conditions and agreements in said Contract and any alteration thereof made as herein provided, in his or their part, to be kept and performed at the time, and in the manner therein specified, and shall indemnify and save harmless County, its officers, agents, and employees, as therein stipulated, then this obligation shall become null and void; otherwise it shall be and remain in full force, virtue and effect.

And the said Surety, for value received, hereby agrees that no change, extension of time, alteration or

addition to the terms of the Contract, or to the work to be performed thereunder, or the specifications accompanying the same shall in anywise affect its obligations on this bond, and it does hereby waive notice of any such change, extension of time, alteration or additions to the terms of the Contract or to the work or to the specifications.

In the event suit is brought upon this Bond by County and judgment is recovered, Surety shall pay all costs incurred by the County in such suit, including a reasonable attorney's fee to be fixed by the court.

Death, illness, disability or disqualification of the Principal shall not relieve Surety of its obligations hereunder.

American Road Maintenance, Inc.
(Principal)

(By) Kyle Paulson / Officer

6/13/25
(Dated)

Travelers Casualty and Surety Company of America
(Surety)

(Signature of Attorney-In-Fact) Sean J McCauley Jr.

One Tower Square
(Address)

Hartford, CT 06183
(City, State & Zip)

Surety's Agent for Service of Process (located within the State of California):

McCauley Bond Agency - ATTN Sean McCauley, Jr.
Name of Agent

2 Ritz Carlton Drive, Suite 204
Address

Dana Point, CA 92629
City, State & Zip

(949) 355-5856
Telephone Number

NOTE: Signature of those executing for Surety must be properly acknowledged.

NOTARY ACKNOWLEDGEMENT

State of Texas

County of Dallas

On this the 11th day of JUNE, 2025, before me, Ashlyn Simchik (name of notary), personally appeared SEAN J. McCAULEY, JR., known to me (or satisfactorily proven) to be the person(s) whose name(s) is (is or are) subscribed to the within instrument and acknowledged that ~~he~~ (he/she/they) executed the same for the purposes therein contained.

In witness whereof, I hereunto set my hand.

Date: JUNE 11, 2025

Ashlyn Simchik


Notary Public

Print Name: Ashlyn Simchik

Notary ID: 13433618-2

My Commission Expires:

June 5, 2027



TRAVELERS

Travelers Casualty and Surety Company of America
Travelers Casualty and Surety Company
St. Paul Fire and Marine Insurance Company

POWER OF ATTORNEY

KNOW ALL MEN BY THESE PRESENTS: That Travelers Casualty and Surety Company of America, Travelers Casualty and Surety Company, and St. Paul Fire and Marine Insurance Company are corporations duly organized under the laws of the State of Connecticut (herein collectively called the "Companies"), and that the Companies do hereby make, constitute and appoint SEAN J MCCAULEY JR of DALLAS , **Texas** , their true and lawful Attorney(s)-in-Fact to sign, execute, seal and acknowledge any and all bonds, recognizances, conditional undertakings and other writings obligatory in the nature thereof on behalf of the Companies in their business of guaranteeing the fidelity of persons, guaranteeing the performance of contracts and executing or guaranteeing bonds and undertakings required or permitted in any actions or proceedings allowed by law.

IN WITNESS WHEREOF, the Companies have caused this instrument to be signed, and their corporate seals to be hereto affixed, this **21st** day of **April, 2021**.

State of Connecticut

City of Hartford ss.

By: _____
Robert L. Raney, Senior Vice President

On this the **21st** day of April, **2021**, before me personally appeared **Robert L. Raney**, who acknowledged himself to be the Senior Vice President of each of the Companies, and that he, as such, being authorized so to do, executed the foregoing instrument for the purposes therein contained by signing on behalf of said Companies by himself as a duly authorized officer.

IN WITNESS WHEREOF, I hereunto set my hand and official seal.

My Commission expires the **30th** day of **June, 2026**

_____
Anna P. Nowik, Notary Public

This Power of Attorney is granted under and by the authority of the following resolutions adopted by the Boards of Directors of each of the Companies, which resolutions are now in full force and effect, reading as follows:

RESOLVED, that the Chairman, the President, any Vice Chairman, any Executive Vice President, any Senior Vice President, any Vice President, any Second Vice President, the Treasurer, any Assistant Treasurer, the Corporate Secretary or any Assistant Secretary may appoint Attorneys-in-Fact and Agents to act for and on behalf of the Company and may give such appointee such authority as his or her certificate of authority may prescribe to sign with the Company's name and seal with the Company's seal bonds, recognizances, contracts of indemnity, and other writings obligatory in the nature of a bond, recognizance, or conditional undertaking, and any of said officers or the Board of Directors at any time may remove any such appointee and revoke the power given him or her; and it is

FURTHER RESOLVED, that the Chairman, the President, any Vice Chairman, any Executive Vice President, any Senior Vice President or any Vice President may delegate all or any part of the foregoing authority to one or more officers or employees of this Company, provided that each such delegation is in writing and a copy thereof is filed in the office of the Secretary; and it is

FURTHER RESOLVED, that any bond, recognizance, contract of indemnity, or writing obligatory in the nature of a bond, recognizance, or conditional undertaking shall be valid and binding upon the Company when (a) signed by the President, any Vice Chairman, any Executive Vice President, any Senior Vice President or any Vice President, any Second Vice President, the Treasurer, any Assistant Treasurer, the Corporate Secretary or any Assistant Secretary and duly attested and sealed with the Company's seal by a Secretary or Assistant Secretary; or (b) duly executed (under seal, if required) by one or more Attorneys-in-Fact and Agents pursuant to the power prescribed in his or her certificate or their certificates of authority or by one or more Company officers pursuant to a written delegation of authority; and it is

FURTHER RESOLVED, that the signature of each of the following officers: President, any Executive Vice President, any Senior Vice President, any Vice President, any Assistant Vice President, any Secretary, any Assistant Secretary, and the seal of the Company may be affixed by facsimile to any Power of Attorney or to any certificate relating thereto appointing Resident Vice Presidents, Resident Assistant Secretaries or Attorneys-in-Fact for purposes only of executing and attesting bonds and undertakings and other writings obligatory in the nature thereof, and any such Power of Attorney or certificate bearing such facsimile signature or facsimile seal shall be valid and binding upon the Company and any such power so executed and certified by such facsimile signature and facsimile seal shall be valid and binding on the Company in the future with respect to any bond or understanding to which it is attached.

I, **Kevin E. Hughes**, the undersigned, Assistant Secretary of each of the Companies, do hereby certify that the above and foregoing is a true and correct copy of the Power of Attorney executed by said Companies, which remains in full force and effect.

Dated this **11th** day of **June** , **2025** .

_____
Kevin E. Hughes, Assistant Secretary

To verify the authenticity of this Power of Attorney, please call us at 1-800-421-3880.
Please refer to the above-named Attorney(s)-in-Fact and the details of the bond to which this Power of Attorney is attached.

No. 6516

STATE OF CALIFORNIA

DEPARTMENT OF INSURANCE

SAN FRANCISCO

Amended

Certificate of Authority

THIS IS TO CERTIFY *that, pursuant to the Insurance Code of the State of California,*

Travelers Casualty and Surety Company of America

of Hartford, Connecticut, organized under the laws of Connecticut, subject to its Articles of Incorporation or other fundamental organizational documents, is hereby authorized to transact within this State, subject to all provisions of this Certificate, the following classes of insurance:

Fire, Marine, Surety, Disability, Plate Glass, Liability, Workers' Compensation, Common Carrier Liability, Boiler and Machinery, Burglary, Credit, Sprinkler, Team and Vehicle, Automobile, Aircraft and Miscellaneous

as such classes are now or may hereafter be defined in the Insurance Laws of the State of California.

THIS CERTIFICATE *is expressly conditioned upon the holder hereof now and hereafter being in full compliance with all, and not in violation of any, of the applicable laws and lawful requirements made under authority of the laws of the State of California as long as such laws or requirements are in effect and applicable, and as such laws and requirements now are, or may hereafter be changed or amended.*

IN WITNESS WHEREOF, *effective as of the 1st day of July, 1997, I have hereunto set my hand and caused my official seal to be affixed this 16th day of June, 1997.*

Fee: $ 92.00
Rec. No.
Filed: 5/28/97

Chuck Quackenbush
Insurance Commissioner

By

Victoria S. Sidbury
Deputy

Certification

I, the undersigned Insurance Commissioner of the State of California, do hereby certify that I have compared the above copy of Certificate of Authority with the duplicate of original now on file in my office, and that the same is a full, true, and correct transcript thereof, and of the whole of said duplicate, and said Certificate of Authority is now in full force and effect.

IN WITNESS WHEREOF, *I have set my hand and caused my official seal to be affixed this 29th day of September, 2020.*

Ricardo Lara
Insurance Commissioner

By

Magnolia Gutierrez

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY): 06/11/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER	CONTACT NAME: Dylan Scott	
Scott & McCauley Insurance Agency	PHONE (A/C, No, Ext): (949) 503-1953	FAX (A/C, No):
2 Ritz Carlton Drive	E-MAIL ADDRESS: dylan@sminsuranceagency.com	
Suite 204		
Dana Point CA 92629		

INSURED	INSURER(S) AFFORDING COVERAGE	NAIC #
American Road Maintenance, Inc	INSURER A : Landmark American Insurance Company	33138
4554 E Eco Industrial Pl	INSURER B : United States Fire Insurance Company	21113
	INSURER C : AXIS Surplus Insurance Company	26620
	INSURER D : Crum & Forster Indemnity Company	31348
	INSURER E :	
Tucson AZ 85756	INSURER F :	

COVERAGES **CERTIFICATE NUMBER:** ARM - COI - 25-26 **REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS	
A	[X] COMMERCIAL GENERAL LIABILITY [ ] CLAIMS-MADE [X] OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: [ ] POLICY [X] PRO-JECT [ ] LOC [ ] OTHER:	Y	Y	LHA115117	03/31/2025	03/31/2026	EACH OCCURRENCE DAMAGE TO RENTED PREMISES (Ea occurrence) MED EXP (Any one person) PERSONAL & ADV INJURY GENERAL AGGREGATE PRODUCTS - COMP/OP AGG	$ 1,000,000 $ 50,000 $ 5,000 $ 1,000,000 $ 2,000,000 $ 2,000,000
B	AUTOMOBILE LIABILITY [X] ANY AUTO [ ] OWNED AUTOS ONLY [ ] SCHEDULED AUTOS [ ] HIRED AUTOS ONLY [ ] NON-OWNED AUTOS ONLY	Y	Y	5069143233	03/31/2025	03/31/2026	COMBINED SINGLE LIMIT (Ea accident) BODILY INJURY (Per person) BODILY INJURY (Per accident) PROPERTY DAMAGE (Per accident)	$ 1,000,000 $ $ $
C	[ ] UMBRELLA LIAB [X] OCCUR [X] EXCESS LIAB [ ] CLAIMS-MADE [ ] DED [ ] RETENTION $	Y	Y	P-001-003628506-02	03/31/2025	03/31/2026	EACH OCCURRENCE AGGREGATE	$ 2,000,000 $ 2,000,000
D	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) Y / N: N If yes, describe under DESCRIPTION OF OPERATIONS below	N / A	Y	4087487619	03/31/2025	03/31/2026	[X] PER STATUTE [ ] OTH-ER E.L. EACH ACCIDENT E.L. DISEASE - EA EMPLOYEE E.L. DISEASE - POLICY LIMIT	 $ 1,000,000 $ 1,000,000 $ 1,000,000
B	INLAND MARINE			5069143233	03/31/2025	03/31/2026	Leased or Rented Deductible	$350,000 $1,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Blanket Additional Insured as required by an executed written contract or agreement on the General Liability, Auto Liability and Umbrella policies. Coverage is Primary & Non-Contributory where required by written contract or agreement with the named insured. Blanket Waiver-of-Subrogation is granted in favor of the Additional Insureds with respects to the General Liability, Auto Liability, and Workers Compensation policies. Thirty (30) days' notice of cancellation with ten (10) days' notice for nonpayment of premium is provided. Excess coverage is Follow Form. The certificate holder is considered a Loss Payee per written contract or agreement on the Contractors Equipment Policy (Leased and Rented).

Type Of Insurance: Excess Liability

CERTIFICATE HOLDER

County of Santa Barbara – Casa Nueva
260 N. San Antonio Road
Santa Barbara CA 93110

CANCELLATION

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE



© 1988-2015 ACORD CORPORATION. All rights reserved.

AGENCY CUSTOMER ID: _____

LOC #: _____

ADDITIONAL REMARKS SCHEDULE

AGENCY	NAMED INSURED
Scott & McCauley Insurance Agency	American Road Maintenance, Inc
POLICY NUMBER	
CARRIER / NAIC CODE	EFFECTIVE DATE:

ADDITIONAL REMARKS

THIS ADDITIONAL REMARKS FORM IS A SCHEDULE TO ACORD FORM,

FORM NUMBER: 25 **FORM TITLE:** Certificate of Liability Insurance: Remarks

Type Of Insurance: Excess Liability
Insurer Affording Coverage: Landmark American Insurance Company
Policy Number: LHA605666
Policy Eff - Exp Dates: 3/31/2025 - 3/31/2026
Limits: $3,000,000
In Excess Of: $2,000,000

© 2008 ACORD CORPORATION. All rights reserved.

The ACORD name and logo are registered marks of ACORD

COMMON POLICY CONDITIONS

All Coverage Parts included in this policy are subject to the following conditions.

A. Cancellation

1. The first Named Insured shown in the Declarations may cancel this policy by mailing or delivering to us advance written notice of cancellation.
2. We may cancel this policy by mailing or delivering to the first Named Insured written notice of cancellation at least:
   a. 10 days before the effective date of cancellation if we cancel for nonpayment of premium; or
   b. 30 days before the effective date of cancellation if we cancel for any other reason.
3. We will mail or deliver our notice to the first Named Insured's last mailing address known to us.
4. Notice of cancellation will state the effective date of cancellation. The policy period will end on that date.
5. If this policy is cancelled, we will send the first Named Insured any premium refund due. If we cancel, the refund will be pro rata. If the first Named Insured cancels, the refund may be less than pro rata. The cancellation will be effective even if we have not made or offered a refund.
6. If notice is mailed, proof of mailing will be sufficient proof of notice.

B. Changes

This policy contains all the agreements between you and us concerning the insurance afforded. The first Named Insured shown in the Declarations is authorized to make changes in the terms of this policy with our consent. This policy's terms can be amended or waived only by endorsement issued by us and made a part of this policy.

C. Examination Of Your Books And Records

We may examine and audit your books and records as they relate to this policy at any time during the policy period and up to three years afterward.

D. Inspections And Surveys

1. We have the right to:
   a. Make inspections and surveys at any time;
   b. Give you reports on the conditions we find; and
   c. Recommend changes.
2. We are not obligated to make any inspections, surveys, reports or recommendations and any such actions we do undertake relate only to insurability and the premiums to be charged. We do not make safety inspections. We do not undertake to perform the duty of any person or organization to provide for the health or safety of workers or the public. And we do not warrant that conditions:
   a. Are safe or healthful; or
   b. Comply with laws, regulations, codes or standards.
3. Paragraphs **1.** and **2.** of this condition apply not only to us, but also to any rating, advisory, rate service or similar organization which makes insurance inspections, surveys, reports or recommendations.
4. Paragraph **2.** of this condition does not apply to any inspections, surveys, reports or recommendations we may make relative to certification, under state or municipal statutes, ordinances or regulations, of boilers, pressure vessels or elevators.

E. Premiums

The first Named Insured shown in the Declarations:

1. Is responsible for the payment of all premiums; and
2. Will be the payee for any return premiums we pay.

F. Transfer Of Your Rights And Duties Under This Policy

Your rights and duties under this policy may not be transferred without our written consent except in the case of death of an individual named insured.

If you die, your rights and duties will be transferred to your legal representative but only while acting within the scope of duties as your legal representative. Until your legal representative is appointed, anyone having proper temporary custody of your property will have your rights and duties but only with respect to that property.

 Copyright, Insurance Services Office, Inc., 1998 □

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

ADDITIONAL INSURED – OWNERS, LESSEES OR CONTRACTORS – COMPLETED OPERATIONS

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART
PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART

SCHEDULE

Name Of Additional Insured Person(s) Or Organization(s)	Location And Description Of Completed Operations
ANY PERSON(S) OR ORGANIZATION(S) REQUIRED BY WRITTEN CONTRACT OR AGREEMENT AND AS PER PARAGRAPHS A. AND B. BELOW	
Information required to complete this Schedule, if not shown above, will be shown in the Declarations.	

A. **Section II – Who Is An Insured** is amended to include as an additional insured the person(s) or organization(s) shown in the Schedule, but only with respect to liability for "bodily injury" or "property damage" caused, in whole or in part, by "your work" at the location designated and described in the Schedule of this endorsement performed for that additional insured and included in the "products-completed operations hazard".

However:

1. The insurance afforded to such additional insured only applies to the extent permitted by law; and

2. If coverage provided to the additional insured is required by a contract or agreement, the insurance afforded to such additional insured will not be broader than that which you are required by the contract or agreement to provide for such additional insured.

 © ISO Properties, Inc., 2004 □

B. With respect to the insurance afforded to these additional insureds, the following is added to **Section III – Limits Of Insurance:**

If coverage provided to the additional insured is required by a contract or agreement, the most we will pay on behalf of the additional insured is the amount of insurance:

1. Required by the contract or agreement; or

2. Available under the applicable Limits of Insurance shown in the Declarations;

whichever is less.

This endorsement shall not increase the applicable Limits of Insurance shown in the Declarations.

© ISO Properties, Inc., 2004

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

ADDITIONAL INSURED – OWNERS, LESSEES OR CONTRACTORS – SCHEDULED PERSON OR ORGANIZATION

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART

SCHEDULE

Name Of Additional Insured Person(s) Or Organization(s)	Location(s) Of Covered Operations
ANY PERSON(S) OR ORGANIZATION(S) REQUIRED BY WRITTEN CONTRACT OR AGREEMENT AND AS PER PARAGRAPHS A., B., AND C. BELOW	
Information required to complete this Schedule, if not shown above, will be shown in the Declarations.	

A. **Section II – Who Is An Insured** is amended to include as an additional insured the person(s) or organization(s) shown in the Schedule, but only with respect to liability for "bodily injury", "property damage" or "personal and advertising injury" caused, in whole or in part, by:

1. Your acts or omissions; or
2. The acts or omissions of those acting on your behalf;

in the performance of your ongoing operations for the additional insured(s) at the location(s) designated above.

However:

1. The insurance afforded to such additional insured only applies to the extent permitted by law; and
2. If coverage provided to the additional insured is required by a contract or agreement, the insurance afforded to such additional insured will not be broader than that which you are required by the contract or agreement to provide for such additional insured.

B. With respect to the insurance afforded to these additional insureds, the following additional exclusions apply:

This insurance does not apply to "bodily injury" or "property damage" occurring after:

1. All work, including materials, parts or equipment furnished in connection with such work, on the project (other than service, maintenance or repairs) to be performed by or on behalf of the additional insured(s) at the location of the covered operations has been completed; or

 © Insurance Services Office, Inc., 2012 □

2. That portion of "your work" out of which the injury or damage arises has been put to its intended use by any person or organization other than another contractor or subcontractor engaged in performing operations for a principal as a part of the same project.

C. With respect to the insurance afforded to these additional insureds, the following is added to **Section III – Limits Of Insurance:**

If coverage provided to the additional insured is required by a contract or agreement, the most we will pay on behalf of the additional insured is the amount of insurance:

1. Required by the contract or agreement; or

2. Available under the applicable Limits of Insurance shown in the Declarations;

whichever is less.

This endorsement shall not increase the applicable Limits of Insurance shown in the Declarations.

© Insurance Services Office, Inc., 2012

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

PRIMARY AND NONCONTRIBUTORY – OTHER INSURANCE CONDITION

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART
LIQUOR LIABILITY COVERAGE PART
PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART

The following is added to the **Other Insurance** Condition and supersedes any provision to the contrary:

Primary And Noncontributory Insurance

This insurance is primary to and will not seek contribution from any other insurance available to an additional insured under your policy provided that:

(1) The additional insured is a Named Insured under such other insurance; and

(2) You have agreed in writing in a contract or agreement that this insurance would be primary and would not seek contribution from any other insurance available to the additional insured.

© Insurance Services Office, Inc., 2018

This Endorsement Changes The Policy. Please Read It Carefully.

WAIVER OF TRANSFER OF RIGHTS OF RECOVERY AGAINST OTHERS TO US

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE FORM
PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE FORM

SCHEDULE

Name of Person or Organization:

Any Person or Organization As Required By Written Contract

The following is added to **SECTION IV – CONDITIONS**, **8. TRANSFER OF RIGHTS OF RECOVERY AGAINST OTHERS TO US**:

We waive any right of recovery we may have against the person or organization shown in the SCHEDULE above because of payment we make for injury or damage arising out of your ongoing operations, "your product" or "your work" done under a written contract with that person or organization and included in the "product-completed operations hazard". This waiver applies only to the person or organization shown in the SCHEDULE above.

This endorsement effective 3/31/2025
forms part of Policy Number LHA115117
issued to AMERICAN ROAD MAINTENANCE, INC.
by Landmark American Insurance Company

 Includes copyrighted material of Insurance Services Office, Inc. 1992
with its permission.

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

COMMERCIAL AUTOMOBILE BROAD FORM ENDORSEMENT

This endorsement modifies insurance provided under the following:

BUSINESS AUTO COVERAGE FORM

SCHEDULE

1. Broadened Insured Status
2. Blanket Additional Insured When Required Under Written Contract
3. Employee Hired Autos Liability Coverage
4. Employees As Insureds
5. Coverage Extensions – Supplementary Payments
6. Limited Fellow Employee Coverage
7. Limited Hired Auto - Physical Damage Coverage – Private Passenger (Includes Employee Hired Autos Physical Damage Coverage)
8. Custom Signs And Decoration
9. Extended Towing Coverage
10. Glass Breakage
11. Reimbursement For Increased Temporary Transportation Expense For Private Passenger And Commercial Vehicles
12. Extra Expense – Stolen Vehicles
13. Personal Effects Coverage
14. Audio, Visual, And Data Electronic Equipment
15. Loan/Lease Payoff Coverage
16. Airbag Coverage
17. Multiple Deductible Protection – Covered "Auto" And Trailer
18. Duties In The Event Of An Accident, Claim, Suit, Or Loss
19. Non-Owned Auto Waiver Of Subrogation
20. Blanket Waiver Of Subrogation When Required Under Written Contract
21. Coverage Territory – Short Term Hired Commercial "Autos"
22. Limited Mexico Coverage
23. Unintentional Failure To Disclose Hazards
24. Mental Anguish Resulting From "Bodily Injury"
25. Waiver Of Sovereign Immunity
26. Application Of This Endorsement

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

1. Broadened Insured Status

SECTION **II** – COVERED AUTOS LIABILITY COVERAGE, Paragraph **A.** Coverage, Subparagraph **1**. Who Is An Insured is amended to include as an insured:

A. Any subsidiary which is a legally incorporated entity of which you own a financial interest of more than 50% of the voting stock on the effective date of this Coverage Form, while using with your permission a covered "auto."

However, the insurance afforded by this provision **1.A.** does not apply to any subsidiary that is an insured under any other automobile liability policy, or would be an insured under such policy but for the termination of such policy or the exhaustion of such policy's limits of insurance.

B. Any organization you newly acquire or form, and over which you maintain majority interest, while using with your permission a covered "auto".

The insurance afforded by this provision **1.B.**:

1. Is effective on the acquisition or formation date, and is afforded only until the end of the policy period of this Coverage Form, or the next anniversary of its inception date, whichever is earlier.
2. Does not apply to "bodily injury" or "property damage" resulting from an "accident" that occurred before you acquired or formed the organization.
3. Does not include any newly acquired or formed organization that is:
   a. A joint venture or partnership; or
   b. An insured under any other automobile liability policy, or would be an insured under such policy but for the termination of such policy or the exhaustion of such policy's limits of insurance.

2. Blanket Additional Insured When Required Under Written Contract

Paragraph **A.1.** Who Is An Insured under SECTION **II** – COVERED AUTOS LIABILITY COVERAGE is amended to add:

d. Any person, organization or governmental entity with respect to the operation, maintenance, or use of a covered "auto" if you are required to add such person, organization or governmental entity to this policy as an additional "insured" in order to comply with the terms of a written contract or written agreement. This Additional Insured status is not conferred when such written contract or written agreement:

(1) Involves the owner or anyone else from whom you hire or borrow a covered "auto" unless it is a "trailer" connected to a covered "auto" you own; or

(2) Is executed after the date of "accident" or "loss";

Paragraph d.(2) above does not apply if:

(a) the terms and conditions of the written contract or written agreement had been agreed upon prior to the "accident" or "loss"; and

(b) you can definitively establish that the terms and conditions of the written contract or written agreement ultimately executed are the same as those which had been agreed upon prior to the "accident" or "loss".

Paragraph **a.** of Condition **5.** Other Insurance of Part **B**. General Conditions under Section **IV** – Business Auto Conditions is amended by the addition of the following:

Regardless of whether other insurance is maintained by an additional insured on a primary basis, the coverage provided by Provision **2.** of the Commercial Auto Broad Form Endorsement will be primary to and noncontributing with other insurance maintained by the additional insured if the written contract or written agreement between

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

you and the additional insured specifically requires that this insurance be primary.

3. Employee Hired Autos Liability Coverage

The following is added to the Who Is An Insured Provision of SECTION II – COVERED AUTOS LIABILITY COVERAGE:

An "employee" of yours is an "insured" while operating an "auto" hired or rented under a written contract or written agreement in that "employee's" name, with your permission, while performing duties related to the conduct of your business.

4. Employees As Insureds

The following is added to the Section **II** – COVERED AUTOS LIABILITY COVERAGE, Paragraph **A.1.** Who Is An Insured Provision:

Any "employee" of yours while using with your permission a covered "auto" you don't own, hire or borrow if such "auto" is being used in your business or your personal affairs.

5. Coverage Extensions - Supplementary Payments

Paragraphs **a.(2)** and **a.(4)** under SECTION **II** – COVERED AUTOS LIABILITY COVERAGE, Paragraph **2.a.** Supplementary Payments are revised as follows:

1. In **a.(2)**, the limit for the cost of bail bonds is increased to $5,000; and
2. In **a.(4)**, the limit for the actual loss of earnings is increased to $1,000 per day.

6. Limited Fellow Employee Coverage

The following is added to Subparagraph **5.** Fellow Employee under Paragraph **B.** Exclusions in SECTION **II** – COVERED AUTOS LIABILITY COVERAGE:

But this exclusion does not apply if:

a. the "bodily injury" results from the use of a covered "auto" you own or hire, and

b. you have Workers Compensation insurance in force covering all of your "employees."

Such coverage as is afforded by this provision is excess over any other collectible insurance.

7. Limited Hired Auto - Physical Damage Coverage - Private Passenger (Includes Employee Hired Autos Physical Damage Coverage)

The following is added to Subparagraph **1.** under Paragraph **A.** Coverage under SECTION **III** – PHYSICAL DAMAGE COVERAGE:

d. Limited Hired Auto – Physical Damage – Private Passenger

If hired "autos" are covered "autos" for Covered Autos Liability Coverage, and if Physical Damage Coverage of Comprehensive or Collision is provided under this Coverage Form for any "auto" you own, then Comprehensive and Collision Physical Damage Coverages as provided under SECTION **III** – PHYSICAL DAMAGE COVERAGE of this Coverage Part are extended to "autos" of the private passenger type you or your employee hires under a written contract or written agreement without a driver, at your direction, for the purpose of conducting your business, subject to the following:

(1) The most we will pay for "loss" to any hired "auto" is $35,000 or the actual cash value or cost to repair or replace, whichever is the least, minus a deductible.

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

(2) The deductible will be equal to the largest deductible applicable to any owned "auto" of the private passenger type for that coverage, or $1,000, whichever is less.

(3) Limited Hired Auto – Physical Damage – Private Passenger coverage is excess over any other collectible insurance.

(4) Subject to the above limit, deductible, and excess provisions we will provide coverage equal to the broadest coverage applicable to any covered "auto" you own of the private passenger type insured under this policy.

Coverage includes loss of use of that hired auto, provided it results from an "accident" for which you are legally liable and as a result of which a monetary loss is sustained by the leasing or rental concern. The most we will pay for any one "accident" is $20 per day subject to a maximum of $1,000.

If a limit for Hired Auto – Physical Damage is shown in the Schedule, then that limit replaces, and is not added to, the $35,000 limit indicated above.

This extension of coverage does not apply to any "auto" you hire or borrow from any of your "employees", partners (if you are a partnership), members (if you are a limited liability company), or members of their households.

8. Custom Signs And Decoration

The following is added to Paragraph **A.** Coverage **1.** under SECTION **III** – PHYSICAL DAMAGE COVERAGE:

In the event of a total loss to an "auto" insured for auto physical damage coverage on this policy, in addition to the actual cash value of the "auto", we will pay the actual cost to repair or replace signage or custom paint details up to $5,000.

9. Extended Towing Coverage

If the named insured carries Comprehensive and Collision Coverage for the damaged covered commercial "auto", then this coverage extension **9.** applies to that covered "auto." If the damaged covered "auto" is of the private passenger type, then in addition to Comprehensive and Collision Coverage, the damaged covered "auto" must also carry Towing Coverage in order for this coverage extension **9.** to apply.

The following is added to Paragraph **A.2.** Towing under SECTION **III** – PHYSICAL DAMAGE COVERAGE:

We will pay for towing and associated labor costs each time a covered "auto" is disabled. All labor must be performed at the place of disablement. If the "auto" is of the private passenger type, there will be no deductible. If the "auto" is not a private passenger type, a $250 deductible will apply to this coverage but it will not reduce the available limit of insurance. For all types of "autos", the most we will pay under this coverage is $1,000 per disablement. "Autos" which are disabled do not include stolen vehicles.

10. Glass Breakage

If you carry Comprehensive Coverage for the damaged covered "auto", then this coverage extension applies to that covered "auto":

The following is added to Paragraph **A.3.** Glass Breakage - Hitting A Bird Or Animal – Falling Objects Or Missiles under SECTION **III** – PHYSICAL DAMAGE COVERAGE:

Any deductible shown in the Declarations will not apply to glass breakage if such glass is repaired, in a manner acceptable to us, rather than replaced. If the glass must be replaced and there is no other damage associated with the "loss", the deductible will be $100 unless

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

a lower deductible is shown on the declarations page for this coverage.

11. Reimbursement For Increased Temporary Transportation Expense For Private Passenger And Commercial Vehicles

A. If The Covered "Auto" Has Comprehensive Or Specified Causes Of Loss Physical Damage Coverage:

Paragraph **a.** Transportation Expenses under SECTION **III** – PHYSICAL DAMAGE COVERAGE, **A.** Coverage, **4.** Coverage Extensions is replaced by the following:

If your covered "auto" is damaged or stolen and the damage or theft is covered by Comprehensive or Specified Causes of Loss coverage provided by this policy, we will pay up to $50 per day subject to a maximum limit of $1,500 for the necessary and actual temporary transportation expenses (including rental reimbursement) incurred by you during the period beginning 24 hours after the theft or damage and ending, regardless of the policy's expiration,

a. when the covered "auto" is returned to use or we pay for its "loss" in the event of a total theft of the covered "auto", or

b. when the covered "auto" is repaired or replaced, or we pay for its "loss", whichever is earlier in the event of a "loss" due to a cause other than the total theft of the covered "auto."

Except with respect to losses pertaining to the total theft of covered "autos" of the private passenger type, this coverage does not apply while there are spare or reserve "autos" available to you.

No deductible applies to this coverage.

B. If The Covered "Auto" Has Collision Physical Damage Coverage:

If your covered "auto" is damaged and the damage is covered by Collision coverage provided by this policy, we will pay up to $50 per day subject to a maximum limit of $1,500 for necessary and actual temporary transportation expenses (including rental reimbursement) incurred by you during the period beginning 24 hours after the "loss" and ending, regardless of the policy's expiration, when the covered "auto" is repaired or replaced, or we pay for its "loss", whichever is earlier.

This coverage does not apply while there are spare or reserve "autos" available to you.

No deductible applies to this coverage.

12. Extra Expense - Stolen Vehicles

The following is added under Paragraph **A.4.a.** Coverage Extensions of SECTION **III** - PHYSICAL DAMAGE COVERAGE:

We will pay for all reasonable and necessary expenses to return a stolen covered "auto" to the named insured if such covered "auto" carries Comprehensive coverage.

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

13. Personal Effects Coverage

Paragraph **A.** Coverage under SECTION **III** – PHYSICAL DAMAGE COVERAGE is amended to add the following coverage:

Personal Effects Coverage

1. We will pay for "loss" to personal property or effects which are owned by an insured and in or on your covered "auto" at the time of "loss" in the event of a total theft of that covered "auto."
2. Subject to Paragraph **C.** Limit Of Insurance under SECTION **III** – PHYSICAL DAMAGE COVERAGE, we will pay up to $500 for "loss" of personal property or effects in any one "accident" involving total theft of a covered "auto".

This insurance will not apply if, at the time of "loss", the covered "auto" is unattended, unless the "loss" is the result of forced entry into the covered "auto" while all doors, windows or other openings are closed and locked and there is evidence of forced entry.

Under this extension, we will not pay for "loss" to the following: accounts, bills, currency, deeds, evidences of debt, money, notes or securities; electronic equipment or tapes, records, discs or other similar audio, visual or data electronic devices designed for use with audio, visual or data electronic equipment; jewelry, watches, necklaces, bracelets, gems, gold, platinum, silver, furs; animals, birds, or fish or any motorized vehicle.

This coverage will be excess over any other collectable insurance. No deductible applies to this coverage.

14. Audio, Visual, And Data Electronic Equipment

The sub-limit in Paragraph **C.2.** of the Limit of Insurance Provision of SECTION **III**- PHYSICAL DAMAGE COVERAGE is increased to $1,500.

15. Loan/Lease Payoff Coverage

The following is added to Limit of Insurance of SECTION **III** - PHYSICAL DAMAGE COVERAGE:

In the event of a total "loss" to a covered "auto" shown in the schedule or declarations for which Collision and Comprehensive Coverage apply, we will pay any unpaid amount due on the lease or loan for that covered "auto," less;

1. The amount paid under the Physical Damage Coverage Section of the policy, and
2. Any;
   a. Overdue lease/loan payments at the time of the "loss";
   b. Financial penalties imposed under a lease for excessive use, abnormal wear and tear or high mileage:
   c. Security deposits not returned by the lessor;
   d. Costs for extended warranties, Credit Life Insurance, Health, Accident or Disability Insurance purchased with the loan or lease; and
   e. Carry-over balances from previous loans or leases.

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

This coverage is limited to a maximum of $1,500 for each covered “auto”.

16. Airbag Coverage

If the named “insured” carries Comprehensive and Collision Coverage for the damaged covered “auto”, then this coverage extension **16.** applies to that covered “auto”.

The following is added to Subparagraph **3.a.** under Paragraph **B.** Exclusions in SECTION **III** - PHYSICAL DAMAGE COVERAGE:

The accidental discharge of an airbag shall not be considered mechanical or electrical breakdown and therefore shall not be excluded. This provision does not apply to "autos" you hire with a driver and it is excess over any warranty specifically designed to provide this coverage.

17. Multiple Deductible Protection – Covered “Auto” And Trailer

If you carry Comprehensive and Collision coverages for the damaged covered “autos”, then this coverage extension **17**. applies to those covered “autos”:

The following is added to Paragraph **D.** Deductible under SECTION **III** - PHYSICAL DAMAGE COVERAGE:
Whenever a covered “auto” and trailer are each damaged in the same “loss" while operating as a combined truck and trailer unit, only one deductible shall apply to the “accident”. The larger of the two deductibles shall apply.

If another policy or coverage form issued by us, that is not an automobile policy or coverage form, applies to the same "loss" or "accident", the following applies:

1. If the deductible under this Business Auto Coverage Form is not the largest deductible, it will be waived.
2. If the deductible under this Business Auto Coverage Form is the largest deductible, it will be reduced by the amount of the smaller (or smallest) deductible.

18. Duties In The Event Of An Accident, Claim, Suit, Or Loss

A. Subparagraph **2.a.** under Paragraph **A.** Loss Conditions in SECTION **IV** – BUSINESS AUTO CONDITIONS is amended so that your obligations relative to notification requirements apply only when the "accident" or "loss" is known to:

   1. You, if you are an individual;
   2. A partner, if you are a partnership;
   3. A member, if you are a joint venture;
   4. An executive officer, insurance manager or any other person designated by you to send notices of “accidents” or “loss” to insurers, if you are a corporation; or
   5. A member, if you are a limited liability company.

B. Subparagraph **2.b.(2)** under Paragraph **A.** Loss Conditions in SECTION **IV** – BUSINESS AUTO CONDITIONS is amended so that your obligations relative to providing us with documents concerning a claim or "suit" will not be considered breached unless the breach occurs after such claim or "suit" is known to:

   1. You, if you are an individual;
   2. A partner, if you are a partnership;
   3. A member, if you are a joint venture;
   4. An executive officer, insurance manager or any other person designated by you to send notices of claims or “suits” to insurers, if you are a corporation; or

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

5. A member, if you are a limited liability company.

19. Non-Owned Auto Waiver Of Subrogation

The following is added to Subparagraph **5.** Transfer Of Rights Of Recovery Against Others To Us, under Paragraph **A.** Loss Conditions in SECTION **IV** – BUSINESS AUTO CONDITIONS:

We hereby waive any right of subrogation against any of your officers, directors, or "employees" which might arise by reason of any payment under the insurance afforded by this policy for the operation, maintenance, use, loading, or unloading of non-owned "autos".

This waiver extends only to payments in excess of other valid and collectible insurance available to the officer, director, or "employee".

20. Blanket Waiver Of Subrogation When Required Under Written Contract

The following is added to Subparagraph **5.** Transfer Of Rights Of Recovery Against Others To Us, under Paragraph **A.** Loss Conditions in SECTION **IV** - BUSINESS AUTO CONDITIONS:

However, we waive any right of recovery we may have against a person, organization or governmental entity when you have waived such right of recovery under a written contract or written agreement provided such written contract or agreement is:

1. currently in effect or becoming effective during the term of this policy; and
2. executed prior to the "accident" or "loss"; or
3. executed after the "accident" or "loss" if:
   a. the terms and conditions of the written contract or written agreement had been agreed upon prior to the "accident" or "loss"; and
   b. you can definitively establish that the terms and conditions of the written contract or written agreement ultimately executed are the same as those which had been agreed upon prior to the "accident" or "loss".

21. Coverage Territory - Short Term Hired Commercial "Autos"

Paragraph **7.** Policy Period, Coverage Territory under Paragraph **B.** General Conditions in SECTION **IV** – BUSINESS AUTO CONDITIONS is amended by the addition of the following:

The coverage territory is extended to anywhere in the world if:

1. A covered "auto" of the commercial van, pick-up, or truck type is leased, hired, rented or borrowed for a period of 30 days or less; and
2. The "insured's" responsibility to pay damages is determined in a "suit" on the merits, in the United States of America, the territories and possessions of the United States of America, Puerto Rico, or Canada or in a settlement we agree to.

We will also cover "loss" to, or "accidents" involving, a covered "auto" while being transported between any of these places.

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

22. Limited Mexico Coverage

WARNING

AUTO ACCIDENTS IN MEXICO ARE SUBJECT TO THE LAWS OF MEXICO ONLY - **NOT** THE LAWS OF THE UNITED STATES OF AMERICA. THE REPUBLIC OF MEXICO CONSIDERS ANY AUTO ACCIDENT A **CRIMINAL OFFENSE** AS WELL AS A CIVIL MATTER.

IN SOME CASES THE COVERAGE PROVIDED UNDER **THIS ENDORSEMENT MAY NOT BE RECOGNIZED BY THE MEXICAN AUTHORITIES** AND WE MAY NOT BE ALLOWED TO IMPLEMENT THIS COVERAGE AT ALL IN MEXICO. YOU SHOULD CONSIDER PURCHASING AUTO COVERAGE FROM A LICENSED MEXICAN INSURANCE COMPANY BEFORE DRIVING INTO MEXICO.

THIS ENDORSEMENT DOES **NOT** APPLY TO ACCIDENTS OR LOSSES WHICH OCCUR OUTSIDE OF 25 MILES FROM THE BOUNDARY OF THE UNITED STATES OF AMERICA.

A. Coverage

1. Paragraph **7.** Policy Period, Coverage Territory of the General Conditions is amended by the addition of the following:

   The coverage territory is extended to include Mexico but only for:

   a. "Accidents" or "losses" occurring within 25 miles of the United States border; and

   b. Trips into Mexico of 10 days or less.

2. Condition **5.** Other Insurance of Part **B.** General Conditions under Section **IV** - Business Auto Conditions is replaced by the following:

   The insurance provided by this Provision **22** will be excess over any other collectible insurance.

B. Physical Damage Coverage is amended by the addition of the following:

If a "loss" to a covered "auto" occurs in Mexico, we will pay for such "loss" in the United States. If the covered "auto" must be repaired in Mexico in order to be driven, we will not pay more than the actual cash value of such "loss" at the nearest United States point where the repairs can be made.

C. Additional Exclusions

The following additional exclusions are added:

This insurance does not apply:

1. If the covered "auto" is not principally garaged and principally used in the United States.
2. To any "insured" who is not a resident of the United States.

23. Unintentional Failure To Disclose Hazards

The following is added to Paragraph **B.** General Conditions in SECTION **IV –** BUSINESS AUTO CONDITIONS:

If you unintentionally fail to disclose any hazards existing on the effective date of this policy, we will not deny coverage under this Coverage Form because of such failure. However, this provision does not affect our right to collect additional premium due to us as a result of these undisclosed hazards in accordance with our filed rating plans.

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

24. Mental Anguish Resulting From "Bodily Injury"

The definition of "bodily injury" in SECTION **V** - DEFINITIONS is replaced by the following:

"Bodily injury" means physical injury, physical sickness or physical disease sustained by any person, including "mental anguish" or death resulting from any of these. It does not include mental anguish to any person which occurs in the absence of physical injury, physical sickness or physical disease to that person.

For the purpose of this provision, the term "mental anguish" shall mean any type of mental or emotional illness or distress.

25. Waiver Of Sovereign Immunity

The following provision applies if you are a “governmental entity” or we have added a “governmental entity” to your policy as an additional insured, and the “governmental entity” requires us to obtain permission prior to asserting a defense involving governmental immunity or the jurisdiction of the tribunal over the “governmental entity”:

We shall not raise any defense involving, in any way, the jurisdiction of the tribunal over the “governmental entity”, the immunity of the “governmental entity” or its commissioners, officers, agents or employees, the governmental nature of such entity, or the provisions of any statutes respecting suits against the “governmental entity” without first obtaining express advance permission from the designated representative of the “governmental entity.”

Application of this provision shall not subject us to liability for any portion of a claim or judgment in excess of the applicable limit of insurance.

For the purposes of this provision, “governmental entity” means a state, county, district, municipality, town, township, borough, parish, village, or other political subdivision or governmental agency or subdivision.

26. Application Of This Endorsement

The coverage enhancements provided by this endorsement apply to the Business Auto Coverage Form. If your policy includes other endorsements in addition to this Commercial Automobile Broad Form Endorsement, and there is a conflict between any of the terms of such endorsement(s) and this Commercial Automobile Broad Form Endorsement, the terms of the other endorsement(s) shall be given priority and control over the terms set forth in this Commercial Automobile Broad Form Endorsement, even if the terms of such other endorsement(s) have the effect of limiting, excluding or reducing the coverage provided under this Commercial Automobile Broad Form Endorsement.

All other terms and conditions remain unchanged.

Includes copyrighted material of Insurance Service Office, Inc. with its permission.

TEXAS WAIVER OF OUR RIGHT TO RECOVER FROM OTHERS ENDORSEMENT

This endorsement applies only to the insurance provided by the policy because Texas is shown in Item 3.A. of the Information Page.

We have the right to recover our payments from anyone liable for an injury covered by this policy. We will not enforce our right against the person or organization named in the Schedule, but this waiver applies only with respect to bodily injury arising out of the operations described in the Schedule where you are required by a written contract to obtain this waiver from us.

This endorsement shall not operate directly or indirectly to benefit anyone not named in the Schedule.

The premium for this endorsement is shown in the Schedule.

Schedule

1. (☐) Specific Waiver
   Name of person or organization

   (☒) Blanket Waiver
   Any person or organization for whom the Named Insured has agreed by written contract to furnish this waiver.

2. Operations:

3. Premium:
   The premium charge for this endorsement shall be _____ percent of the premium developed on payroll in connection with work performed for the above person(s) or organization(s) arising out of the operations described.

4. Advance Premium: **NA**

This endorsement changes the policy to which it is attached and is effective on the date issued unless otherwise stated.
(The information below is required only when this endorsement is issued subsequent to preparation of the policy.)

Endorsement Effective 03-31-2025 Policy No. 4087487619 Endorsement No.

Insured **AMERICAN ROAD MAINTENANCE, INC. MIDWEST TAR SEALE** Premium $ **INCL.**

Insurance Company **UNITED STATES FIRE INSURANCE COMPANY**

Countersigned By _____

© Copyright 2014 National Council on Compensation Insurance, Inc. All Rights Reserved.

WAIVER OF OUR RIGHT TO RECOVER FROM OTHERS ENDORSEMENT

We have the right to recover our payments from anyone liable for an injury covered by this policy. We will not enforce our right against the person or organization named in the Schedule. (This agreement applies only to the extent that you perform work under a written contract that requires you to obtain this agreement from us.)

This agreement shall not operate directly or indirectly to benefit anyone not named in the Schedule.

Schedule

ANY PERSON OR ORGANIZATION WITH WHOM OR WITH WHICH YOU HAVE AGREED IN A WRITTEN CONTRACT TO WAIVE YOUR RIGHT OF RECOVERY AGAINST, PROVIDED SUCH WRITTEN CONTRACT:
1. IS CURRENTLY IN EFFECT OR WILL BECOME EFFECTIVE DURING THE TERM OF THIS POLICY; AND
WAS EXECUTED AND BECAME EFFECTIVE PRIOR TO THE OCCURRENCE OF THE INJURY COVERED BY THIS POLICY.
THIS FORM DOES NOT APPLY IN: CA, TX, KY, NH, NJ AND UT.

This endorsement changes the policy to which it is attached and is effective on the date issued unless otherwise stated.
(The information below is required only when this endorsement is issued subsequent to preparation of the policy.)

Endorsement Effective 03-31-25 Policy No. 4087487619 Endorsement No.
Insured AMERICAN ROAD MAINTENANCE, INC. MIDWEST TAR SEALE Premium $ INCL.
Insurance Company UNITED STATES FIRE INSURANCE COMPANY

Countersigned By _____

© 1983 National Council on Compensation Insurance.

EXHIBIT D
GRANT AGREEMENT

(Attached herein by reference. 3-06-0243-025-2025-Grant Agreement)

EXHIBIT E
CONTRACT CHANGE ORDER FORM

County of Santa Barbara
General Services Department
Capital Projects Division
1105 Santa Barbara Street
Santa Barbara, California 93101
(805) 569-3055 FAX (805) 568-3249

CHANGE ORDER NO. *{CCO NO.}*

PROJECT TITLE: {PROJECT TITLE} **PROJECT NO.:** {PRJNO.}

CONTRACTOR: {LEGAL CONTRACTOR NAME} **CONTRACT NO.:** {CONT. NO.}

Except as provided herein, all terms and conditions of the contract referenced above remain unchanged and in full force and effect. The contractor may not exceed the price shown below without further written instruction from the Owner.
NOTE: This contract Change Order is not effective until signed by the Owner's Project manager and until signed by the Owner's Authorized Representative.

DESCRIPTION OF WORK TO BE PERFORMED:

The purpose of Contract Change Order **{CCONO.}** is:

By reason of this Change Order, the Contract Amount and Completion Date is hereby changed as shown below:

AMOUNT OF THIS CHANGE: {$AMT} **ADDT'L DAYS AWARDED**: {NO.DAYS} DATE ISSUED: {DD/MM/YY}

We the undersigned have given careful consideration to all aspects of the change order proposed and hereby agree.

Contractor acknowledges receipt of this Change Order and the not to exceed amount stated above. Contractor understands that the final price for this work will be determined in accordance with General Conditions.
CONTRACTOR:

NAME AND TITLE OF SIGNER (Type or Print):

(Signature of person authorized to sign) Date

By signing below, Owner revises the Contract as provided above, in accordance with General Conditions.

OPM: (Type or Print)

Owner Project Manager Date

OAR NAME: {NAME}, Capital Division Manager

Owner's Authorized Representative Date
